

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी -1

पत्रांक :- 1421

/दिनांक:- 9/07/2020

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी - 1

सेवा में,

अधीक्षक अभियंता,
ग्रामीण कार्य विभाग, कार्य अंचल
मुजफ्फरपुर।

विषय:- शीर्ष मुख्यमंत्री ग्राम संपर्क योजना अंतर्गत दुबियाही पीच रोड भवानीपुर से अनुसूचित जाति टोला निर्माण कार्य का समय वृद्धि की स्वीकृति के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष मुख्यमंत्री ग्राम संपर्क योजना अंतर्गत दुबियाही पीच रोड भवानीपुर से अनुसूचित जाति टोला निर्माण कार्य संवेदक मनजीत कुमार को आवंटित किया गया था। इस कार्य का समय वृद्धि हेतु संवेदक द्वारा विहित प्रपत्र में भरकर आवेदन समर्पित किया गया है, जिसे मूल रूप में संलग्न किया जा रहा है। एकरारनामा से संबंधित मूल विषय निम्न प्रकार है:-

1. एकरारनामा संख्या : 28SBD/2019-20
2. एकरारनामा राशि : 27.70046 लाख
3. एकरारनामा के अनुसार कार्य प्रारंभ करने की तिथि : 20.05.2019
4. एकरारनामा के अनुसार कार्य समाप्ति की तिथि : 19.02.2020
5. और जो अधिक समय की माँग की जा रही है : 27.05.2020

संवेदक द्वारा आवेदन पत्र एवं संलग्न विहित प्रपत्र में कार्य में विलंब का कारण अतिक्रमण तथा जमीनी विवाद दर्शाया गया है। विदित है कि अंचलाधिकारी कुढ़नी के पत्रांक 1056 दिनांक 12.06.2020 द्वारा दिये गये पत्र में जमीन विवाद रहने के कारण पथ का कार्य बाधित रहा।

अतः संवेदक से प्राप्त आवेदन पत्र विहित पत्र सहित, गुण नियंत्रण प्रतिवेदन की छाया प्रति, MIS Report, शपथ पत्र, मापी पुस्त की छाया प्रति तथा पथ का फोटोग्राफ मूल में संलग्न कर भेजते हुए दिनांक 27.05.2020 तक समय वृद्धि स्वीकृत करने की अनुशंसा की जाती है।

अनुलग्नक : यथोक्त

विश्वासभाजन

कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

1. अभिकर्ता का नाम : मन्जित कुमार
2. कार्य का नाम : दुबियाही पीच रोड भवानीपुर से अन्तर्मुखित जाति होना ।
3. एकरारनामा संख्या : 28/SBD/19-20
4. एकरारनामा अंतर्गत कार्य का मूल्य : 27,70,046.00
5. प्रशासनिक स्वीकृति की राशि : 28,12,230.00
6. एकरारनामा के अनुसार कार्य प्रारंभ की तिथि : 20.05.2019
7. एकरारनामा के अनुसार कार्य समाप्ति की तिथि : 19.02.2020
8. और अधिक समय जो माँग की जा रही है : 27.05.2020
9. तिथि एवं समय जिसमें कार्य संपादन में व्यवधान उत्पन्न हुआ : 01.10.2019
10. आवेदन की तिथि तक कार्य पूर्णतः का अनुपात : 100%.
11. क्या पूर्व में समय वृद्धि की गयी थी, यदि हाँ तो कब तक तिथि अंकित करें : नहीं
12. पूर्व में समय वृद्धि किस कारण दी गयी थी : X
13. अभिकर्ता का हस्ताक्षर : *Mangaj Kumar*
14. अनुशंसा की तिथि तक कार्य की अद्यतन स्थिति : कार्य पूर्ण
15. कनीय अभियंता की अनुशंसा : जमीन विवाद के कारण कार्य में विराम हुआ। समय वृद्धि की स्वीकृति दी जा सकती है। *Bumw*
10.06.2020
16. अवर प्रमंडल पदाधिकारी की अनुशंसा स्पष्ट एवं ठोस कारण सहित : *due to land dispute, work could not completed on time, T/E may be given. K. Anand*
10/06/20
17. कार्यपालक अभियंता की अनुशंसा स्पष्ट एवं ठोस कारण सहित अपने लिखावट में : *Recommended A.E.*
29/6
18. अधीक्षण अभियंता की अनुशंसा :

समय वृद्धि हेतु प्रपत्र

योजना शीर्ष:- MMGSY (SC)

पथ का नाम :- दुधियाही पीच रोड भवानीपुर से आगुश्वित जाति रोना ।

1. एजेन्सी का नाम :- मन्जीत कुमार
2. प्रस्तावित पथ किस पैकेज में है
या एकल पथ है :- स्कल पथ है।
3. पैकेज के सारे पथों के पूर्णता प्रमाण पत्र :- कार्य पूर्ण
4. समय वृद्धि कारण का साक्ष्य :- सलबन है।
5. संवेदक द्वारा भविष्य में वित्तीय दावा नहीं करने का प्रमाण पत्र :- सलबन
6. मापी पुस्त पर अंकित कार्य विशिष्टियों के अनुरूप पूर्ण है एवं
मापी पुस्त की छाया प्रति कार्यपालक अभियंता द्वारा सत्यापित :- सलबन
7. अंतिम विपत्र पर कार्यपालक अभियंता का हस्ताक्षर :- सलबन
8. कनीय अभियंता एवं संवेदक के साथ खीचा हुआ तीन फोटो पथ
का रोड फर्निचर, मुख्य सूचना पट्ट, रोड फलैंक, किमी पोस्ट का
फोटो कार्यपालक अभियंता द्वारा सत्यापित :- सलबन
9. संवेदक द्वारा अनुरक्षण Defect Libility में एकरारनामा के अनुसार
संतोषप्रद अनुरक्षण कार्य का संपादन किया जा रहा है :- हाँ
10. ATR लंबित है या नहीं :- नहीं


Sumu
10.06.2020
कनीय अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रशाखा

K. Anand
10/06/20
सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल

27/5/20

HS 0000345962

GOVERNMENT OF BIHAR
e-Court Fee



DATE & TIME :

29-MAY-2020 10:40:25

NAMES OF THE ACC/ REGISTERED USER :

SREINFRASTRUCTURE FINANCE LIMITED

LOCATION :

CIVIL COURT MUZAFFARPUR

e-COURT RECEIPT NO :

BRCT2931E2038K643


e-COURT FEE AMOUNT :

₹ 90

(Rupees Ninety Only)



BRCT2931E2038K643

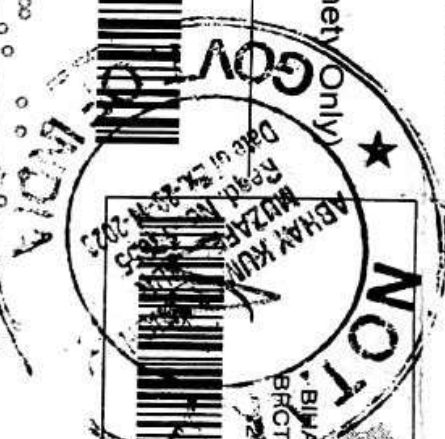


BIHAR COURT FEE
BRCT2750493E2011N
27-MAY-2020

₹ 10

Statutory Alert : The authenticity of this e-Court fee receipt should be verified at www.sreinfra.stamp.gov.in. Any discrepancy in the details on this receipt and as available on the website renders it invalid. In case of any discrepancy please inform the Competent Authority. This receipt is valid only after verification & locking by the Court Official.

Book No... 01. Sr. 39.
Date... 29 MAY 2020



समक्ष,

लेख्य प्रमाणक,
मुजफ्फरपुर।

शपथ-पत्र

मैं मंजीत कुमार, ई 121, पीसी कॉलोनी, कंकड़बाग, पटना-20 शपथ पूर्वक बयान करता

हूँ:-

1. यह कि मैंने "दुबियाही पीच रोड भवानीपुर से अनुसूचित जाति टोला पथ" तक मुख्यमंत्री ग्राम संपर्क योजना अंतर्गत सड़क का निर्माण कार्य पूर्ण कर चुका हूँ।
2. यह कि ग्रामीण जमीन विवाद के कारण समय वृद्धि की मांग कर रहा हूँ।
3. यह कि समय वृद्धि के पश्चात रख-रखाव एवं जमानत की राशि के अतिरिक्त वित्तीय दावा नहीं करूँगा।
4. यह कि शपथ पत्र के सारे तथ्य मेरी जानकारी में सही है।

अतः यह शपथ-पत्र है।

Manjeet Kumar
शपथकर्ता का हस्ताक्षर

मैं प्रमाणित करता हूँ कि शपथकर्ता ने मेरे समक्ष अपना हस्ताक्षर बनाया।

Deponent Solemnly
Affirmed & declared before me

ABHAY KUMAR SINGH
Notary, Regd 13655
Court of 12th Affirm

Mukesh Kumar
अधिवक्ता
Advocate
29.05.2020

HEAD - MMGSY

NAME OF ROAD : DUBIYAH PITCH ROAD BHAWANIPUR TO ANUSUCHIT JATI TOLLA



HEAD - MMGSY
NAME OF ROAD : DUBIYAH PITCH ROAD BHAWANIPUR TO
ANUSUCHIT JATI TOLLA



Bum
10.06.2020
JE

AE

For 29/6

अंचल कार्यालय, कुढ़नी, मुजफ्फरपुर

पत्रांक:- 1058 /

प्रेषक,

अंचल अधिकारी

कुढ़नी

सेवा में,

सहायक अभियंता

ग्रामीण कार्य विभाग

कार्य अवर प्रमंडल कुढ़नी

दिनांक:- 12/06/2020 /

विषय:- मुख्यमंत्री ग्राम सड़क सम्पर्क योजना का सीमांकन के संबंध में।

महाशय,

उर्पयुक्त विषयक सूचित करना है कि मुख्यमंत्री ग्राम सड़क सम्पर्क योजना अंतर्गत दुबियाही पक्की सड़क से भवानीपुर अनुसूचित जाति टोला तक अंचल अमीन से सीमांकन कराया गया। ग्रामीणों से पुछताछ से पता चला कि सड़क किनारे सीमांकन को लेकर ग्रामीणों के बीच विवाद था। कई बार ग्रामीणों के साथ बैठ कर अंचल अमीन द्वारा दिनांक 10.06.2020 को उक्त कार्य का निस्तार करा दिया गया। जिस कारण सड़क निर्माण कार्य में विलम्ब हुआ।

सूचनार्थ एवं आवश्यक कार्रवाई हेतु प्रेषित।

विश्वासभाजन


अंचल अधिकारी

कुढ़नी

Wind:-CE-3. Palma

Division:-Muzaffarpur East-1

No Of Visit:-65

Contractors Black List

Contractors Black List Maintenance

MONTHLY PROGRESS ROAD(PHYSICAL PROGRESS)

Содержание: 1. Введение. 2. Описание системы. 3. Требования к системе. 4. Анализ системы. 5. Проектирование системы. 6. Реализация системы. 7. Тестирование системы. 8. Заключение.

Scheme	MMGSY[SC]	Fin Year	2018-19

Name of Road(English) DUBIYAH PICH ROAD BHAWANIPUR to ANUSUCHIT JATI TOLA(Complete)

Selection of Schemes

Amount: 26.94800

Technical Approval

Amount: 26.94800

Amount: 27.47700
Updated Expenditure (Maintenance Amt)

Amount: 0.000

agreement

Main Work Amt: 24.205460

Expenditure(In Lakhs)

Upto 31/03/20: 0.000000

Sub Base(In KM)

Upto 31/03/20: 0.000

ase(In KM)

Upto 31/03/20: 0.000

surface(In KM)

Upto 31/03/20: 0.000

Project Status: Complete

Environmental Social Management & FrameWork

road Insurance YES (Policy No.2019-E00€

Upload Files:

<https://sqms.nwdbihar.gov.in/Entry/RoadMonthlyProgress.aspx>

REGIONAL ENGINEER
R.W.D., MUZAFFARPUR

GRADATION TEST OF GAB - Grading - 7
Dubiyahi Pich Road Bhawanipur TO Anusuehit Jati Tola
 NAME OF WORK:- under NMGS

NAME OF DIVISION:- R.W.D. WORKS DIVISION Muz. East-1 RECEIPT
DATE OF COLLECTION 17.12.19

NAME OF AGENCY:- Manjeet Kumar
281 SBD/19-20 DATE OF TEST 24.12.19
 REF:- PIU (A.E. R.W.D. Works Sub. Div. Kudhami Muz. East-1) Letter No - 61 Dt. 25/10/19

Sl. No	Sieve No. m.m	Weight Retained (kg)	% Wt. of Retained	Cumulative % Retained (kg)	% of passing (kg)	Required Limit %	Remarks
1	2	3	4	5	6	7	8
			<u>ch - 210M</u>				
			<u>wt. of sample - 14.551 kg</u>				
	75	Nil	Nil	Nil	100.00	100	
	26.5	6.080	41.78	41.78	58.22	55-75	<i>Permissible</i>
	4.75	4.491	30.86	72.64	27.36	10-30	
	0.075	3.063	21.05	93.69	6.31	2-10	

MEMO NO 1262 Dt. 28.12.2019

COPY FORWARDED TO - EXECUTIVE ENGINEER
 R.W.D., WORKS DIVISION Muz East-1

[Signature]
24.12.19
 L.A.

[Signature]
24/12/19
 A.E.

[Signature]
24.12.19
 E.E.

PHYSICAL & GRADATION TEST OFWBM - Gr-IIINAME OF WORK Durblyahi Pich Road Bhawanipura To Anusuchit Jati Tola
Under mmsyNAME OF DIVISION: - R.W.D WORKS DIV Muz. East-1AGENCY :- Mamteet Kumar
28/ SBD/ 19-20RECEIPT 17.12.19
DATE OF COLLECTION:-REF :- PIU (A.E. R.W.D. works Sub Div. Kudhani muz. East-1 DATE OF TEST :- 24.12.19Letter No - 61 dt 25.10.19PHYSICAL TEST

SL.NO	A.I.V		WATER ABSORPTION		REMARKS
	TEST VALUE %	REQUIRED LIMIT %	TEST VALUE %	REQUIRED LIMIT %	
	21.49%	40%	753%	3%	Permissible

GRADATION TEST

Sl.no	Sieve No m.m	Weight Retained (KG)	% Wt of Retained	Cumulative % Retained (Kg)	% of passing (kg)	Required limit %	Remarks
			ch -	225-m.			
		wt. of Sample -		25.696 kg.			
		wt. of Screening -		4.530 kg.			
		wt. of S/m -		21.166 kg.			
	63	Nil	Nil	Nil	100.00	100	
	53	0.763	3.60	3.60	96.40	95-100	
	45	6.164	29.12	32.72	67.28	65-90	Permissible
	22.4	12.227	57.75	90.49	9.51	0-10	
	11.2	1.852	8.75	99.24	0.76	0-5	

Memo No 1263Date 28.12.2019

Copy To - E.E R.W.D. Works Div

Muz. East-1

[Signature]
24.12.19
L.A

[Signature]
24/12/19
A.E

[Signature]
24.12.19
E.E

ISSUE NO:- 584 DATE: 11.5.20

REGIONAL LABORATORY

RURAL WORKS DEPARTMENT, MUZAFFARPUR

TEST RESULT FOR BINDER CONTENT (BITUMEN) OF PAVING MIXTURE THROUGH CERTRIFUGE

Dubiyahi Pich Road Bhawanipuri To Anusuchit Jaha Tola - under MMSG

NAME OF ROAD:-

NAME OF WORKS DIVISION:- R.W.D. Works Division Mu2 East-1

NAME OF AGENCY:- mandak Kumar

REF./AGGEMENT:- 28/SDD/19-20

LOCATION:- PIV (A-E-R.W.D. works sub.Div. Kudhari Mu2. East-1 Letter No- 48 dt 6.5.20

Ch- 275 m.

Receipt
DATE OF COLLECTION:- 11.5.20

DATE OF TEST:- 15.5.20

Sl. NO	OBSERVATIONS	NO. OF TEST			Mean Value	Remarks
		1	2	3		
1	Wt. of mix taken before extraction (A)	486	450	448		
2	Wt. of filter paper before extraction (B)	8.275	6.740	7.935		
3	Wt. of mix after extraction (C)	465	431	429		
4	Wt. of filter paper after extraction (D)	8.630	7.000	7.545		ble
5	Wt. of filler collected from extract after allowing for setting (E)	0.985	0.475	0.720	4.046	Percentage of Bitumen
6	Wt. of filler collected in filter paper (D-B)=F	0.355	0.260	0.210		
7	Wt. of aggregate + filler collected after extraction (C+E+F)=G	466.340	431.735	429.930		
8	Percentage of Bitumen (In the mix) $\frac{(A-G) \times 100}{A}$	4.045	4.059	4.033		

Copy To :- E.E R.W.D Works Division Mu2 East-1

15.5.20
L.A

15/5/20
A.E

28/5/20
E.E
कार्यवाहक अभियंता
आजीन कार्क विभाग
कोशीगंगा, मुजफ्फरपुर

Isionak bill No 8,79,695-00

Sch. XLV-Form No. 134
 Details of actual measurement
 12

Particulars	No.	L.	B.	D.	Contents of area
		Memo of Payment			
S. 9.1	79	172	00		
G. 1.1	79	375	00		
S. 1.1	87	97			
L. 1.1	87	97			
CONST	187	97			
S. 1.1	87	97			
Regulatory	23024				
Choke	732309				

Total 8,79,695-00
 Parsed for Rs. 8,79,695-00
 Lakh seventy nine thousand six
 hundred ninety three only

Executive Engineer
 RWD Works Division
 Muzaffarpur East-1
 3/12/19

T.V. NO. PPNB/19/2844800002K96
 24-04-19

clp
 9/12
 4/12

2nd

Sch. XLV—Form No. 134

Details	
No.	

Paid - 369461

Total - 369461

Lady Six thousand four hundred

Sixty one only

Executive Engineer

RWD Works Division
Farapur East.

Executive Engineer
RWD Works Division
Roorkee East

2/5/20

20050822 28/28/20

Continuation

Ch XLV Form No 134

Particulars	Details of actual measurement			Contents of area
	No.	L	H	
				RI R ₁ 495312.50
①	24	Boundary and fixing MGSY		
		for maintaining 5 year boundary.		
		Qty vide TMBP(18) = 2 Nos		
		@ R 11726 = 95 each - R 23454 = 0		
②	26	Boundary and fixing of		
		200M stone post.		
		Qty vide TMBP(18) = 2 Nos		
		@ R 594291 each - R 1190 = 0		
③	25	Boundary and fixing boundary		
		KM posts.		

		Qty vide TMBP(18) = 1 No		
		@ R 1900 = 89 each - R 1905 = 0		
④	27	Boundary and fixing RCC		
		boundary pillar.		
		Qty vide TMBP(19) = 7 Nos		
		@ R 512 = 73 each - R 9589 = 0		
⑤	29	Boundary and fixing 5 Years		
		maintenance band.		
		Qty vide TMBP(19) = 1 No		
		@ R 11726 = 95 - R 11727 = 0		
⑥	30	Construction of road and bankmt		
		width 10m up to 1000M		
		Qty vide TMBP(19) = 572 94M		
		@ R 174 = 91/M ³ → R 99869 = 0		
		R 1140059 = 0		

Continuation

Job XLV Form No 134

Particulars	Details of actual measurement				Quantity of Area
	No.	L	B	D	
				Rt. G.	11401.57
(14) Provisioning of road embankment					
as per local up to 100 ft					
Qty vide T.M.B.P (19) = 145.27					
@ 6.141 = 10/11					20177.50
(15) Provisioning and fixing of RCC					
Concrete posts					
Qty vide T.M.B.P (19) = 8 Nos					
@ 512 = 77 each					4102.00
(16) Provisioning and fixing of M.H.C.S.Y					
Log board					
Qty vide T.M.B.P (19) = 1 No					
@ 11726 = 95 each					11727.00

(17) Provisioning and fixing of					
31 triangular board					
Qty vide T.M.B.P (19) = 2 Nos					
@ 4502 = 98 each					9006.00
(18) Provisioning and fixing of 600 mm					
32 Circular board					
Qty vide T.M.B.P (20) = 1 No					
@ 6433 = 43 each					6433.00
(19) Provisioning and fixing of 600x450 mm					
33 Rectangular board					
Qty vide T.M.B.P (20) = 1 No					
@ 6356 = 09 each					6356.00
(20) Provisioning and applying					
10 primer coat					
				R	1197880.00

Continuation

Continuation
JL

B.S. Form No 131

	Quantity of material			Quantity of work
	I	II	III	
Material Statement				
(i) Stone chips = 40.92 MT				
0.475 = 28/MT				
(ii) Bitumen = 2.879 MT				
(iii) Bitumen Emulsion SS-1 = 1.288 MT				
RS-1 = 0.417 MT				

Supply of Bitumen from HP Co Ltd.

Invoice No.	Date	Qty
13076GI 2000153	04-05-2020	3.286 MT

Consumption = 2.879 MT

Balance = 0.357 MT

Bitumen Emulsion for Emulze Bitumin Puta

Invoice No - FY 10-20 GB 346 dt 31-3-2020

SS-1 = 1.400 MT
Consumption = 1.288 MT
Balance = 0.112 MT
RS-1 = 0.600 MT
Consumption = 0.417 MT
Balance = 0.183 MT

Sum
27-05-2020
TLK

K. Dumbala
27/05/20
A.E
