



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail – eerwd.marhaura@yahoo.com

पत्रांक:- 548(अनु०)

मढ़ौरा/दिनांक:- 16/04/2025

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:- शीर्ष **MR-3054** योजनान्तर्गत बिहार ग्रामीण पथ नई अनुसूचना नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु०, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-**3054 (MR-3054)** अंतर्गत बिहार ग्रामीण पथ नई अनुसूचना नीति-2018 के तहत संवेदक जे०के० एण्ड कम्पनी के द्वारा पथ में किये गये कार्य का अध्याचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अध्याचना-पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अध्याचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं०-18 के अनुरूप पथ में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथ में कराये गये कार्य का भुगतान किया जा सकें।


अनु०-1) अध्याचना प्रपत्र।

2) 19 ए प्रपत्र।

3) BOMP Indicator Report संलग्न।

विश्वासभाजन


15/4/25


15/04/25
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।


15/4/25

FORM GER-19-A

(See Government of India'S Decision (I) below Rule -150)

Form of Utilization Certificate up to the Month of March-2025


PIU:- Executive Engineer RWD Works Division, Marhaura

SL No	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 Rural Road Maintenance Policy-2018 (Ledger ID-7069)	सचिव ब्राडा के पत्रांक-29 वे दिनांक-30-03-2025	10760.54279	Certified that out of Rs- 10760.54279 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22, 22-23, 23-24 & 2024-25 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 10714.22499 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-46.31780 Lacs remaining unutilized at CFMS the end of the period under report.


15/4/25


Sr. DAO

R.W.D. (W) Division Marhaura


15/04/25

Executive Engineer

R.W.D. (W) Division Marhaura


15/4/25

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Saran jila antargat amnour prakhand me dorahi kethal P.C.C path se mahrauli mahadalit tola hote hue aphar bank tak path nirmaan.	31306505001	Lt. - No-6115 Date-04-12-2023	2.470	146.91000	111.08038	18.07852	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3126.14	25 mm	5%	63.24381	63.24381	47.25585	Work Completed
2	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Jalalpur Shivganj PMGSY Path To Pakridih baniya Tola	31306512019	Lt. - No-6115 Date-04-12-2023	1.200	86.59000	68.59394	7.08893	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3019.83	25 mm	5%	39.07092	39.07092	27.91029	Work Completed
3	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Amnour Firojpur PMGSY Path To Uttar Tola Tak	31306513010	Lt. - No-6115 Date-04-12-2023	1.400	79.33000	59.12531	9.61231	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3179.85	25 mm	5%	32.34969	32.34969	26.57749	Work Completed
4	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	L062-Salkhua Madhoura PMGSY Rd. to Manourpur (VR41)	31306502030	Lt. - No-6115 Date-04-12-2023	1.091	65.41200	49.27845	8.30197	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3050.45	25 mm	5%	25.54185	25.54185	21.72014	Work Completed
5	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	L045-Repura Rasulpur rd. to Shikarpur (VR26)	31306502024	Lt. - No-6115 Date-04-12-2023	1.010	41.86800	28.07923	9.27163	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2721.63	25 mm	5%	21.46628	21.46628	6.26135	Work Completed
6	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	L068-Beldehi Amnour Main Rd. to Balha Mahi River (VR47)	31306502034	Lt. - No-6115 Date-04-12-2023	0.780	52.32800	40.80178	5.04816	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2999.25	25 mm	5%	36.58979	36.58979	4.19073	Work Completed

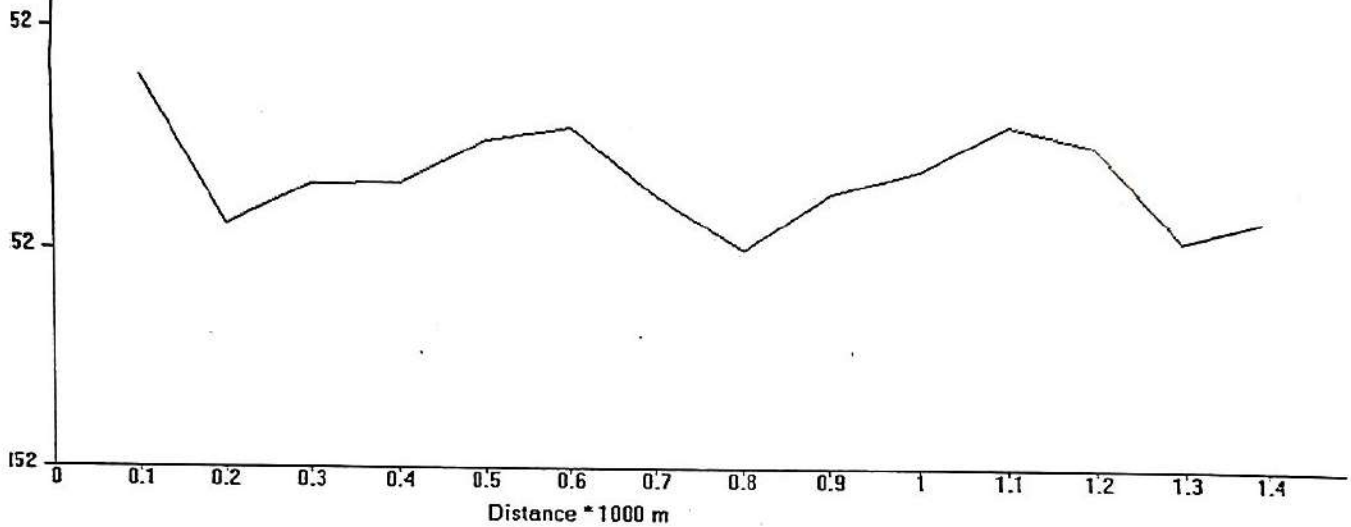
Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
7	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Katsa Jogani PMGSY Path To Dasai Sah Tola Tak	31306512020	Lt.- No-6115 Date-04-12-2023	1.400	59.96500	40.50470	10.73996	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2774.64	25 mm	5%	31.27367	31.27367	8.92581 ✓	Work Completed
8	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	KATSA MARHAURA PMGSY PATH TO RAHIMPUR KURMI TOLA.	31306512018	Lt.- No-6115 Date-04-12-2023	0.900	51.23800	38.39203	6.77279	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2954.55	25 mm	5%	21.58164	21.58164	16.59971 ✓	Work Completed
Total:-															271.11765	271.11765	159.44137	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to-date Physical Progress has been Uploaded in MIS.

15/04/25

15/04/25
Executive Engineer
Rural Work Department
Work Division, Marhaura
15/04/25

File : F:\BUMP\JK AND COMPANY BUMP\Katsa Jogani PMGSY Path To Dasai Sah Tola Tak\125673.Xls, Section
Name of Customer : M/S J K And Company, Name of Work/ Road : Katsa Jogani PMGSY Path To Dasai Sah Tola



Signature
04/10/24
26

Signature
10/10/2024

Signature
07/10/24
EE

Name of Customer :M/S J K And Company

Name of Work/ Road :Katsa Jogani PMGSY Path To Dasai Sah Tola Tak

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	Longitude	Event
3/24	17:37:00	52	0.1	140	30.1	1400	3232	G	25.85386	84.91633	Normal
3/24	17:37:14	52	0.1	280	30.5	2800	2569	G	25.85374	84.91704	Normal
3/24	17:37:28	52	0.1	220	30.2	2200	2754	G	25.85362	84.91769	Culvert
3/24	17:37:45	52	0.1	320	30.1	3200	2759	G	25.85356	84.91832	Curve
3/24	17:38:02	52	0.1	110	25.8	1100	2956	G	25.85383	84.91901	Normal
0/24	17:38:15	52	0.1	190	30.5	1900	3008	G	25.85443	84.91912	Normal
0/24	17:38:29	52	0.1	220	30.7	2200	2698	G	25.85468	84.91975	Curve
0/24	17:38:42	52	0.1	270	30.3	2700	2452	G	25.85443	84.92247	Normal
0/24	17:39:00	52	0.1	270	27.9	2700	2689	G	25.85402	84.92269	Normal
0/24	17:39:23	52	0.1	300	25.8	3000	2785	G	25.85346	84.92249	Curve
0/24	17:39:38	52	0.1	310	28.8	3100	2985	G	25.85299	84.92244	Normal
0/24	17:39:52	52	0.1	250	26.9	2500	2898	G	25.85008	84.92197	Culvert
0/24	17:40:08	52	0.1	300	25.5	3000	2478	G	25.84895	84.92207	Normal
0/24	17:40:33	52	0.1	300	26.8	3000	2582	G	25.84895	84.92212	Normal
Length			1.4	IRI Value		2774.64					

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 0$$

$$Y = 249$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Signature
04/10/24

Signature
04/10/24

Signature
07/10/24
EE

Lab Job number :384

Date :04/10/2024

Name of Customer :M/S J K And Company

Name of Work/ Road :Katsa Jogani PMGSY Path To Dasal Sah Tola Tak

Road category

Sr.no Location of Corrected U.I
test(in km) value(mm/km)

1	0.1	3232 G
2	0.2	2569 G
3	0.3	2754 G
4	0.4	2759 G
5	0.5	2956 G
6	0.6	3008 G
7	0.7	2698 G
8	0.8	2452 G
9	0.9	2689 G
10	1	2785 G
11	1.1	2985 G
12	1.2	2898 G
13	1.3	2478 G
14	1.4	2582 G

[Signature]
04/10/24

[Signature]
04/10/24

[Signature]
07/10/24
EE

NAME OF ROAD: — KATBA JOHANI PMB & PATH TO DASAI
SAH TOLA TAK.

Schedule XLV-Form No. 134

M.B. NO. — 1000.

Executive Engineer
Rural Work's Department
Works Division, Marhaura

DIVISION

MR 3054
NMP 2018
24/0002

APINDUR.

SUB-DIVISION

Measurement Book

J. K. And Company.

2nd & Final Bill

9

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Road—	M/R	05 Road from Katsa			
		Jigni Pmash to dani shah			
		tola			
Agency—	J.K. Company				
Agreement No—	03/MR-3054-N/MRD/2024-25				
Date of commence—	22.08.24				
Date of completion—	04.05.2025				
Record Entry:—					
①	Construction of sub-grade and earthen Shoulders with approved material/ do-do all complete Job				
	10X2X 30X	1.10X	$\frac{0.35+0.32}{2}$	= 221.10m ³	
	5X2X 30X	1.0X	$\frac{0.38+0.35}{2}$	= 109.50m ³	
	10X2X 30X	1.125X	$\frac{0.35+0.32}{2}$	= 232.875m ³	
	10X2X 30X	1.10X	$\frac{0.4+0.32}{2}$	= 237.60m ³	
	5X2X 30X	1.12X	$\frac{0.32+0.34}{2}$	= 110.88m ³	
	1X2X 10X	1.125X	0.350	= 7.875m ³	
	3X2X 30X	0.50X	0.150	= 13.50m ³	
	1X2X 10X	0.50X	0.150	= 1.50m ³	
				= 934.83m ³	
②	R.C.C m-15 grade Km				
	Local Stone do do				
	all complete Job				
(i)	Km Stone				03 Nos.
(ii)	200 m Stone				05 Nos.

Continuation

Abstract of cost

2nd Final bill

13

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1/1	Clearing and grubbing of Road land-do-do-all complete Job				
TMBP-01	0.210 Ha	@	76926.08/11	R	16154.00
2/3	Construction of G.S.B gr-II by providing well graded material do-do-all complete Job				
TMBP-01	11.225 m ³	@	2541.33/m ³	R	28526.00
3/4	Prov. laying and spreading WBM gr-II do-do-all complete Job				
TMBP-02	12.294 m ³	@	5624.13/m ³	R	69143.00
4/5	Prov. laying & spreading WBM gr-III do-do-all complete Job				
TMBP-02	49.164 m ³	@	5144.83/m ³	R	252940.00
5/6	Prov. & applying Primer Coat with SS-I do-do-all complete Job				
TMBP-03	655.52 m ²	@	57.36/m ²	R	37600.00
				C.O.R	4.04 363.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				B.F.R	4,04,363.00
6/7	Prov and applying tack coat with RS-1				
	do-do-all complete Job				
TMBP-03	487500m ² @ 16.47/m ² - R 80291.00				
7/8	Prov & applying S.D.B.C				
	25mm thick - do-do-all complete Job				
	121.876 m ³ @ 14675.14/m ³ - R 17,88,547.00				
8/9	Construction of D.L.C				
	Sub base - do-do-all complete Job				
TMBP-02	1.50m ³ @ 5233.08/m ³ - R 7850.00				
9/10	Construction of m-30 Panel concrete - do-do-all complete Job				
TMBP-02	47.35m ³ @ 9252.89/m ³ - R 4,38,124.00				
10/11	Prov & Firing mmGSY in Formatory 100 - do-do-all complete Job				
TMBP-04	02 Nos @ R 10927.63 each - 21855.00				
TMBP-11	01 Nos @ R 10927.63 each - 10927.63				
	R - 32783.00				
	C.O.R 27,51,958.00				

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				B.F.R	27,51,958.00
11/02	Construction of sub-grade & earthen				
	Shoulders - do - do -				
	all complete Job				
TMBP-09	69.30 m ³	@	R 264.72/m ³	- R	18345.00
TMBP-09	934.83 m ³	@	R 264.72/m ³	- R	247,468.00
				R	2,65,813.00
12/11	R.C.C m-15 grade Km				
	Stone - do - do - all				
	Complete Job				
TMBP-09	Km Stone				
	03 Nos	@	R 2913.65 each	- R	8741.00
	200 m Stone				
TMBP-09	05 Nos	@	R 813.72	- R	4069.00
13/12	Retro-reflectorised				
	traffic signs - do - do				
	all complete Job				
TMBP-10	2.88 m ²	@	R 14995.56/m ²	- R	43187.00
14/13	Proc. & Fixing of retro-				
	reflectoised cautionary				
	- do - do - all complete Job				
(i)	600 mm equilateral				
	& triangle				
TMBP-10	06 Nos	@	R 4436.68 each	- R	26620.00
				CO - R	31,00,388.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				B.F.R	3100388.00
(ii) 600mm circular					
TMBP-10	01 Nos	@ R 4307.51	- R	4308.00	
(iii) 600mm x 450mm rectangles					
TMBP-10	01 Nos	@ R 4162.98	- R	4163.00	
(iv) 900 mm Side octagon					
TMBP-10	01 Nos	@ R 8632.34	- R	8632.00	
15/14 R.C.C m-15 grade beam					
dry pillars - do - do -					
all complete Job					
TMBP-10	04 Nos	@ R 6779.39	- R	43,353.00	
16/15 Planting of trees					
by the road side -					
do-do-all complete Job					
TMBP-10	65 Nos	@ R 1305.10	- R	84831.00	
17/16 Prov. & laying of hot					
applied thermoplastic					
Compound - do do-all					
Complete Job					
For S.T. portion &					
Pedestrian crossing					
TMBP-10	260.75 m ²	@ R 886.50/m ²	- R	2,31,155.00	
For C.C. Portion					
TMBP-11	20 m ²	@ R 988.82/m ²	- R	19776.00	
				C.O. R	34,96,606.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				B.F.R	3496606.00
18.	H.P.C 600 mm ϕ				
	Parapet painting				
	Painting two coats				
	including primer				
	coat - do - do - all				
	complete Job				
TMBP-11	14.40 m ²			@ R 136.59/m ²	R 1967.00
	H.P.C 1000 mm ϕ				
	Parapet repair				
19.	Brick masonry work				
	in cement mortar				
	(1:3) in parapet -				
	do - do - all complete Job				
TMBP-11	6.06 m ³			@ R 6550.60/m ³	R 39,696.00
20.	Plastering with				
	Cement mortar (1:4)				
	on brick work - do -				
	do - all complete Job				
TMBP-12	43.20 m ²			@ R 200.09/m ²	R 8643.00
	Painting two coats				
	including primer coat				
	do - do - all complete Job				
TMBP-12	43.20 m ²			@ R 136.59/m ²	R 5901.00
					RS - 35,52,813.00

Continuation

Continuation
