

**कार्यपालक अभियंता का कार्यालय**  
**ग्रामीण कार्य विभाग कार्य प्रमण्डल, बाँका-2**

पत्रांक 3170 / बाँका

दिनांक 09/12/2025

प्रेषक,

कार्यपालक अभियंता  
ग्रामीण कार्य विभाग,  
कार्य प्रमण्डल, बाँका-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव  
बिहार ग्रामीण पथ विकास अभिकरण, पटना।

विषय:-


शीर्ष 4515 मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के कार्यों के भुगतान हेतु निधि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के भुगतान हेतु 4,30,19,057/- (मो० चार करोड़ तीस लाख उन्नीस हजार संतावन रुपये) मात्र की अधियाचना विहित प्रपत्र में तैयार कर आपके आवश्यक कार्यवाई हेतु समर्पित की जाती है।

- अनु० :-
1. विहित प्रपत्र में आवंटन की मांग।
  2. उपयोगिता प्रमाण पत्र।
  3. मापी पुस्त की छाया प्रति।

विश्वासभाजन

  
कार्यपालक अभियंता  
ग्रा०का०वि०, कार्य प्रमण्डल  
बाँका-2  
09/12/25



**GFR 12-B**  
[See Rule 256 (2)]

**FORM OF UTILIZATION CERTIFICATE**

(1) Certified that out of the Loan of Rs. **5056.44559**, Sanctioned under MMGSUY (RRSMP-GEN), Lt. No.-102 dated.-18.11.2025 in favour of E.E.R.W.D.(W) Division Banka-2 during the year **2025-26**, an amount of Rs. **5056.15539**, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. **0.29020** remaining unutilized at the end of the year.-2024 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Allotment
2. MB
3. Cash book

Signature.....  
Designation Executive Engineer  
R.W.D(W) Division, Banka-2  
Date.- 09.12.2025

*9/12/25*



Name of the Works Division :- Banka 2

Requisition Format for Scheme MMSUY/RRSMP (General)

| Sl. No. | Package No.            | Project ID as per MIS | Name of Road                                            | AA Length (in km.) | Administrative Approval (construction work) Amount (in Lakh) | Agreement (construction work) Amount (in Lakh) | Agreement No. & Date    | Date of Completion as per Agreement | Actual Date of Completion | Work Status (WBM/WMM/B M/SDBC etc.) | Value of IRI (in mm/km) | Thickness of Bitumen Layer (in mm) | Value of Bitumen Content (in %) | Total Previous Allotted Amount (in Lakh) | Upto date Expenditure as per MIS (in Lakh) | Value of Work Done (in Lakh) | Current Demand (in Lakh) | Remarks         |
|---------|------------------------|-----------------------|---------------------------------------------------------|--------------------|--------------------------------------------------------------|------------------------------------------------|-------------------------|-------------------------------------|---------------------------|-------------------------------------|-------------------------|------------------------------------|---------------------------------|------------------------------------------|--------------------------------------------|------------------------------|--------------------------|-----------------|
| 1       | RRSMP/24-25 Banka-2/07 | 3070360350165         | Chalna to Kasiyatiher Via Chandrapura                   | 1.750              | 83.722                                                       | 68.30634                                       | 05CMBD/2025-26 09.06.25 | 08.06.26                            | -                         | PCC Completed                       | 2352                    | 25mm                               | 5%                              | 0.00000                                  | 0.00000                                    | 19.21370                     | 19.21370                 | Work in process |
| 2       | RRSMP/24-25 Banka-2/07 | 3070360350164         | L105-T02 Pipra More To Khatigaria, Lakshmakitta (VR105) | 3.300              | 175.117                                                      | 150.68384                                      | 05CMBD/2025-26 09.06.25 | 08.06.26                            | -                         | Surface Completed                   | 2532                    | 25mm                               | 5%                              | 0.00000                                  | 0.00000                                    | 100.72301                    | 100.72301                | Work in process |
| 3       | RRSMP/24-25 Banka-2/07 | 3070360350156         | Longay to bailce                                        | 2.370              | 111.982                                                      | 92.68486                                       | 05CMBD/2025-26 09.06.25 | 08.06.26                            | -                         | Surface Completed                   | 2533                    | 25mm                               | 5%                              | 0.00000                                  | 0.00000                                    | 25.78429                     | 25.78429                 | Work in process |
| 4       | RRSMP/24-25 Banka-2/07 | 3070360350161         | Jhakra Village to Velaya Kali Asthan Tola               | 4.456              | 236.877                                                      | 191.26769                                      | 05CMBD/2025-26 09.06.25 | 08.06.26                            | -                         | Surface Completed                   | 2497                    | 25mm                               | 5%                              | 0.00000                                  | 0.00000                                    | 32.70189                     | 32.70189                 | Work in process |
| 5       | RRSMP/24-25 Banka-2/06 | 3070360350157         | Debaya Sibanchak To Mohanpur                            | 2.650              | 131.439                                                      | 106.32270                                      | 01CMBD/2025-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                   | 2597                    | 25mm                               | 5%                              | 20.23796                                 | 20.23796                                   | 63.17903                     | 42.94107                 | Work in process |
| 6       | RRSMP/24-25 Banka-2/06 | 3070360350143         | NAWADA Dhoraiya RD T03 - Hasanpur                       | 2.070              | 135.020                                                      | 114.80408                                      | 01CMBD/2025-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                   | 2619                    | 25mm                               | 5%                              | 20.21818                                 | 20.21818                                   | 63.17588                     | 42.95770                 | Work in process |
| 7       | RRSMP/24-25 Banka-2/06 | 3070360350163         | T01 To Bajr Via Balam Chak To Logaya                    | 2.120              | 107.643                                                      | 94.39198                                       | 01CMBD/2025-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                   | 2555                    | 25mm                               | 5%                              | 47.06184                                 | 47.06184                                   | 68.84667                     | 21.78483                 | Work in process |
| 8       | RRSMP/24-25 Banka-2/06 | 3070360350168         | Purniya Dhoraiya PWD Road To Baniya Chak Parsa          | 8.510              | 574.764                                                      | 492.97266                                      | 01CMBD/2025-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                   | 2493                    | 25mm                               | 5%                              | 251.69399                                | 251.69399                                  | 329.36970                    | 77.67571                 | Work in process |
| 9       | RRSMP/24-25 Banka-2/06 | 3070360350194         | Raghuinika To Maliya Chack                              | 1.240              | 58.104                                                       | 48.15103                                       | 01CMBD/2025-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                   | 2563                    | 25mm                               | 5%                              | 16.58278                                 | 16.58278                                   | 29.96529                     | 13.38251                 | Work in process |
| 10      | RRSMP/24-25 Banka-2/06 | 3070360350155         | Birbalpur To Karanga Anisabad                           | 2.780              | 125.102                                                      | 105.26769                                      | 01CMBD/2025-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                   | 2565                    | 25mm                               | 5%                              | 38.70370                                 | 38.70370                                   | 70.35156                     | 31.64786                 | Work in process |
| 11      | RRSMP/24-25 Banka-2/06 | 3070360350193         | L022-Asi Mathurachak Rd to Nandegola (VR22)             | 1.100              | 57.405                                                       | 44.74984                                       | 01CMBD/2025-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                   | 2693                    | 25mm                               | 5%                              | 0.00000                                  | 0.00000                                    | 21.37800                     | 21.37800                 | Work in process |
|         |                        | Total                 |                                                         |                    |                                                              |                                                |                         |                                     |                           |                                     |                         |                                    |                                 |                                          |                                            |                              |                          |                 |
|         |                        |                       |                                                         |                    |                                                              |                                                |                         |                                     |                           |                                     |                         |                                    |                                 |                                          |                                            |                              |                          | 430.19057       |

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excell) of recorded IRI is enclosed (As Applicable).

Senior D.A.O./D.A.O. 125  
RWD, Works Division Banka-2

Executive Engineer  
RWD, Works Division, Banka-2

31/12/25



Road Name : L022-Assi Mathurachak Rd to Nandgola (VR22), Contractor Name : Anil Kumar Singh

| Date     | Time     | Section No. | Length in km | Bumps in mm | Speed Rate | OR mm/km  | IRI mm/km | CATEGORY ROAD | Latitude | Longitude | Event  |
|----------|----------|-------------|--------------|-------------|------------|-----------|-----------|---------------|----------|-----------|--------|
| 24/11/25 | 10:25:19 | 5           | 0.1          | 230         | 30.3       | 2300      | 2442      | G             | 25.05366 | 87.16091  | Normal |
| 24/11/25 | 10:25:29 | 5           | 0.1          | 290         | 30.4       | 2900      | 3014      | G             | 25.05318 | 87.16154  | Curve  |
| 24/11/25 | 10:25:43 | 5           | 0.1          | 210         | 30.3       | 2100      | 2251      | G             | 25.0529  | 87.16253  | Normal |
| 24/11/25 | 10:25:52 | 5           | 0.1          | 300         | 30.3       | 3000      | 3110      | G             | 25.05324 | 87.16312  | Curve  |
| 24/11/25 | 10:26:00 | 5           | 0.1          | 230         | 30.4       | 2300      | 2442      | G             | 25.05305 | 87.16412  | Normal |
| 24/11/25 | 10:26:09 | 5           | 0.1          | 200         | 30.4       | 2000      | 2156      | G             | 25.05276 | 87.16506  | Normal |
| 24/11/25 | 10:26:21 | 5           | 0.1          | 220         | 30.3       | 2200      | 2347      | G             | 25.05287 | 87.16598  | Normal |
| 24/11/25 | 10:26:26 | 5           | 0.1          | 310         | 30.2       | 3100      | 3205      | G             | 25.05287 | 87.16688  | Curve  |
| 24/11/25 | 10:26:35 | 5           | 0.1          | 240         | 30.1       | 2400      | 2537      | G             | 25.05269 | 87.16782  | Normal |
| 24/11/25 | 10:26:53 | 5           | 0.1          | 290         | 30.1       | 2900      | 3014      | G             | 25.05287 | 87.16584  | Curve  |
| 24/11/25 | 10:27:19 | 5           | 0.1          | 300         | 30.2       | 3000      | 3110      | G             | 25.0537  | 87.16818  | Curve  |
|          |          | Length      | 1.1          |             |            | Average : | 2693      |               |          |           |        |

$$Y = 0 * X^2 + 0.954 * X + 247.70$$

$$X = 3000$$

$$Y = 3110$$

(R) RURAL ROAD  
Good Average Poor  
<4000 4001-5000 >5001

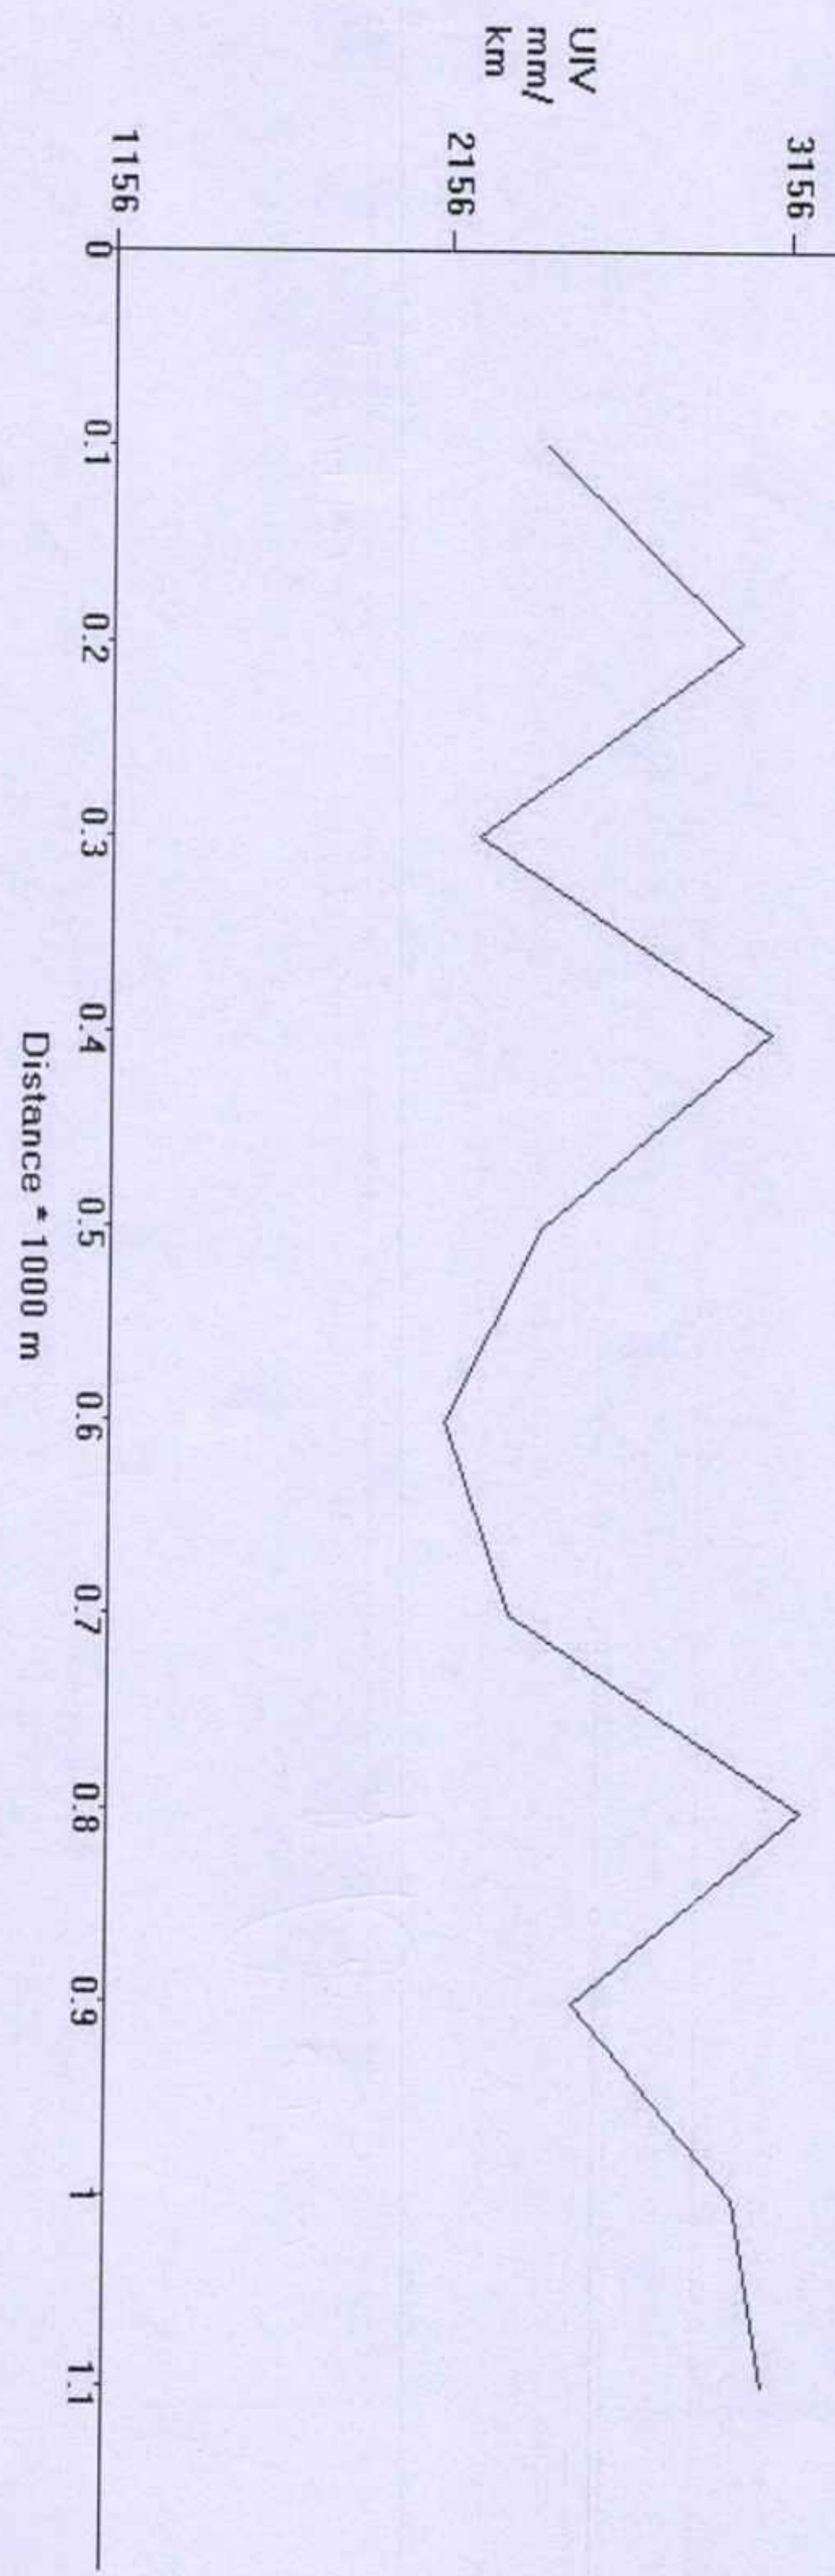
*[Signature]*  
5-11-25  
Junior Engineer  
Rural Works Department  
Works Section, Dhoraiya

*[Signature]*  
05-11-25  
Assistant Engineer  
Rural Works Department  
Works Sub-Division, Dhoraiya

*[Signature]*  
9.12.25  
Executive Engineer  
Rural Works Department  
Works Division, Banka-2



File : D:\Steeco Bump\Sec\_5.xlsx    Section No. : 5,    Eqn :  $Y = 0 * X^2 + 0.954 * X + 247.70$   
 Name of Customer : Anil Kumar Singh,    Name of Work/ Road : L022-Assi Mathurachak Rd to Nandgola,    Lab Job



*Q/k*  
*5/12/25*  
*J.F.*

*Sec*  
*05/11/25*  
*AC*


*12/9/25*




## अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि MMGSUY/RRSMP (General )  
योजनान्तर्गत, पैकेज सं०- RRSMP/24-25 Banka-2/06


1. पथ L022-Assi Mathurachak Rd to Nandgola (VR22) में कराये गये  
कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के  
अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है  
जिसका सत्यापन कर लिया गया है। -

  
5/12/25

कनीय अभियंता  
ग्रामीण कार्य विभाग  
कार्य प्रशाखा धोरैया

  
05/12/25

सहायक अभियंता  
ग्रामीण कार्य विभाग  
कार्य अवर प्रमण्डल धोरैया

  
9.12.25

कार्यपालक अभियंता  
ग्रामीण कार्य विभाग  
कार्य प्रमण्डल बाँका-2
