

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिकहरना, ढाका।

पत्रांक - ...2341.../सिकहरना, ढाका, दिनांक-...12.../2...25

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिकहरना, ढाका।

सेवा में,

नोडल पदाधिकारी,
मुख्यमंत्री ग्राम संपर्क योजना,
बिहार, पटना।

विषय :- RRSMP (Gen.) योजनान्तर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन हेतु अधियाचना प्रपत्र समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि इस प्रमंडलान्तर्गत RRSMP (Gen.) के अधीन प्रगतिशील पथों में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने हेतु अधियाचना विहित-प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।
अनुलग्नक :- यथोक्त।

विश्वासभाजन

12/12/25
Surat
12/12/25
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिकहरना, ढाका।

Rural Works Department
RRSMP (Gen.) Allotment Requisition Formate

Name of the Division :- Rural Works Department, Works Div. Dhaka																		
Sl. No.	Package no.	Project ID	Name of Road	AA Length (In KM)	Administrative Approval (Construction Work) Amount	Agreement (Construction Work) Amount (In Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status	Value of IRI (in mm/km)	Thickness of Bitumin Content in Percentage	Value of Bitumin	Previous Total Allotted Amount (in Lakh)	Up to date expenditure as per MIS (in Lac)	Value of Work Done (in lakh)	Current Demand	Remarks
1		517086035016 7	Purnahiya jharokhar jagiraha path to Anariya Mishra Tola Ward no. 4 Anariya Uturwan Tola, Ward no. 5	1.200		72.36010		30.05.2026		Surface Completed	2604.25	25%	5	0.00000	0.00000	61.62532	61.62532	
2		517086035017 3	Construction of PCC Road from Ghorasahan- Dhaka Road To kurniya Mata Mandir in Purnahiya Under Ghorasahan Block	0.180		12.36786		30.05.2026		Surface Completed	2568	25%	5	10.08064	10.08064	11.95702	1.87638	
3		517086035016 2	Madhubani Kapildev mahto's house to birendra Kushwaha's house	1.800		96.71621		30.05.2026		Surface Completed	2432.44	25%	5	77.37662	77.37662	92.78879	15.41217	
4		517086035018 1	Bairiya se baluaa sadak nirman	0.850		50.04873		30.05.2026		Surface Completed	2470	25%	5	38.21902	38.21902	48.12870	9.90968	
5		517086035018 4	Construction of PCC road from Indo-Nepal border Laxminiya tola to 55B Camp road	0.250		16.03717		30.05.2026		Surface Completed	2350	25%	5	8.06693	8.06693	15.49151	7.42458	
6		517086035014 5	Ambika cinema ghodasahan se Atal Sabhagar AVN gas godam hote shripur road tak sadak nirman karya	1.530		88.66832		30.05.2026		Surface Completed	2408.87	25%	5	31.51584	31.51584	85.30954	53.79370	

7	
8	
9	
10	
11	
12	
13	
14	

517086035014 7	Araria se Samanpura tak sadak nirman	1.100		63.80478
517086035015 4	Constructin of PCC Road From Birta Chouk To Anusuchit jati Tola	0.300		17.09893
517086035018 6	Lala Tola Laukhan to Lala Tola Laukhan Ward No (Kushwaha Tola)	0.512		26.63299
517086035018 8	Dostiya Main road to Brahaman toil	0.800		43.33494
517086035017 5	Dhaka Ghorasahan To Bhaserwa Sadak nirman	1.220		67.37674
517086035018 3	Purvi champaran jila antargat ghorasahan prakhand ke gram sripur kaswa me mukhya path se harijan toli path me mandir tak path nirmaan.	0.400		21.91494
517086035015 9	Ghorasahan bakulia to Ghughwa Purwari Tola Ward no.-2	0.900		90.06151
517086035015 8	Ghodasahan Veerta Chawk se Madarsa Chawk	0.700		35.36175

30.05.2026		Surface Completed	2575.91	25%	5	41.82115	41.82115	47.79192	5.97077	
30.05.2026		Surface Completed	2568	25%	5	13.74053	13.74053	16.47250	2.73197	
30.05.2026		Surface Completed	2550.6	25%	5	20.78773	20.78773	25.45714	4.66941	
30.05.2026		Surface Completed	2415.38	25%	5	33.09121	33.09121	41.50084	8.40963	
30.05.2026		Surface Completed	2568	25%	5	0.00000	0.00000	64.58204	64.58204	
30.05.2026		Surface Completed	2481	25%	5	17.29902	17.29902	21.00280	3.70378	
30.05.2026		Surface Completed	2451.78	25%	5	65.80499	65.80499	75.28680	9.48181	
30.05.2026		Surface Completed	2555.57	25%	5	28.54431	28.54431	33.83525	5.29094	

15	
16	
17	
18	
19	
20	
21	

517086035018 5	Construction of PCC road in Jamuniya Pithwa laxman tola village under Ghorasahan block	0.300		21.76191
517086035016 8	Purvi champaran jila antargat ghorasahan prahand me gram mahuaahi mukhya path mandir se gramin path tak path nirmaan.	0.300		15.43211
517086035019 2	Champapur koiriya nanak thakur's house to narsingh sah's house via sukhdev mahtoo's house	0.300		17.66404
517086035014 6	Anwarul Haq' s house to Badli Masjid via kalu tola	1.000		58.53085
517086035017 9	Baghi Sheliwa Bankatwa Road Ke Gidhauna Road To Bijayee	2.080		130.78397
517086035016 3	Madhubani mahadev tola (Mahadev mandir) to Dukhlu pater's house	1.000		54.69069
517086035016 0	Ghorasahan bazar to Ghorasahan Gularia Ward no.-2	1.160		63.72281

30.05.2026		Surface Completed	2393.67	25%	5	13.75558	13.75558	21.10841	7.35283	
30.05.2026		Surface Completed	2306.33	25%	5	0.00000	0.00000	14.74837	14.74837	
30.05.2026		Surface Completed	2481	25%	5	13.85620	13.85620	16.97989	3.12369	
30.05.2026		Surface Completed	2437.3	25%	5	48.79883	48.79883	56.34898	7.55015	
30.05.2026		Surface Completed	2454.7	25%	5	83.98375	83.98375	89.20253	5.21878	
30.05.2026		Surface Completed	2463.4	25%	5	45.27732	45.27732	52.60292	7.32560	
30.05.2026		Surface Completed	2568	25%	5	45.72101	45.72101	56.13130	10.41029	

01 CMRD/2025-26 date-31.05.2025

22	
23	
24	
25	
26	
27	

5170860350170	Samanpur mukhya Sadak Se Mai siban Mein Sadak Nirman	0.450	25.58347	
5170860350193	Dhaka Ghorasahan to Jahabar Lal Memorial Collage pathua me Sadak Nirman	0.710	38.75622	
5170860350190	Araria mukhya Sadak se Krishna Kumar jha ke ghar hote hain school tak Sadak Nirman	0.900	50.14879	
5170860350172	Bijayee Gram Math To Mahadalit Basti Via Kahwar Toli	1.700	107.02794	
5170860350189	Ghorasahan Kundwa Chainpur Path to Barwa khurd Tola, Jagirahan (Yadav Tola) Ward No 13	0.910	47.75511	
5170860350157	Construction of PCC Road From Singraha Chanardev Pandit's House to Raj Mangal Tiwari's House via Brahmasathan in Samanpur Panchayat Under Ghorasahan Block	0.400	23.25089	

30.05.2026		Surface Completed	2261.5	25%	5	20.45176	20.45176	24.55026	4.09850	
30.05.2026		Surface Completed	2592.86	25%	5	31.00368	31.00368	44.83663	13.83295	
30.05.2026		Surface Completed	2606.67	25%	5	40.51759	40.51759	48.08627	7.56868	
30.05.2026		Surface Completed	2424.41	25%	5	58.16991	58.16991	84.43375	26.26384	
30.05.2026		Surface Completed	2451.89	25%	5	37.79455	37.79455	45.38100	7.58645	
30.05.2026		Surface Completed	2175.75	25%	5	16.44257	16.44257	21.48581	5.04324	

28	
29	
30	
31	
32	
33	
34	

517086035015 6	Construction of PCC Road From Ghorasahan Police Station To Gowari Tola Via Sanjay Jaiswal's House in Ghorasahan Block	0.400		21.97688
517086035016 9	Purvi champaran jila antargat ghorasahan prakhand ke parriya mukhya sarak se parriya mahadalit toli tak path niirmaan.	0.600		43.29843
517086035018 2	Construction of PCC road from athmuhian Prathmik vidyalaya to athmuhian SSB Camp	0.500		29.81989
517086035016 4	Madhubani pokhar to Brahamaasthan	0.600		35.19282
517086035018 0	Chiraiya Purnahiya road to vijay tola, barka madhubani road se dakshin, ward no.-12	0.875		55.12711
517086035019 1	Changapur Koeriya chouk to garhaeya mui road	0.950		53.58126
517086035017 8	Hasanpur se Baluaa tola Sadak Nirman	1.040		63.79964

30.05.2026		Surface Completed	2346.25	25%	5	17.47415	17.47415	20.55945	3.08530	
30.05.2026		Surface Completed	2510	25%	5	27.59004	27.59004	42.02254	14.43250	
30.05.2026		Surface Completed	2533.2	25%	5	22.97351	22.97351	28.67061	5.69710	
30.05.2026		Surface Completed	2451.83	25%	5	27.60336	27.60336	35.19268	7.58932	
30.05.2026		Surface Completed	2415.38	25%	5	45.89567	45.89567	53.11968	7.22401	
30.05.2026		Surface Completed	2500.22	25%	5	41.70098	41.70098	53.47788	11.77690	
30.05.2026		Surface Completed	2524.5	25%	5	43.35954	43.35954	61.39346	18.03392	

35	517086035016 5	Nanaura - Gurmiya South	1.350	79.18871				Surface Completed	2366.69	25%	5	61.78079	61.78079	66.55963	4.77884	
36	517086035017 6	Birta Chowk Ghorasahan To Mahuri Ward No. 03	1.450	102.29325				Surface Completed	2437.29	25%	5	69.53624	69.53624	80.29302	10.75678	
37	517086035017 1	Ramayani Baba ghodasahan se Ambika cinema Durga Mandir Hote Shyam Babu ke ghar Tak Sadak Nirman	1.000	57.53358				Surface Completed	2550.6	25%	5	27.74996	27.74996	55.24249	27.49253	
38	517086035016 6	Parariya village main road to mahadalit basti and shiv mangal singh's house via Ram bilas mukhiya's house	0.400	106.55355				Surface Completed	2432.44	25%	5	83.39493	83.39493	97.08715	13.69222	
Total :-												1311.17991	1311.17991	1810.74488	499.56497	

Sureal
Divisional Accounts Officer
Rural Works Div, Dhaula
12/12/25

12/12/25
Executive Engineer
RWD (W) Div, Dhaula

नोट

- 1 सर्व का निदान एम्पायर्मेंट से होना आवश्यक है।
- 2 अधिपतिता राशि का प्रकार भागीदारी की प्रणाली में अतिरिक्त राशि को अधिपतिता राशि में जोड़ना आवश्यक है।
- 3 पूर्व निर्धारित राशि का उपयोग प्रमाण-पत्र में शामिल होना आवश्यक है।
- 4 योजनावार सभी वर्षों का अधिपतिता एक साथ भेजना आवश्यक है।
- 5 निर्धारित राशि का वीपीओ विपत्र 15 दिनों के अंदर जमा करवाया जाना आवश्यक है।

12/12/25
Executive Engineer
RWD (W) Div, Dhaula

GFR 12-B
[See Rule 256 (2)]
Form of Utilizations Certificate

Certified that out of the Loan of Rs 83541317.00, Sanctioned under letter No -79 Dated-12.09.2025 in Favor of R.W.D., Works Division Dhaka, during the Year 2025-26, an amount of Rs...83541317.00, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. Nil, remaining unutilized at the end of the Year 2025-26 will be adjusted towards the loan payable during the next financial year.

Certified that I have satisfied my self that the condition on which the grants-in-aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Susat
Divisional Accounts Officer
Rural Works Department
Works Division, Dhaka

2/12/25
Executive Engineer
R.W.D.(W) Div., Dhaka

अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि RRSMP/24-25/Dhaka/03 योजनान्तर्गत:-

- Purvi Champaran Jila antargat ghosarahan prakhanda ke
1. पथ/पुल Parviya mukhya sarak se: में कराये गये कार्य की
Parviya mahadwari toli tak path nisman.
गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।

2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका
सत्यापन कर लिया गया है।

कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा-

6.12.05
सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल-

6/12/25
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-

Steco Analyzer

Name of Customer : Vijayee Champaran Construction
 Name of Work/ Road : Purvi Champaran Jila Antargat
 Lab Job number : 32
 Date : 17.11.2025
 Section No. : 32

Test Date : 17.11.2025
 Machine No : 483
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : Purvi Champaran Jila Antargat
 Road Type : (R) RURAL ROAD
 Side :
 UIV Range : 1394 To 4000 Interval 1000 mm/km
 Dist Range : 0 To 0.7 0.1 * 1000 m
 Equation : $Y = 0 \cdot X^2 + 0.872 \cdot X + 127$


Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\USER\Desktop\17111105.Xls, Section No.: 32, Eqn : $Y = 0 \cdot X^2 + 0.872 \cdot X + 127$

Name of Customer : Vijayee Champaran Construction Ms (Jy), Name of Work/ Road : Purvi Champaran Jila Antargat

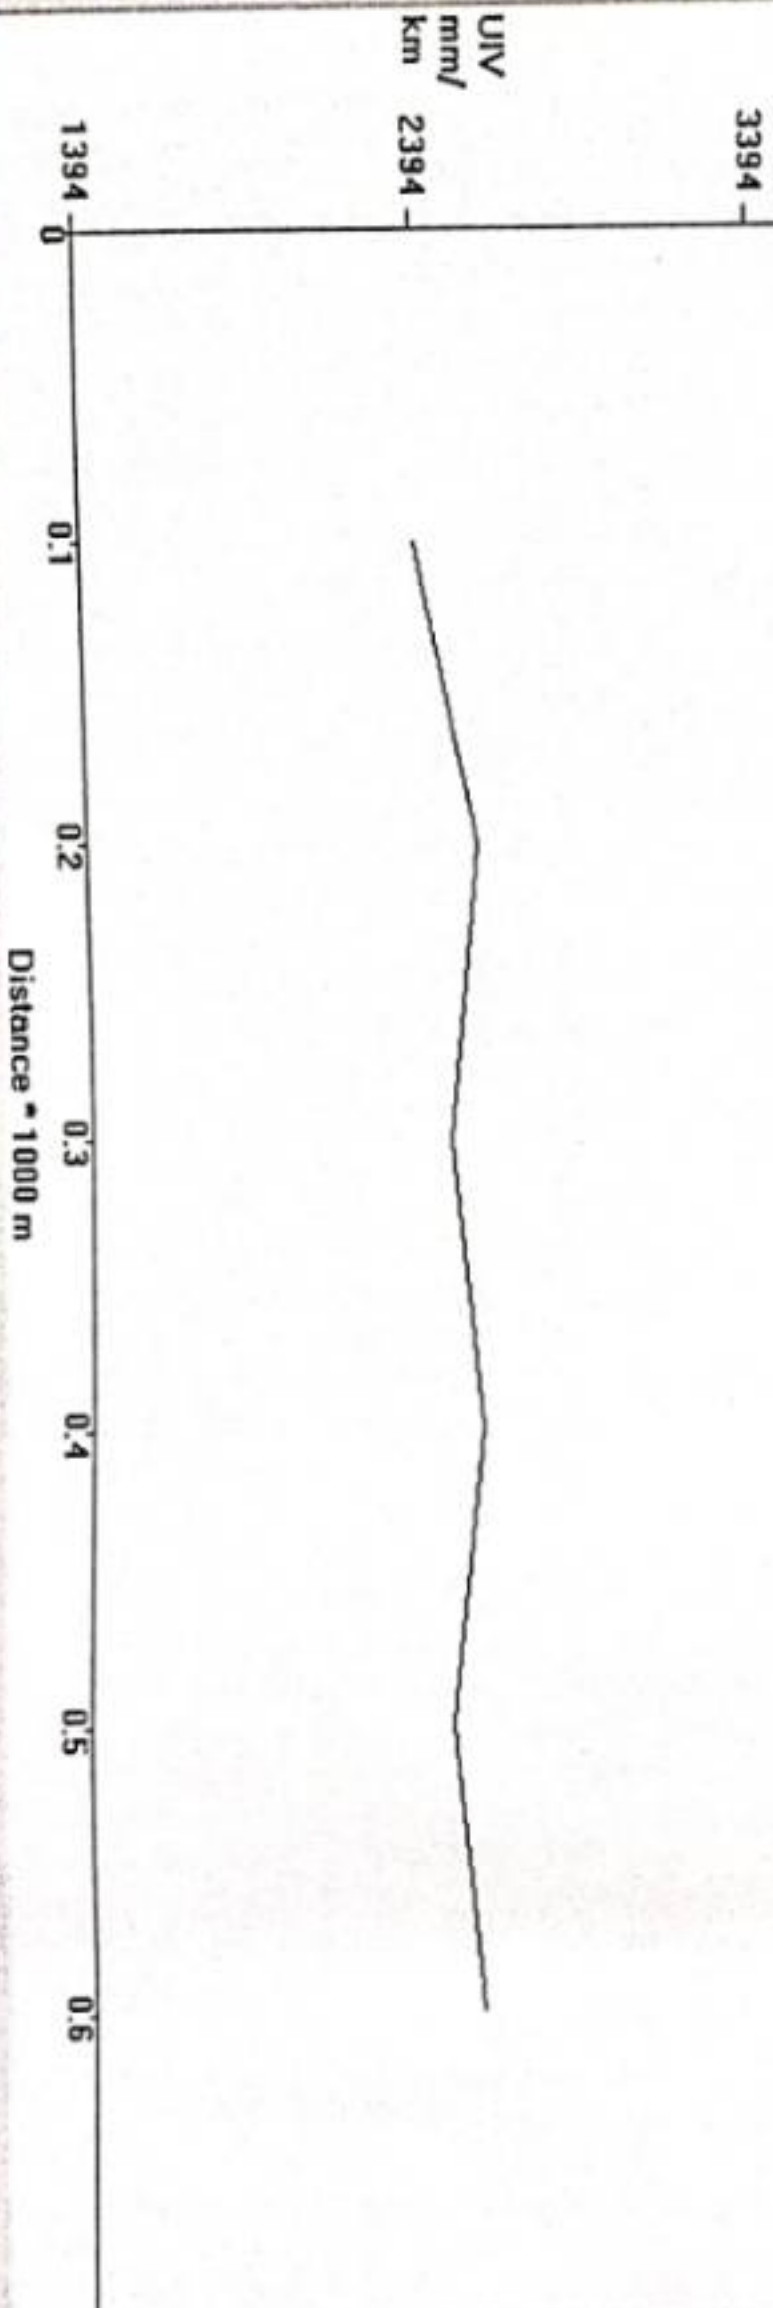

Handwritten signature and date:
17.11.25
17/11/25
E.L

Name of Road :- Purvi Champaran Jila Antargat Ghorasahan Prakhanda ke Parriya Mukhya Sarak Se Pariya Mahadalit Toli Tak.

Section no.32

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
17/ 11/ 25	11: 2: 5	32	0.1	260	0	2600	2394	G	26.805712	85.092316	Normal
17/ 11/ 25	11: 3: 39	32	0.1	280	10.1	2800	2568	G	26.805847	85.092492	Normal
17/ 11/ 25	11: 4: 11	32	0.1	270	10.1	2700	2481	G	26.805987	85.092672	Normal
17/ 11/ 25	11: 4: 40	32	0.1	280	10.1	2800	2568	G	26.806127	85.092852	Normal
17/ 11/ 25	11: 5: 9	32	0.1	270	10.1	2700	2481	G	26.806267	85.093032	Normal
17/ 11/ 25	11: 5: 37	32	0.1	280	10.1	2800	2568	G	26.806407	85.093212	Normal
Total=			0.60	Km	Avg. 2510.00						

Executive Engineer
R.W.D. (W) Division,
Sikharma (Dhaka)

Handwritten signature and date:
17.11.25
