

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, गोपालगंज-1

पत्रांक:-2120अनु

/ गोपालगंज

दिनांक:-18/12/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय:- शीर्ष RRSMP (General) अन्तर्गत में अधियाचित राशि का आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि शीर्ष RRSMP (General) अन्तर्गत राशि की माँग संलग्न विहित प्रपत्र में पथवार की जा रही है।

अतः भवदीय से अनुरोध है कि विहित प्रपत्र के कॉलम-18 में अंकित कुल राशि का आवंटन उपलब्ध कराने की कृपा की जाय। अधियाचित राशि के संदर्भ में C & P किये मापी पुस्तिका की छाया प्रति, एवं उपयोगिता प्रमाण-पत्र संलग्न कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनु0-यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

18.12.25

Requisition Format for Scheme MMGSUY/RRSMP (General/SC/ST)

Name of the Works Division :- Gopalganj-1

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WB/M/W MM/BM /SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	RRSMP/24/25 Gopalganj-1/05	5140690350036	PMGSY to Rajput Tola	0.550	25.589	25.69756	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	04.12.2025	SDBC	3235.16	25	5.01	12.39350	12.39350	20.46284	8.06934	Completed
2	RRSMP/24/25 Gopalganj-1/05	5140690350073	PMGSY Road Bodha Chhapar to Sukdeo Pati	2.830	121.560	124.22347	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	11.12.2025	SDBC	3025.06	25	5.02	18.56932	18.56932	78.90070	60.33138	Completed
3	RRSMP/24/25 Gopalganj-1/05	5140690350034	PMGSY Prathmik Vidyalay raj to Baniya tola balesra	0.305	15.546	15.61907	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	05.12.2025	SDBC	2904.75	25	5.03	7.80305	7.80305	12.42081	4.61776	Completed
4	RRSMP/24/25 Gopalganj-1/05	5140690350075	PMGSY Road Musthar tola pul to Dube tola Kartanah Mandir	3.000	144.590	146.85647	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	11.12.2025	SDBC	2930.56	25	5.02	38.45810	38.45810	102.09787	63.63977	Completed
5	RRSMP/24/25 Gopalganj-1/02	5140690350031	L035-Sohnwa to Bhopipur (ODR 8)	2.600	154.410	149.98824	05/CMBD (MMGSUY)2 025-26 dt. 29.05.2025	28.05.2026	-	SDBC	3050.57	25	5.01	0.00000	0.00000	83.64251	83.64251	Surface Completed
6	RRSMP/24/25 Gopalganj-1/05	5140690350038	PMGSY Path to Malah Tola Sallihpur	0.680	34.114	34.36952	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	Pol Patch/ PCC	-	-	-	3.41797	3.41797	13.67187	10.25390	Pol Patch/ PCC Completed

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilization Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy of recorded IRI is enclosed (As Applicable).

R.W.D. Works Division
Gopalganj-1

[Signature]
D.A.O.

Executive Engineer
R.W.D. Works Division
Gopalganj-1

[Signature]
18.12.25

GFR 12-B

[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs.468206853.00 Sanctioned under MMGSUY/RRSMP GEN dated 17.12.2025, in favour of Executive Engineer, RWD Works Division Gopalganj-1, during the year 2025-26, an amount of Rs.454843403.00 has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.13363450.00 remaining unutilized at the end of the year 2025 has been surrendered to the Government (vide No..... dated.....) will be adjusted towards the loan payable during the next financial year.


(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.



D.A.O.

R.W.D. Works Division,
Gopalganj-1


Executive Engineer,
R.W.D. Works Division,
Gopalganj-1
17.12.25

अधियाचना हेतु प्रमाण पत्र

- प्रमाणित किया जाता है कि **MMGSUY (RRSMP GEN)** योजनान्तर्गत
1. पथ/पुल **PMGSY to Rajput Tola** में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
 2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।



सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल कुचायकोट।



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल गोपालगंज-1

Name of Road:-PMGSY to Rajput Tola

Name of Contractor :-M/s Pawan and Tiwari Construction J.V.

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
7/12/25	9: 9: 0	37	0.1	280	0	2800	2862	G	26.618688	84.2200	Normal
7/12/25	9: 9: 0	37	0.1	320	10.1	3200	3206	G	26.619157	84.217172	Normal
7/12/25	9: 9: 33	37	0.1	340	10.1	3400	3379	G	26.618762	84.218013	Normal
7/12/25	9: 10: 8	37	0.1	350	10.1	3500	3465	G	26.618207	84.218922	Normal
7/12/25	9: 10: 43	37	0.1	330	10.1	3300	3293	G	26.617728	84.219747	Normal
7/12/25	9: 11: 0	37	0.1	320	10.1	3200	3206	G	26.617182	84.220588	Normal
AVERAGE 3235.16											

$$Y = 0 * X^2 + 0.862 * X + 448.5$$

$$X = 3200$$

$$Y = 3206$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

IRI Value

Average IRI-3235.16

AE

07/12/25

17/11/25

Name of Customer : M/s Pawan and Tiwan Construction
Name of Work/ Road : PMGSY to Rajput Tola
Lab Job number : 37
Date : 07-12-2025
Section No. : 37

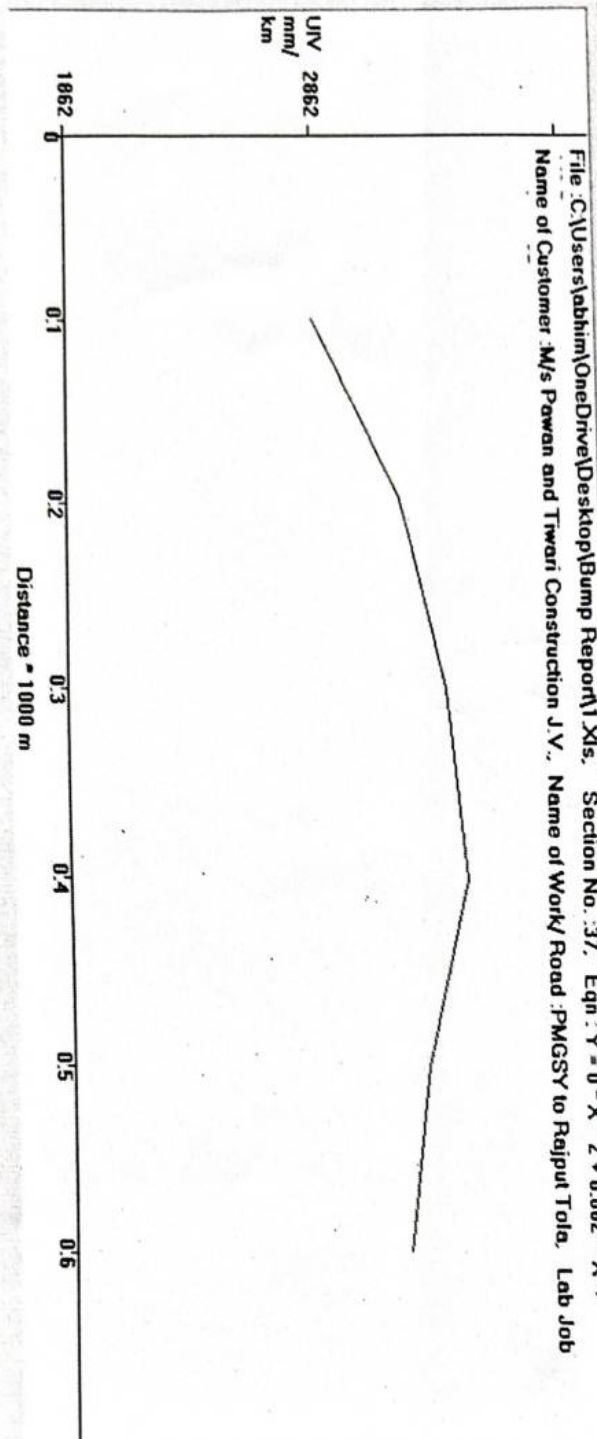
Print **Generate Report and Graph**

Test Date : 07-12-2025
Machine No. : 413
Start S No. :
Start E No. :
Weather :
Start Location :
End Location :

Road Name : PMGSY to Rajput Tola
Road Type : (R) RURAL ROAD
Side :
Interval :
U/V Range : 1862 To 4000 mm/km
Dist Range : 0 To 0.7 * 1000 m
Equation : $Y = 0 * X^2 + 0.862 * X + 448.5$

Redraw Graph **Map View**

File : C:\Users\abhim\OneDrive\Desktop\Bump Report\1 Xis. Section No. 37. Eqn : $Y = 0 * X^2 + 0.862 * X +$
 Name of Customer : M/s Pawan and Tiwan Construction J.V., Name of Work/ Road : PMGSY to Rajput Tola. Lab Job



U/V 2862 mm/km

Handwritten: 07/12/25
Handwritten: PE
Handwritten: 07/12/25
