

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, गोपालगंज-1

पत्रांक:-2120 अरु

/ गोपालगंज

दिनांक:-18/12/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय:- शीर्ष RRSMP (General) अन्तर्गत में अधियाचित राशि का आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि शीर्ष RRSMP (General) अन्तर्गत राशि की माँग संलग्न विहित प्रपत्र में पथवार की जा रही है।

अतः भवदीय से अनुरोध है कि विहित प्रपत्र के कॉलम-18 में अंकित कुल राशि का आवंटन उपलब्ध कराने की कृपा की जाय। अधियाचित राशि के संदर्भ में C & P किये मापी पुस्तिका की छाया प्रति, एवं उपयोगिता प्रमाण-पत्र संलग्न कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनु०-यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

18-12-25

Requisition Format for Scheme MMGSUY/RRSMP (General/SC/ST)

Name of the Works Division :- Gopalganj-1

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WB/M/W MM/BM /SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	RRSMP/24/25 Gopalganj-1/05	5140690350036	PMGSY to Rajput Tola	0.550	25.589	25.69756	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	04.12.2025	SDBC	3235.16	25	5.01	12.39350	12.39350	20.46284	8.06934	Completed
2	RRSMP/24/25 Gopalganj-1/05	5140690350073	PMGSY Road Bodha Chhapar to Sukdeo Pati	2.830	121.560	124.22347	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	11.12.2025	SDBC	3025.06	25	5.02	18.56932	18.56932	78.90070	60.33138	Completed
3	RRSMP/24/25 Gopalganj-1/05	5140690350034	PMGSY Prathmik Vidyalay raj to Baniya tola balesra	0.305	15.546	15.61907	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	05.12.2025	SDBC	2904.75	25	5.03	7.80305	7.80305	12.42081	4.61776	Completed
4	RRSMP/24/25 Gopalganj-1/05	5140690350075	PMGSY Road Musthar tola pul to Dube tola Kartanah Mandir	3.000	144.590	146.85647	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	11.12.2025	SDBC	2930.56	25	5.02	38.45810	38.45810	102.09787	63.63977	Completed
5	RRSMP/24/25 Gopalganj-1/02	5140690350031	L035-Sohnwa to Bhopipur (ODR 8)	2.600	154.410	149.98824	05/CMBD (MMGSUY)2 025-26 dt. 29.05.2025	28.05.2026	-	SDBC	3050.57	25	5.01	0.00000	0.00000	83.64251	83.64251	Surface Completed
6	RRSMP/24/25 Gopalganj-1/05	5140690350038	PMGSY Path to Mallah Tola Sallihpur	0.680	34.114	34.36952	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	Pol Patch/ PCC	-	-	-	3.41797	3.41797	13.67187	10.25390	Pol Patch/ PCC Completed

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilization Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy of recorded IRI is enclosed (As Applicable).

R.W.D. Works Division
Gopalganj-1

[Signature]
D.A.O.

Executive Engineer
R.W.D. Works Division
Gopalganj-1

[Signature]
18.12.25

GFR 12-B

[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs.468206853.00 Sanctioned under MMGSUY/RRSMP GEN dated 17.12.2025, in favour of Executive Engineer, RWD Works Division Gopalganj-1, during the year 2025-26, an amount of Rs.454843403.00 has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.13363450.00 remaining unutilized at the end of the year 2025 has been surrendered to the Government (vide No..... dated.....) will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.


D.A.O.

R.W.D. Works Division,
Gopalganj-1


Executive Engineer,
R.W.D. Works Division,
Gopalganj-1
17.12.25

अधियाचना हेतु प्रमाण पत्र

प्रमाणित किया जाता है कि **MMGSUY (RRSMP GEN)** योजनान्तर्गत

1. पथ/पुल **L035-Sohnwna to Bhoptpur (ODR8)** में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।

Ruchi Dwivedi
17/12/2025

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल कटेया।

Xm
13/12/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल गोपालगंज-1

RECEIVED
CORRALOAN

Name of Road:-L035-Sohnwaa to Bhopitpur (ODR 8)												
Name of Contractor:-Sri Nivash Prasad Engicons and Management Pvt. Ltd.												
Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	
18/11/25	14:38:0	72	0.1	260	0	2600	2689 G		26.24074	84.739713	Normal	
18/11/25	14:38:0	72	0.1	280	10.1	2800	2862 G		26.2408	84.740723	Normal	
18/11/25	14:38:31	72	0.1	300	10.1	3000	3034 G		26.24129	84.741515	Normal	
18/11/25	14:38:31	72	0.1	260	10.1	2600	2689 G		26.24202	84.74202	Normal	
18/11/25	14:39:5	72	0.1	280	10.1	2800	2862 G		26.24288	84.742473	Normal	
18/11/25	14:39:40	72	0.1	340	10.1	3400	3379 G		26.24366	84.74313	Normal	
18/11/25	14:40:16	72	0.1	330	10.1	3300	3293 G		26.24437	84.743703	Normal	
18/11/25	14:41:0	72	0.1	300	10.1	3000	3034 G		26.24466	84.744662	Normal	
18/11/25	14:41:26	72	0.1	320	10.1	3200	3206 G		26.24496	84.745522	Normal	
18/11/25	14:42:2	72	0.1	330	10.1	3300	3293 G		26.24556	84.745638	Normal	
18/11/25	14:42:37	72	0.1	340	10.1	3400	3379 G		26.24588	84.744697	Normal	
18/11/25	14:42:37	72	0.1	310	10.1	3100	3120 G		26.246	84.74372	Normal	
18/11/25	14:43:12	72	0.1	280	10.1	2800	2862 G		26.24602	84.74271	Normal	
18/11/25	14:43:12	72	0.1	310	10.1	3100	3120 G		26.24621	84.74172	Normal	
18/11/25	14:43:47	72	0.1	270	20.2	2700	2775 G		26.24638	84.739747	Normal	
18/11/25	14:44:0	72	0.1	280	20.2	2800	2862 G		26.24655	84.738753	Normal	
18/11/25	14:44:23	72	0.1	270	20.2	2700	2775 G		26.24756	84.103518	Normal	
18/11/25	14:44:23	72	0.1	280	20.2	2800	2862 G		26.24804	84.104023	Normal	
18/11/25	14:44:23	72	0.1	290	20.2	2900	2948 G		26.24985	84.10508	Normal	
18/11/25	14:44:23	72	0.1	320	10.1	3200	3206 G		26.24985	84.104628	Normal	
18/11/25	14:44:23	72	0.1	330	10.1	3300	3293 G		26.24985	84.10508	Normal	
18/11/25	14:44:23	72	0.1	300	10.1	3000	3034 G		26.24985	84.105823	Normal	
18/11/25	14:44:23	72	0.1	320	10.1	3200	3206 G		26.24985	84.1067	Normal	
18/11/25	14:44:23	72	0.1	310	10.1	3100	3120 G		26.24985	84.107793	Normal	
18/11/25	14:44:23	72	0.1	320	10.1	3200	3206 G		26.24985	84.115185	Normal	
AVERAGE			3050.57									

$$Y = 0 * X^2 + 0.862 * X + 448.5$$

$$X = 3200$$

$$Y = 3206$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

IRI Value
Average IRI-3050.57

Rudh Desai
18/11/2025

AE

Km
18/11/25

Name of Customer : Sri Nivash Prasad Engicon and
 Name of Work/ Road : S. Nivash Prasad Engicon and Management Pvt. Ltd.
 Lab Job number : 72
 Date : 18-11-2025
 Section No : 72

Test Date : 18-11-2025
 Machine No : 413
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : S. Nivash Prasad Engicon and Management Pvt. Ltd.
 Road Type : (R) RURAL ROAD
 Side :
 UIV Range : 1689 To 4000 Interval 1000 mm/km
 Dist Range : 0 To 27 01 * 1000 m
 Equation : $Y = 0.0001X^2 + 0.862X + 448.5$


Print

Generate Report and Graph

Redraw Graph

Map View

File C:\Users\abhin\OneDrive\Desktop\Bump Report\Xs. Section No. 72. Eqn : $Y = 0.0001X^2 + 0.862X + 448.5$
 Name of Customer : Sri Nivash Prasad Engicon and Management Pvt. Ltd. Name of Work/ Road : L035-Sohnwara to

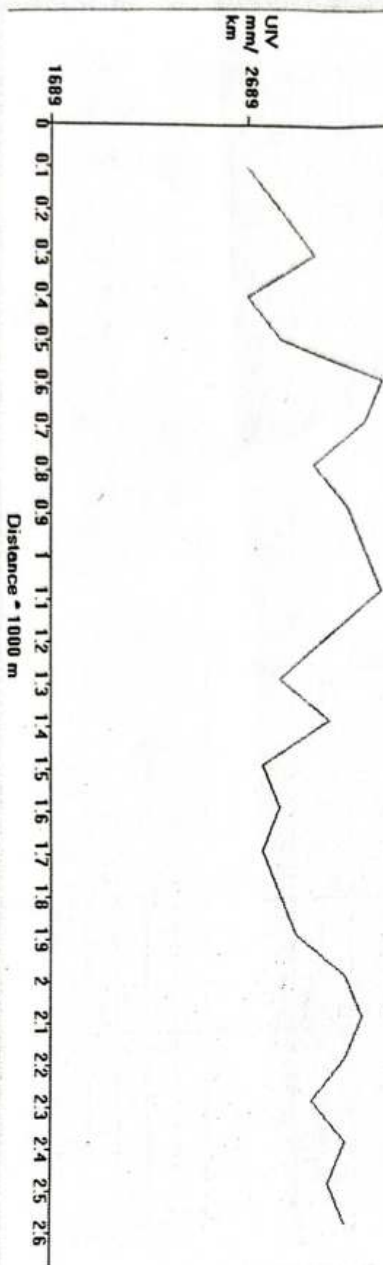

Prashant Prasad
 10/11/2025

Amir
