

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमण्डल, बाँका-2

पत्रांक 3251 (3-गु०) / बाँका

दिनांक 19/12/2025

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बाँका-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण, पटना।


विषय:- शीर्ष 4515 मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के कार्यों के भुगतान हेतु निधि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के भुगतान हेतु **39445621/-** की अधियाचना विहित प्रपत्र में तैयार कर आपके आवश्यक कार्यवाई हेतु समर्पित की जाती है।

- अनु० :-
1. विहित प्रपत्र में आवंटन की मांग।
 2. उपयोगिता प्रमाण पत्र।
 3. मापी पुस्त की छाया प्रति।

विश्वासभाजन


कार्यपालक अभियंता
ग्रा०का०वि०, कार्य प्रमण्डल
बाँका-2

19/12/25

GFR 12-B
[See Rule 256 (2)]


FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs. **5056.44559**, Sanctioned under MMGSUY (RRSMP-GEN), Lt. No.-102 dated.-18.11.2025 in favour of E.E.R.W.D.(W) Division Banka-2 during the year **2025-26**, an amount of Rs. **5056.15539**, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. **0.29020** remaining unutilized at the end of the year.-2024 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Allotment
2. MB
3. Cash book


Signature.....
Designation Executive Engineer
R.W.D(W) Division, Banka-2
Date.- 15.12.2025

Requisition Format for Scheme MMGSUY/RRSMP (General)																		
Name of the Works Division :-Banka 2																		
Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/B M/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/24-25 Banka-2/01	3070360350205	L059-Bheramoe Panjwara RD to Pipra (Track59)	3.380	245.480	196.69489	06CMBD/20 25-26 19.06.25	18.06.26	-	PCC Work in Progress.	2445	25mm	5%	0.00000	0.00000	154.85301	154.85301	Work in process
2	RRSMP/24-25 Banka-2/01	3070360350202	Barahar Block Gram Chilmil to Moghtia	2.260	111.040	86.04477	06CMBD/20 25-26 19.06.25	18.06.26	-	BT Work in Progress.	2715	25mm	5%	0.00000	0.00000	60.62402	60.62402	Work in process
3	RRSMP/24-25 Banka-2/01	3070360350203	Bhagalpur Dumka Road to Motihat to Khiripather	1.720	82.080	62.33471	06CMBD/20 25-26 19.06.25	18.06.26	-	BT Work in Progress.	2464	25mm	5%	0.00000	0.00000	40.68317	40.68317	Work in process
4	RRSMP/24-25 Banka-2/01	3070360350200	L053-BGP Dumka RD to Chihar (Track53)	1.700	100.880	75.31518	06CMBD/20 25-26 19.06.25	18.06.26	-	PCC Work in Progress.	2565	25mm	5%	0.00000	0.00000	39.81792	39.81792	Work in process
5	RRSMP/24-25 Banka-2/01	3070360350198	Chihar to Gopalpur Singarpur	1.900	92.760	71.27930	06CMBD/20 25-26 19.06.25	18.06.26	-	PCC Work in Progress.	2663	25mm	5%	0.00000	0.00000	48.62196	48.62196	Work in process
6	RRSMP/24-25 Banka-2/01	3070360350209	Birangarh Chihar Se Upar Tola Chihar Arkatta	0.830	40.897	31.00357	06CMBD/20 25-26 19.06.25	18.06.26	-	BT Work in Progress.	2382	25mm	5%	0.00000	0.00000	19.87773	19.87773	Work in process
7	RRSMP/24-25 Banka-2/01	3070360350208	BOUNSI BHURNA ROAD to KANUATIKAR	0.967	38.694	32.00887	06CMBD/20 25-26 19.06.25	18.06.26	-	Surface completed		25mm	5%	0.00000	0.00000	29.97840	29.97840	Work in process
			Total														394.45621	

It is certified that Physical & Financial Progress has been updated in MIS.

Senior D.A.O./D.A.O.
RWD, Works Division Banka-2

Executive Engineer
RWD, Works Division Banka-2

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed (As Applicable).


अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि MMGSUY/RRSMP (General)
योजनान्तर्गत, पैकेज सं०- RRSMP/24-25 Banka-2/01

1. पथ Bhagalpur Dumka Road to Motihat to Khiripather में कराये
गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों
के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है
जिसका सत्यापन कर लिया गया है।


कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा बाराहाट


सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमण्डल बाराहाट


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल बाँका-2


Road Name : Bhagalpur Dumka Road to Motihat to Khiripather, Contractor Name : Anil Kumar Singh

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
10/12/25	13:57:12	22	0.1	250	30.3	2500	2633	G	24.8577	86.99853	Normal
10/12/25	13:57:22	22	0.1	220	30.4	2200	2347	G	24.8587	86.99853	Normal
10/12/25	13:57:36	22	0.1	210	30.3	2100	2251	G	24.85953	86.9983	Normal
10/12/25	13:57:45	22	0.1	230	30.3	2300	2442	G	24.86037	86.9985	Normal
10/12/25	13:57:53	22	0.1	200	30.4	2000	2156	G	24.86119	86.99863	Normal
10/12/25	13:58:02	22	0.1	260	30.4	2600	2728	G	24.86216	86.9985	Normal
10/12/25	13:58:14	22	0.1	240	30.3	2400	2537	G	24.86289	86.9991	Normal
10/12/25	13:58:30	22	0.1	270	30.2	2700	2824	G	24.86378	86.99929	Normal
10/12/25	13:58:42	22	0.1	230	30.1	2300	2442	G	24.86467	86.99923	Normal
10/12/25	13:58:57	22	0.1	260	30.1	2600	2728	G	24.86533	86.99911	Normal
10/12/25	13:59:23	22	0.1	240	30.2	2400	2537	G	24.86619	86.99888	Normal
10/12/25	13:59:39	22	0.1	200	30.2	2000	2156	G	24.86707	86.9988	Normal
10/12/25	13:59:57	22	0.1	220	30.2	2200	2347	G	24.86794	86.99918	Normal
10/12/25	14:00:18	22	0.1	230	30.3	2300	2442	G	24.86871	86.99961	Normal
10/12/25	14:00:37	22	0.1	210	30.3	2100	2251	G	24.86952	87.00012	Normal
10/12/25	14:01:23	22	0.1	230	30.3	2300	2442	G	24.87029	87.00054	Normal
10/12/25	14:01:39	22	0.1	250	30.4	2500	2633	G	24.87175	87.00093	Normal
		Length -	1.7			Average -	2464,				

$Y = 0 * X^2 + 0.954 * X + 247.70$
 $X = 2500$
 $Y = 2347$

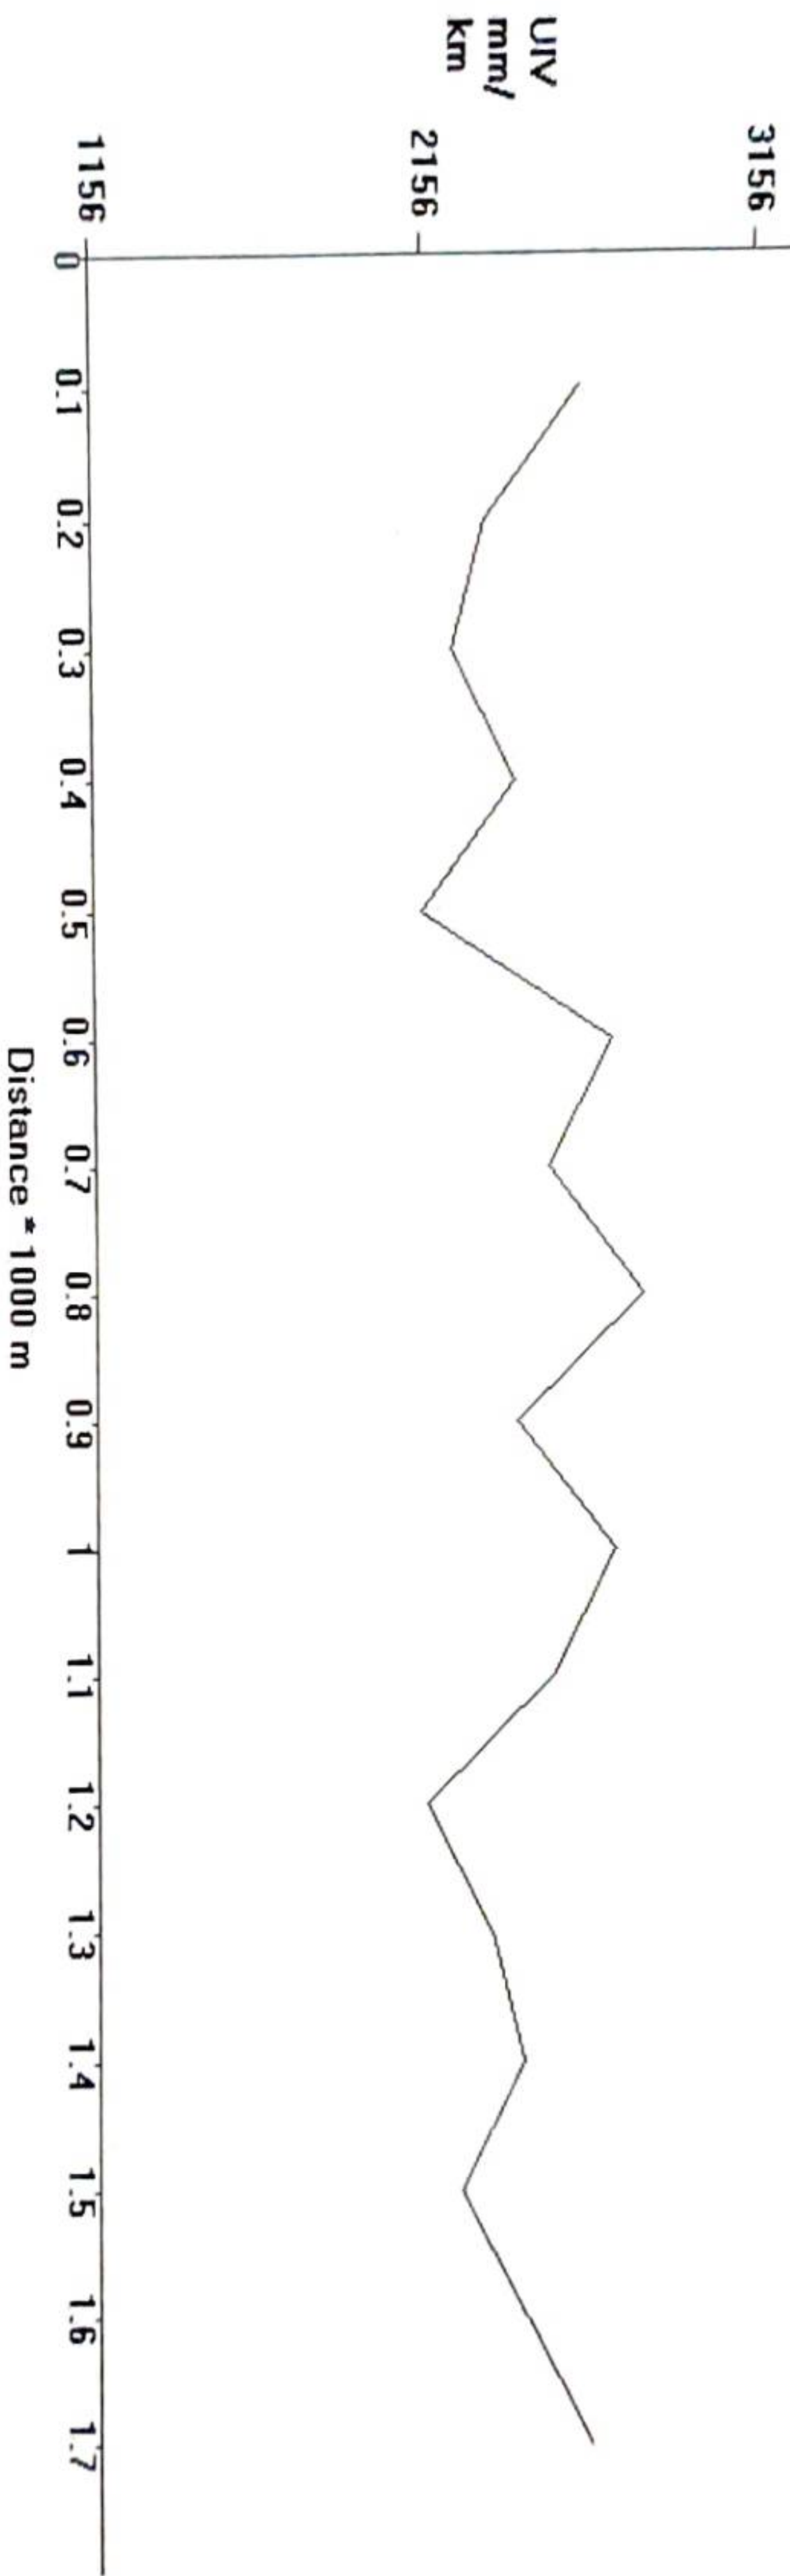
(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001


Junior Engineer
Rural Works Department
Works Section, Barahat-2


Assistant Engineer
Rural Works Department
Works Sub-Division, Barahat


Executive Engineer
Rural Works Department
Works Division, Banka-2

File :E:\Steco\Sec_22.xlsx Section No. :22 Eqn :Y = 0 * X ^ 2 + 0.954 * X + 247.70
Name of Customer :Anil Kumar Singh, Name of Work/ Road :Bhagalpur Dumka Road to Motihat to Khiripather, Lab



Handwritten signature
15/12/25
S.E

Handwritten signature
16/12/25
S.E

Handwritten signature
16.12.25
