

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2

पत्रांक... 3057 अति. सिवान, दिनांक... 17/12/2025

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण (ब्राडो), पटना।

विषय :- वित्तीय वर्ष 2024-25 में मुख्यमंत्री ग्राम सड़क उन्नयन योजना (Gen.) अंतर्गत संवेदक के द्वारा पथ में किये गये कार्य का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2 के अधीन मुख्यमंत्री ग्राम सड़क उन्नयन योजना (Gen.) अंतर्गत चयनित पथ का अधियाचना प्राप्त विहित प्रपत्र में पूर्ण रूप से भरकर संलग्न करते हुए अनुरोध पूर्वक कहना है कि उक्त पथों में (संलग्न विहित प्रपत्र के अनुसार) कुल राशि 231.19036 (दो करोड़ एकतीस लाख उनीस हजार छतीस) ₹0 मात्र आवंटित करने की कृपा की जाए, ताकि उक्त पथों में किए गये कार्य का भुगतान किया जा सकें।
अनु- 1) अधियाचना विहित प्रपत्र में।

विश्वासभाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमंडल, सिवान-2

17.12.25

Requisition Format for Scheme MMGSUY (General/SC/ST)

Name of the Works Division :- RWD, Siwan-2

Name of the Works Division :- RWD, Siwan-2																		
Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	RRSMIP/24-25/Siwan-2/07	5140670350188	Warendar Pur Ke Shiv Mandir Se Kamashis Vnday Ke Char Tank	0.760	40.440	37.11447	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Complete	GSB Done, PCC Done	2580	0	0	35.20208	35.20208	37.08551	1.88343	Complete
2	RRSMIP/24-25/Siwan-2/07	5140670350166	1.034 Vijaypur Chanduli to Bhikpur	0.800	41.873	38.37807	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Complete	GSB Done, WBM-III Done, PCC Done	2320	0	0	0.00	0.00	38.36603	38.36603	Complete
3	RRSMIP/24-25/Siwan-2/07	5140670350169	Ziradai Me Bahindra Singh Ke Char Se Manager Bihari Ke Char Tank	0.510	24.871	25.58198	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Complete	GSB Done, WBM-III Done, PCC Done	2437	0	0	0.00	0.00	25.54398	25.54398	Complete
4	RRSMIP/24-25/Siwan-2/07	5140670350170	1.034 Vijaypur Chanduli to Shivpur	1.560	77.358	65.30878	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Complete	GSB Done, WBM-III Done, SDBC Done, PCC Done	2450	25 mm	5%	45.66673	45.66673	61.98513	16.31840	Complete

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	5	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
5	RRSMP/24-25/Siwan-2/07	5140670350173	1.246-1.233 to Hasanpurwa (VR12)	3.200	229.426	185.32155	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Complete	GSB Done, WBM-III B.M + SDBC Done,	2278	75 mm	5%	161.71345	161.71345	182.51938	20.80593	Comp lete
6	RRSMP/24-25/Siwan-2/07	5140670350177	Miya Ke Bhatakan Me Hasan Ansari Ke Ghar (Ghar Tuk)	0.300	17.472	16.10543	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Complete	GSB Done, WBM-III Done, PCC Done	2332	0	0	0.00	0.00	16.07173	16.07173	Comp lete
7	RRSMP/24-25/Siwan-2/07	5140670350184	1.249-1.229 to Majhiwalla (VR14)	2.200	114.799	89.13692	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Complete	GSB Done, WBM-III Done, PCC Done, SDBC Done	2447	25 mm	5%	41.52129	41.52129	75.83773	34.31644	Comp lete
8	RRSMP/24-25/Siwan-2/05	5140670350145	Siwan Guthani Path to Gopalchak	1.700	89.603	65.75152	12 CMBD/ 2025-26/ 06.08.2025	01.08.26	Work in Progress	GSB Done, WBM-III Done,		75 mm	5%	0.00	0.00	5.06485	5.06485	Ongoi ng
9	RRSMP/24-25/Siwan-2/05	5140670350137	Svetapur Atwa Road to Atwa Shiv Mandir	0.910	50.959	43.24797	12 CMBD/ 2025-26/ 06.08.2025	01.08.26	Complete	GSB Done, WBM-III Done, PCC Done	2386	0	0	0.00	0.00	35.22428	35.22428	Comp lete

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WM/ BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
10	RRSNIP/25-26/Siwan-2/07	5140670350259	Thepha (handpatti PMSY Road to T05	1.300	60.300	51.52389	28 CMBD/ 2025-26/ 26.09.2025	15.09.26	Work in Progress	G5B Done, PCC Done, WBM-III	2380	0	0	0.00	0.00	37.59529	37.59529	Ongoing
Total															284.10	515.29391	231.19036	

It is certified that Physical & Financial Progress has been updated in MIS.

[Signature]
 DIVISIONAL ACCOUNT OFFICER
 RURAL WORKS DEPARTMENT
 WORKS DIVISION, SIWAN-2

[Signature]
 EXECUTIVE ENGINEER
 RURAL WORKS DEPARTMENT
 WORKS DIVISION, SIWAN-2

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excell) of recorded IRI is enclosed (As Applicable).

GFR 12-B

[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs. 784.13898, Sanctioned under RRSMP (Gen.), dated 13.10.2025, in favour of EXECUTIVE ENGINEER, RWD, WORKS DIVISION, SIWAN-2, during the year 2025-26, an amount of Rs. 784.13898, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. 0.00, remaining unutilized at the end of the year 2025-26 has been surrendered to the Government (vide No C.E. (M&U)-4515-01-1479/2025- 91, (Encl)/ Patna, date 13.10.2025)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.


17/12/25
EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION SIWAN-2
Signature
Designation
Date
17.12.25

अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि MMGSUY (RRSMP-Gen) योजनान्तर्गत :-

1. पथ/पुल L034 Vijaypur Chanduli to Shivpur में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा, जीरादेई


सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, जीरादेई


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2


Name of work : L034 Vijaypur Chanduli to Shivpur															
Name of customer : M/S Adarsh Construction															
(R)Rural Road															
Good Average Poor															
< 4000 4001 - 5000 > 5000															
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	Ullim(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction?	Remarks
22/11/25	10:13:56	128	100	100	22.0 cm	24.1 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.2045352	N	84.2279481	E	Normal
22/11/25	10:14:10	128	100	200	24.0 cm	26.4 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.2056771	N	84.2278175	E	Normal
22/11/25	10:15:25	128	100	300	28.0 cm	23.4 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.2030173	N	84.2269984	E	Normal
22/11/25	10:15:41	128	100	400	23.0 cm	23.4 Km/Hr	2300.0 mm/Km	2332	3.22	Good	26.2027557	N	84.2263785	E	Normal
22/11/25	10:16:50	128	100	500	24.0 cm	14.2 Km/Hr	2400.0 mm/Km	2422	3.33	Good	26.2021700	N	84.2259811	E	Normal
22/11/25	10:17:12	128	100	600	18.0 cm	16.2 Km/Hr	1800.0 mm/Km	1890	2.65	Good	26.2014334	N	84.2251850	E	Normal
22/11/25	10:17:40	128	100	700	22.0 cm	13.1 Km/Hr	2200.0 mm/Km	2241	3.11	Good	26.2005221	N	84.2249552	E	Normal
22/11/25	10:18:02	128	100	800	20.0 cm	16.1 Km/Hr	2000.0 mm/Km	2080	2.88	Good	26.1998232	N	84.2244078	E	Normal
22/11/25	10:18:28	128	100	900	25.0 cm	14.2 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1988920	N	84.2247837	E	Normal
22/11/25	10:19:36	128	100	1000	26.0 cm	14.1 Km/Hr	2600.0 mm/Km	2603	3.55	Good	26.1984873	N	84.2253920	E	Normal
22/11/25	10:20:51	128	100	1100	30.0 cm	24.2 Km/Hr	3000.0 mm/Km	2964	3.99	Good	26.1979472	N	84.2262725	E	Normal
22/11/25	10:21:04	128	100	1200	25.0 cm	27.6 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1975720	N	84.2271384	E	Normal
22/11/25	10:21:27	128	100	1300	28.0 cm	16.2 Km/Hr	2800.0 mm/Km	2784	3.77	Good	26.1970573	N	84.2281322	E	Normal
22/11/25	10:22:49	128	100	1400	29.0 cm	15.8 Km/Hr	2900.0 mm/Km	2874	3.88	Good	26.1965301	N	84.2288884	E	Normal
22/11/25	10:23:12	128	100	1500	25.0 cm	10.8 Km/Hr	2500.0 mm/Km	2512	3.44	Good	26.1962122	N	84.2294175	E	Normal
22/11/25	10:24:22	128	60	1560	20.0 cm	17.5 Km/Hr	2000.0 mm/Km	2060	2.85	Good	26.1958230	N	84.2301322	E	Normal

Approved
12/11/25
JE

Be
12/11/25
AC


EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION SIMAN-2

Name of Customer: M/S Adarsh Construction , Machine no: 19208 , Road: L034 Vijaypur Chauduli to Shivpur , Date: 22-11-25 , Section No: 129 , Equation: $Y=0.904X+252.3$

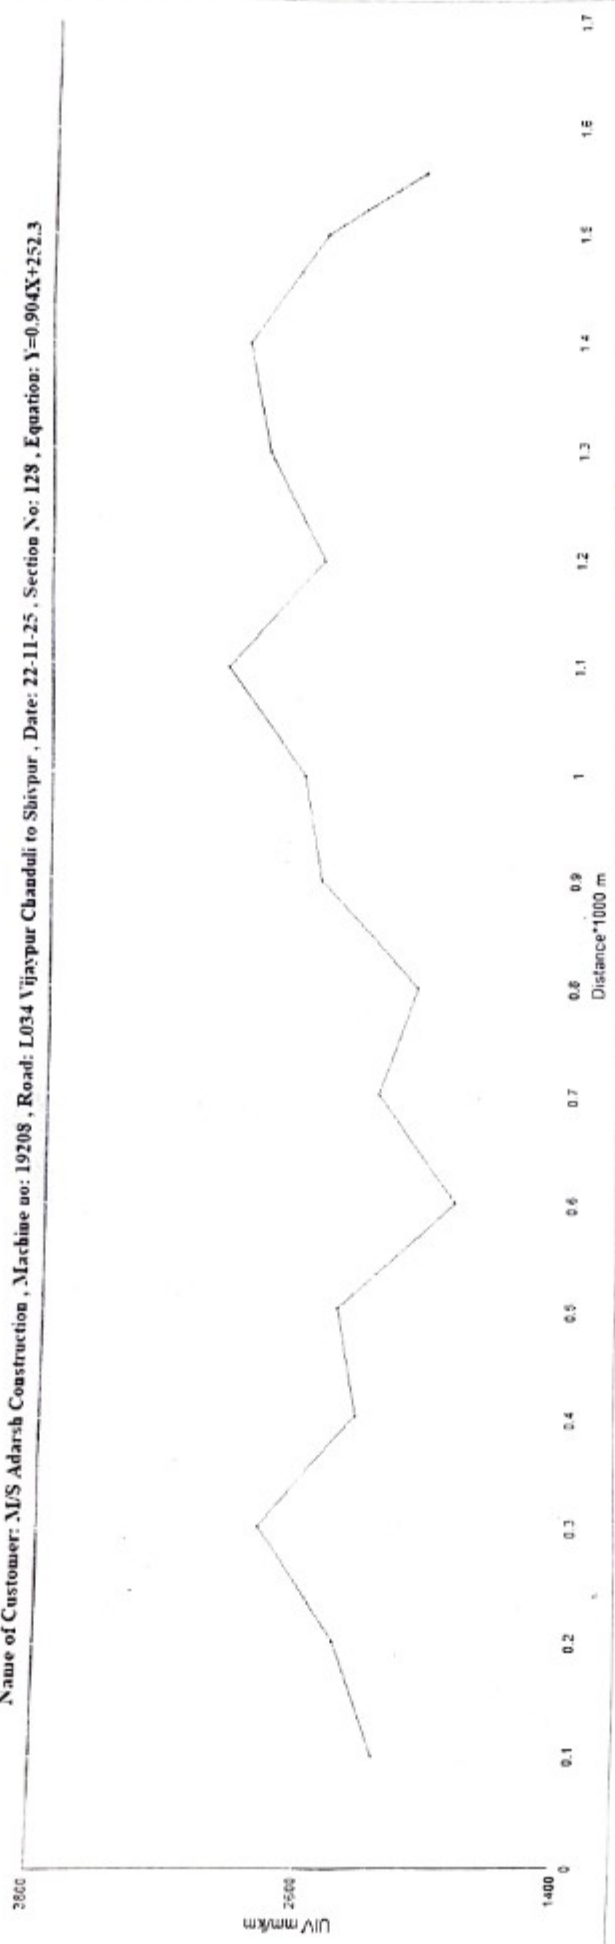

Adarsh
Shivpur
SE

Be
Shivpur
AS


EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION SIWAN-2
