

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, जयनगर

पत्रांक1840..... / , दिनांक17/12/2025/

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जयनगर ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
पटना ।

विषय :- (RRSMP SC) योजनाअंतर्गत चल रहे योजनाओं हेतु आवंटन उपलब्ध कराने के संबंध में ।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि (RRSMP SC) योजना हेतु अध्याचना अंतर्गत अध्याचना विहित प्रपत्र में तैयार कर समर्पित है ।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय ।

अनु० :-यथोक्त ।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, जयनगर

GFR 12-B

[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(3) Certified that out of the Loan of Rs.616.74069, Sanctioned under..RRSMP(SC), dated..19.08.2025, in favour of EE RWD JAYNAGAR., during the year .2025-26., an amount of Rs..616.74069, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.0.00 remaining unutilized at the end of the year..... has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(4) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.

Signature.....

Designation EE JAYNAGAR

Date..16.12.2025

Requisitio Format For Scheme MMGSUY/RRSMP(SC)

Name of Division-Jaynagar

SI No	Pkg No	Project ID As per MIS	Name Of Road	AA Length(n km)	Administrative Approval(C onstruction Work)Amount (in lakh)	Agreement(Constructio n work)Amou nt (in Lakh)	Agreement No & Date	Date of Complition as per Agreement	Actual Date of Complition	work Status(W BM/WM M/BM/S DBC etc)	Value of IRI(in mm/Km)	Thickness of Bitumen Contenet(in n %)	Value of Bitumen content(in %)	Total Previous Alloteed amount(in lakh)	Upto dateExpendi ture as per MIS(in lkah)	value of work done(in lakh)	Current Demand(in lakh)	Remarks
1	RRSMP/24-25 Jaynagar/01	62209703 60025	BASOPATI T04 To DUBI	9.600	1546.327	1566.38081	02 mbd/25-26 mmgsuy(09/06/2025)	08/06/2026	-	Surface completed	3447.71	25mm	5%	1179.43028	1179.43028	1314.40933	134.97905	
2	RRSMP/24-25 Jaynagar/01	62209703 00010	Manapatti MMGSY Road to Kaithani Tola Manapatti	0.190	13.39	12.63240	02 mbd/25-26 mmgsuy(09/06/2025)	08/06/2026	-	Surface completed	3540	25mm	5%	9.90555	9.90555	12.29183	2.38628	
3	RRSMP/24-25 Jaynagar/01	62209703 00013	L053-T03 To Jouki (VR053)	2.58	154.497	147.07215	02 mbd/25-26 mmgsuy(09/06/2025)	08/06/2026	-	Surface completed	3474.42	25mm	5%	111.97376	111.97376	126.77665	14.80289	
4	RRSMP/24-25 Jaynagar/01	62209703 00012	L037-T04 To Patauna (VR037)	3.210	183.954	176.72859	02 mbd/25-26 mmgsuy(09/06/2025)	08/06/2026	-	Surface completed	3415.18	25mm	5%	103.60757	103.60757	133.67698	30.06941	
5	RRSMP/24-25 Jaynagar/01	62209703 00006	Basopatti Main Road to Mshari Tola Parsa	0.48	31.746	29.88361	02 mbd/25-26 mmgsuy(09/06/2025)	08/06/2026	-	Surface completed	3403.8	25mm	5%	24.80814	24.80814	28.98509	4.17695	
6	RRSMP/24-25 Jaynagar/01	62209703 00015	L056-L055 To Kamalbari (VR056)	2.400	128.54	125.93635	02 mbd/25-26 mmgsuy(09/06/2025)	08/06/2026	-	pcc completed	-	-	-	0	0	49.68995	49.68995	
7	RRSMP/24-25 Jaynagar/01	62209703 60020	CHANDAN BAZAR TO CHANDAN KASERA	1.19	60.398	60.99643	02 mbd/25-26 mmgsuy(09/06/2025)	08/06/2026	-	pcc completed	-	-	-	0	0	31.55781	31.55781	

1/14



8	RRSMP/24-25 Jaynagar/01	62209703 60016	Construction of Belouna to Koriapatti road under Basopatti Block	1.71	97.345	93.63849	02 mbd/25-26 mmgsuy(09/06/ 2025)	08/06/2026	-	pcc completed	-	-	-	66.88399	66.88399	77.32402	10.44003
9	RRSMP/24-25 Jaynagar/01	62209703 60017	Blat to Khaira Tol	1.750	87.298	105.45469	02 mbd/25-26 mmgsuy(09/06/ 2025)	08/06/2026	-	pcc completed	-	25mm	5%	86.02767	86.02767	101.03878	15.01111
10	RRSMP/24-25 Jaynagar/01	62209703 60015	MMGSY UCCHAL TO CHITAH CHOWK	1.61	104.168	117.15422	02 mbd/25-26 mmgsuy(09/06/ 2025)	08/06/2026	-	Surface completed	3441.6	25mm	5%	99.28026	99.28026	113.58931	14.30905
11	RRSMP/24-25 Jaynagar/01	62209703 00016	Madhubani jila antargat wasopatti prakhand me bhaluaahi goan se mahadalit ewn dalito ke colony ewn mochi tola bhanpatti se nya prathamik vidhyalay paswan tola hote hue wasopatti se mukhya sarak tak path nirmaan	2.2	125.926	148.98619	02 mbd/25-26 mmgsuy(09/06/ 2025)	08/06/2026	-	pcc completed	3409.35	25mm	5%	69.4339	69.4339	138.86957	69.43567

It is certified that Physical & financial Progress has been updated in MIS

Senior D.A.O/D.A.O
RWD, Works Division Jaynagar

Handwritten signature
12/12/21
Executive Engineer
RWD, Works Division Jaynagar

Note-Above signed copy along with forwarding letter & utilisation certificate must be uploaded in MIS
2 Signed hard copy and soft copy(in excell)of recorded IRI is enclosed(AsApplicable)



Name-MMGSY UCCHAL TO CHITAH CHOWK
Cont Name-Nilamber Tower Pvt Ltd

Date	Time	Section	Length	Bumps	Speed	OR	IRI	ATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
6/12/25	14:26:0	96	0.1	310	0	3100	3654	G	26.8888	86.149487	Normal
6/12/25	14:26:0	96	0.1	300	20.2	3000	3540	G	26.888003	86.101413	Normal
6/12/25	14:26:24	96	0.1	310	10.1	3100	3654	G	26.887495	86.10237	Normal
6/12/25	14:27:0	96	0.1	260	10.1	2600	3086	G	26.88672	86.104863	Normal
6/12/25	14:27:0	96	0.1	320	20.2	3200	3767	G	26.888205	86.107312	Normal
6/12/25	14:27:35	96	0.1	270	20.2	2700	3199	G	26.890295	86.109762	Normal
6/12/25	14:27:35	96	0.1	310	20.2	3100	3654	G	26.89115	86.111555	Normal
6/12/25	14:28:10	96	0.1	320	10.1	3200	3767	G	26.891463	86.112613	Speed Breaker
6/12/25	14:28:10	96	0.1	270	20.2	2700	3199	G	26.892775	86.114763	Normal
6/12/25	14:28:45	96	0.1	260	10.1	2600	3086	G	26.893542	86.116345	Curve
6/12/25	14:29:20	96	0.1	320	10.1	3200	3767	G	26.893425	86.11897	Speed Breaker
6/12/25	14:29:20	96	0.1	260	20.2	2600	3086	G	26.893588	86.120803	Normal
6/12/25	14:30:0	96	0.1	320	10.1	3200	3767	G	26.89335	86.121988	Normal
6/12/25	14:30:0	96	0.1	300	10.1	3000	3540	G	26.895995	86.123562	Curve
6/12/25	14:30:31	96	0.1	240	20.2	2400	2858	G	26.896922	86.12428	Normal
TOTAL			1.5			43700	51624				
Average-3441.60											

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 2400$$

$$Y = 2858$$

RURAL ROAD

Average Poor
4001-5000 >5001

Handwritten Signature
Executive Engineer
RWD, Works Division Jaynagar



Customer: Nilamber Tower Private Limited
 Name of Work/Road: UCCHAL TO CHITAH CHOWK
 Lab Job number:
 Date: 06-12-2025
 Section No. 96

Test Date: 06-12-2025 Road Name: UCCHAL TO CHITAH CHOWK
 Machine No: 19578 Road Type: (R) RURAL ROAD
 Start S No: Side: Interval
 Start E No:
 Weather: Normal UIV Range: 1858 To 5000 1000 mm/km
 Start Location: 26.533280 Dist Range: 0 To 1.6 0.1 * 1000 m
 End Location: 86.074570 Equation: $Y = 0 * X^2 + 1.136 * X + 132.5$


Print

Generate Report and Graph

Redraw Graph

Map View

File: C:\Users\dell\OneDrive\Desktop\Bumb report\Nilamber Tower\mmgsy ucchal to chitahi chowk(1.610).Xls.
 Name of Customer: Name of Work/Road: Lab Job number:

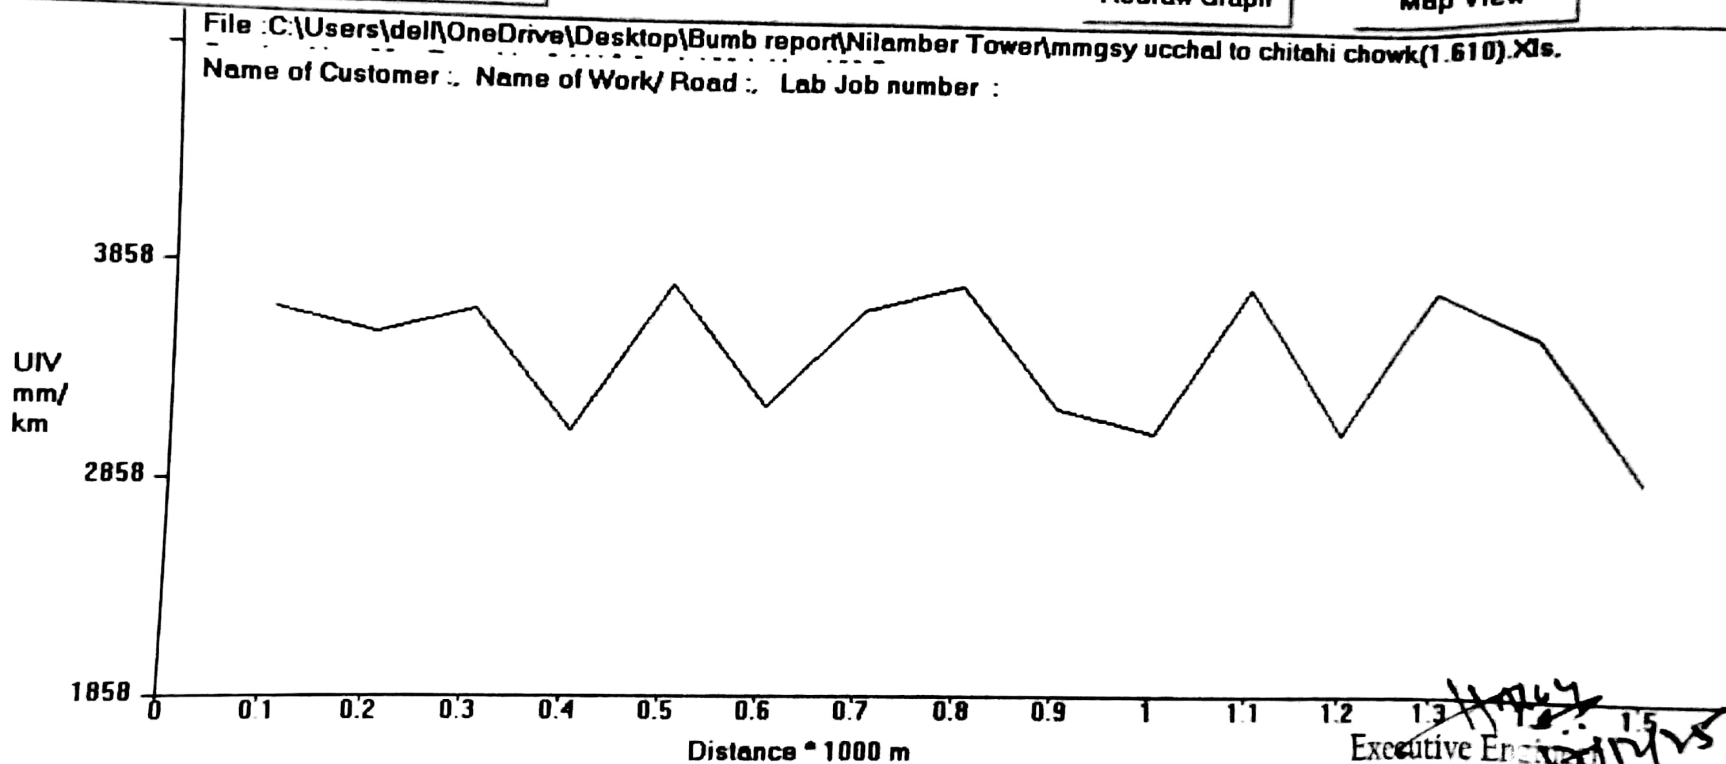

Executive Engineer
 Rural Works Department
 District Road

