

**कार्यपालक अभियंता का कार्यालय**  
**ग्रामीण कार्य विभाग कार्य प्रमण्डल, बाँका-2**

पत्रांक... 3221/..... / बाँका

दिनांक 22/12/25.

प्रेषक,

कार्यपालक अभियंता  
ग्रामीण कार्य विभाग,  
कार्य प्रमण्डल, बाँका-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव  
बिहार ग्रामीण पथ विकास अभिकरण, पटना।

विषय:-


शीर्ष 4515 मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के कार्यों के भुगतान हेतु निधि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के भुगतान हेतु 66696348/- की अधियाचना विहित प्रपत्र में तैयार कर आपके आवश्यक कार्यवाई हेतु समर्पित की जाती है।

- अनु० :-
1. विहित प्रपत्र में आवंटन की मांग।
  2. उपयोगिता प्रमाण पत्र।
  3. मापी पुस्त की छाया प्रति।

विश्वासभाजन

  
कार्यपालक अभियंता  
ग्रा०का०वि०, कार्य प्रमण्डल  
बाँका-2  
22/12/25



**GFR 12-B**  
[See Rule 256 (2)]

**FORM OF UTILIZATION CERTIFICATE**

(1) Certified that out of the Loan of Rs. **5056.44559**, Sanctioned under MMGSUY (RRSMP-GEN), Lt. No.-102 dated.-18.11.2025 in favour of E.E.R.W.D.(W) Division Banka-2 during the year **2025-26**, an amount of Rs. **5056.15539**, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. **0.29020** remaining unutilized at the end of the year.-2024 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Allotment
2. MB
3. Cash book

Signature.....  
Designation Executive Engineer  
R.W.D(W) Division, Banka-2  
Date- 22.12.2025



**Requisition Format for Scheme MMGSUY/RRSMP (General)**

**Name of the Works Division :-Banka 2**

| Sl. No. | Package No.            | Project ID as per MIS | Name of Road                                                            | AA Length (in km.) | Administrative Approval (construction work) Amount (in Lakh) | Agreement (construction work) Amount (in Lakh) | Agreement No. & Date     | Date of Completion as per Agreement | Actual Date of Completion | Work Status (WBM/WM/B M/SDBC etc.) | Value of IRI (in mm/km) | Thickness of Bitumen Layer (in mm) | Value of Bitumen Content (in %) | Total Previous Allocated Amount (in Lakh) | Upto date Expenditure as per MIS (in Lakh) | Value of Work Done (in Lakh) | Current Demand (in Lakh) | Remarks         |
|---------|------------------------|-----------------------|-------------------------------------------------------------------------|--------------------|--------------------------------------------------------------|------------------------------------------------|--------------------------|-------------------------------------|---------------------------|------------------------------------|-------------------------|------------------------------------|---------------------------------|-------------------------------------------|--------------------------------------------|------------------------------|--------------------------|-----------------|
| 1       | RRSMP/24-25 Banka-2/06 | 3070360350188         | Baniya chak to Navotiya Baraitkar                                       | 1.040              | 43.177                                                       | 38.56044                                       | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                  | 2575                    | 25mm                               | 5%                              | 7.77339                                   | 7.77339                                    | 31.09357                     | 23.32018                 | Work in process |
| 2       | RRSMP/24-25 Banka-2/06 | 3070360350144         | L068-Kathra to Phulwariya (VR68)                                        | 1.370              | 68.650                                                       | 59.09527                                       | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                  | 2464                    | 25mm                               | 5%                              | 27.49743                                  | 27.49743                                   | 36.45891                     | 8.96148                  | Work in process |
| 3       | RRSMP/24-25 Banka-2/06 | 3070360350146         | L101-Kathra To Bhalu (VR101)                                            | 1.150              | 62.700                                                       | 51.63688                                       | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                  | 2581                    | 25mm                               | 5%                              | 16.46549                                  | 16.46549                                   | 31.65992                     | 15.19443                 | Work in process |
| 4       | RRSMP/24-25 Banka-2/06 | 3070360350150         | L111-T02 Kusmi To Kotra (VR111)                                         | 1.720              | 89.745                                                       | 71.12558                                       | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | Surface Completed                  | 2470                    | 25mm                               | 5%                              | 32.25118                                  | 32.25118                                   | 39.00049                     | 6.74931                  | Work in process |
| 5       | RRSMP/24-25 Banka-2/06 | 3070360350172         | Punsiya Dhoraiya road to Kathouni                                       | 1.450              | 81.442                                                       | 68.10618                                       | 05CMBD/20 25-26 09.06.25 | 08.06.26                            | -                         | Surface Completed                  | 2490                    | 25mm                               | 5%                              | 31.06368                                  | 31.06368                                   | 45.65149                     | 14.58781                 | Work in process |
| 6       | RRSMP/24-25 Banka-2/07 | 3070360350141         | Chakra More To Dhopsanda                                                | 1.900              | 102.376                                                      | 83.35699                                       | 05CMBD/20 25-26 09.06.25 | 08.06.26                            | -                         | PCC Completed                      | 2582                    | 25mm                               | 5%                              | 7.91410                                   | 7.91410                                    | 16.66126                     | 8.74716                  | Work in process |
| 7       | RRSMP/24-25 Banka-2/07 | 3070360350136         | Sanhola Panjwar Road To Mathurapur                                      | 2.973              | 146.670                                                      | 121.20147                                      | 05CMBD/20 25-26 09.06.25 | 08.06.26                            | -                         | Surface Completed                  | 2597                    | 25mm                               | 5%                              | 57.46111                                  | 57.46111                                   | 82.25751                     | 24.79640                 | Work in process |
| 8       | RRSMP/24-25 Banka-2/07 | 3070360350162         | Punsiya Dhoraiya Road Manihar Rajabandho Parhar.                        | 6.125              | 385.540                                                      | 332.62209                                      | 05CMBD/20 25-26 09.06.25 | 08.06.26                            | -                         | PCC Completed                      | 2556                    | 25mm                               | 5%                              | 95.49122                                  | 95.49122                                   | 251.35895                    | 155.86773                | Work in process |
| 9       | RRSMP/24-25 Banka-2/06 | 3070360350167         | Punsiya Dhoraiya Road To Porachuk                                       | 5.300              | 368.442                                                      | 314.94961                                      | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | BT Completed, PCC in progress      | 2446                    | 25mm                               | 5%                              | 202.09810                                 | 202.09810                                  | 227.38293                    | 25.28483                 | Work in process |
| 10      | RRSMP/24-25 Banka-2/06 | 3070360350140         | Newad Bander main Road To Kharant Via Mfyagadha Dhangarsa Mahedali Tola | 12.010             | 796.953                                                      | 704.46339                                      | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | PCC & BT in Progress               | 2533                    | 25mm                               | 5%                              | 298.92012                                 | 298.92012                                  | 458.86707                    | 159.94695                | Work in process |
| 11      | RRSMP/24-25 Banka-2/06 | 3070360350159         | ASTA TO T T MANGAR                                                      | 1.500              | 73.992                                                       | 58.92331                                       | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | PCC & BT Completed                 | 2734                    | 25mm                               | 5%                              | 29.14163                                  | 29.14163                                   | 35.93775                     | 6.79612                  | Work in process |
| 12      | RRSMP/24-25 Banka-2/06 | 3070360350170         | L052-Punsiya Dhoraiya Manipur Rd. to Makekar (VR52)                     | 1.760              | 87.035                                                       | 72.99169                                       | 01CMBD/20 25-26 02.05.25 | 01.05.26                            | -                         | BT Completed, PCC in progress      | 2795                    | 25mm                               | 5%                              | 33.24976                                  | 33.24976                                   | 43.36650                     | 10.11674                 | Work in process |



|              |                           |               |                                                                  |       |         |           |                                |          |   |                       |      |      |    |          |          |           |           |                    |
|--------------|---------------------------|---------------|------------------------------------------------------------------|-------|---------|-----------|--------------------------------|----------|---|-----------------------|------|------|----|----------|----------|-----------|-----------|--------------------|
| 13           | RRSMP/24-25<br>Banka-2/01 | 3070360350206 | Barahat Market<br>(Bajrangwali Temple)<br>to Chilmil via Akagora | 1.840 | 92.250  | 78.36900  | 06CMBD/20<br>25-26<br>19.06.25 | 18.06.26 | - | PCC Completed         | 2495 | 25mm | 5% | 18.52443 | 18.52443 | 74.09770  | 55.57327  | Work in<br>process |
| 14           | RRSMP/24-25<br>Banka-2/01 | 3070360350204 | L055-BGD Dumka RD<br>to Mohanpur (Track 55)                      | 4.620 | 312.900 | 251.38552 | 06CMBD/20<br>25-26<br>19.06.25 | 18.06.26 | - | PCC & BT<br>Completed | 2647 | 25mm | 5% | 47.62034 | 47.62034 | 174.08058 | 126.46024 | Work in<br>process |
| 15           | RRSMP/24-25<br>Banka-2/07 | 3070360350153 | JAGATPUR to<br>JHAKIYA GONRA                                     | 1.260 | 62.436  | 51.09109  | 05CMBD/20<br>25-26<br>09.06.25 | 08.06.26 | - | PCC Completed         | 2506 | 25mm | 5% | 7.88804  | 7.88804  | 16.60639  | 8.71835   | Work in<br>process |
| 16           | RRSMP/24-25<br>Banka-2/07 | 3070360350149 | L104-T01 Rifaetpur To<br>Rampur (VR104)                          | 1.870 | 92.721  | 75.98642  | 05CMBD/20<br>25-26<br>09.06.25 | 08.06.26 | - | Surface<br>completed  | 2502 | 25mm | 5% | 35.19503 | 35.19503 | 51.03751  | 15.84248  | Work in<br>process |
| <b>Total</b> |                           |               |                                                                  |       |         |           |                                |          |   |                       |      |      |    |          |          |           | 666.96348 |                    |

It is certified that Physical & Financial Progress has been updated in MIS.

Senior D.A.O./B.A.O.  
RWD, Works Division Banka-2

Executive Engineer  
RWD, Works Division, Banka-2

Note :-


- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excell) of recorded IRI is enclosed (As Applicable).

22/12/25  
22/12/25

## अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि RRSMP  
योजनान्तर्गत

1. पथ/पुल L068 Kothra to Phudwariya (PK 68) में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुरतिका में दर्ज है जिसका सत्यापन कर लिया गया है।

  
25/10/25  
कनीय अभियंता  
ग्रामीण कार्य विभाग  
कार्य प्रशाखा .....।.....

  
31/10/25  
सहायक अभियंता  
ग्रामीण कार्य विभाग  
कार्य अवर प्रमण्डल.....

  
1.10.25  
कार्यपालक अभियंता  
ग्रामीण कार्य विभाग  
कार्य प्रमण्डल बाँका-2



Road Name : L068-Kathra to Phulwariya (VR68), Contractor Name : Anil Kumar Singh

| Date     | Time     | Section No. | Length in km | Bumps in mm | Speed Rate | OR mm/km | IRI mm/km | CATEGORY ROAD | Latitude | Longitude | Event  |
|----------|----------|-------------|--------------|-------------|------------|----------|-----------|---------------|----------|-----------|--------|
| 23/10/25 | 10:22:23 | 58          | 0.1          | 240         | 30.3       | 2400     | 2537      | G             | 25.02464 | 87.06555  | Normal |
| 23/10/25 | 10:22:33 | 58          | 0.1          | 210         | 30.4       | 2100     | 2251      | G             | 25.0255  | 87.06548  | Normal |
| 23/10/25 | 10:22:47 | 58          | 0.1          | 250         | 30.3       | 2500     | 2633      | G             | 25.0264  | 87.06527  | Normal |
| 23/10/25 | 10:22:56 | 58          | 0.1          | 230         | 30.3       | 2300     | 2442      | G             | 25.02701 | 87.06499  | Normal |
| 23/10/25 | 10:23:04 | 58          | 0.1          | 190         | 30.4       | 1900     | 2060      | G             | 25.02801 | 87.06475  | Normal |
| 23/10/25 | 10:23:13 | 58          | 0.1          | 220         | 30.4       | 2200     | 2347      | G             | 25.02705 | 87.06556  | Normal |
| 23/10/25 | 10:23:25 | 58          | 0.1          | 240         | 30.3       | 2400     | 2537      | G             | 25.02734 | 87.06636  | Normal |
| 23/10/25 | 10:23:30 | 58          | 0.1          | 200         | 30.2       | 2000     | 2156      | G             | 25.02834 | 87.0673   | Normal |
| 23/10/25 | 10:23:39 | 58          | 0.1          | 230         | 30.1       | 2300     | 2442      | G             | 25.02914 | 87.06765  | Normal |
| 23/10/25 | 10:23:57 | 58          | 0.1          | 310         | 30.1       | 3100     | 3205      | G             | 25.02994 | 87.06771  | Curve  |
| 23/10/25 | 10:24:23 | 58          | 0.1          | 230         | 30.2       | 2300     | 2442      | G             | 25.03055 | 87.06788  | Normal |
| 23/10/25 | 10:24:39 | 58          | 0.1          | 250         | 30.2       | 2500     | 2633      | G             | 25.0314  | 87.06816  | Normal |
| 23/10/25 | 10:24:57 | 58          | 0.1          | 220         | 30.2       | 2200     | 2347      | G             | 25.0324  | 87.06852  | Normal |
| Length - |          |             | 1.3          | Average -   |            |          | 2464      |               |          |           |        |

$$Y = 0 * X^2 + 0.954 * X + 247.70$$


$$X = 2200$$

$$Y = 2347$$

(R) RURAL ROAD  
 Good Average Poor  
 <4000 4001-5000 >5001

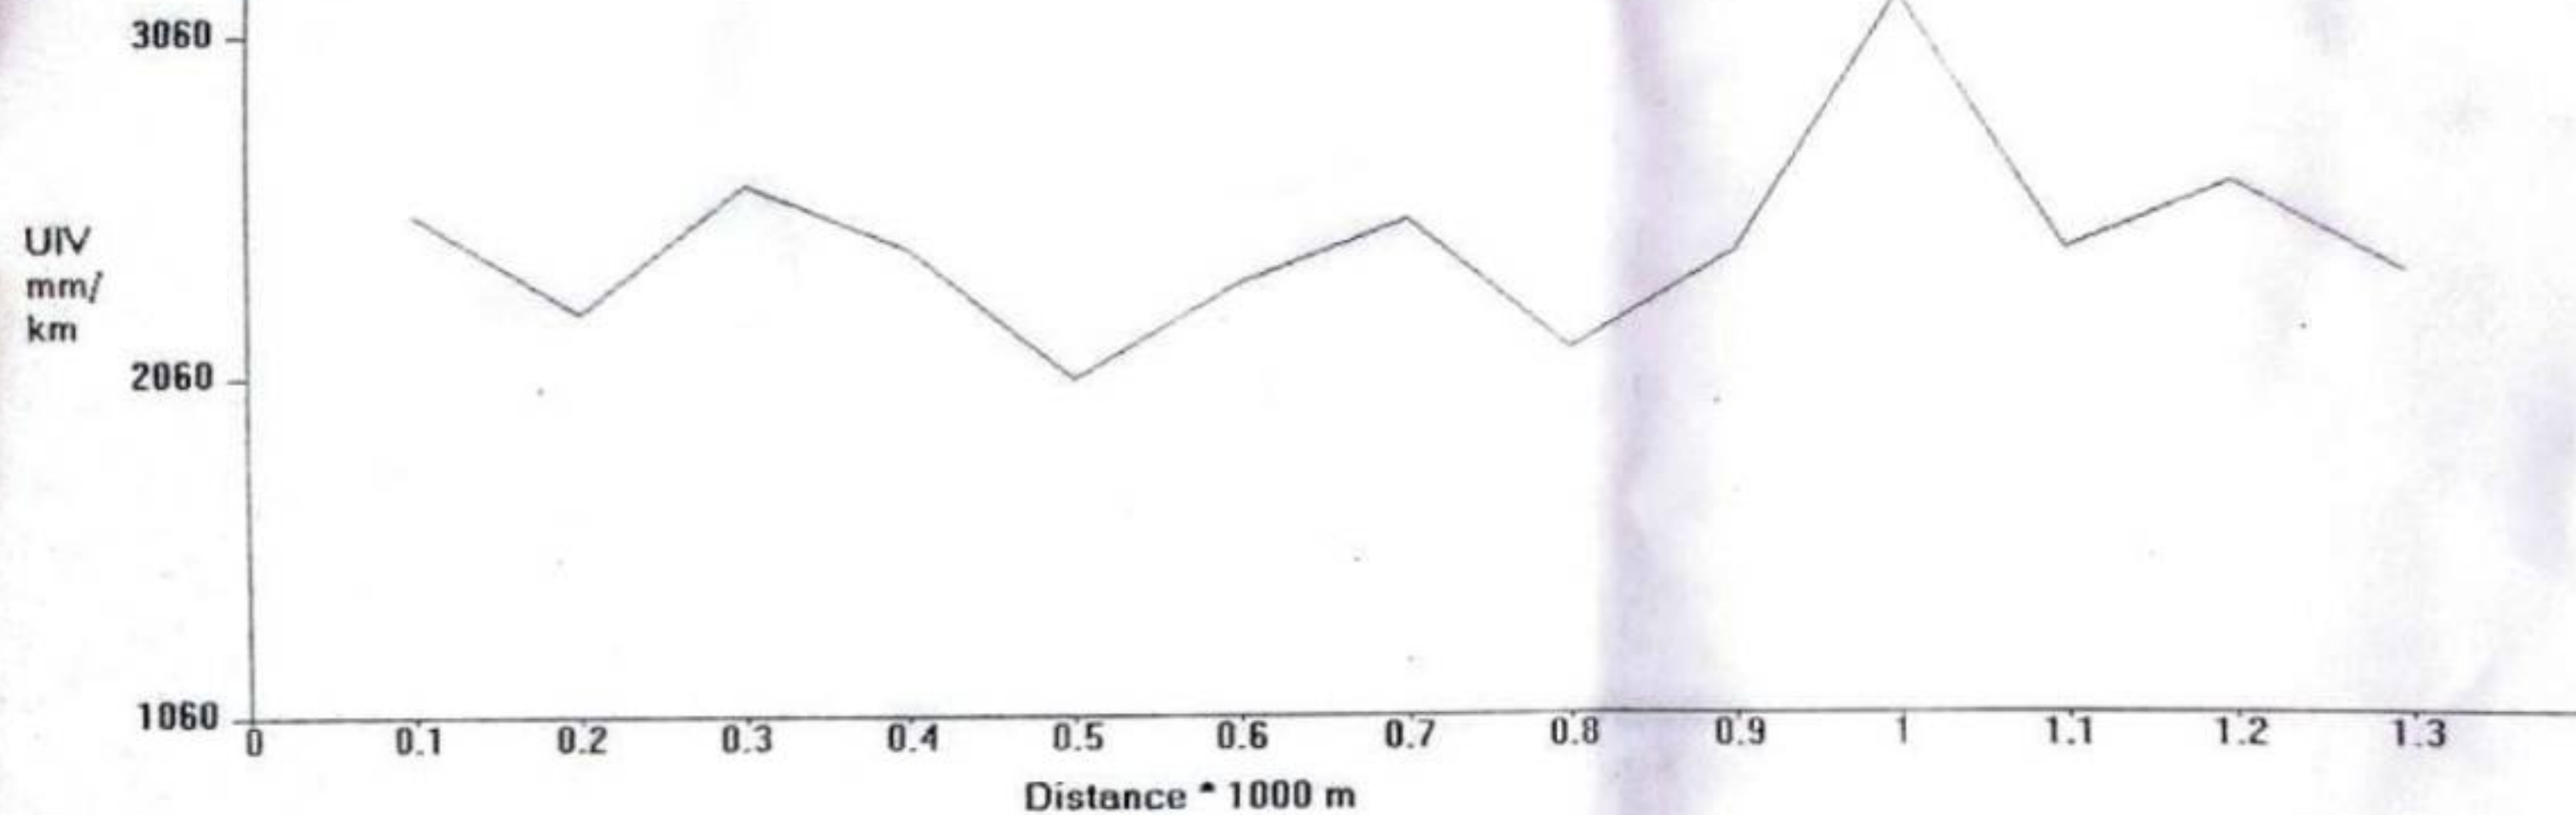
  
 25/10/25  
 Junior Engineer  
 Rural Works Department  
 Works Section, Dhoraiya-1


  
 31/10/25  
 Assistant Engineer  
 Rural Works Department  
 Works Sub-Division, Dhoraiya

  
 31.10.25  
 Executive Engineer  
 Rural Works Department  
 Works Division, Banka-2

File :D:\Steco Bump\Sec\_58.xlsx Section No. :58. Eqn : $Y = 0 * X^2 + 0.954 * X + 247.70$

Name of Customer :Anil Kumar Singh, Name of Work/ Road : L068-Kathra to Phulwariya (VR68). Lab Job number :



  
25/10/25  
J.E

  
31/10/25  
AE

  
31-10-25
