

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल, नवगछिया

Email Id-ccnavgachhiya@gmail.com

पत्रांक - १२१० (अनु०)

नवगछिया / दिनांक- ०३/०७/२५

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नवगछिया।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
विश्वेश्वरैया भवन, वेली रोड़, पटना।


विषय:- **RRSMP (Gen)** योजनान्तर्गत पथ में आवंटन उपलब्ध कराने के संबंध में।

महाशय


उपर्युक्त विषय के संबंध में कहना है कि संलग्न विवरणी अनुसार **RRSMP (Gen)** योजनान्तर्गत के निर्माण कार्य मद में राशि- **1096.96433** लाख रुपये का आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक द्वारा कराये गये निर्माण कार्य का भुगतान किया जा सके।

अनु०-पथ विवरणी, उपयोगिता प्रमाण-पत्र,
मापी पुस्त की छाया प्रति।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नवगछिया


०३/०७/२०२५

Requisition Form for Scheme RRSMP (Gen)

Name of the Works Division :- Navgachhiya																		
Sl No	Package No	Project ID as per MIS	Name of Road	AA Length (in km)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WEM/NA MBEN/SDB C etc)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/24-25 Navgachhiya 06	30703303500041	NAGRAH KALI STHAN TO MANDAL TOLA	1.300	125.4300	121.94172	06/CNMBD/2 025-26 10.06.2025	09.06.2026	-	Work in progress	2628.00	PCC	-	0.000	0.000	80.65403	80.65403	
2	RRSMP/24-25 Navgachhiya 06	30703303500042	REO ROAD TO MANDAL TOLA (TETRI)	1.200	102.4900	83.67344	06/CNMBD/2 025-26 10.06.2025	09.06.2026	-	PCC Work Complete	-	PCC	-	0.000	0.000	81.50430	81.50430	
3	RRSMP/24-25 Navgachhiya 07	30703303500001	L025-NH 31 To Jaunva Nagrah (VR5)	3.700	475.8590	391.44042	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	3199.86	75 mm	5.10	122.89748	122.89748	337.06056	214.16308	
4	RRSMP/24-25 Navgachhiya 07	30703303500002	RCD ROAD To KHAGGA	3.000	309.5200	237.95424	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	SDBC Work in progress	2820.76	25 mm	5.20	0.000	0.000	193.64996	193.64996	
5	RRSMP/24-25 Navgachhiya 07	30703303500003	Garaya Chawk To Jamania Bujangbahi Asthan Thatheri	2.260	282.0700	211.80557	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	2546.86	75 mm	5.10	0.000	0.000	176.27242	176.27242	
6	RRSMP/24-25 Navgachhiya 07	30703303500005	Road No.-14 (Guraniya School) to Choudhary Tola	2.000	184.4690	151.93264	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	1992.35	25 mm	5.20	0.000	0.000	122.83939	122.83939	
7	RRSMP/24-25 Navgachhiya 07	30703303500006	punama nagar de paswan tola se barah hote hue ujant tak	2.400	182.1690	140.33876	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	2220.25	PCC	-	45.64816	45.64816	131.92490	86.27674	
8	RRSMP/24-25 Navgachhiya 07	30703303500007	NH31 to president school se ujant masjid idgarah hote hue	1.900	131.7200	97.38221	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	3002.42	25 mm	5.20	0.000	0.000	70.92342	70.92342	
9	RRSMP/24-25 Navgachhiya 07	30703303500010	NH31 Raj Inn hotel ke samne se RWD road tak	0.900	54.8000	43.26562	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	2944.22	PCC	-	0.000	0.000	39.98012	39.98012	
10	RRSMP/24-25 Navgachhiya 07	30703303500015	Vikramshila approach path jagapur to shiv mandir Road	0.450	21.8300	16.94232	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	2681.40	PCC	-	0.000	0.000	16.17864	16.17864	
11	RRSMP/24-25 Navgachhiya 07	30703303500016	RCD road to tetri Brahman tola	0.300	17.6300	15.22948	01/CNMBD/2 025-26 20.05.2025	19.05.2026	-	Surface work Complete	2835.66	PCC	-	0.000	0.000	14.52223	14.52223	
Total=														1096.96433				

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the Month-June-2025
RRSMP (Gen)

PIU - R.W.D. Works Division Navgachhiya

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in Lacs Rs.)	Particulars
1.	Construction of Rural Roads under RRSMP (Gen)	Letter No:CE.(M&U)-4515-01-873/2025-39 Patna- Date-21.05.2025	168.54564	Certified that out of Rs. 168.54564 Lakhs received upto the years 2025-26 in favour of Ex. Engineer, RWD Bihar, Navgachhiya a sum of Rs 168.54564 lakhs has been utilized for the purpose of MMGSY(NDB) Schemes as given in the margin for which it was sanctioned and that the balance of Rs.00.00 lakhs the end of the period under.
Total			168.54564	

2. Certified that I have satisfied may self that the conditions on which the grants in aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.
Kinds of Checks exercised-
 - i. Works have been supervised by Executive Engineer/Superintending Engineer
 - ii. Periodical inspection has been conducted by Executive engineer/Superintending Engineer
 - iii. Construction materials have been tested.
 - iv. Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer
 - v. All other codal formalities have been observed.
3. Physical Progress achieved-
 - i. Construction of Road Works
 - ii. Construction of C.D. Works


 Executive Engineer
 Rural Work Department
 Works Division, Navgachhiya

 21/05/2025

Name of Road-RCD road to tetri Brahman tola
Contractor Name-Gautam Kumar Yadav

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	ATEGOR ROAD	Latitude	Longitude	Event	$Y = 0 * X^2 + 0.889 * X + 228.2$
28/6/25	16:13:40	54	0.1	300	0	3000	2895	G	25.37475	87.06903	Normal	X = 2900
28/6/25	16:14:0	54	0.1	290	10.1	2900	2806	G	25.3783	87.06949	Normal	Y = 2806
28/6/25	16:14:15	54	0.1	290	10.1	2900	2806	G	25.37472	87.06922	Normal	
AVG=2835.66												

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Chintha
28/06/25
(PATIL)

Mr. A. Rahman
28/06/25
J.E

J.E
28/06/25

Name of Customer: GAUTAM KUMAR YADAV
 Name of Work: RCD road to tein Brahman tola
 Lab Job number: 28/6/25
 Date: 28/6/25
 Section No: 54


Test Date: 28 Jun '25	Road Name: RCD road to tein Brahman tola
Machine No: 435	Road Type: (R) RURAL ROAD
Start S No:	Side:
Start E No:	Interval:
Weather:	UVI Range: 1606 To 4000 mm/Am
Start Location:	Dist Range: 0 To 0.4 0.1 - 1000 m
End Location:	Equation: $Y = 0 \cdot X^2 + 0.837 \cdot X + 228.2$

Print: Generate Report and Graph

Redraw Graph

Map View

File: C:\Users\BIRDA\Downloads\54.xls, Section No: 54, Eqn: $Y = 0 \cdot X^2 + 0.837 \cdot X + 228.2$
 Name of Customer: GAUTAM KUMAR YADAV, Name of Work: Road RCD road to tein Brahman tola, Lab Job numb

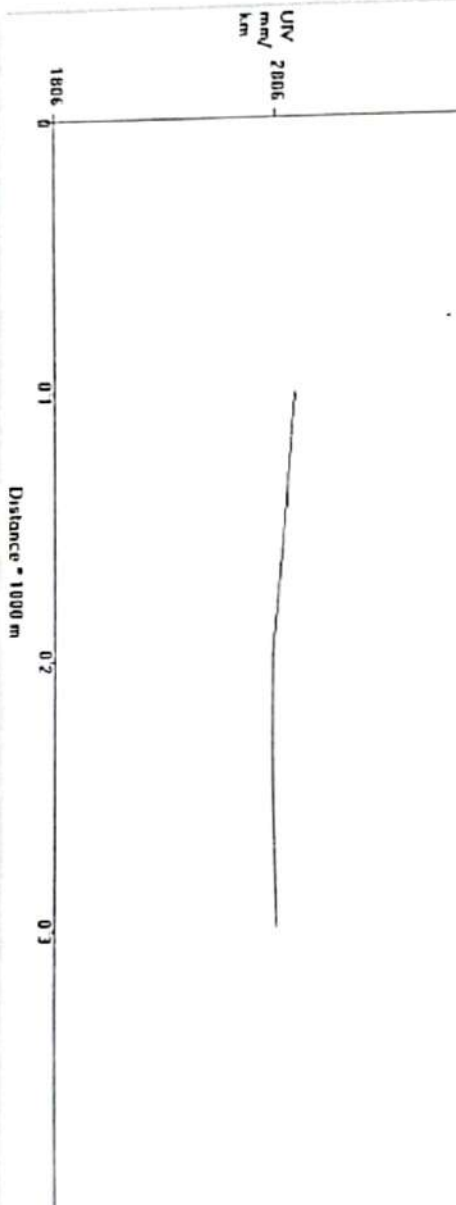

Shubra
 28/6/25
 (ATTN)

Wd. A. P. Sharma
 28/6/25
 J-E

28/6/25
