

**कार्यपालक अभियन्ता का कार्यालय**  
**ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बेगूसराय**

पत्रांक... 6743230... बेगूसराय,

दिनांक 16/05/2025

प्रेषक:— कार्यपालक अभियन्ता,  
ग्रामीण कार्य विभाग,  
कार्य प्रमण्डल, बेगूसराय।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी—सह—सचिव  
बिहार ग्रामीण पथ विकास अभिकरण,  
बुद्ध मार्ग, पटना

विषय:— शीर्ष— MMGSUY (SC) योजना अन्तर्गत अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MMGSUY (SC) योजना अन्तर्गत कराये गये कार्यों के भुगतान हेतु राशि की अधियाचना विहित प्रपत्र में समर्पित किया जा रहा है।

अनुरोध है कि MMGSUY (SC) अन्तर्गत कराये गये कार्यों का कुल आवंटन रू० 34,25,171.00 (चौतीस लाख पच्चीस हजार एक सौ एकहत्तर रुपये मात्र) उपलब्ध कराने की कृपा की जाय।

अनु० — यथोक्त।

विश्वासभाजन

*(Handwritten Signature)*  
16.5.2025  
कार्यपालक अभियन्ता,  
ग्रामीण कार्य विभाग,  
कार्य प्रमण्डल, बेगूसराय।

*(Handwritten Signature)*  
16/05/2025



# Requisition Format for Scheme MMGSUY (SC)

Name of the Works Division :- Begusarai

Sl. No	Package No.	Project ID as per MIS	Name of Road	AA Length (in km)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work status (WBM/WM/ BM/SDB C etc.)	Value of IRI (in mm/ km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MMGSUY/23-24 Begusarai/03	32110503000006	L030-L027 To Sankh Bich Tola	2.252	134.90	118.21360	04 MBD/ MMGSUY/ 2024-25	04.06.2025	Completed (20.04.2025)	SDBC	3246	25	5.01	80.59052	80.59052	114.84223	34.25171	4th & Final Bill

It is certified that Physical & Financial Progress has been updated in MIS.

Senior D.A.O./D.A.O.  
RWD, Works Division, Begusarai

Executive Engineer  
RWD, Works Division, Begusarai

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed (As Applicable).

16.05.2025

21/6/25



**GFR 12-B**  
[See Rule 256 (2)]


**FORM OF UTILIZATION CERTIFICATE**


(1) Certified that out of the Loan of **Rs. 840.66837 Lakh**, Sanctioned under **MMGSUY(SC) Scheme. dated.21-03.2025**, in favour of **.E.E RWD(W),Div-Begusarai**, during the FY **2024-2025**, an amount of **Rs. 837.85946 Lakh**, has been utilized for the purpose for which it was sanctioned, and that the balance of **Rs.2.80891 Lakh**, remaining unutilized at the end of the year 2025 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.


(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.Works have been supervised by Executive Engineer/Superitending Engineer.2
- 2.Periodical inspection has been conduted by Executive Engineer/ Superitending Engineer.
- 3.Construction materials have been tested.
- 4.Measurements have been recorded in the MBs and test checks conducted by the Assistant Engineer/Executive Engineer.
- 5.All other codal formalities have been observed.

  
Divisional Accounts Officer  
Rural Works Department  
Works Division, Begusarai

  
Executive Engineer  
Rural Works Department  
Works Division, Begusarai

  
16/05/2025



Name of Road:-L030-L027 To Sankh Bitch Tola; Name of Contractor:-Aastha And Saumya Construction

Date	Time	Section	Bumps	Speed	OR	REGORY	IRI	Latitude	ongitude	Event		
		No.	in mm	Rate	mm/km	UVI						
18/4/25	12:42:53	49	320	20.2	3200	3767	G	4.93	25.4727	86.1708	Normal	Y = 0 * X ^ 2 + 1.136 * X + 132.5
18/4/25	12:43:28	49	330	30.3	3300	3881	G	5.06	25.4727	86.1708	Speed Breaker	X = 3000
18/4/25	12:44:4	49	310	20.2	3100	3654	G	4.8	25.4727	86.1708	Normal	Y = 3540
18/4/25	12:44:39	49	300	30.3	3000	3540	G	4.66	25.4727	86.1708	Speed Breaker	
18/4/25	12:45:14	49	250	30.3	2500	2972	G	3.99	25.4727	86.1708	Normal	
18/4/25	12:45:14	49	190	30.3	1900	2290	G	3.16	25.4727	86.1708	Normal	(R) RURAL ROAD
18/4/25	12:45:50	49	260	30.3	2600	3086	G	4.13	25.4727	86.1708	Curve	Good
18/4/25	12:46:25	49	330	30.3	3300	3881	G	5.06	25.4727	86.1708	Curve	<4000
18/4/25	12:47:0	49	310	30.3	3100	3654	G	4.8	25.4727	86.1708	Normal	4001-500(>5001
18/4/25	12:47:0	49	300	30.3	3000	3540	G	4.66	25.4727	86.1708	Normal	
18/4/25	12:47:0	49	260	30.3	2600	3086	G	4.13	25.4727	86.1708	Normal	
18/4/25	12:47:35	49	300	30.3	3000	3540	G	4.66	25.4727	86.1708	Normal	
18/4/25	12:47:35	49	250	30.3	2500	2972	G	3.99	25.4727	86.1708	Curve	
18/4/25	12:48:11	49	330	30.3	3300	3881	G	5.06	25.4727	86.1708	Normal	
18/4/25	12:48:46	49	230	30.3	2300	2745	G	3.72	25.4727	86.1708	Normal	
18/4/25	12:48:46	49	190	30.3	1900	2290	G	3.16	25.4727	86.1708	Normal	
18/4/25	12:49:21	49	230	30.3	2300	2745	G	3.72	25.4727	86.1708	Normal	
18/4/25	12:49:57	49	200	30.3	2000	2404	G	3.3	25.4727	86.1708	Normal	
18/4/25	12:50:32	49	260	20.2	2600	3086	G	4.13	25.4727	86.1708	Normal	
18/4/25	12:53:8	49	250	20.2	2500	2972	G	3.99	25.478	86.1834	Normal	
18/4/25	12:53:43	49	330	30.3	3300	3881	G	5.06	25.478	86.1834	Normal	
18/4/25	12:54:19	49	300	30.3	3000	3540	G	4.66	25.478	86.1834	Normal	
Avg_IRI_Value						71407						
						3246						


18/04/2025  
J.E

18/04/2025  
J.E

16.5.2025



File : C:\Users\user\Desktop\STECO\RI Report\Ashtha and saumya\sanjk bichh tola.xlsx Section No. : 49, Eqn : Y  
Name of Customer : Astha\_Saumya Construction, Name of Work/ Road : L030-L027 To Sankh Bichh Tola, Lab Job

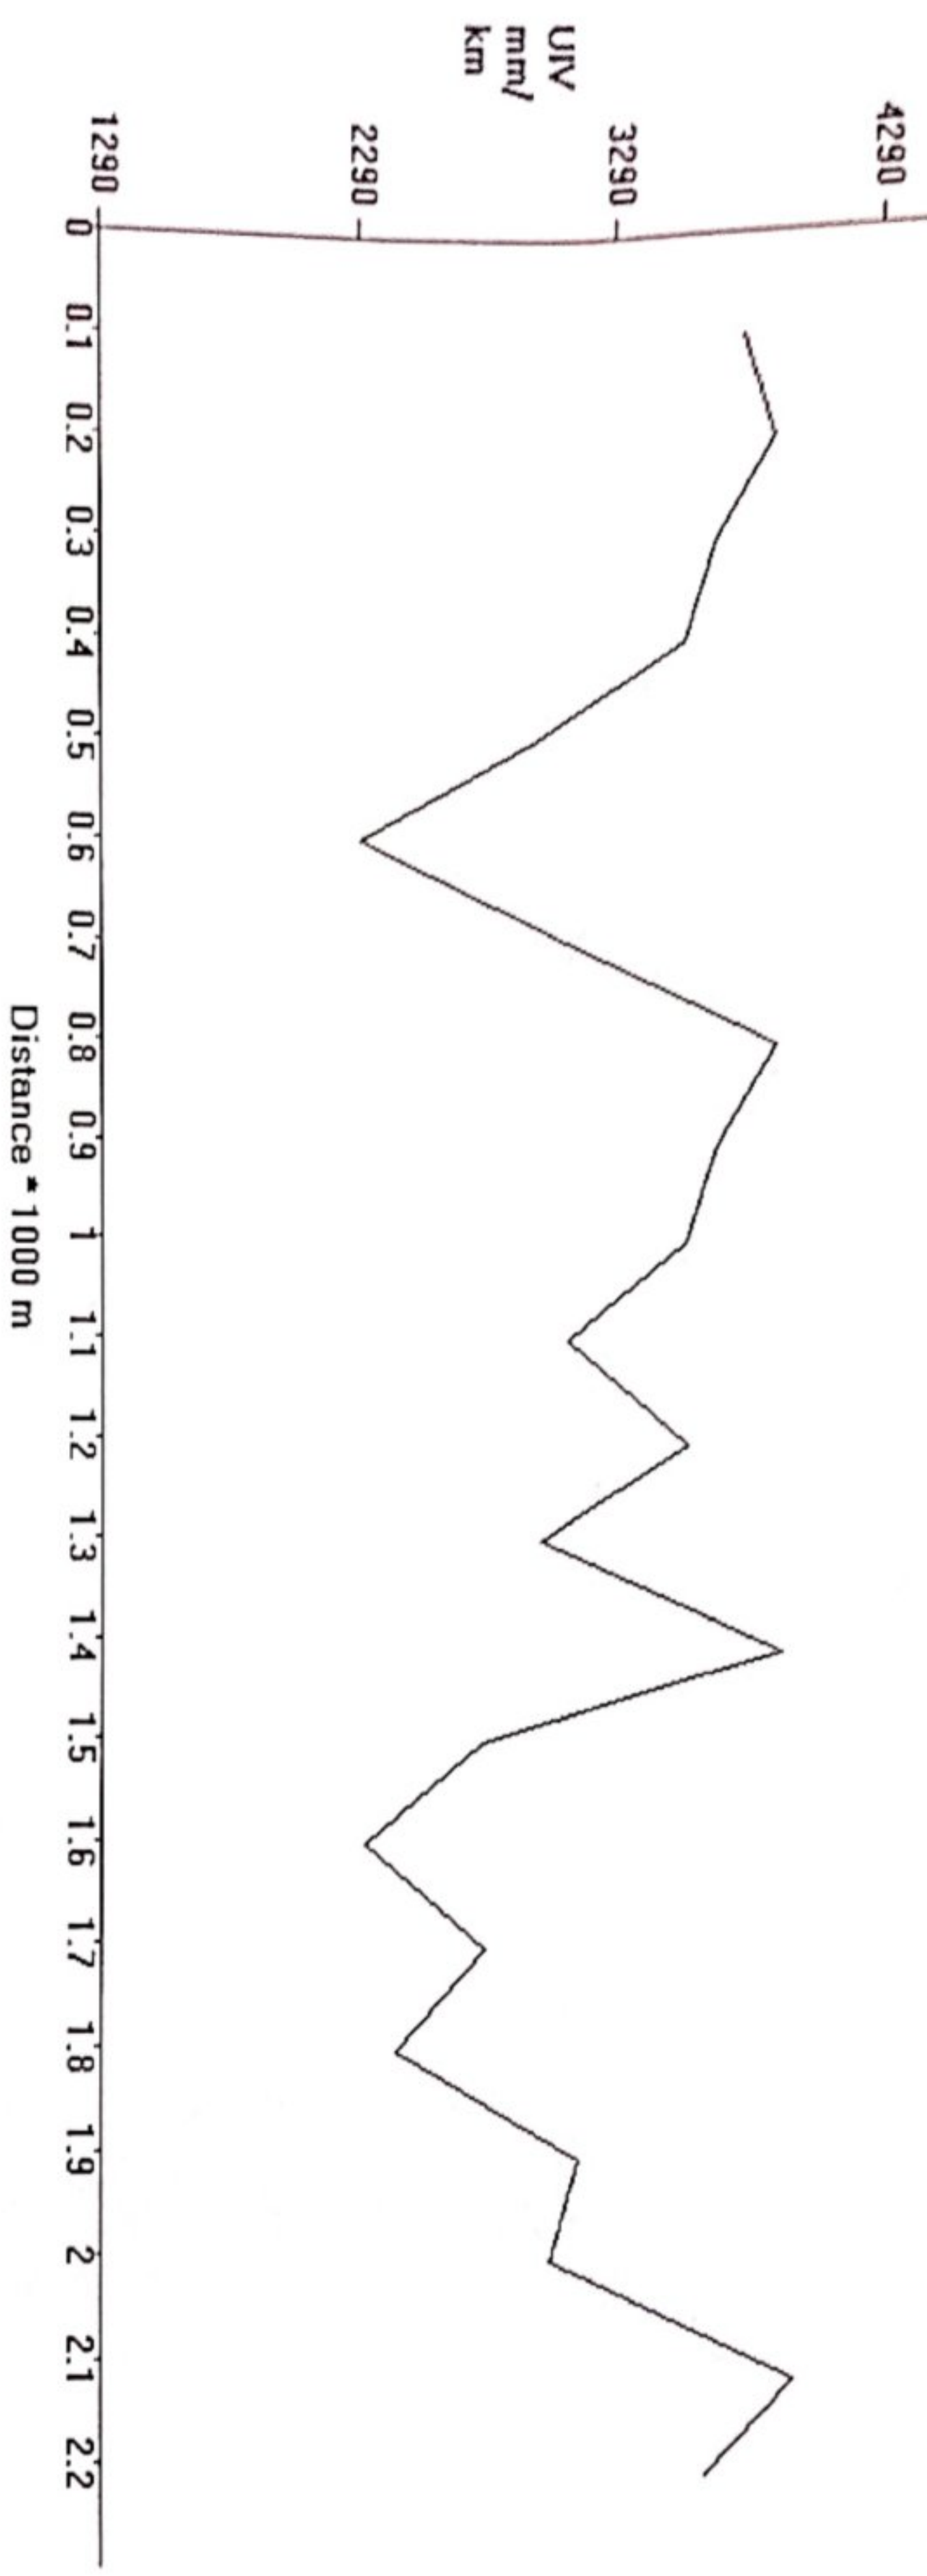

Dr. J. K. Singh  
18/06/2025

Dr. J. K. Singh  
18/06/2025

Dr. J. K. Singh  
18/06/2025



## Schedule XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
NAME OF WORK - Construction of					
Road	FROM	L030 - L027	(R95 Mahala		
CHOWK ) to Sanku Bitch tola					
Under MMUSOY - 2024					
NAME OF Agency -		M/S	AASTHA and		
			SAUMYA CONSTRUCTION		
			(BEUSAPAT)		
Agreement No -		04 MBD /	MMUSOY		
			2024-2025		
Agreement date -		05/09/2024			
WORK COMPLETION AS per Agreement					
		04/06/2025			
Agreement Rate -		12.377 below of			
		B.O.D			
Measurement date -		27/03/2025			
" measurement entry "					
Item No-01 Clearing and grubbing Road					
Land --- etc					
Refer T.M.B / P - (2)					
	Qty				0.44 Hq
Item No-02 Surfacing the existing					
Bituminous Surface --- etc					
Refer T.M.B / P - (2)					
	Qty				213.40 m <sup>2</sup>
Item No-03 Excavation for Road					
Way Box cutting work. --- etc					
CH- 0.0 to 800.0 M (widening existing P.C.C)					
Refer T.M.B / P - (3)					
	Qty				98.43 M <sup>3</sup>
Both sides	2.0x	30.0x	0.375x	0.175=	3.93 M <sup>3</sup>
Both sides	2.0x	20.0x	0.375x	0.175=	2.81 M <sup>3</sup>
				Total Qty=	101.70 M <sup>3</sup>
Continuation					104.98 M <sup>3</sup>



Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
591.50 M <sup>3</sup> @ Rs 264.72 / M <sup>3</sup> — R					1,56,582.00
					Rs 1,08,89,627
Add G.S.T 18% —					Rs 19,60,133.00
Add L.C 1% —					Rs 1,08,896.00
Add S.F 10% —					Rs 1,46,700.00
					Rs 1,31,05,356.00
As per Agreement 12.37% less(-)					16,21,133.00
					Rs 1,14,84,223.00
1st Previous payment less (-)					24,00,000.00
2nd " " " " (-)					24,00,000.00
3rd " " " " (-)					32,59,052.00
					Rs 34,25,171.00

20/04/2025  
J.E

20/04/25  
AE

C&P  
20/05/25  
EE

### Material Statement

- ① E/W — 591.50 M<sup>3</sup>
- ② Stone Metal — 6.07 M<sup>3</sup>
- ③ Stone screening — 0.68 M<sup>3</sup>
- ④ Local sand — 1.80 M<sup>3</sup>
- ⑤ Cement — 112.33 MT
- ⑥ sand — 151.33 M<sup>3</sup>
- ⑦ Stone chips — 302.68 M<sup>3</sup>

20/04/2025  
J.E

20/04/2025  
AE

### Certify that:

- ① No tools and plants issued to the contractor
- ② work done is satisfactory and as per specifications.
- ③ Quantity being paid is not more than the quantity actually done at

20/04/2025  
J.E

Continuation

20/04/25  
AE
