

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2

पत्रांक 2235 21 सिवान, दिनांक 12-11-2025

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण (ब्राडो), पटना।

विषय :- वित्तीय वर्ष 2024-25 में मुख्यमंत्री ग्राम सड़क उन्नयन योजना (Gen.) अंतर्गत संवेदक के द्वारा पथ में किये गये कार्य का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2 के अधीन मुख्यमंत्री ग्राम सड़क उन्नयन योजना (Gen.) अंतर्गत चयनित पथ का अधियाचना प्राप्त विहित प्रपत्र में पूर्ण रूप से भरकर संलग्न करते हुए अनुरोध पूर्वक कहना है कि उक्त पथों में (संलग्न विहित प्रपत्र के अनुसार) कुल राशि 157.11468 (एक करोड़ सन्तावन लाख ग्यारह हजार चार सौ अड़सठ) रु० मात्र आवंटित करने की कृपा की जाए, ताकि उक्त पथों में किए गये कार्य का भुगतान किया जा सकें।
अनु०- 1) अधियाचना विहित प्रपत्र में।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सिवान-2

12.11.25

.equisition Format for Scheme MMGSUY (General/SC/ST)

Name of the Works Division :- RWD, Siwan-2

Sl. No.	Sl. Packag e No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrativ e Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/ BM/SDBC etc.)	Value of IRI (in mm/ km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	RRSMP/24-25/Siwan-2/07	31406702050	T03 to Mishrauli Path	5.020	469.325	368.1149	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Work in Progress	GSB Done, WBM-III Done, B.M + SDBC Done	2248	75 mm	5%	339.27	339.27	364.74460	25.47845	Ongoing
2	RRSMP/24-25/Siwan-2/07	NS14067024154	Maniya Narendra Path Se Pustakalay Bhawan Tak	0.470	26.10873	23.76675	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Work in Progress	GSB Done, WBM-III Done, B.M + SDBC Done	2621			0.00	0.00	23.74407	23.74407	Ongoing
3	RRSMP/24-25/Siwan-2/07	31406708048	Repair of Road from Vijaypur More to Chandpali	6.410	498.31	403.81319	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Work in Progress	GSB Done, WBM-III Done, B.M + SDBC Done	2244	75 mm	5%	358.45	358.45	400.22095	41.76632	Ongoing
4	RRSMP/24-25/Siwan-2/07	31406712032	L046 to Hasanpurwa	1.250	111.048	70.84773	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Work in Progress	GSB Done, WBM-III Done, B.M + SDBC Done	2471	75 mm	5%	29.08	29.08	58.79580	29.71939	Ongoing

Sl. No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks	
5	RRSNIP/24-25/Siwan-2/07	Jampur Panchayat Me Indra Choudhary Ke Ghar Se Musafir Choudhary Ke Ghar Tak	0.330	21.709	18.12635	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Work in Progress	GSB Done, WBM-III Done, B.M + SDBC Done	2467	—	—	0.00	0.00	17.45236	17.45236	Ongoing	
6	RRSNIP/24-25/Siwan-2/07	Nonia Chhapar Nahar Se Semra Nahar Pul Tak	0.100	7.882	6.51752	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Work in Progress	GSB Done, WBM-III Done, B.M + SDBC Done	2151	—	—	0.00	0.00	6.51700	6.51700	Ongoing	
7	RRSNIP/24-25/Siwan-2/07	Miya Bharkhan Me Ramayan Sah Ke Dukan Se Idgah Tak	0.250	15.134	12.44005	03 CMBD/ 2025-26/ 05.06.2025	28.04.26	Work in Progress	B.M + SDBC Done, GSB Done, WBM-III Done,	2392	—	—	0.00	0.00	12.43709	12.43709	Ongoing	
Total														726.80	726.80	883.91187	157.11468	

It is certified that Physical & Financial Progress has been updated in MIS.


 DIVISIONAL ACCOUNT OFFICER
 RURAL WORKS DEPARTMENT
 WORKS DIVISION, SIWAN-2


 EXECUTIVE ENGINEER
 RURAL WORKS DEPARTMENT
 WORKS DIVISION, SIWAN-2
 12.11.25

Note :-

1. Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
2. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed (As Applicable).

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs. 784.13898, Sanctioned under RRSMP.(Gen.), dated 13.10.2025, in favour of EXECUTIVE ENGINEER, RWD, WORKS DIVISION, SIWAN-2, during the year 2025-26, an amount of Rs. 784.13898, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. 0.00, remaining unutilized at the end of the year 2025-26 has been surrendered to the Government (vide No C.E. (M&U)-4515-01-1479/2025- 91, (Encl)/ Patna, date 13.10.2025)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.


Signature

Designation



Date.
12.11.25

अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि MMGSUY (RRSMP-Gen) योजनान्तर्गत :-

1. पथ/पुल L046 to Hasanpurwa में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा, जीरादेई


सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, जीरादेई


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

Name of work : LO46 to Hasanpurwa

Name of customer : M/S Adarsh Construction

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

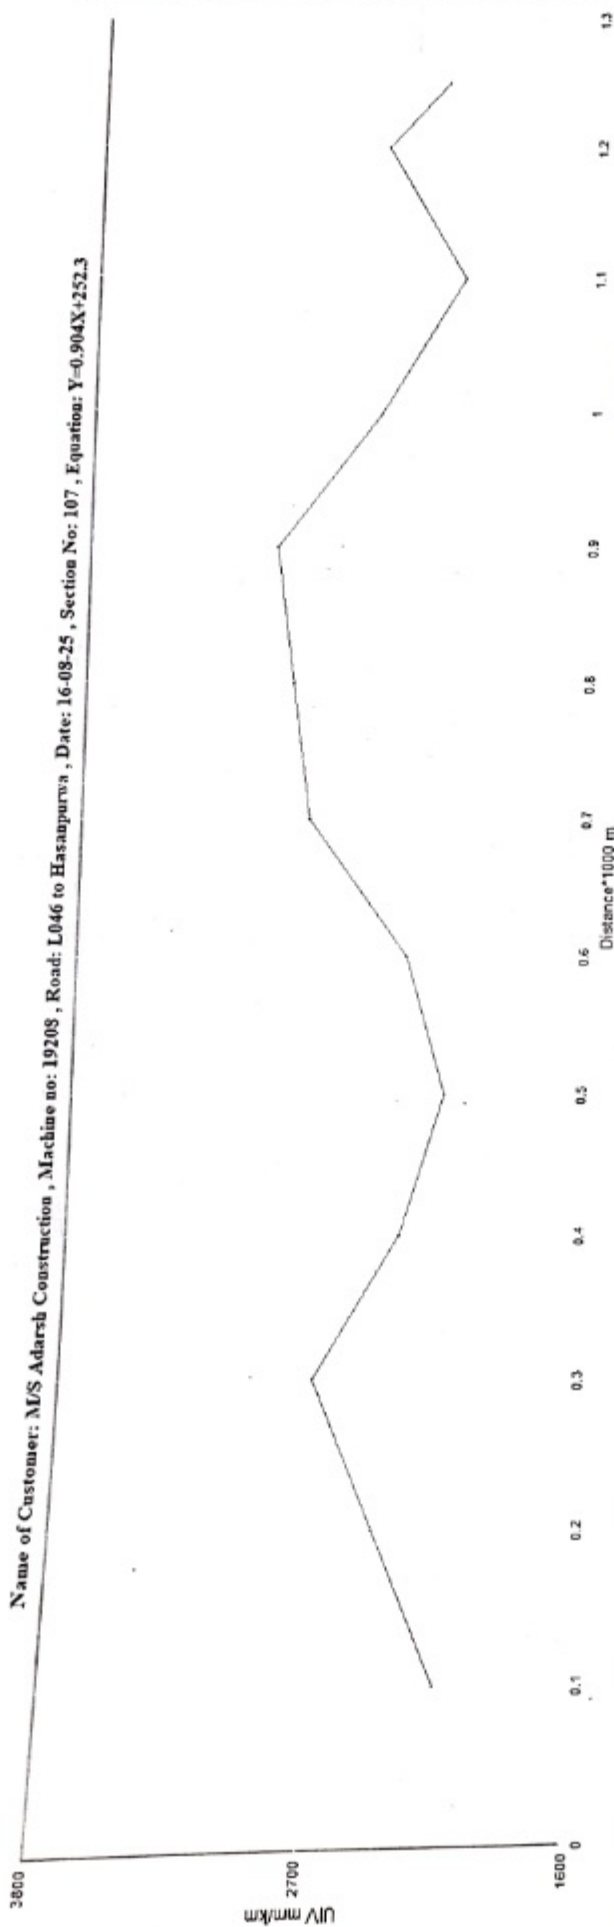
Date	Time	Test No	Distance (m)	Total Distance (m)	BUMP (cm)	Speed (km/hr)	Uplift (mm/Km)	Corrected Lift (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
15/08/25	09:04:11	107	100	100	21.0 cm	13.6 Km/hr	2100.0 mm/Km	2151	2.99	Good	26.1725631	N	84.2938714	E	Normal
16/08/25	09:04:56	107	100	200	24.0 cm	16.2 Km/hr	2400.0 mm/Km	2422	3.33	Good	26.1730775	N	84.2931672	E	Normal
16/08/25	09:05:27	107	100	300	27.0 cm	22.2 Km/hr	2700.0 mm/Km	2863	3.66	Good	26.1727140	N	84.2924991	E	Normal
16/08/25	09:06:03	107	100	400	23.0 cm	15.8 Km/hr	2300.0 mm/Km	2332	3.22	Good	26.1717273	N	84.2919332	E	Normal
16/08/25	09:06:47	107	100	500	21.0 cm	18.0 Km/hr	2100.0 mm/Km	2151	2.99	Good	26.1709442	N	84.2916940	E	Normal
16/08/25	09:07:09	107	100	600	23.0 cm	27.6 Km/hr	2300.0 mm/Km	2332	3.22	Good	26.1701090	N	84.2916521	E	Normal
16/08/25	09:07:57	107	100	700	28.0 cm	16.2 Km/hr	2800.0 mm/Km	2794	3.77	Good	26.1699152	N	84.2910293	E	Normal
16/08/25	09:08:36	107	100	800	29.0 cm	15.8 Km/hr	2900.0 mm/Km	2874	3.88	Good	26.1685780	N	84.2908194	E	Normal
16/08/25	09:09:04	107	100	900	30.0 cm	11.8 Km/hr	3000.0 mm/Km	2964	3.90	Good	26.1677835	N	84.2905178	E	Normal
16/08/25	09:09:44	107	100	1000	25.0 cm	17.5 Km/hr	2500.0 mm/Km	2512	3.46	Good	26.1670987	N	84.2911354	E	Normal
16/08/25	09:10:23	107	100	1100	21.0 cm	16.2 Km/hr	2100.0 mm/Km	2151	2.99	Good	26.1660795	N	84.2915113	E	Normal
16/08/25	09:11:15	107	100	1200	24.0 cm	10.8 Km/hr	2400.0 mm/Km	2512	3.44	Good	26.1661538	N	84.2916230	E	Normal
16/08/25	09:11:47	107	50	1250	22.8 cm	13.2 Km/hr	2200.0 mm/Km	2241	3.11	Good	26.1661540	N	84.2924682	E	Normal

Adarsh
12/11/25
SC

BB
RMS
AK


EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION SIWAN-2

Name of Customer: M/S Adarsh Construction , Machine no: 19208 , Road: L046 to Hasaapurwa , Date: 16-08-25 , Section No: 107 , Equation: $Y=0.904X+252.3$



Asst. Engr
21/11/25
JG

Engr
12/11/25
JG


EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION SIMLA-2
