

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल बेतिया।

पत्रांक:- 1590 फा 25 / दिनांक:- 18/11/25 /

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बेतिया

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार राज्य ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय:-

MMGSUY/RRSMP (GENERAL/SC/ST) योजना अंतर्गत निर्माण कार्य की राशि के अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MMGSUY/RRSMP (GENERAL/SC/ST) योजना अंतर्गत संलग्न सुची के आधार पर पथ में निर्माण कार्य की राशि का आवंटन उपलब्ध कराने की कृपा की जाए।

अनु०- यथोक्त।

विश्वासभाजन

[Signature]
18/11/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेतिया

ज्ञापांक- 1590 फा 25

दिनांक- 18/11/25

नोडल पदाधिकारी, MMGSUY/RRSMP (GENERAL/SC/ST) ग्रामीण कार्य विभाग,
प्रतिलिपि:- बिहार पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

[Signature]
18/11/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,

कार्य प्रमंडल, बेतिया
18/11/25

at for Scheme MMSUY/RRSMP (GENERAL/SC/ST)
Works Division :- Bettiah

Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in lakh)	Agreement (construction work) Amount (in lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/MS DBC etc.)	Value of RPI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in lakh)	Upto date Expenditure as per MIS (in lakh)	Value of Work Done (in lakh)	Current Demand (in lakh)	Remarks	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
RRSMP/24-25 Bettiah/0	5180880350016	L058-Bairiya Pich Gujarnath To Tamulla (TRACK58)	1.450	108.714	82.26919	13/RRSMP/25-26 29.07.2025	28.07.2026		Complete	2800.86	25mm	5%	44.95913	44.95913	71.28185	26.32272		
RRSMP/24-25 Bettiah/01	5180880350001	L070-Dubaulia Bairiya To Dubaulia (TRACK70)	1.310	102.790	72.95471	13/RRSMP/25-26 29.07.2025	28.07.2026		BM	N/a	N/a	N/a	0.00	0.00	24.59919	24.59919		
RRSMP/24-25 Bettiah/01	5180880350005	Gram Panchayat Raj Bairia Kc Ward No 4 Men Bairia Colony Virendra Warman Kc Char Se Khagendra Warman Kc Char Tak	0.350	28.105	21.49448	13/RRSMP/25-26 29.07.2025	28.07.2026		Complete	2811.25	25mm	5%	18.85392	18.85392	20.85947	2.00555		
RRSMP/24-25 Bettiah/01	5180880350007	L056-Gulab Chouk Pich To Siwa (TRACK56)	1.800	126.707	93.24548	13/RRSMP/25-26 29.07.2025	28.07.2026		BM	N/a	N/a	N/a	0.00	43187.17	21.04234	21.04234		
RRSMP/24-25 Bettiah/01	5180880350013	Repair of road from Betiya Sant Chat to Pakinaha	11.050	2194.619	1728.91628	13/RRSMP/25-26 29.07.2025	28.07.2026		BM	N/a	N/a	N/a	277.35679	277.35679	457.08792	179.73113		
RRSMP/24-25 Bettiah/01	5180880350022	L052-L026 to P. Nishar Tola (TRACK52)	0.630	42.179	33.08342	13/RRSMP/25-26 29.07.2025	28.07.2026		BM	N/a	N/a	N/a	0.00	0.00	28.62746	28.62746		

It is certified that Physical & Financial Progress has been updated in MIS.

D.A.O.
RWD, Works Division Bettiah

Executive Engineer
RWD, Works Division Bettiah
18/11/25

- Note :-
- Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
 - Signed Hard Copy and Soft Copy (in excel) of recorded RRI is enclosed (As Applicable).

FORM GFR 19-A**(SEE Government of India's Decision (I) below Rule-150)****Form of Utilisation Certificate upto the month of Oct- 2025****MMGSUY/RRSMP (GENERAL)****PIU - RWD (W), DIV.- Bettiah**

Sl. No.	Name of Scheme	Sanction No. & Date (in Lacs)	Amount Received (In Lacs)	Particulars
1	Construction of Rural Roads under MMGSUY/RRSMP (GENERAL/SC/ST)	Lt No.-39 dt 21.05.2025 Lt No.-62 dt 26.07.2025 Lt No.-86 dt 27.09.2025 Lt No.-90 dt 13.10.2025 Lt No.-94 dt 31.10.2025	172.22254 809.6916 202.42290 81.87363 35.65537	Certified that out of Rs. 1301.86604 lacs received during the years in favour of Ex. Engineer, RWD (W), Div. Bettiah, a sum of Rs. 1301.86604 lacs has been utilized for the purpose of MMGSUY/RRSMP (GENERAL) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 0.00000 lacs remaining unutilized at the end of the period under.
Total - 1301.86604				

- 2 Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Supertending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Supertending Engineer.
- Construction materials have been tested
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road works
- Construction of CD works



D.A.O.

R.W.D. (W) Div. Bettiah



Executive Engineer

R.W.D. (W) Div. Bettiah
18/11/25

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल बैतिया।

अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि **RRSMP(GEN)** योजना अंतर्गत:-

1. पथ Gram Panchayat Raj Bairia Ke Ward No 4 Men Bairia Colony
Virendra Warman Ke Ghar Se Khagendra Warman Ke Ghar Tak में कराये
गए कार्य की गुणवत्ता की जांच की गई है, जो निर्धारित मानक के अनुरूप है।
2. अद्यतन कराये गए कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है, जिनका
सत्यापन कर लिया गया है।



कनीय अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रशाखा बैरिया



सहायक अभियंता
ग्रामीण कार्य विभाग,
कार्य अ0प्रमंडल, बैरिया



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बैतिया

Name of Road- Gram Panchayat Raj Bairia Ke Ward No 4 Men Bairia Colony
Virendra Warman Ke Ghar Se Khagendra Warman Ke Ghar Tak

Name of Contractor-RAJ- JAI BHAWANI (JV)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
17/11/25	16:48:10	79	0.1	280	0	2800	2787	G	26.76613543	84.44561071	Normal
17/11/25	16:49:0	79	0.1	300	10.1	3000	2981	G	26.76585365	84.44541923	Normal
17/11/25	16:50:0	79	0.1	270	10.1	2700	2690	G	26.76572701	84.446288	Normal
17/11/25	16:50:7	79	0.1	280	10.1	2800	2787	G	26.76565735	84.44684827	Normal
Total							11245.00				
Average							2811.25				

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2600$$

$$Y = 2593$$

(R) RURAL ROAD
Good <4000
Poor >5001

[Signature]
19/11/25

[Signature]
18-11-25

[Signature]
18/11/25

Name of Customer : RAJ JAI BHAWANI JV
 Name of Work : GRAM PANCHAYAT RAJ BAUF
 Road :
 Lab Job number : 79
 Date : 17-11-2025
 Section No. : 79


Print Generate Report and Graph

Test Date :	17-11-2025	Road Name :	DRA WARMAN KE CHAR TAK
Machine No :	402	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval :	
Weather :		UV Range :	1690 To 4000 mm/km
Start Location :		Dial Range :	0 To 0.5 0.1 • 1000 m
End Location :		Equation :	test

Redraw Graph

Map View

File : D:\BUMP MACHINE 22-23\BUMP MACHINE 22-23\BUMP_REPORT_ALL\18112025_350.xlsx, Section No. : 79,
 Name of Customer : RAJ JAI BHAWANI JV, Name of Work/ Road : GRAM PANCHAYAT RAJ BAUF KE WARD NO 4

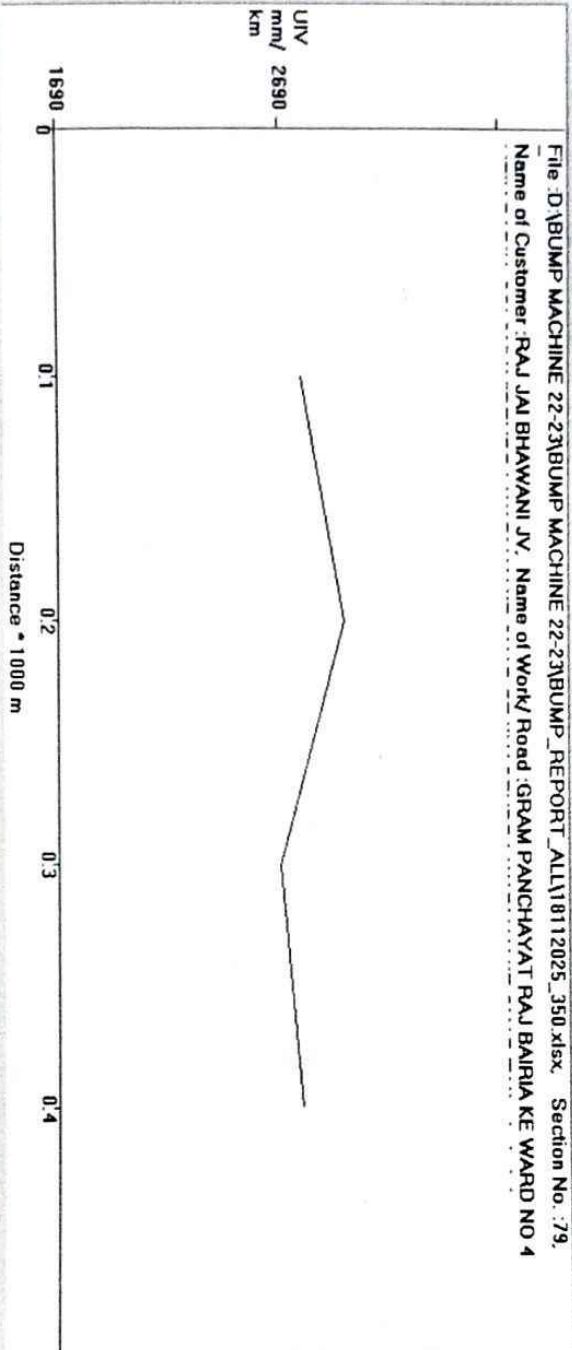

Signature
18/11/25

Signature
18-11-25

Signature
18/11/25
