

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक 5840 अक

दिनांक : 18/11/25

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय: शीर्ष RRSMP (Gen) अंतर्गत वित्तीय वर्ष 2025-26 में व्यय हेतु आवंटन की मांग ।

महाशय,

उपर्युक्त विषय के संबंध में शीर्ष RRSMP (Gen) अंतर्गत वित्तीय वर्ष 2025-26 में व्यय हेतु संलग्न विवरणी के अनुसार 149.65066 (एक करोड़ उनचास लाख पैसठ हजार छेयासठ) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त

विश्वासभाजन


कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

18/11/25
19/11/25

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs. Nil, Sanctioned under RRSMP (GEN), dated....., in favour of **Executive Engineer, RWD Works Division Muzaffarpur East-1** during the year 2025-26, an amount of Rs. Nil, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. Nil, remaining unutilized at the end of the year 2025-26 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.


Sr. D.A.O.
R.W.D. Works Division
Muzaffarpur East-1


Executive Engineer
R.W.D. Works Division
Muzaffarpur East-1

Requisition Format for Scheme RRSMP (General)

the Works Division :-Muzaffarpur East-1

Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in lakh)	Agreement (construction work) Amount (in lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM / WMM / BM / SDBC/PCC etc.)	Value of IRI (in mm/ km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in lakh)	Upto date Expenditure as per MIS (in lakh)	Value of Work Done (in lakh)	Current Demand (in lakh)	Remarks
2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
RRSMP/24-25 Muzaffarpur East-1/04	5150720350008	Murtupur To Hattha Tak Path	4.750	230.45900	231.91079	01CMBD/ 2025-26 29.04.2025	28.04.2026	----	SDBC	2114.479	25mm	5.02	63.72826	63.72826	102.48160	38.75334	
RRSMP/24-25 Muzaffarpur East-1/04	5150720350153	BARGAW MALANG CHOWK (MASIID CHOWK) to BISHUNPUR HARJAN TOLA	0.750	33.35700	33.27249	01CMBD/ 2025-26 29.04.2025	28.04.2026	29.10.2025	Work Complete	2545.00	----	----	28.94250	28.94250	30.25413	1.31163	
RRSMP/24-25 Muzaffarpur East-1/04	5150720350159	LO52-T02 to madhurapur Lakhrai (VR16)	1.150	54.23500	54.44272	01CMBD/ 2025-26 29.04.2025	28.04.2026	30.10.2025	Work Complete	2201.667	25mm	5.02	17.47795	17.47795	38.54114	21.06319	
RRSMP/24-25 Muzaffarpur East-1/04	5150720350160	LO57-Rawara Devari Road Sundarpur Ratwara Harjan tola (VR24)	1.200	54.83700	55.13673	01CMBD/ 2025-26 29.04.2025	28.04.2026	12.11.2025	Work Complete	2129.00	25mm	5.02	14.21956	14.21956	35.76784	21.54828	
RRSMP/24-25 Muzaffarpur East-1/04	5150720350161	LO54-T02 to muzaffarpur labraj (VR18)	1.430	70.20100	70.51474	01CMBD/ 2025-26 29.04.2025	28.04.2026	09.11.2025	Work Complete	2104.667	25mm	5.02	9.61490	9.61490	46.81599	37.20109	
RRSMP/24-25 Muzaffarpur East-1/04	5150720350162	RATW/ARA HANUNMAN CHOWK to MEGH RATWARA	1.550	74.36900	74.66598	01CMBD/ 2025-26 29.04.2025	28.04.2026	12.11.2025	Work Complete	2070.125	25mm	5.02	20.62161	20.62161	50.39474	29.77313	
		Total														149.65066	

It is certified that Physical & Financial Progress has been updated in MIS.

Senior D.A.O./D.A.O.

Executive Engineer

RWD, Works Division, Muzaffarpur East-1

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excell) of recorded IRI is enclosed (As Applicable).

अधियाचना हेतु प्रमाण पत्र

प्रमाणित किया जाता है कि **RRSMP (GEN)** योजनान्तर्गत:-

1. पथ/पुल्ल BARGAW MALANG CHOWK (MASJID CHOWK) to BISHUNPUR HARIJAN TOLA में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


17/11/25

कनीय अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रशाखा बंदरा


17/11/25

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल बंदरा


18/11/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1


Name of contractor:- Abs Infra Solution Prop Babli Singh															
Name of Road :- BARGAW MALANG CHOWK (MASJID CHOWK) to BISHUNPUR HARIJAN TOLA															
Date	Time	Section	Length	Bumps	Speed	OR		CATEGO RY	IRI	Latitude	Longitud e	Event			
		No.	in km	in mm	Rate	mm/km	UIV	ROAD							
9/11/25	17:5:18	25	0.1	240	0	2400	2360	G	3.25	26.69127	85.58685	Normal	$Y = 0 * X^2 + 0.989 * X - 13.58$		
9/11/25	17:5:18	25	0.1	210	10.1	2100	2063	G	2.88	26.6832	85.5864	Normal	X = 4600		
9/11/25	17:6:0	25	0.1	200	10.1	2000	1964	G	2.76	26.67525	85.58577	Normal	Y = 4535		
9/11/25	17:6:28	25	0.1	250	10.1	2500	2458	G	3.37	26.66727	85.58495	Speed Breaker			
9/11/25	17:7:3	25	0.1	240	10.1	2400	2360	G	3.25	26.6605	85.58418	Normal	RURAL ROAD		
9/11/25	17:7:39	25	0.1	250	10.1	2500	2458	G	3.37	26.65213	85.58364	Normal	Good	Average	Poor
9/11/25	17:8:0	25	0.1	220	10.1	2200	2162	G	3	26.64243	85.58367	Normal	<4000	4001-5000	>5001
9/11/25	17:8:0	25	0.05	230	10.1	4600	4535	A	5.82	26.64163	85.58372	Normal			
						Avg:-	2545								

Babli Singh
 17/11/25
 SE

Babli Singh
 17/11/25
 AE

Babli Singh
 BB

File : C:\Users\amc\Desktop\ABS INFRA\8\09111708.Xls, Section No. :25, Eqn : $Y = 0 * X^2 + 0.989 * X - 13.58$
 Name of Customer : , Name of Work Road : , Lab Job number :

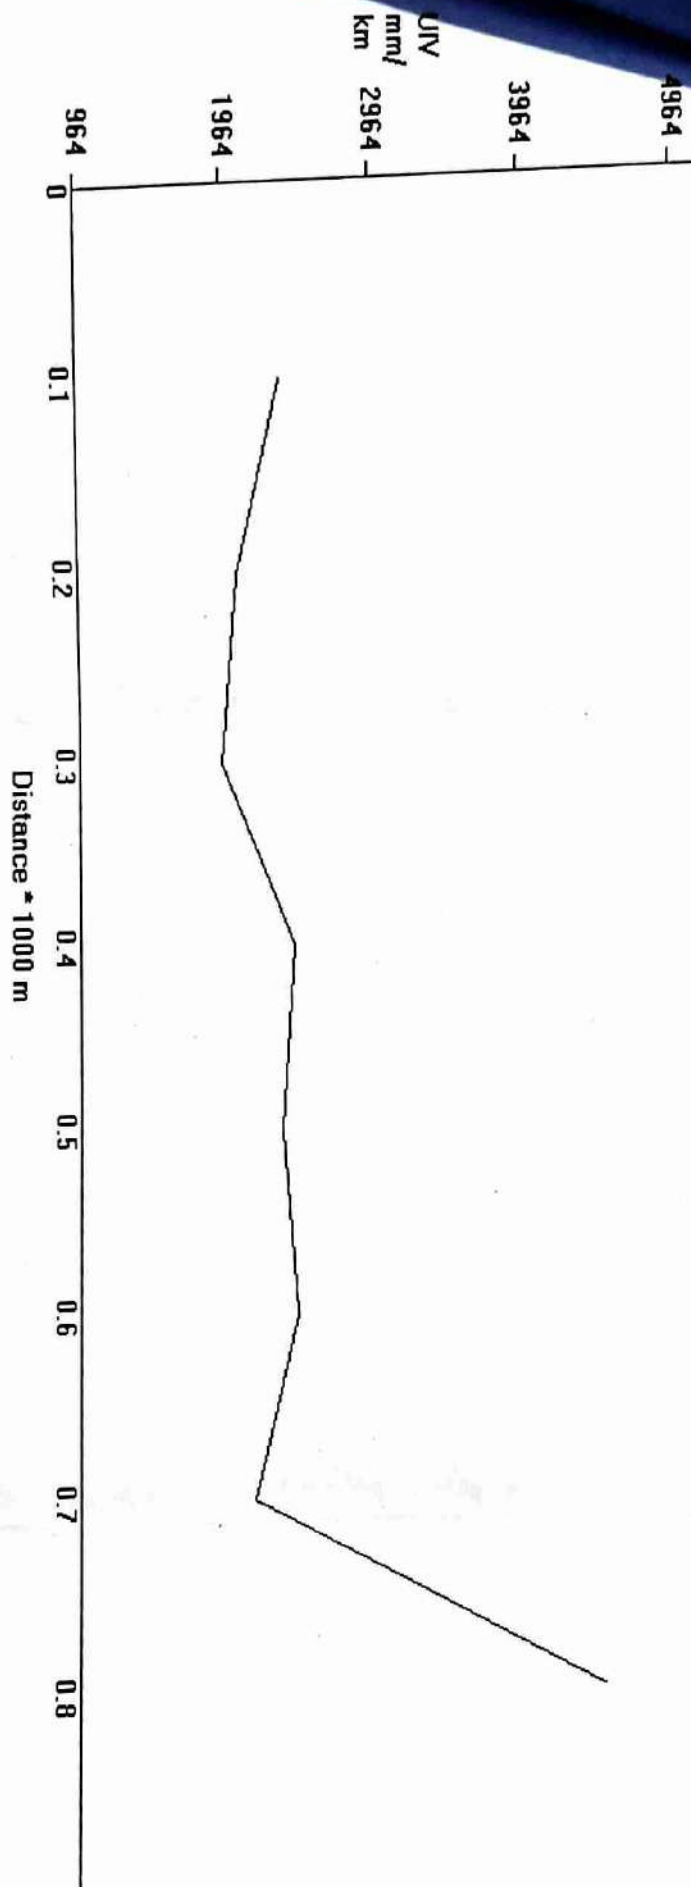

Handwritten signature
 17/11/15
 (SE)

Handwritten signature
 19/11/15
 AZ

Handwritten signature
 18/11/15
