

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, गोपालगंज-1

पत्रांक:-1601 अतु

/ गोपालगंज

दिनांक:-25/09/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय:- शीर्ष RRSMP (General) अन्तर्गत में अधियाचित राशि का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि शीर्ष RRSMP (General) अन्तर्गत राशि की माँग संलग्न विहित प्रपत्र में पथवार की जा रही है।

अतः भवदीय से अनुरोध है कि विहित प्रपत्र के कॉलम-18 में अंकित कुल राशि का आवंटन उपलब्ध कराने की कृपा की जाय। अधियाचित राशि के संदर्भ में C & P किये मापी पुस्तिका की छाया प्रति, एवं उपयोगिता प्रमाण-पत्र संलग्न कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनु0-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

25.09.25

Requisition Format for Scheme MMGSUY/RRSMP (General/SC/ST)

Name of the Works Division :- Gopalganj-1

Sl. No.	Package No.	Project ID as per MTS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WB/M/W MM/BM /SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MTS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/24/25 Gopalganj-1/05	5140690350039	PMGSY Road to Asandi Kanu tola	0.800	36.244	35.87167	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	20.08.2025	SDBC	2236.75	25	5.02	30.32170	30.32170	34.13590	3.81420	Completed
2	RRSMP/24/25 Gopalganj-1/05	5140690350056	PMGSY Road Mairwa Karan to Khargauli Pandey Tola Via Suklauli	1.850	86.270	87.37140	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	02.09.2025	SDBC	2339.89	25	5.03	35.02973	35.02973	61.31261	26.28288	Completed
3	RRSMP/24/25 Gopalganj-1/05	5140690350067	NH-28 to Barhana Harizan toli	2.500	117.350	119.02699	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	SDBC	2234.12	25	5.01	53.24876	53.24876	73.03325	19.78449	Surface Completed
4	RRSMP/24/25 Gopalganj-1/05	5140690350057	Shivshankar Prasad House in PMGSY Road to Kanai Ram ke Tola Jalalpur	2.000	89.140	90.40518	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	SDBC	2253.9	25	5.01	36.29296	36.29296	54.29320	18.00024	Surface Completed
5	RRSMP/24/25 Gopalganj-1/05	5140690350044	Sipaya Polytechnic to Roop Chhap	1.000	54.250	54.81048	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	SDBC	2163.40	25	5.02	26.51566	26.51566	32.69693	6.18127	Surface Completed
6	RRSMP/24/25 Gopalganj-1/05	5140690350068	L063-NH-28 to Karmann Gazi Railway Dhalda Rajput tola (ODR41)	2.500	115.570	116.74391	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	SDBC	2189.36	25	5.03	69.55261	69.55261	72.12306	2.57045	Surface Completed
7	RRSMP/24/25 Gopalganj-1/05	5140690350048	PMGSY Road to Karmann Gazi Pandey tola (Uttar tola)	1.350	60.700	61.31678	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	SDBC	2184.35	25	5.03	19.52741	19.52741	37.62389	18.09648	Surface Completed
8	RRSMP/24/25 Gopalganj-1/05	5140690350046	REO Road to Bindwalia Via Laxampur	1.100	60.450	61.50589	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	02.09.2025	SDBC	2297.36	25	5.02	34.42946	34.42946	41.61737	7.18791	Completed
9	RRSMP/24/25 Gopalganj-1/05	5140690350035	PMGSY Road Nalwar Pul to Mathania Tiwari Tola Dhinohi Tola	0.520	24.963	24.71756	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	05.09.2025	SDBC	2660.33	25	5.02	20.49036	20.49036	23.59722	3.10686	Completed

10	RRSNP/24/25 Gopalganj-1/05	5140690350045	Mathania Tiwari to L024	1.000	43.213	44.21462	04/CMBD (NMGU/Y)2 025-26 dt. 20.05.2025	19.05.2026	25.08.2025	SDBC	2198.00	25	5.02	22.47143	22.47143	25.39315	2.92172	Completed
11	RRSNP/24/25 Gopalganj-1/05	5140690350043	PMGSY Road to Kankar tola Serpur	0.980	43.656	44.63651	04/CMBD (NMGU/Y)2 025-26 dt. 20.05.2025	19.05.2026	-	SDBC	2801.20	25	5.01	22.93857	22.93857	26.67441	3.73584	Surface Completed
12	RRSNP/24/25 Gopalganj-1/05	5140690350080	Madhomath to Bangal Khad	4.585	218.140	221.00687	04/CMBD (NMGU/Y)2 025-26 dt. 20.05.2025	19.05.2026	02.08.2025	SDBC	2404.36	25	5.03	139.79754	139.79754	155.51482	15.71728	Completed

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy of recorded IRI is enclosed (As Applicable).

R.W.D. Works Division
Gopalganj-1

D.A. 25/09/25

Executive Engineer
R.W.D. Works Division
Gopalganj-1

25/09/25

25.09.25

GFR 12-B
[See Rule 256 (2)]


FORM OF UTILIZATION CERTIFICATE


(7) Certified that out of the Loan of Rs.269669021.00 Sanctioned under MMGSUY/RRSMP GEN dated 25.09.2025, in favour of Executive Engineer, RWD Works Division Gopalganj-1, during the year 2025-26, an amount of Rs.269669021.00 has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.0.00 remaining unutilized at the end of the year 2025 has been surrendered to the Government (vide No..... dated.....) will be adjusted towards the loan payable during the next financial year.

(8) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.


D.A.O.
R.W.D. Works Division,
Gopalganj-1


Executive Engineer,
R.W.D. Works Division,
Gopalganj-1
25-09-25

अधियाचना हेतु प्रमाण पत्र

प्रमाणित किया जाता है कि MMGSUY (RRSMP GEN) योजनान्तर्गत

1. पथ/पुल L063 NH-28 to Karmaini Gazi Railway Dhala Rajput Tola (ODR41) में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।

[Signature]
24/09/25

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल कुचायकोट।

Bishwajit

24/9/25

T.S

[Signature]
24/09/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल गोपालगंज-1

RECD. COPY

Name of Road :- L063-NH-28 to Karmaini Gazi Railway Dhala Rajpur tola (ODR41)

Name of Contractor:- M/s Pawan and Tiwari Construction J.V.

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
4/7/25	8:25:20	34	0.1	190	0	1900	2086 G		26.575412	84.322137	Normal
4/7/25	8:25:55	34	0.1	210	10.1	2100	2258 G		26.57623	84.322357	Normal
4/7/25	8:26:0	34	0.1	200	20.2	2000	2172 G		26.577155	84.32244	Normal
4/7/25	8:26:0	34	0.1	180	20.2	1800	2000 G		26.577422	84.321565	Normal
4/7/25	8:26:31	34	0.1	190	10.1	1900	2086 G		26.577672	84.320555	Normal
4/7/25	8:32:15	34	0.1	280	10.1	2800	2862 G		26.572472	84.32003	Normal
4/7/25	8:32:15	34	0.1	290	20.2	2900	2948 G		26.572577	84.319007	Normal
4/7/25	8:32:50	34	0.1	180	10.1	1800	2000 G		26.572335	84.318097	Normal
4/7/25	8:33:0	34	0.1	200	10.1	2000	2172 G		26.572688	84.317137	Normal
4/7/25	8:33:26	34	0.1	210	10.1	2100	2258 G		26.572977	84.316212	Normal
4/7/25	8:34:0	34	0.1	160	10.1	1600	1827 G		26.572835	84.315268	Normal
4/7/25	8:34:35	34	0.1	180	10.1	1800	2000 G		26.572505	84.31441	Normal
4/7/25	8:34:35	34	0.1	200	20.2	2000	2172 G		26.572608	84.31345	Normal
4/7/25	8:35:0	34	0.1	220	20.2	2200	2344 G		26.572688	84.31244	Normal
4/7/25	8:35:11	34	0.1	180	10.1	1800	2000 G		26.572788	84.31143	Normal
4/7/25	8:35:46	34	0.1	190	20.2	1900	2086 G		26.572615	84.310505	Normal
4/7/25	8:36:0	34	0.1	210	20.2	2100	2258 G		26.57251	84.309697	Normal
4/7/25	8:36:0	34	0.1	170	20.2	1700	1913 G		26.573057	84.308838	Normal
4/7/25	8:55:38	34	0.1	190	10.1	1900	2086 G		26.580362	84.32303	Normal
4/7/25	8:56:0	34	0.1	180	10.1	1800	2000 G		26.579707	84.323687	Normal
4/7/25	8:56:13	34	0.1	280	20.2	2800	2862 G		26.579055	84.324308	Normal
4/7/25	8:56:13	34	0.1	180	20.2	1800	2000 G		26.57863	84.3251	Normal
4/7/25	8:56:48	34	0.1	190	20.2	1900	2086 G		26.57828	84.32601	Normal
4/7/25	8:57:0	34	0.1	210	10.1	2100	2258 G		26.577903	84.326952	Normal
4/7/25	8:57:0	34	0.1	180	10.1	1800	2000 G		26.57765	84.327912	Normal
AVERAGE 2189.36											

$$Y = 0 * X^2 + 0.862 * X + 448.5$$

$$X = 1800$$

$$Y = 2000$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

IRI Value

Average IRI-2189.36

Rd. 04/07/25

P. E. 4/7/25

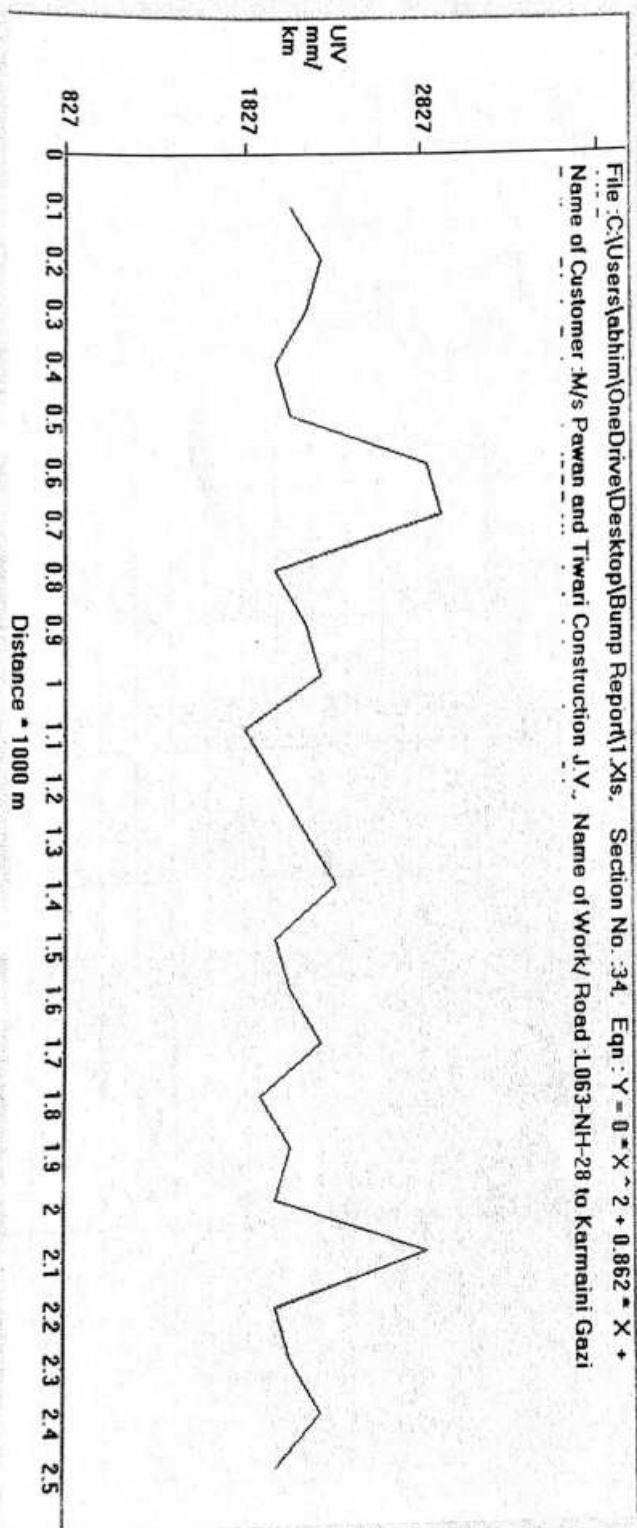
Name of Customer : M/s Pawan and Tiwari Construction
 Name of Work/ Road : L063-NH-28 to Karmaini Gazi R
 Lab Job number : 34
 Date : 04-07-2025
 Section No. : 34

Test Date : 04-07-2025
 Machine No : 413
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : L063-NH-28 to Karmaini Gazi R
 Road Type : (R) RURAL ROAD
 Side :
 UIV Range : 927 To 4000 Interval 1000 mm/km
 Dist Range : 0 To 2.6 0.1 1000 m
 Equation : $Y = 0 * X^2 + 0.862 * X + 448.5$

Print Generate Report and Graph

Redraw Graph Map View

File : C:\Users\abhim\OneDrive\Desktop\Bump Report\1.Xls. Section No. : 34. Eqn : $Y = 0 * X^2 + 0.862 * X +$
 Name of Customer : M/s Pawan and Tiwari Construction J.V. Name of Work/ Road : L063-NH-28 to Karmaini Gazi



Robert
 04/07/25
 (Rushes)
 4/7/25
 A.E.
 ee
