

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमण्डल, बाँका-2

पत्रांक 2843 / बाँका

दिनांक 18/10/25

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बाँका-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण, पटना।

विषय:-


शीर्ष 4515 मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के कार्यों के भुगतान हेतु निधि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (RRSMP-GEN) के अन्तर्गत विभिन्न पथों के भुगतान हेतु 6,91,15,216 /-(मो0 छः करोड़ एकानवे लाख पन्द्रह हजार दो सौ सोलह रुपये) मात्र की अधियाचना विहित प्रपत्र में तैयार कर आपके आवश्यक कार्यवाई हेतु समर्पित की जाती है।

- अनु0 :-
1. विहित प्रपत्र में आवंटन की मांग।
 2. उपयोगिता प्रमाण पत्र।
 3. मापी पुस्त की छाया प्रति।

विश्वासभाजन


कार्यपालक अभियंता
ग्रा0का0वि0, कार्य प्रमण्डल
बाँका-2
18/10/25

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs. **4482.75207**, Sanctioned under MMGSUY (RRSMP-GEN), Lt. No.-86 dated.-27.09.2025 in favour of E.E.R.W.D.(W) Division Banka-2 during the year **2025-26**, an amount of Rs. **4482.46187**, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. **0.29020** remaining unutilized at the end of the year.-2024 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Allotment
2. MB
3. Cash book

Signature.....

Designation Executive Engineer
E.E.R.W.D(W) Division, Banka-2

Date.- 18.10.2025

Requisition Format for Scheme MMGSUY/RRSMP (General)

Name of the Works Division :-Banka 2

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/B M/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/24-25 Banka-2/06	3070360350167	Punsiya Dhoriya Road To Porachak	5.300	368.442	314.94961	01CMBD/20 25-26 02.05.25	01.05.26	-	BT Completed, PCC in progress	2446	25mm	5%	181.44088	181.44088	224.92976	43.48888	Work in process
2	RRSMP/24-25 Banka-2/06	3070360350140	Nawad Bandev main Road To Khraunt Via Miyagadha Dhangarsa Mahedali Tola	12.010	796.953	704.46339	01CMBD/20 25-26 02.05.25	01.05.26	-	PCC & BT in Progress	2533	25mm	5%	154.20631	154.20631	458.86707	304.66076	Work in process
3	RRSMP/24-25 Banka-2/06	3070360350159	ASTA TO T T MANGAR	1.500	73.992	58.92331	01CMBD/20 25-26 02.05.25	01.05.26	-	PCC & BT Completed	2734	25mm	5%	22.95276	22.95276	35.93775	12.94499	Work in process
4	RRSMP/24-25 Banka-2/06	3070360350170	L052-Punsiya Dhoriya Manikpur Rd. to Makesar (VRS2)	1.760	87.035	72.99169	01CMBD/20 25-26 02.05.25	01.05.26	-	BT Completed, PCC in progress	2795	25mm	5%	24.36920	24.36920	43.06511	18.69591	Work in process
5	RRSMP/24-25 Banka-2/01	3070360350206	Barahat Market (Bajrangwali Temple) to Chhimi via Akagora	1.840	92.250	78.36900	06CMBD/20 25-26 19.06.25	18.06.26	-	PCC Completed	2495	25mm	5%	0.00000	0.00000	74.09770	74.09770	Work in process
6	RRSMP/24-25 Banka-2/01	3070360350204	L055-BGID Dunksa RD to Mohanpur (Track55)	4.620	312.900	251.38552	06CMBD/20 25-26 19.06.25	18.06.26	-	PCC & BT Completed	2647	25mm	5%	0.00000	0.00000	190.48137	190.48137	Work in process
7	RRSMP/24-25 Banka-2/07	3070360350153	JAGATPUR to JHAKIYA GONRA	1.260	62.436	51.09109	05CMBD/20 25-26 09.06.25	08.06.26	-	PCC Completed	2506	25mm	5%	0.00000	0.00000	16.60639	16.60639	Work in process
8	RRSMP/24-25 Banka-2/07	3070360350149	L104-T01 Rinaipur To Rampur (VR104)	1.870	92.721	75.98642	05CMBD/20 25-26 09.06.25	08.06.26	-	Surface completed	2502	25mm	5%	20.86135	20.86135	51.03751	30.17616	Work in process
			Total														691.15216	

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed (As Applicable).

Senior A.O. P.O.
RWD, Works Division Banka-2

Executive Engineer
RWD, Works Division Banka-2

18/10/25

18.10.25

Road Name : L052-Punsiya Dhoraiya Manikpur Rd. to Makesar (VR52),
Contractor Name : Anil Kumar Singh

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
16/10/25	14:10:22	41	0.1	230	30.3	2300	2442	G	24.96316	87.08113	Normal
16/10/25	14:10:32	41	0.1	300	30.4	3000	3110	G	24.96234	87.08088	Curve
16/10/25	14:10:46	41	0.1	310	30.3	3100	3205	G	24.96176	87.08163	Curve
16/10/25	14:10:55	41	0.1	190	30.3	1900	2060	G	24.96139	87.08231	Normal
16/10/25	14:11:03	41	0.1	310	30.4	3100	3205	G	24.96067	87.08211	Curve
16/10/25	14:11:12	41	0.1	300	30.4	3000	3110	G	24.96015	87.08286	Curve
16/10/25	14:11:20	41	0.1	210	30.3	2100	2251	G	24.95986	87.08369	Normal
16/10/25	14:11:29	41	0.1	300	30.2	3000	3110	G	24.95927	87.0838	Curve
16/10/25	14:11:38	41	0.1	320	30.1	3200	3301	G	24.95845	87.08396	Curve
16/10/25	14:11:56	41	0.1	310	30.1	3100	3205	G	24.95797	87.08417	Curve
16/10/25	14:12:22	41	0.1	300	30.2	3000	3110	G	24.95735	87.08469	Curve
16/10/25	14:12:38	41	0.1	220	30.2	2200	2347	G	24.95665	87.08483	Normal
16/10/25	14:12:56	41	0.1	220	30.2	2200	2347	G	24.95655	87.08574	Normal
16/10/25	14:13:12	41	0.1	200	30.3	2000	2156	G	24.9566	87.08663	Normal
16/10/25	14:13:36	41	0.1	310	30.3	3100	3205	G	24.95677	87.08756	Curve
16/10/25	14:14:22	41	0.1	300	30.3	3000	3110	G	24.95745	87.08779	Curve
16/10/25	14:14:38	41	0.1	210	30.4	2100	2251	G	24.95776	87.08676	Normal
		Length -		1.7			Average -	2795			

$$Y = 0 * X^2 + 0.954 * X + 247.70$$

$$X = 2100$$

$$Y = 2251$$

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

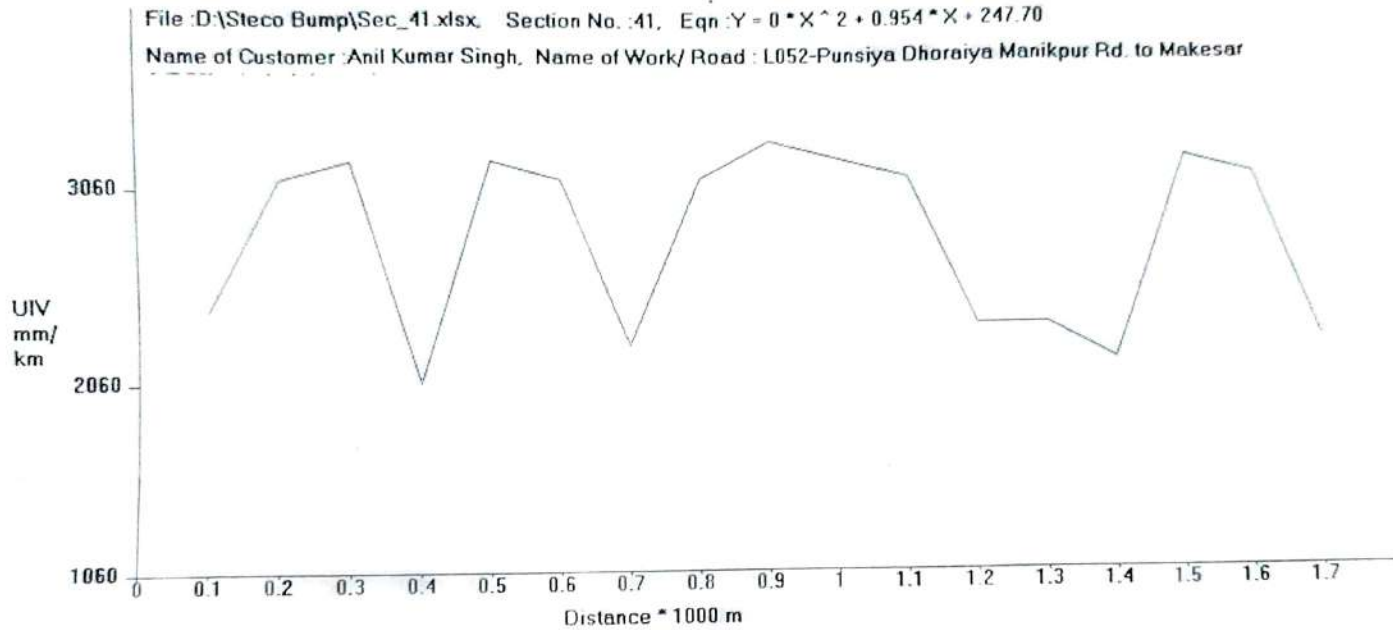

 14/10/25
 Junior Engineer
 Rural Works Department
 Works Section, Dhoraiya


 18/10/25
 AE
 Rural Works Department
 Works Sub-Division, Dhoraiya


 18-10-25
 Executive Engineer
 Rural Works Department
 Works Division, Banka-2

File :D:\Steco Bump\Sec_41.xlsx Section No. :41, Eqn : $Y = 0 * X^2 + 0.954 * X + 247.70$

Name of Customer :Anil Kumar Singh, Name of Work/ Road : L052-Punsiya Dhoraiya Manikpur Rd. to Makesar



17/10/25
J.E


18/10/25
AE

18.10.25

अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि RRSMP
योजनान्तर्गत

1. पथ/पुल 6052 Punsingha Chhoringa Manikpur Rd. to Makegar. में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


18/10/25
कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा बाँका-2


18/10/25
AE
सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमण्डल.....


18-10-25
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल बाँका-2
