

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बाढ़

पत्रांक 983 अनु० / बाढ़ / दिनांक 25/11/2020
प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल बाढ़।

सेवा में

अधीक्षक अभियन्ता
ग्रामीण कार्य विभाग
कार्य अंचल, पटना।

विषय :- शीर्ष एम0एम0जी0एस0वाई0 (WB) योजनान्तर्गत Construction of Chanradip Rai Primar School to Sahab Baba Kutiya तक पथ निर्माण का समय-वृद्धि के संबंध में।

महाशय,

उपरोक्त विषय के संदर्भ में कहना है कि शीर्ष एम0एम0जी0एस0वाई0 (WB) योजनान्तर्गत Construction of Chanradip Rai Primar School to Sahab Baba Kutiya तक पथ निर्माण का समय-वृद्धि हेतु प्रस्ताव समर्पित किया जाता है।


योजना का विन्दुवार प्रतिवेदन भेजा जा रहा है -


1. स्थल का फोटोग्राफ।
2. (क) कार्य प्रारम्भ करने की तिथि-21.04.2018 है।
(ख) एकरारनामा के अनुसार कार्य पूर्ण करने की तिथि-20.04.2019 है।
3. जमीन विवाद, टाल क्षेत्र में पानी आ जाने के कारण एवं लॉकडाउन में मजदूर नहीं मिलने के कारण कार्य में विलम्ब हुआ है, विषयांकित कार्य दिनांक-25.11.2020 तक पूर्ण करने का शपथ पत्र दिया गया है, कार्य प्रगति में है।
4. कार्य विशेषियों के अनुरूप किया जा रहा है। अतः दिनांक-25.11.2020 तक समय-वृद्धि की अनुशंसा की जाती है।

अतः अनुरोध है, कि उक्त कार्य का समय-वृद्धि प्रस्ताव की स्वीकृति देने की कृपा की जाय।

अनु०-यथोक्त।


विश्वासभाजन


कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बाढ़।


25/11/20

APPLICATION FOR EXTENTION OF TIME

- 1 Name of Contractor :- Nishant Kumar
- 2 Name of Work :- Chandredip Rai Primary School to Sahels
Baba Katiya (MMGSY-WB16-BARH-01)
- 3 Agreement No. & Date :- 021MBD/2018-19 Dt. 21.04.2018
- 4 Agreement Value :- 134.36212
- 5 Date of Commencement :- 21.04.2018
- 6 Original Date of Completion :- 20.04.2019
- 7 Extension Previously Granted or not :- Yes. (30.03.2020)
- 8 Extension applied for :- 25.11.2020
- 9 Head :- MMGSY (WB)
- 10 Percentage of Work Done :- 70%.
- 11 Reason of Hindrence :- Due to Covid-19 Lock Down, Land Dispute.
Water Logging.
- 12 Recommendation by J.E. :- Recommended upto 25.11.2020 *15/10/20*
AF
- 13 Recommendation by S.D.O. :- Reasons stated by contractor are true
Time extension may be granted upto
25.11.2020 *15.10.20*
AF
- 14 Recommendation by the
Executive Engineer :- T.E. may be granted. *24/11/20*
- 15 Recommendation by S.E. :-
- 16 Final Order of the C.E. :-



Signature
of the Contractor



No. B - 2020

Authorised u/s 8 (1) (C) of the
Notaries Act 1952 (Act LIII of 1952)

2260

Barh (Patna) बाढ़ (पटना)

AFFIDAVIT

05 NOV 2020

शपथ-पत्र

Book 32, Serial 14, Dated

De/...
who is identified by Sri...
Advocate Sonamiv Affirm...
and declared before me
05/11/2020
Rajesh Kumar Verma
NOTARY BARH, PATNA
INDIA

मैं निशान्त कुमार पिता श्री वीरेन्द्र कुमार गवर्नमेंट रजिस्टर्ड
कन्ट्रैक्टर एण्ड सप्लायर्स ग्राम पचमहला, पोस्ट-जलालपुर, थाना-मरांची
जिला-पटना निम्नलिखित बातों की घोषणा सत्य एवं निष्ठापूर्वक
करता हूँ।

1. यह कि मुझे बाबा साहेब कुटिया से चन्द्रदीप राय ग्रामरी स्कूल तक सड़क निर्माण, थाना-अमलगोला, जिला-पटना से सड़क निर्माण का ठेका मिला है।
2. यह कि मैं दिनांक 28/10/2020 तक ग्रेड-3 का कार्य पूर्ण कर दिया।
3. यह कि मैं दिनांक 11/11/2020 तक अपना दूसरा कार्य बी.टी.वर्क पूर्ण कर दूंगा।
4. यह कि मैं अपना तीसरा कार्य रोड फर्निचर और फ्लैक दिनांक 25/11/2020 तक पूर्ण कर दूंगा।

06/11/2020
शपथकर्ता
06/11/2020



उपरोक्त बातें मेरे निर्देशानुसार लिखी गई है जिसे मैं पढ़ कर
समझ लिया तथा सही पाकर अपना हस्ताक्षर बना दिया।

Identity Sri/Smt. ...
who has Signed in my presence
Sheo Shankar ...
Advocate, En. ...

5/11/2020

शपथकर्ता
[Signature]

सहायक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य अवर प्रमंडल, अधमलगाँवा

पत्रांक 58 / दिनांक 12.9.2020
प्रेषक,

सहायक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, अधमलगाँवा

सेवा में,

कार्यपालक अभियन्ता,
क्षेत्रीय प्रयोगशाला,
ग्रामीण कार्य विभाग, गुलजारबाग, पटना-7

विषय :- MMGSy (World Bank) अन्तर्गत चन्द्रदीप रात्र पाइपरी
स्कूल से साहब बाबा कुटिया तक पथ निर्माण में प्रयुक्त WBM
Gr. III कार्य की गुणवत्ता जाँच के संबंध में।

महाशय,

उपरोक्त विषय के संदर्भ में सूचित करना है कि विषयांकित पथ में WBM Gr. III
कार्य दिनांक 12.9.2020 को प्रारंभ किया गया
है।

अनुरोध है कि इस पथ के कार्य की गुणवत्ता की जाँच कर जाँचफल उपलब्ध कराने
की कृपा की जाय।

अनु०: WBM Gr. III stone metal - 1 bag
(CH - 0.600 Km)

N.B - विषयांकित पथ में किसी प्रकार का
ATR ठेकना पीदाद नहीं है।

Attested

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बाढ़ (पटना)
6.11.20

विश्वास भाजन
12.9.2020
सहायक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, अधमलगाँवा

अनाथ कर्मालय, अनामलगोला

पत्रांक 767 दिनांक 9.10.19

प्रेषक

कटीप उप लम्बाई
- लह- अनामलगोला
अनामलगोला।

लेना में

मिशनर कुमार्
जनरल मैट रिजर्व्ड कन्स्ट्रक्टर लॉड साहबगंज
ग्राम- पन्चमहला
पोस्ट- गजालपुर
जिला- पटना।

विषय:-

बाबा लोहेव कुटिया ले चन्द्रदीप राय के हबुल तक सड़क
निर्माण कार्य में ग्रामीणों द्वारा मिजी जमीन नसाक (फर्षि)
कारियत करने के संबंध में।

गवर्नर,

उपरोक्त विषयक आपसे द्वारा प्राप्त अवैतनापत्र के
आधारे में अन्वेषण करने पाया गया कि बाबा लोहेव कुटिया ले
चन्द्रदीप राय के हबुल तक जो सड़क निर्माण किया जा रहा
है वह धूमि है नहीं है जो मीना रामनगर कटारी बचकाट बाबा
नं० 148 में पड़ता है। सड़क निर्मित धूमि है नहीं है जिलापट,
कितानों द्वारा सहमति के बिना कार्य करना संभव नहीं है।

Attested

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बाढ़ (पटनो)

काशी
6.11.20

विश्वरामजी

कटीप 13.10.19 उप लम्बाई
- लह- अनामलगोला
अनामलगोला।



Indian Oil Corporation Limited

ISSUANCE UNDER RULE 49 of GST Rules

We hereby certify that the goods covered by this document have suffered applicable Taxes on clearance



Doc Name TAX INVOICE
Doc Number 018520050461

From No AQ3 31A
Dist Mode Road
Cont Code LI No 200

SAP Doc No 732054002
T.T. No. DR00R5050
Dated 15 0.00

Date 20-06-2020 Twentieth June Two Thousand Twenty
Time 14:00 Fourteen Hours Eight Minutes
Run Date/Time 20-06-2020 14:00

Code
Name & Address
Dist
C. E. Range
C. E. Division

2323 (GIN L23201AM110500011300)
Borani Marketing Terminal
PO : Barani, Dist. Begusarai
Begusarai
Bihar(10)

243870 (Mob No -8878083005)
NISHANT KUMAR
PACHAMAILA, JALALPUR
BARAHUYA, PATNA
Patna
Bihar(10)

D.O. No LI No 200 (W4) W400 Barh
01.10.2020

GST Registration No.
PAN

GSTIN 10AAAGH10010124
GST: 10010110170
LST: 10010110002

GSTIN 10AGJPK70020125
AGJPK70020

Invoice Charge Applicable : No

PAYEE : 243870 NISHANT KUMAR

Ordering Party: 243870
GSTIN 10AGJPK70020125
NISHANT KUMAR
PACHAMAILA, JALALPUR
BARAHUYA, PATNA
Patna

Item Material Code / Material Description

Place of supply Bihar(10)

Item	Material Code / Material Description	Place of supply	Quantity/Unit	Unit	Rate/Unit	Tax Code	Total
1	131070 DUMPAVE BITUMEN VG-10 Pack - 150.5 Kg	Bihar(10)	70.000	EA		2713	
	CAVE Transportation Value		10.000	TO	33472.000	TO	330005.70
	Taxable Value		10.000	TO	33472.000	TO	330005.70
	JOCG IN Central Tax			%	9.000	%	33001.72
	JOSG IN State Tax			%	9.000	%	33001.72
	Deductible 15.000			%		%	432002.20
	Total for material						432002.20

Zero Rounding Difference

Total

432002.00

Attested

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमुख, बाढ़ (पटना)

25/11/20
6/11/20

Contract Balance Subject to reconciliation: 162097.00 - (CR)

Delivery No: 0513926779 / Sales Order 03203/3439
PO ref: 20061409323001439

Contact No: 001814132
Cont. No: 87000
Cont. No: 78000

Net Total (in words) thirty-two thousand six hundred eighty-nine

RECEIVED IN GOOD CONDITION

PREPARED BY

PAGE No 1 / 1

1 Original for Recipient

Declaration: All the particulars given above are true and correct and the amount indicated represents the price actually charged and that there is no scope of additional consideration directly or indirectly from the buyer.

CUSTOMER'S SIGNATURE/DEAL

TRANSPORTER'S AUTH. REP. SIGNATURE/DEAL

00703038

AUTHORIZED BY

RELEASED BY

FOR INDIAN OIL CORPORATION LTD.

HEAD OFFICE: Indian Oil Bhawan, G-9 All Vihar Jung Marg, Bandra (EAST) Mumbai - 400051

681103565616

TAX INVOICE
(See Rule Sec-23)

Licensee: Patented Technology of



VA-10 10 Harder Grade Bitumen

Reg. Office : A-3, 2nd Floor, Luv-Kush Tower Exhibition Road, Patna - 800001

GSTIN : 10AACCJ1657K1ZS, PAN : AACCJ1657K

Corporate Identity No. U23203UP2009PTC037080

E-mail : contact@unobiltumix.com | Ph. No Tel: +91-612-2323781

Donell, 2595E : HARPUR, P/O-TILRATH P/S-DARAUNI, DISTT-BEGUSARAI-851

112 DIICAR



JUNO BITUMIX

Serial No. of Invoice :	JH/120-21/000057	Transporter :	BY SELF
Date of Invoice :	16-05-2020 14:08	Vehical No. :	BR 09M 3211
Challan No. :	CHANDRADIP RAI PRIMARY SCHOOL TO SA	LR No. / LR Date :	
Road Name :	HAB BEHA KUTIA.	DO / PG No. / Date :	289 DT. 18.03.2020
		Division :	RWD, BARIH (PATNA)

Details of Reciever (Billed to)	Details of Consignee (Shipped to)
Name : SRI NISHANT KUMAR Address : AT. PACHMAHALA PO- JALALPUR MARANGI IN DISTT- PATNA State : BIHAR State Code : 10 GSTIN/Unique ID : 10AGJPK7902Q1Z5	Name : SRI NISHANT KUMAR Address : BARH, DISTT.- PATNA State : BIHAR State Code : 10 GSTIN/Unique ID : 10AGJPK7902Q1Z5

Sr. No.	Description of Goods	HSN/ACS	Qty.	Unit	Rate	Total	Disc.	Taxable Charges	Taxable Value	CGST		SGST		IGST	
										%	Amt.	%	Amt.	%	Amt.
	BITUMEN EMULSION (JUNO SS-1)	2710090 5000	MT	30092.00	184960.00	0.00	184960.00	184960.00	9	16646.40	9	16646.40	0	0.00	
Total							184960.00	184960.00		16646.40		16646.40		0.00	

Total Invoice Value (In figure): 218253.00

Total Invoice Value (in word) : Two Lakh Eighteen Thousand Two Hun

Education; dred And Fifty Three Rupees And Zero Paise

Electronic Reference Number: **Zero Pulse**

Amount Of Tax Subject to Reverse Charges	Yes	☐	No	☒
--	-----	--------------------------	----	-------------------------------------

Total Amount Before Tax :	184960.00
---------------------------	-----------

Total CGST :	16646.40
--------------	----------

Total SGST :	16616.40
--------------	----------

Total IGST :	0.00
--------------	------

Total Amount GST :	11292.80
--------------------	----------

Total Amount After Tax	218253.00
------------------------	-----------

Work Details

Bank Name Axis Bank Ltd.

Branch : Sector-02, Noida (U.P.)

013020034264169

For JUNO BITUMIX PVT. LTD.



Nishant Kumar

Govt. Reg. Contractor & Suppliers

WORK PROGRAME

Work Name :- Chandradeep Rai Primary School To Sahab Baba Kutiya
(MMGSY - WB16 - Barh - 01)

Ag No :- 02/MBD/2018-19

1	Grade III	28-10-2020	Work Done Com.
2	BT Work	11-11-2020	Work Done Com.
3	Road Furniture & Flank Complete	25-11-2020	Work Done Com.

[Signature]
14.10.2020

Attested

1
[Signature] 25/11/20
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
जनकपुर, बाढ़ (पटना)

[Signature]
25/11/20

At : Pachmahla, Post - Jalalpur, Dist. - Patna (Bihar) 811302

Phone : 9955607172

E-Mail : nishantkumar7172@gmail.com

MS. 54. 11. 18.
Name of Work -> Charwardip Rai Primary School to School Baha
Hudiyar (WB)

Schedule XLV-Form No. 134

Name of Agency -> Alsthand Kumar

Panchmahal, Motama

DIVISION

Pटना

SUB-DIVISION

Ex. 1000
RWD, Works Division
Bihar

Measurement Book

Date of work order - 21.11.18

Date of completion - 20.11.19

312

Accepted

20/11/20

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बाढ़ (पटना)

20/11/20

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2nd on A/c Bill					
1/4 mile - construction & maintenance of five years					
old road from Chamluadi Baf					
primary school to Sahab Baf					
Kuliyga					
Agency: - Sri Hishant Kumar.					
Bg No: - 02 MBD/2018-19					
Bg value -					
Date of start: - 21.04.18					
Date of completion: - 20.04.19					

- ① Elevation in excavation in trench
- trenches complete - do - do -
- $$4 \times 2 \times 6.45 \times 1.40 \times 1.50 = 108.36$$
- $$4 \times 1 \times 4.35 \times 1.53 \times 0.365 = 10.018$$
- $$118.378 \text{ m}^3$$
- ② ply put in trench in gravel com
- ply of gravel - do - do -
- $$4 \times 2 \times 6.45 \times 1.4 \times 0.15 = 10.836$$
- $$4 \times 1 \times 4.35 \times 1.53 \times 0.25 = 7.511$$
- $$18.38$$
- ③ ply work masonry work in
- con (1:1) in trench wall - do - do -
- 1/4 mile of E/B

Continuation

Attested

20/11/20
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमुख, बाढ़ (पटना)
6/11/20

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2nd on A/c Bill					
W/L - concrete & maintenance of 10 years					
for road from Chaudharpur					
primary school to school bus					
station					
Agency - Sri. Nishant Kumar					
Ag. No. - 02 MMD/2018-19					
Ag. value -					
Date of start - 21.09.18					
Date of completion - 20.09.19					

① E/W in excavation in border					
branches complete - do - do -					
$4 \times 9 \times 6.45 \times 1.4 \times 1.50 = 108.36$					
$4 \times 1 \times 4.5 \times 1.53 \times 0.365 = 10.018$					
					118.37818
② P/W P.C.C. in ground in					
plate of P.C.C. - do - do -					
$4 \times 9 \times 6.45 \times 1.4 \times 0.5 = 10.836$					
$4 \times 1 \times 4.5 \times 1.53 \times 0.25 = 1.543$					
					12.379
③ P/W brick masonry work in					
channel in drainage in border					
labor of 1/10					

Continuation

A-11001001

05/11/20
कार्यपालक अभियंता
सार्वजनिक कार्य विभाग
कार्य प्रमुख, बाढ़ (पटना)
05/11/20

25

Alleged

A-5/1/20

कार्यपालक अगियंता

ग्राहीण कार्य विभाग

कार्य प्रगंडल, बाढ़ (पटना)

6/11/20

Sch. XLV-Form No. 134

11

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑦ constn of granular sub base					
by providing 100 mm thick					
1x30x30x6.20x0.10 = 18.60					
24x30x4.50x0.10 = 390.80					
27x30x5.50x0.10 = 445.50					
21x30x5.50x0.10 = 346.50					
1x25x4.50x0.10 = 11.25					
21x30x4.05x0.075 = 191.362					
27x30x4.05x0.075 = 244.037					
1x25x4.05x0.075 = 7.593					
					199.042 m ³
					141.842 m ³
					1250.792 m ³
⑧ pvc laying spreading & compo-					
eting 10mm stone mixed with					
with specific size					
1x30x3.75x0.075 = 8.4375					
24x30x3.75x0.075 = 177.45					
27x30x3.75x0.075 = 202.50					
1x25x3.75x0.075 = 7.031					
					217.0684 m ³
					213.44 m ³
					217.968 m ³

C. nuation

Attested

9/11/20
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बाढ़ (पटना)
6/11/20

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Abstract of cost					
(1/2) clearing & grubbing road					
Land including etc etc					
1.25 Hect wide TMA page (5)					
@ RS 44809.00/Ha					RS 57107.00
(2/2) (2/2) const of embankment					
with approved material etc					
13200 m ³ wide TMA page (3)					
@ RS 171.00/m ³					RS 2257200.00
(3/4) const of subgrade & surface					
shoulder with etc etc					
33000.00 m ³ wide TMA page (5)					
@ RS 131.00/m ³					RS 4323000.00
(4/25) F/W excavation in drain					
drained complete etc etc					
29.80 m ³ wide TMA page (5)					
118.375 m ³ wide TMA page (3)					
148.178 m ³					
@ RS 265.00/m ³					RS 398600.00
(5/5) P.V.C.C. in drain etc					
4.59 m ³ wide TMA page (6)					
18.38 m ³ wide TMA page (3)					
22.97 m ³ @ RS 600.00/m ³					RS 137820.00
					RS 27540.00
					RS 2924207.00

Continuation

Attested

28/11/20
 कार्यपालक अभियंता
 ग्रामीण कार्य विभाग
 कार्य प्रमंडल, बाढ़ (पटना)
 28/11/20

Particulars	Details of actual measurement			Contents of area
	No.	L.	B.	
			51.502	29.251287
(6/25) PIV 1.5 m thick cement				
17.65 m ² side TMA page (1)				
110.63 m ² side TMA page (10)				
128.28 m ²				
			@ 101.6567.57/m ²	05.34.1272/c
(7/25) PIV 1.5 m thick cement				
7.5 m side TMA page (6)				
26.0 m side TMA page (10)				
			@ 112.00.05/m ²	01.12.0007/c
(8/25) PIV plastering with 5 cm				
11.9 m side TMA page (1)				
65.38 m ² side TMA page (1)				
135.159 m ² side TMA page (10)				
201.039 m ²			@ 186.07/m ²	24072-
14m 139.45				05.37.3937/c
(9/25) PIV 1.5 m thick cement				
21.30 m ² side TMA page (1)				
53.04 m ² side TMA page (10)				
74.94 m ²				
12m 186.3			@ 116.00/m ²	3050=
				05.24.47/c
			210 05.4326393=000/c	
			4312687=	

Continuation

Attested

21/11/20

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल, बाढ़ (पटना)

मार्ग
6/11/20

Continuation

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, वाढ़ (पटना)
२१/११/२०

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Materials used.</u>					
Causeway sand:-	40.24 m ²		0.50	0.10	2.012 m ³
4 mm stone egg	3.82 m ²		0.50	0.10	0.191 m ³
20 mm stone egg	1.41 m ²		0.50	0.10	0.0705 m ³
10 mm stone egg	1.47 m ²		0.50	0.10	0.0735 m ³
Brick	55715 Nos		0.25	0.125	131.6375 m ³
20 mm to 9.5 mm stone egg					
	512.839 m ²		0.50	0.10	25.64195 m ³
9.5 mm to 2.0 mm	452.74 m ²				
					@ 0.425 m ³ /m ² = 192.414 m ³
Local sand	637.85 m ²		0.50	0.10	31.8925 m ³
63 mm to 9.5 mm stone	263.74 m ²				
					@ 0.440 m ³ /m ² = 116.7256 m ³
stone set p-B	58.95 m ²				
					@ 0.255 m ³ /m ² = 14.92325 m ³
<u>Total</u>					3.64451
22102/2024					764224
J.E					
Statement of S. free					
Total Amount x 10%					
764224 =					
260451 = x 10%					
76422 =					
26045 =					
Statement of Principal					
1) Sand 678.18 m ² @ 75/m ³					50864
2) Stone 1300 36114 m ² @ 150/m ³					195054
3) Brick 55715 Nos @ 45/100					249
Continuation					
					2516167

Attested

28/11/20
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, यादव (परना)

6/11/20

Particulars	Details of actual measurement				Contents of area
	No.	Part	Part	D.	
Work done as per No. B-				68	36179-
Int. Payment				27	83365-
Current Bill Amount				40	52812-
By S.D. 8/12				3	24225-
By 9.12.12					40528-
By 10.12.12					40528-
By 11.12.12					40528-
By 12.12.12					40528-
By 13.12.12					40528-
By 14.12.12					76422-
By 15.12.12				2	46167-
				77	208926-
By 16.12.12				32	43386-
				32	46
				40	52812-
Amount for Rs. 4052812- (Fourty lac fifty two thousand eight hundred twelve only) Pay by Bank Rs. 3243386- (Thirty two lac forty three thousand eight hundred six only) 19/12/20 19/12/20 19/12/20					

Continuation

Attested

28/11/20
 कार्यपालक अभियंता
 प्राचीन कार्य विभाग
 कार्य प्रगंडल, नांद (पटना)

6/11/20



Latitude: 25.96306
Longitude: 83.620187
Elevation: 97.97 m
Accuracy: 3.8 m
Time: 08-28-2020 10:43
Name: chandni roy pathy school to which life begins

—सत्यदीप राम शर्मा रजिस्ट्रार ऑफ दानगंगा प्रेसीडेंसी—

C/S

17/10/20

सत्यदीप
राम शर्मा
श.स.

15.10.20

सत्यदीप राम शर्मा
सत्यदीप राम शर्मा
सत्यदीप राम शर्मा (सत्यदीप)



—पुनर्वीप सांग २१० ए.एम. री २११६९१९१' कुडीम.

८/९

१५/१०/२०२०
२.८

१५/१०/२०२०
१५.१०.२०२०

१५/१०/२०
६६
कार्यपालक अभियंता
भामिणी कार्य विभाग
कार्य प्रमंजल, वाड (पटना)

2/5

15.10.2020
HE

Scanned with CamScanner

Latitude: 25.46331
Longitude: 85.593117
Elevation: 4652 m
Accuracy: 3.8 m
Time: 08-28-2020 10:45
Note: church rd primary school to school baba kanna m



—संग्रहीत २१० रुकुम र्द जाद कावा सुदीन

C/S

११/११/२०

कार्यपालक अभियंता
शान्ति कार्य विभाग
कार्य प्रमोद, याद (पटना)

२१.०१.२१
११/११/२०

२०.११.२०
११/११/२०



Latitude: 25.96306
Longitude: 85.60067
Elevation: 495 m
Accuracy: 3.8 m
Time: 08-12-2020 10:44
Note: chand-ho-roy primary school, chand-ho-roy, bhojpur, nepal

चन्द्रशीपरा म नो मल्लुम ले आहणा नुदीना


C/5

१५/१०/२०२०

१५/१०/२०२०

१५/१०/२०

कार्यालोक अभियंता
आभीण कार्य विभाग
कार्य प्रमंडल, वाड (पटना)

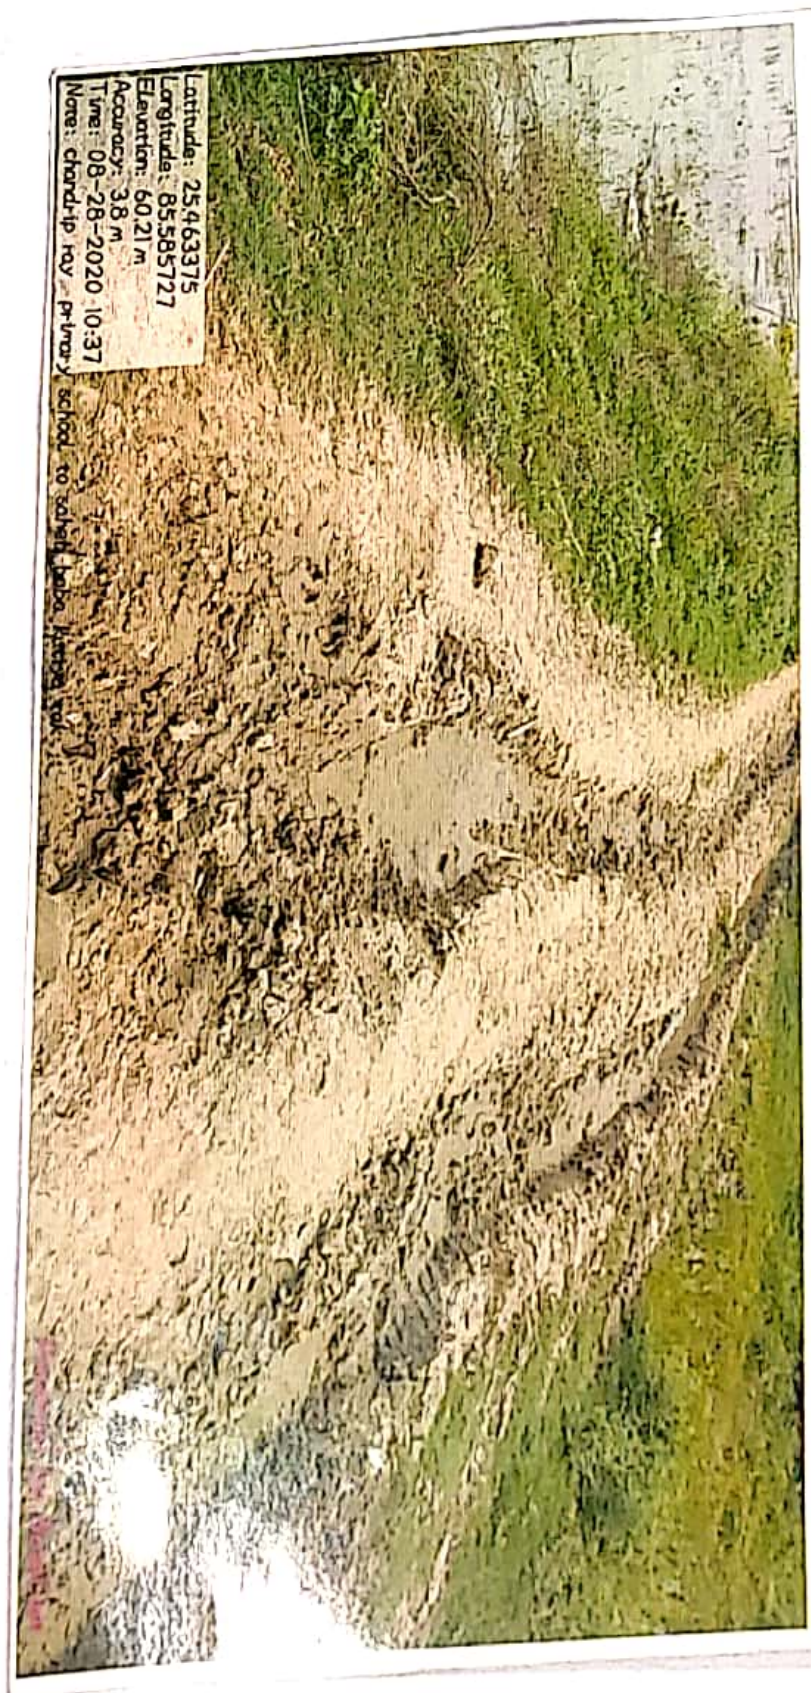

—सन्तुलीयता प्राप्त करने के लिए २०१९/२० प्रगति

C/S

प्रति
15/10/2020
प्रति

प्रति
15.10.2020
प्रति

१५/१०/२०

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, वाइ (पटना)
