

Road Name :- Nainijod se Semadar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY mm/km ROAD	Latitude	Longitude	Event
12/11/20	14:15:11	43	0.1	140	0	1400	1632 G	26.21086	84.54393	Normal
12/11/20	14:16:0	43	0.1	160	0	1600	1806 G	26.21	84.54225	Curve
12/11/20	14:16:21	43	0.1	210	10.1	2100	2243 G	26.20912	84.54192	Normal
12/11/20	14:17:0	43	0.1	270	10.1	2700	2767 G	26.20836	84.54292	Normal
12/11/20	14:17:32	43	0.1	160	10.1	1600	1806 G	26.20768	84.54073	Normal
12/11/20	14:18:7	43	0.1	260	10.1	2600	2679 G	26.2069	84.53687	Curve
12/11/20	14:18:42	43	0.1	170	10.1	1700	1894 G	26.20609	84.53298	Normal
12/11/20	14:19:18	43	0.1	100	10.1	1000	1283 G	26.20528	84.52945	Normal
12/11/20	14:19:53	43	0.1	140	10.1	1400	1632 G	26.20441	84.52743	Normal
12/11/20	14:20:0	43	0.1	120	10.1	1200	1457 G	26.20356	84.52508	Normal
12/11/20	14:20:28	43	0.1	90	10.1	900	1195 G	26.2027	84.52373	Normal
12/11/20	14:21:4	43	0.1	200	10.1	2000	2156 G	26.20181	84.52222	Normal
12/11/20	14:22:0	43	0.1	130	0	1300	1545 G	26.20093	84.52288	Curve
12/11/20	14:22:14	43	0.1	160	10.1	1600	1806 G	26.20022	84.5173	Normal
12/11/20	14:22:49	43	0.04	60	20.2	1500	1719 G	26.19991	84.51515	Normal

$$Y = 0 * X^2 + 0.873 * X + 410.1$$

$$X = 2100$$

$$Y = 2243$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

[Signature]
12/11/2020
J.G

Name of Customer : Shri Vijay Singh
Name of Work/ Road : Nainijod se Semadar
Lab Job number :
Date : 02-Jun-09
Section No. : 43

Test Date : 28-Apr-10
Machine No : 390
Start S No :
Start E No :
Weather :
Start Location :
End Location :
Road Name : Nainijod se Semadar
Road Type : (R) RURAL ROAD
Side :
Interval :
UIV Range : 195 To 4000 1000 mm/km
Dist Range : 0 To 1.6 0.1 * 1000 m
Equation : $Y = 0 \cdot X^2 + 0.873 \cdot X + 410.1$

Print


Generate Report and Graph

Redraw Graph

Map View

File H:\15111153.Xls, Section No. : 43, Eqn : $Y = 0 \cdot X^2 + 0.873 \cdot X + 410.1$

Name of Customer : Shri Vijay Singh, Name of Work/ Road : Nainijod se Semadar, Lab Job number :

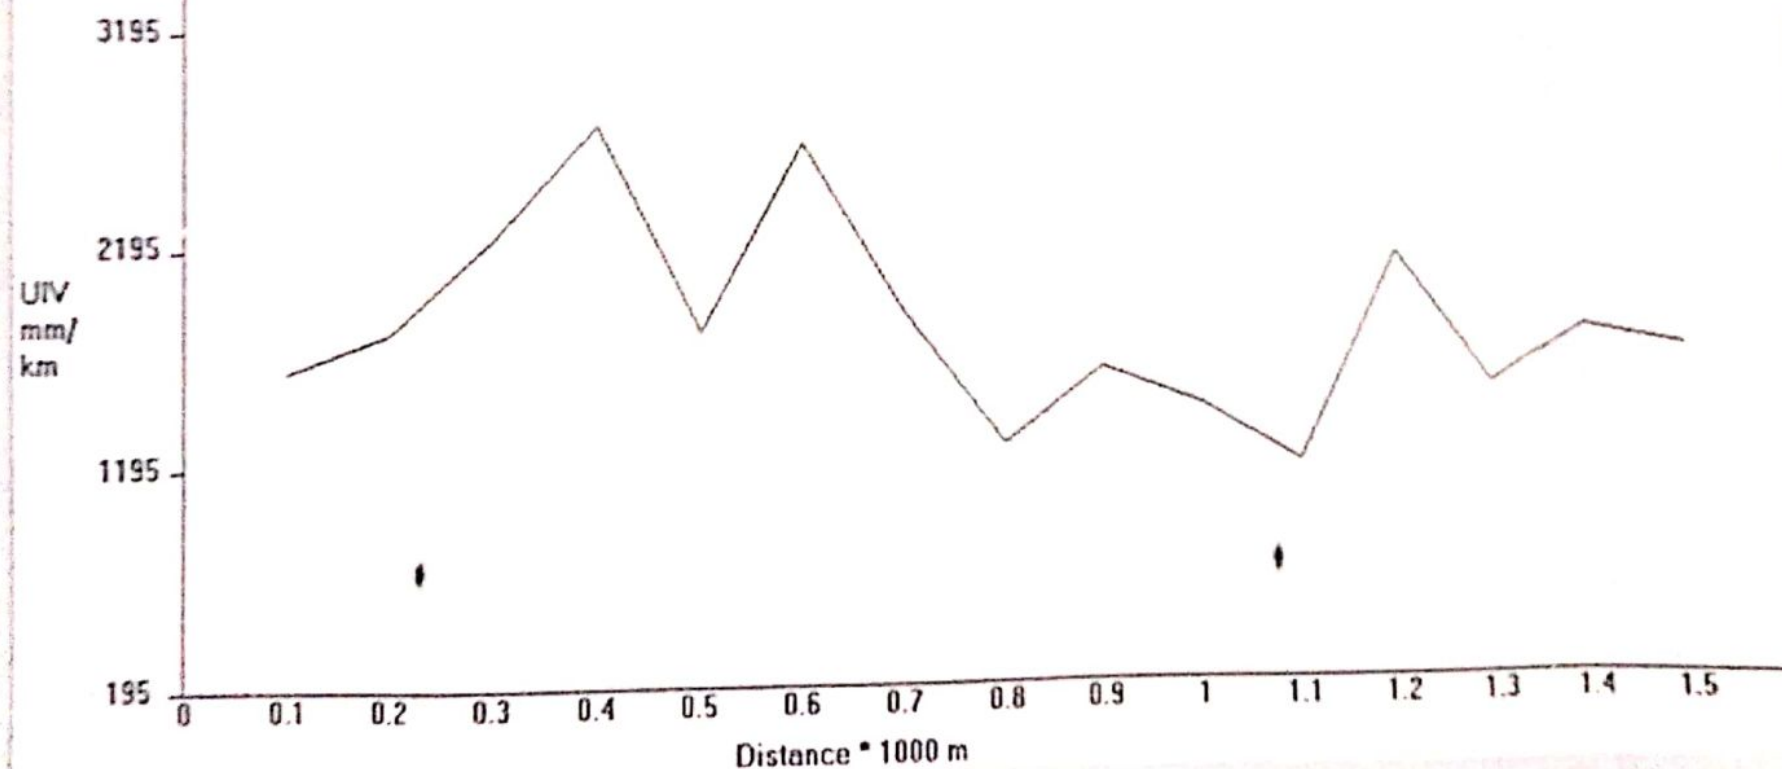

12-11-2020
J.E

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2

पत्रांक..... 1958 अ३७ सिवान, दिनांक..... 27/11/20

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

सेवा में,

सचिव-सह-प्राधिकृत पदाधिकारी
बिहार ग्रामीण पथ विकास एजेन्सी
भूमि विकास बैंक भवन
बुद्ध मार्ग, पटना।

विषय:- योजना शीर्ष नई अनुरक्षण निति 2018 MR/3054 अन्तर्गत पथों में मरम्मत हेतु
अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के आलोक में कहना है कि योजना शीर्ष नई अनुरक्षण
निति 2018 MR/3054 अन्तर्गत संलग्न विहित प्रपत्र में 78.98870 लाख (अठहत्तर लाख
अन्तानबे हजार आठ सौ सत्तर) रुपये मात्र आवंटन देने की कृपा की जाय।

अनु0-अधियाचना पत्र, Bump Integrator Equipment Report की छाया प्रति,
एकरारनामा की छाया प्रति,

विश्वासभाजिन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिवान-2

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- RWD, WORKS DIVISION, SIWAN-2

S.N.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance Maint. (in Lakh)										
1		Guthani to Sohagra	31406708029	1877/ 24.06.2019	11.00	454.1160	284.94236	94.81598	139MBD/ 19-20 16.01.20	30.12.2020	30.12.2020	Good	25 mm	5.031	273.325	273.325	0	Complete
2	MR-N/19-20 Siwan-2/02	Guthani Darauli Salarao Road to Harpur	31406701003	1877/ 24.06.2019	2.800	94.5320	58.00427	21.17897	139MBD/ 19-20 16.01.20	30.12.2020	30.12.2020	Good	25 mm	5.038	40.855	40.855	0	Complete
3		Sohagra Road to Bakulari	31406701006	1877/ 24.06.2019	1.70	59.8580	36.12334	13.84236	139MBD/ 19-20 16.01.20	30.12.2020	30.12.2020	Good	25 mm	5.037	36.12334	36.12334	0	Complete
4	MR-N/19-20 Siwan-2/01	Makarwar to Anoni Path	31406701019	1877/ 24.06.2019	1.800	62.4230	38.17403	14.14724	141MBD/ 19-20 15.02.20	31.12.19	30.12.2020	Good	25 mm	5.036	34.03423	34.03423	0	Complete
5		PWD Road to Bisawaniya	220001242	1877/ 24.06.2019	4.40	155.6160	94.14988	36.41117	141MBD/ 19-20 15.02.20	30.12.2020	30.12.2020	Good	25 mm	5.032	93.90567	93.90567	0	Complete
6	MR-N/19-20 Siwan-2/05	T02 Sarai Via Safi Tola to Amarpur	31406702047	5139/ 24.09.2019	3.20	111.2009	65.47033	32.86766	105MBD/ 20-21 17.09.20	16.06.21	30.12.2020	0.00	0	0.000	0.00	0.00	0	
7		PWD Path Se Tarwan Taruwani	31406602033	5139/ 24.09.2019	3.90	135.8480	80.10775	40.04263	105MBD/ 20-21 17.09.20	16.06.21	01.11.2020	Good	25 mm	5.031	79.14848	79.14848	0	Complete
8		CMDG Road to Bishwaniya Via Balhu	314671033666	6132/ 20.11.2019	7.00	254.6024	155.25400	69.47072	105MBD/ 20-21 17.09.20	16.06.21	30.12.2020	0.00	0	0.000	0.00	0.00	0	
9	MR-N/19-20 Siwan-2/10	Babhanauli to Bargawa Tak Via Kathauliya	31406602016	5139/ 24.09.2019	6.10	205.2256	125.29266	60.69045	104MBD/ 20-21 17.09.20	16.06.21	30.12.2020	0.00	0	0.000	0.00	0.00	0	
11		L026 to Nautan to Kurmatta (VR10)	31406702033	5139/ 24.09.2019	2.50	84.4215	51.33843	25.15108	104MBD/ 20-21 17.09.20	30.12.2020	01.11.2020	Good	25 mm	5.034	50.8059	50.8059	0	Complete
11		Akolohi to Valuhi Via Sishani	31406701001	1877/ 24.06.2019	3.30	104.8720	64.0953	23.79127	140MBD/ 19-20 15.02.20	14.11.2020	30.11.2020	0.00	0	0	0.00	0.00	0	
12		Guthani Balua to Mamur Path	31406701014	1877/ 24.06.2019	2.50	82.9270	51.4269	17.9899	140MBD/ 19-20 15.02.20	14.11.2020	09.11.2020	Good	25 mm	5.034	0.00	0.00	50.9898	Complete

	MR-N/19-20 Siwan-2/03	Guthani Darauli Road to Damodara	31406701004	1877/24.06.2019	1.46	48.5180	29.0178	11.53854	140MBD/19-20/15.02.20	14.11.2020	30.11.2020	0.00	0	0	0.00	0.00	0	
14		Guthani Mairwa (Takaniya) to Chavariya Path	31406701015	1877/24.06.2019	2.50	80.4920	49.581	17.73496	140MBD/19-20/15.02.20	14.11.2020	30.11.2020	0.00	0	0	0.00	0.00	0	
15		Guthani Nainijore Via Sematar Chilmarwa	31406701005	1877/24.06.2019	1.40	55.3266	28.7748	21.02097	140MBD/19-20/15.02.20	14.11.2020	06.11.2020	Good	25 mm	5.032	0.00	0.00	27.9989	Complete
16		Guthani Mairwa Path to Kolharua to Bhagwanpur, via Baheliya	31406701023	1877/24.06.2019	2.40	82.5300	50.2353	18.88126	140MBD/19-20/15.02.20	14.11.2020	30.11.2020	0.00	0	0.000	0.00	0.00	0	
															608.19762	608.19762	78.98870	

प्रमण्डलीय लेखा/पदाधिकारी
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिवान-2

Executive Engineer
RWD Works Division
Siwan-2

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate up to 27th November 2020
NEW MAINTENANCE POLICY (2018)

Sl.No	Name of Scheme	Sanction No.& Date with Amount, (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural roads under NEW MAINTENANCE POLICY (2018)	24/19.03.2020 59/18.08.2020 78/29.10.2020 82/13.11.2020	309.44834 40.85500 127.93990 129.95438	Certified that out of Rs 608.19762 lacs received during the years 2020-21 in favour of Ex. Engineer, RWD, Works Division, siwan-2 Bihar, a sum of Rs 608.19762 Lacs has been utilized for the purpose of NEW MAINTENANCE POLICY-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs 0.00 lacs remaining unutilized at the end of the period under.
Total :			608.19762	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

3. **Physical Progress achieved :-**

- Construction of Road works.
- Construction of CD works.

[Signature]
20/11/20

DAO

RWD, WORKS DIVISION
SIWAN-2

[Signature]
20/11/20

EXECUTIVE ENGINEER
RWD, WORKS DIVISION
SIWAN-2
