

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, दरभंगा-1।

पत्रांक-1932/2020

दिनांक-30/9/2020

प्रति,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, दरभंगा-1।

सेवा में,

अधीक्षक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अंचल, दरभंगा।

विषय- एम0एम0जी0एस0वाई0 योजना अन्तर्गत ग्रामीण कार्य विभाग, कार्य प्रमण्डल, दरभंगा-1 के अधीन SIHULIYAH VILLAGE to SIMRI (MMGSY-SC) पथ निर्माण कार्य के अग्रिम समय वृद्धि स्वीकृत करने के संबंध में।


महाशय,

उपर्युक्त विषयक संदर्भ में कहना है कि एम0एम0जी0एस0वाई0 (MMGSY-SC) योजना अन्तर्गत ग्रामीण कार्य विभाग, कार्य प्रमण्डल, दरभंगा-1 के अधीन एकरारनामा सं0-80SBD/2018-19 (MMGSY-SC) का SIHULIYAH VILLAGE to SIMRI (MMGSY-SC) निर्माण कार्य एकरारनामा के अनुसार दिनांक-22.01.2020 को समाप्त करना था। लेकिन पथ में निजी भूमि विवाद के कारण कार्य ससमय पूर्ण नहीं हो सका अब वर्तमान में कार्य 30.10.2020 तक पूर्ण कर दिया जायगा। किया गया कार्य विशिष्ट के अनुरूप है। पथ में कोई ATR लंबित नहीं है। निदेशानुसार कार्य के समय में स्थिति निम्न प्रकार है:-

1. समय वृद्धि हेतु प्राप्त अभ्यावेदन एकरारनामा प्रावधान के तहत है।
2. समय वृद्धि के लिए अंकित कारण एकरारनामा प्रावधान के तहत मान्य है।
3. किये गये कार्य का MIS Entry प्रतिवेदन संलग्न है।
4. समय वृद्धि हेतु चेक लिस्ट संलग्न है।
5. इस कार्य के विरुद्ध कोई विभागीय / निगरानी जांच लंबित नहीं है।
6. मापि पुस्तिका संलग्न है।

अतः अनुरोध है कि प्राप्त अग्रिम समय वृद्धि पर अपनी सहमति प्रदान करने की कृपा की जाय ताकि अग्रेतर कार्रवाई की जा सके।

विश्वासभाजन


30/9/2020

कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमण्डल, दरभंगा-1।



51
30/9/20

लेख्य प्रमाणक महोदय,
शपथ पत्र मुज0।

शपथ पत्र

मैं **Shubodh Kumar Singh, Vill- Korigama, P.O.- Niamthi, P.S-Baheri**

Dist-Darbhangha उम्र-35 वर्ष, शपथ पूर्वक बयान करता हूँ कि :-

1. यह कि मैं उपरोक्त पते का स्थायी निवासी हूँ।
2. यह कि मैं (MMGSY-SC) योजनान्तर्गत ग्रामीण कार्य विभाग, कार्य प्रमंडल, दरभंगा-1 के अधीन पथ निर्माण कार्य किया हूँ।
3. **SIHULIYAH VILLAGE to SIMRI (MMGSY-SC)** तक पथ निर्माण कार्य।
4. उक्त पथ का निर्माण कार्य मेरे द्वारा 30.10.2020 को कार्य पूर्ण कर दिया जाएगा।
5. उपरोक्त कार्य में अगर समय वृद्धि की स्वीकृति प्राप्त होती है तो मेरे द्वारा किसी प्रकार का वित्तीय दावा का मांग नहीं करूँगा।
6. यह कि शपथ पत्र में वर्णित सभी तथ्य मेरे जानकारी में सत्य वो सही है।

अतः यह शपथ पत्र है।

शुबोध कुमार सिंह,

शपथ कर्ता का हस्ताक्षर

Shubodh Kumar Singh
D. Singh
30/9/20

Notary Seal
30/9/20

कार्यपालक अभियंता का कार्यसमय, कनीय कार्य विभाग, कार्य प्रमाणपत्र

हरमना-11

समय वृद्धि हेतु आवेदन पत्र

1. अभिकर्ता का नाम - SUBODH KUMAR SINGH

2. कार्य का नाम - ASHTA VILLAGE IN SEMRE (MMGSY-SC)

3. एकराश्या संख्या - 80SBD/2018-19 (MMGSY-SC)

4. एकराश्या अंतर्गत कार्य का मूल्य - 136.53609 लाख

5. प्रशासनिक स्वीकृति की राशि - 100.00 लाख

6. एकराश्या के अनुसार कार्य प्रारम्भ की तिथि - 23.01.2019

7. एकराश्या के अनुसार कार्य समाप्ति की तिथि - 22.01.2020

8. वास्तविक के अनुसार कार्य समाप्ति की तिथि :-

9. कार्य विलम्ब का कारण - पथ में निजी भूमि विवाद के कारण कार्य ससमय पूर्ण नहीं हो सका।

10. आवेदन की तिथि तक कार्य पूर्णता का अनुपात - 85%

11. क्या पूर्व में समय वृद्धि की गयी थी, यदि हाँ तो कब तक तिथि अंकित करें - नहीं।

12. पूर्व में समय वृद्धि किस कारण दी गई थी - नहीं।

13. अनुशंसा की तिथि तक कार्य की अद्यतन स्थिति - अपूर्ण।

14. अभिकर्ता का हस्ताक्षर - सुबोध कुमार सिंह
24/9/20

15. कनीय अभियंता की अनुशंसा - संवेदक द्वारा वर्णित कारणों के आधार पर समग्र वृद्धि दिया जा सकता है।

16. अवर प्रमंडल पदाधिकारी की अनुशंसा :- संवेदक द्वारा वर्णित

कारणों के आधार पर समग्र वृद्धि दिया जा सकता है।

17. कार्यपालक अभियंता की अनुशंसा :-

विलम्ब 24 दिनों के लिए है।

18. अधीक्षण अभियंता की अनुशंसा :-

विलम्ब 24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।
24 दिनों के लिए है।

24/9/2020

कार्यपालक अभियंता

कनीय कार्य विभाग, कार्य

हरमना-1

अंचल कार्यालय, बहेड़ी।

पत्रांक 503

दिनांक 17/09/2020

प्रेषक,

अंचलाधिकारी
बहेड़ी।

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, दरभंगा-1

विषय:- पथ को अतिक्रमण मुक्त कराने के संबंध में।

प्रसंग:- आपका पत्रांक 05..... दिनांक 15/08/20

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के आलोक के संबंध में कहना है कि मुख्यमंत्री ग्राम सम्पर्क एस0सी0 योजना के अंतर्गत, SIHULIYAH VILLAGE to SIMRI पथ का निर्माण कार्य जो ग्रामीण द्वारा निजी भूमि बताकर योजना कार्य बाधित किया गया था। सरकारी अमीन द्वारा वर्तमान में उक्त पथ सरकारी जमीन चिन्हित कर अतिक्रमण मुक्त कर दिया गया है।

सूचनार्थ समर्पित।



SUBODH KUMAR SINGH

Korigama, Nimaithi, Darbhanga

GOVERNMENT CONTACTOR & METARIAL SUPPLIER

Date 10/08/2020

Ref. No.

संख्या नं.

कार्यपालक अमियन्ता

नं० कार्य विमारा परमंगा-1

विषय :- असमय वृद्धि लेने के संबंध में,

महोदय,

निर्बल्लभ पूर्वक कहूंगा कि मैंने द्वारा- भुलीयाही गाँव में सीमरी लेला तब अड़क निर्माण कार्य किया जा रहा है आपकी अतिक्रमण होने के कारण मुझे तीन सप्ताहों का असमय- 30-10-20 तक वृद्धि दिया जाय.

अतः भीमान और निर्बल्लभ कि उपयुक्त धारों को देवर्त हूँ असमय-वृद्धि देने की कृपा की जाय.

आपका विश्वासी
अर्वाध कुं सिंह
9430044689

Revised Work Programme

Name of Work- Sihuliyahi Village To Simri (MMGSY-SC)

Name of Division-RWD WORK'S DIVISION DARBHANGA1

S.No	ITEM	Status	Oct-20
1	E/W	Complete	
2	GSB	Complete	
3	CD	Complete	
4	GR III /PCC	Complete	
4	BT	ON-GOING	
5	Road Furnitures	ON-GOING	

Contractor Sign

सुभाष कुमारी ,
२५/१०/२०२०

Amount of work

Location of work

Agreement for different work to be executed

Order of measurement

Unit and rate of measurement

(These four items should be repeated at the commencement of the measurement relating to each work)

Particulars	Particulars of actual measurement				Quantity of work
	No.	L	B	H	
	200	20	10	1.11	
Name of work - Construction of					
Canal for Silulgaon village					
to Bimari hole canal					
Below Bokeri					
Agency - Sri Subodh Kumar Singh					
Agreement No - 80 SBD of 2018-2019					
(mmbsy - SC)					
Agreement Value - Rs 1,34,48,592 = Rs					

Rate of BOB - 10% below

Date of start - 23-01-2019

Date of completion - 22-01-2020

Recover Measurement

(1) Cost of reference boring

Each meter = 2.00 Rs

(2) Cost of reference pillar

= 10.00 Rs

(3) Cost of leveling of

each level.

$2405 \times 3.52 = 8417.50$

= 0.8418 Rs

(4) Cost of embankment

for some pits level.

Particulars	No.	L.	B.	D.	Contents of area
1000 ft. and 1000 ft.					
Approximate and irregular					
5/10/10					
0 to 100 = 100 x 5.00 x 0.20 =					100.00 cu ft
100 to 200 = 100 x 5.00 x 0.20 =					100.00 cu ft
200 to 300 = 100 x 5.00 x 0.25 =					125.00 cu ft
300 to 400 = 100 x 6.00 x 0.20 =					120.00 cu ft
400 to 500 = 100 x 6.00 x 0.25 =					150.00 cu ft
500 to 600 = 100 x 5.20 x 0.30 =					156.00 cu ft
600 to 700 = 100 x 5.75 x 0.35 =					201.25 cu ft
700 to 800 = 100 x 6.00 x 0.36 =					216.00 cu ft
800 to 900 = 100 x 5.00 x 0.30 =					150.00 cu ft
900 to 1000 = 100 x 5.00 x 0.30 =					150.00 cu ft

1000 to 1100 = 100 x 6.00 x 0.35 =	210.00 cu ft
1100 to 1200 = 100 x 5.75 x 0.30 =	172.50 cu ft
1200 to 1300 = 100 x 6.00 x 0.30 =	180.00 cu ft
1300 to 1400 = 100 x 6.50 x 0.30 =	195.00 cu ft
1400 to 1500 = 100 x 6.25 x 0.30 =	187.50 cu ft
1500 to 1600 = 100 x 5.20 x 0.25 =	130.00 cu ft
1600 to 1700 = 100 x 5.10 x 0.20 =	102.00 cu ft
1700 to 1800 = 100 x 5.30 x 0.25 =	132.50 cu ft
1800 to 1900 = 100 x 4.90 x 0.35 =	171.50 cu ft
1900 to 2000 = 100 x 5.40 x 0.30 =	162.00 cu ft
2000 to 2100 = 100 x 5.50 x 0.30 =	165.00 cu ft
2100 to 2200 = 100 x 5.90 x 0.30 =	177.00 cu ft
2200 to 2300 = 100 x 5.60 x 0.25 =	140.00 cu ft
2300 to 2400 = 100 x 5.40 x 0.20 =	108.00 cu ft
2400 to 2465 = 65 x 5.60 x 0.20 =	72.80 cu ft

Continuation

3849.03

		21	
100	100	26	700/19
A8			5-8

①	Crust. of 80% grade and
	50% 80% grade with
	abnormal reaction. at

1020. 45 1/2

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				14	1838.753
	2	4	18	0.20	10.153
	3	4	20	0.20	16.003
	4	4	20	0.20	16.003
	5	4	20	0.20	16.003
	6	4	18	0.20	14.403
	7	4	15	0.20	12.003
	8	4	30	0.10	12.003
	9	4	15	0.10	6.003
					1783.693
 P. K. Singh A.B. 12/02/19 J.E.					

Revised measurement					
(1) primary h.s.B. with					
for graded material of -					
RT Portion					
	2	30	4.050	0.20	48.603
	2	20	4.05	0.20	16.203
	1	30	4.00	0.20	24.003
Deleted 10/2/19	3	30	4.65	0.20	32.903
	2	20	4.05	0.20	16.203
	1	30	4.05	0.20	24.303
	4	30	4.05	0.20	32.403
	6	30	4.65	0.20	32.903
	3	30	4.00	0.20	24.003
	2	30	4.05	0.20	24.303
					600.603

Particulars	Details of actual measurement				Contents of area
	No.	L	B	D	
				87	630.000
	87	30	4.00	0.20	194.400
	3	30	4.00	0.20	69.600
	13	30	4.00	0.20	291.600
Handwritten	19	30	4.00	0.20	461.200
	9	30	4.00	0.20	218.400
	14	30	4.00	0.20	16.000
					1862.200
Handwritten					

ABSTRACT OF COST

①	Cost of reference exp	
	Money back note -	
	Qty 2.00 H. Page - 1	
	Exp. 4197.30 / cell + 8394 = 10	
2/2	Cost of reference pillar	
	Qty 10.00 H. Page - 1	
	Exp. 1926.46 / H. Page - 19265 = 10	
3/3	Cost of greening.	
	Qty 0.8418 H. Page - 1	
	Exp. 50148.60 / H. Page - 43215 = 10	
4/4	Cost of end outlet tank	
	Money back note -	

Particulars	Details of Survey Measurements				Remarks of area
	No.	L.	B.	D.	
				42	698370
Qty 125.234 ³ pag - 3					
				42	127212
35- Consideration of environment					
for land pit dug 100 ft					
Qty 2694.220 ³ pag - 3					
				42	313863
6/6 Grit. of soil zone and					
Random 3/10122 km approach					
Material.					
Qty - 1783.699 ³ pag - 4					
				42	2799862

7/7	P/V	H.S.B	1512	1000
greatest method. graduation				
day	(1862.2003)		page	5
		2578.43	1000	4838.796
				576.81.766
less	104.	6060	e	5768.177
				5113.589
		16/02/19		758.673
Material statement				
E/W (100m)				1154.72 m ³
E/W (1000m)				4478.02 m ³
Aggregate				1787.71 cum
Coarse Sand				446.93 cum
Fine Sand				5113.589
Total				758.673
Continuation				

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
CA ST - 255.679					
AS ST - 13.000					
CT 1% - 51.26					
B ST 2% - 102.272					
L.C. 1% - 91.135					
Reg. - 325.038					
my chag. - 4174.920					
G. total - 513.589					
checked for 18-513589/08-000 all the fac. station. Record are found correct (one line only)					
<i>[Signature]</i> Executive Engineer R. W. D. Works Division Darbhanga-1					

CHEQUE DRAWN

Ch. No. 1358

Date 30/8/19

[Signature]

30/8/19

CO. 18-758673

Received for Re-	758,873/1000
Seven Lacs fifty eight thousand six	
Hundred forty only	Three paise
1950	1950

Cybernation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	

Name of work: Construction of road from Simlipali village to Simari dolan (Length: 2.165 km) under Baku blocu

Name of Agency: Sai Subodh Kumar Singh

Agreement No - 80 SBD/2018-19 (MHW)

Estimated Cost - Rs. 1,49,42,880 = 00

Agreement Value - 1,34,48,592 = 00

Rate: ^{10.00%} 10.00% below from B.O.G

Date of Start: 23.01.2019

Date of Completion: 22.01.2020

Record measurement on date 17/19					
For 600 mm dia H.P culvert					
① E/W Excavation for structure -					
Headwall:	2	4.15	1.40	1.67	17.08 m ³
Bedding:	1	5.78	1.07	0.25	1.55 m ³
Total qty =					18.63 m ³
For 2 nos H.P culvert					
Qty =					2 x 18.63 = 37.26 m ³
② Type B (1st class) Bedding laying					
1 x 5.78 x 1.07 x 0.55 =					3.40 m ³
deduction for pipe Embedment					
1 x 5.78 x 0.22 =					1.27 m ³
Qty =					2.13 m ³
For 2 nos H.P Culvert					
Qty =					2 x 2.13 = 4.26 m ³

Continuation

Particulars	Details of actual measurements				Contents of area
	No.	L	B	D	
③ PV Pipe in open foundation					
	2	3.85	1.40	0.15	$= 1.62 \text{ m}^2$
For 2.0 NOS H.P Culvert					
					$\text{Qty} = 2.0 \times 1.62 = 3.24 \text{ m}^2$

④ Head wall & wing masonry work in cement mortar (1:4)					
Head wall -					
	2	3.85	$(1.25 + 0.40)$	0.20	$= 12.71 \text{ m}^2$
Parapet	2	3.85	0.40	0.60	$= 1.85 \text{ m}^2$
Less pipe	2	0.465	0.61		$= 0.57 \text{ m}^2$
Net Qty					$= 13.99$
For 2.0 NOS H.P Culvert					

$\text{Qty} = 2.0 \times 13.99 = 27.98 \text{ m}^3$

⑤ P.V & laying R.C pipe NP 3 (6mm dia)					
Qty ^{cm}	3.0	2.5			$= 7.5 \text{ M}$
For 2.0 NOS H.P Culvert					
					$\text{Qty} = 2.0 \times 7.5 = 15.0 \text{ M}$

⑥ Plastering with cement mortar (1:4) 15 mm thick in brick work					
Parapet side	4	3.85	1.40		$= 15.40 \text{ m}^2$
Parapet face	4	0.50	0.60		$= 0.80 \text{ m}^2$
Parapet top	2	3.85	0.40		$= 3.08 \text{ m}^2$
Head wall side	2	3.85	0.60		$= 4.62 \text{ m}^2$
Total Qty					$= 23.90 \text{ m}^2$

Ticked & initialed
18/10/14.

17.10.19

TE

Particulars	Details of actual measurements				Contents of area
	No.	L	B	H	
General wing (approx.)					23.18 m
For (Service in dia) 110 mm, (1.1 m)					

① P/W Excavation for Structure:

Head wall: $2 \times 8.33 \times 1.40 \times 1.50 = 34.99 \text{ m}^3$

Bedding: $1 \times 5.78 \times 3.36 \times 0.25 = 4.86 \text{ m}^3$

Total Qty = 39.85 m^3

② Type-B (First class) Bedding laying on well compacted local sand, approved material

Bedding - $1 \times 5.78 \times 3.36 \times 0.55 = 10.68 \text{ m}^3$

Deduction - $2 \times 5.78 \times 0.44 = 5.09 \text{ m}^3$

for pipe Embedment
Total Qty = 5.59 m^3

③ P/W PCC M15 in open foundation

Qty = $2 \times 8.33 \times 1.40 \times 0.150 = 3.50 \text{ m}^3$

④ Head wall in brick masonry work with C:M (1:4)

Head wall - $2 \times 8.03 \times (1.25 + 0.40) \times 2.465 = 32.66$

Parapet - $2 \times 8.03 \times 0.4 \times 0.60 = 3.85 \text{ m}^3$

Low pipe - $4 \times 1.188 \times 0.61 = 2.90 \text{ m}^3$

Net Qty = 33.61 m^3

⑤ P/W Laying Rcc pipe NF3 (2x1000 mm dia)

Qty = $6.0 \times 2.50 = 15.0 \text{ m}$

⑥ Plastering with C:M (1:4)

Parapet side - $4 \times 8.03 \times 1.0 = 32.12 \text{ m}^2$

Parapet face - $4 \times 0.5 \times 0.60 = 0.80 \text{ m}^2$

Parapet top - $2 \times 8.03 \times 0.60 = 6.42 \text{ m}^2$

Head wall side - $2 \times 8.03 \times 0.60 = 9.64 \text{ m}^2$

Total Qty = 48.98 m^2

Particulars	Details of actual measurement				Quantity of area
	No.	L	B	D	
Detailed measurement of work					
For (1st class) in (m) H.P. Culvert					

① Excavation for foundation (structure)

Head wall $2 \times 6.45 \times 1.40 \times 1.50 = 27.09 \text{ m}^3$

Bedding $1 \times 5.78 \times 1.53 \times 0.25 = 2.21 \text{ m}^3$

$\Sigma = 29.30 \text{ m}^3$

For 4.0 NOS H.P. Culvert

$\Sigma = 4.0 \times 29.30 = 117.20 \text{ m}^3$

② Type B (1st class) Bedding laying on well

compacted local sand, approved material.

Bedding $1 \times 5.78 \times 1.53 \times 0.55 = 4.86 \text{ m}^3$

Deduction -

for pipe em
bedment

$1 \times 5.78 \times 0.22 = 1.30$

$\Sigma = 3.56 \text{ m}^3$

For 4.0 NOS H.P. Culvert

$\Sigma = 4.0 \times 3.56 = 14.24 \text{ m}^3$

③ P.V. PCC mix in open foundation

$\Sigma = 2 \times 6.45 \times 1.40 \times 0.15 = 2.71 \text{ m}^3$

For 4.0 NOS H.P. Culvert

$\Sigma = 4.0 \times 2.71 = 10.84 \text{ m}^3$

④ Head wall in Brick masonry work

in cement mortar (1:4) -

Head wall - $2 \times 6.20 \times \frac{(1.25 + 0.40)}{2} \times 2.465 = 25.21 \text{ m}^3$

Parapet - $2 \times 6.20 \times 0.40 \times 0.60 = 2.98 \text{ m}^3$

Let pipe $2 \times 1.88 \times 0.61 = 1.45 \text{ m}^3$

$\Sigma = 26.75 \text{ m}^3$

Particulars	Details of actual measurement				Quantity of area
	No.	L	B	H	

For 100 NOS H.P. (W.Vent)

$$Qty = 100 \times 36.78 = 3678.0 \text{ m}^2$$

④ P.V. & laying for pipe nos. 100 nos.

$$Qty = 3 \times 2.5 = 7.5 \text{ m}^2$$

For 4.0 NOS H.P. culvert

$$Qty = 4.0 \times 7.5 = 30.0 \text{ m}^2$$

⑤ Plastering with cement mortar (1:4)

$$\text{Parapet side} - 4 \times 6.2 \times 0.60 = 14.88 \text{ m}^2$$

$$\text{Parapet base} - 4 \times 0.60 \times 0.60 = 0.96 \text{ m}^2$$

$$\text{Parapet top} - 2 \times 6.20 \times 0.40 = 4.96 \text{ m}^2$$

Head wall

$$\text{Side} - 2 \times 6.2 \times 1.115 = 13.83 \text{ m}^2$$

$$\text{Total Qty} = 34.63 \text{ m}^2$$

For 4.0 NOS H.P. culvert

$$Qty = 4.0 \times 34.63 = 138.52 \text{ m}^2$$

Items checked & in
check as per
Bill 119.
A.C.

5.11.19
J.E

Record measurement

Date - 26.12.19

① P/V GSB (grading I material)

$$1 \times 6' \times \frac{4.70 + 4.05}{2} \times 0.20 = 5.25 \text{ m}^2$$

$$24 \times 30 \times 4.05 \times 0.20 = 583.2 \text{ m}^2$$

$$1 \times 5' \times \frac{4.05 + 5.40}{2} \times 0.20 = 4.73 \text{ m}^2$$

$$\text{Total Qty} = 593.18 \text{ m}^2$$

Continuation

Particulars	Details of actual measurement				Quantity of area
	No.	L	B	D	
RT					Rs - 8832947.54
(13/2) P.V. C.C. Pavement					
M30 grade					
Qty - 100.83 m ² vide TMD page 12					
@ 7351.70/m ²					Rs - 741272.00
					Rs - 9574221.00
Less 10.00% below from D.O.G (-) Rs					957422.00
					Rs - 8616799.00
Less previous payment					
vide TMD, page no 20 (-) Rs					7390893.00
					Rs - 1225906.00

Amthigh
16/03/2020
A.E.

9.03.2020
J.E.

Seigniorage Fee			
Item	Qty	Rate	Amount
① GSB m-3 366.93 m ³			
53 to 22.4 mm	443.986	366.20	= 162587.67
Type B. 11.2 mm	88.06	250.99	= 22102.80
② C.C (M5) 2.71 m ³			
Coarse Sand	1.30	111.80	= 145.34
40 mm Agg.	1.30	348.67	= 453.27
20 mm Agg.	0.65	460.84	= 299.57
10 mm Agg.	0.22	525.62	= 115.63
			Rs - 1185706.00

$\Sigma_{ij}^2(\text{Pr})$	123	75	max 5.30 = 701.55 ± 0
----------------------------	-----	----	-----------------------

Answer) $6.751 \times 10^{-90} = 7.576 \mu\text{g}$

Course length - $0.506 \times 111.80 = 56.571$

13-257669.5/2

10.00 % Storage fee -

RS-25766.952

$$\text{Sav} - 25767 = 00$$


91.03 - 20 20
J.C.

Material Statement

① Stone Aggregate - 467.936 m³

(2) Stone Screening - 88.06 m

(3) Coarse Sand - 7.247 m

④ Bricks - 13375.00000

9.03.2020

7.2

Form 50 Date 10/20/20

Ref No. 1225906

1225906

Form 50-100

Particulars	Details of Asset Measurement				Total of area
	No.	L.	B.	D.	
CTF 1 -	61235				
PTD 1 -	36777				
GRAT 1 -	84518				
IT 1 -	12257				
L. 1 -	12259				
Royalty -	84,545				
S. fee -	25767				
CTMS -	968486				
Pay -					
Grat 1 -	1225906				

passed for B 1225906. Twelve
Lac Twenty Five Thousand nine hundred
SIX only

Executive Director
R.W.D. Works Division

25/07/2020

CFMS Ref No. 20200901004017

dt. 1.9.2020

21-09-2020
TE
Duke

25/9/20
NE

सुखमंजरी ग्राम सभापक योजना

Latitude: 25.983353


Longitude: 85.989231

Elevation: 52.47 m

Accuracy: 3.2 m

Time: 14-09-2020 09:12

Note: shuiyehi vihage ho sam

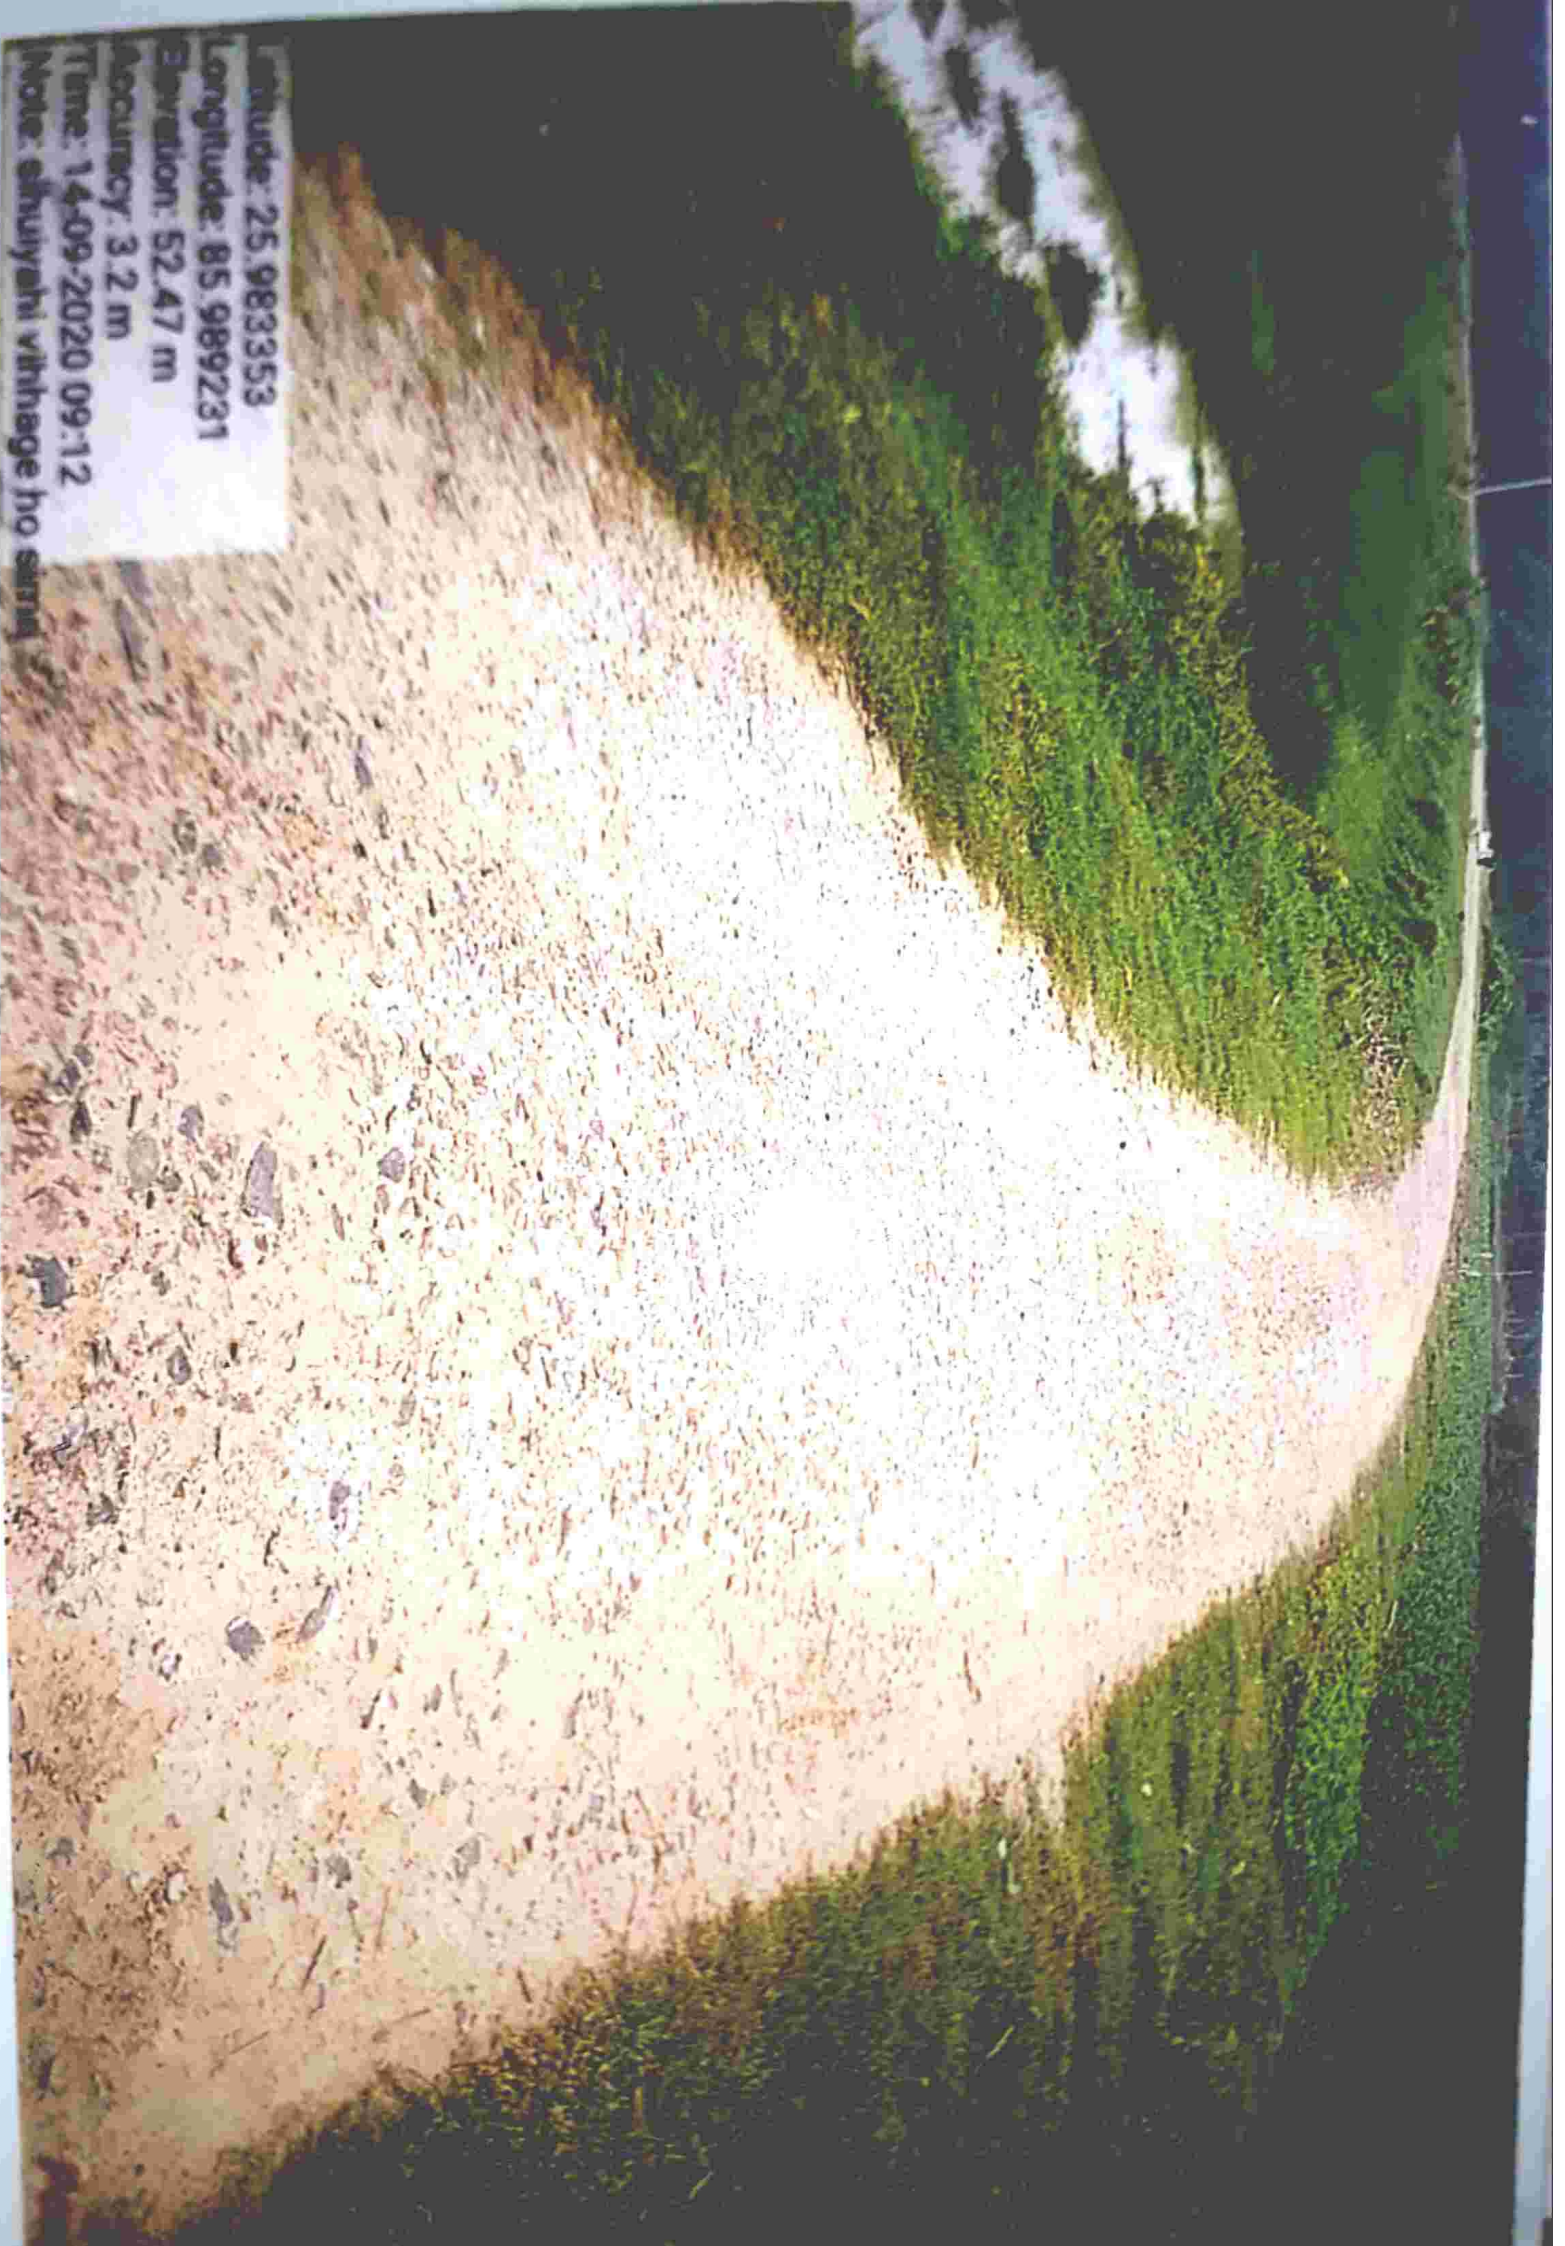

Latitude: 25.982415

Longitude: 86.012636

Accuracy: 2600.0 m

Time: 14-09-2020 09:32

Note: siluiyahi vihage ho samr





Latitude: 25.98384


Longitude: 85.991834

Elevation: 21.76 m

Accuracy: 6.4 m

Time: 14-09-2020 09:17

Note: shtuyahil vilhage hro smm

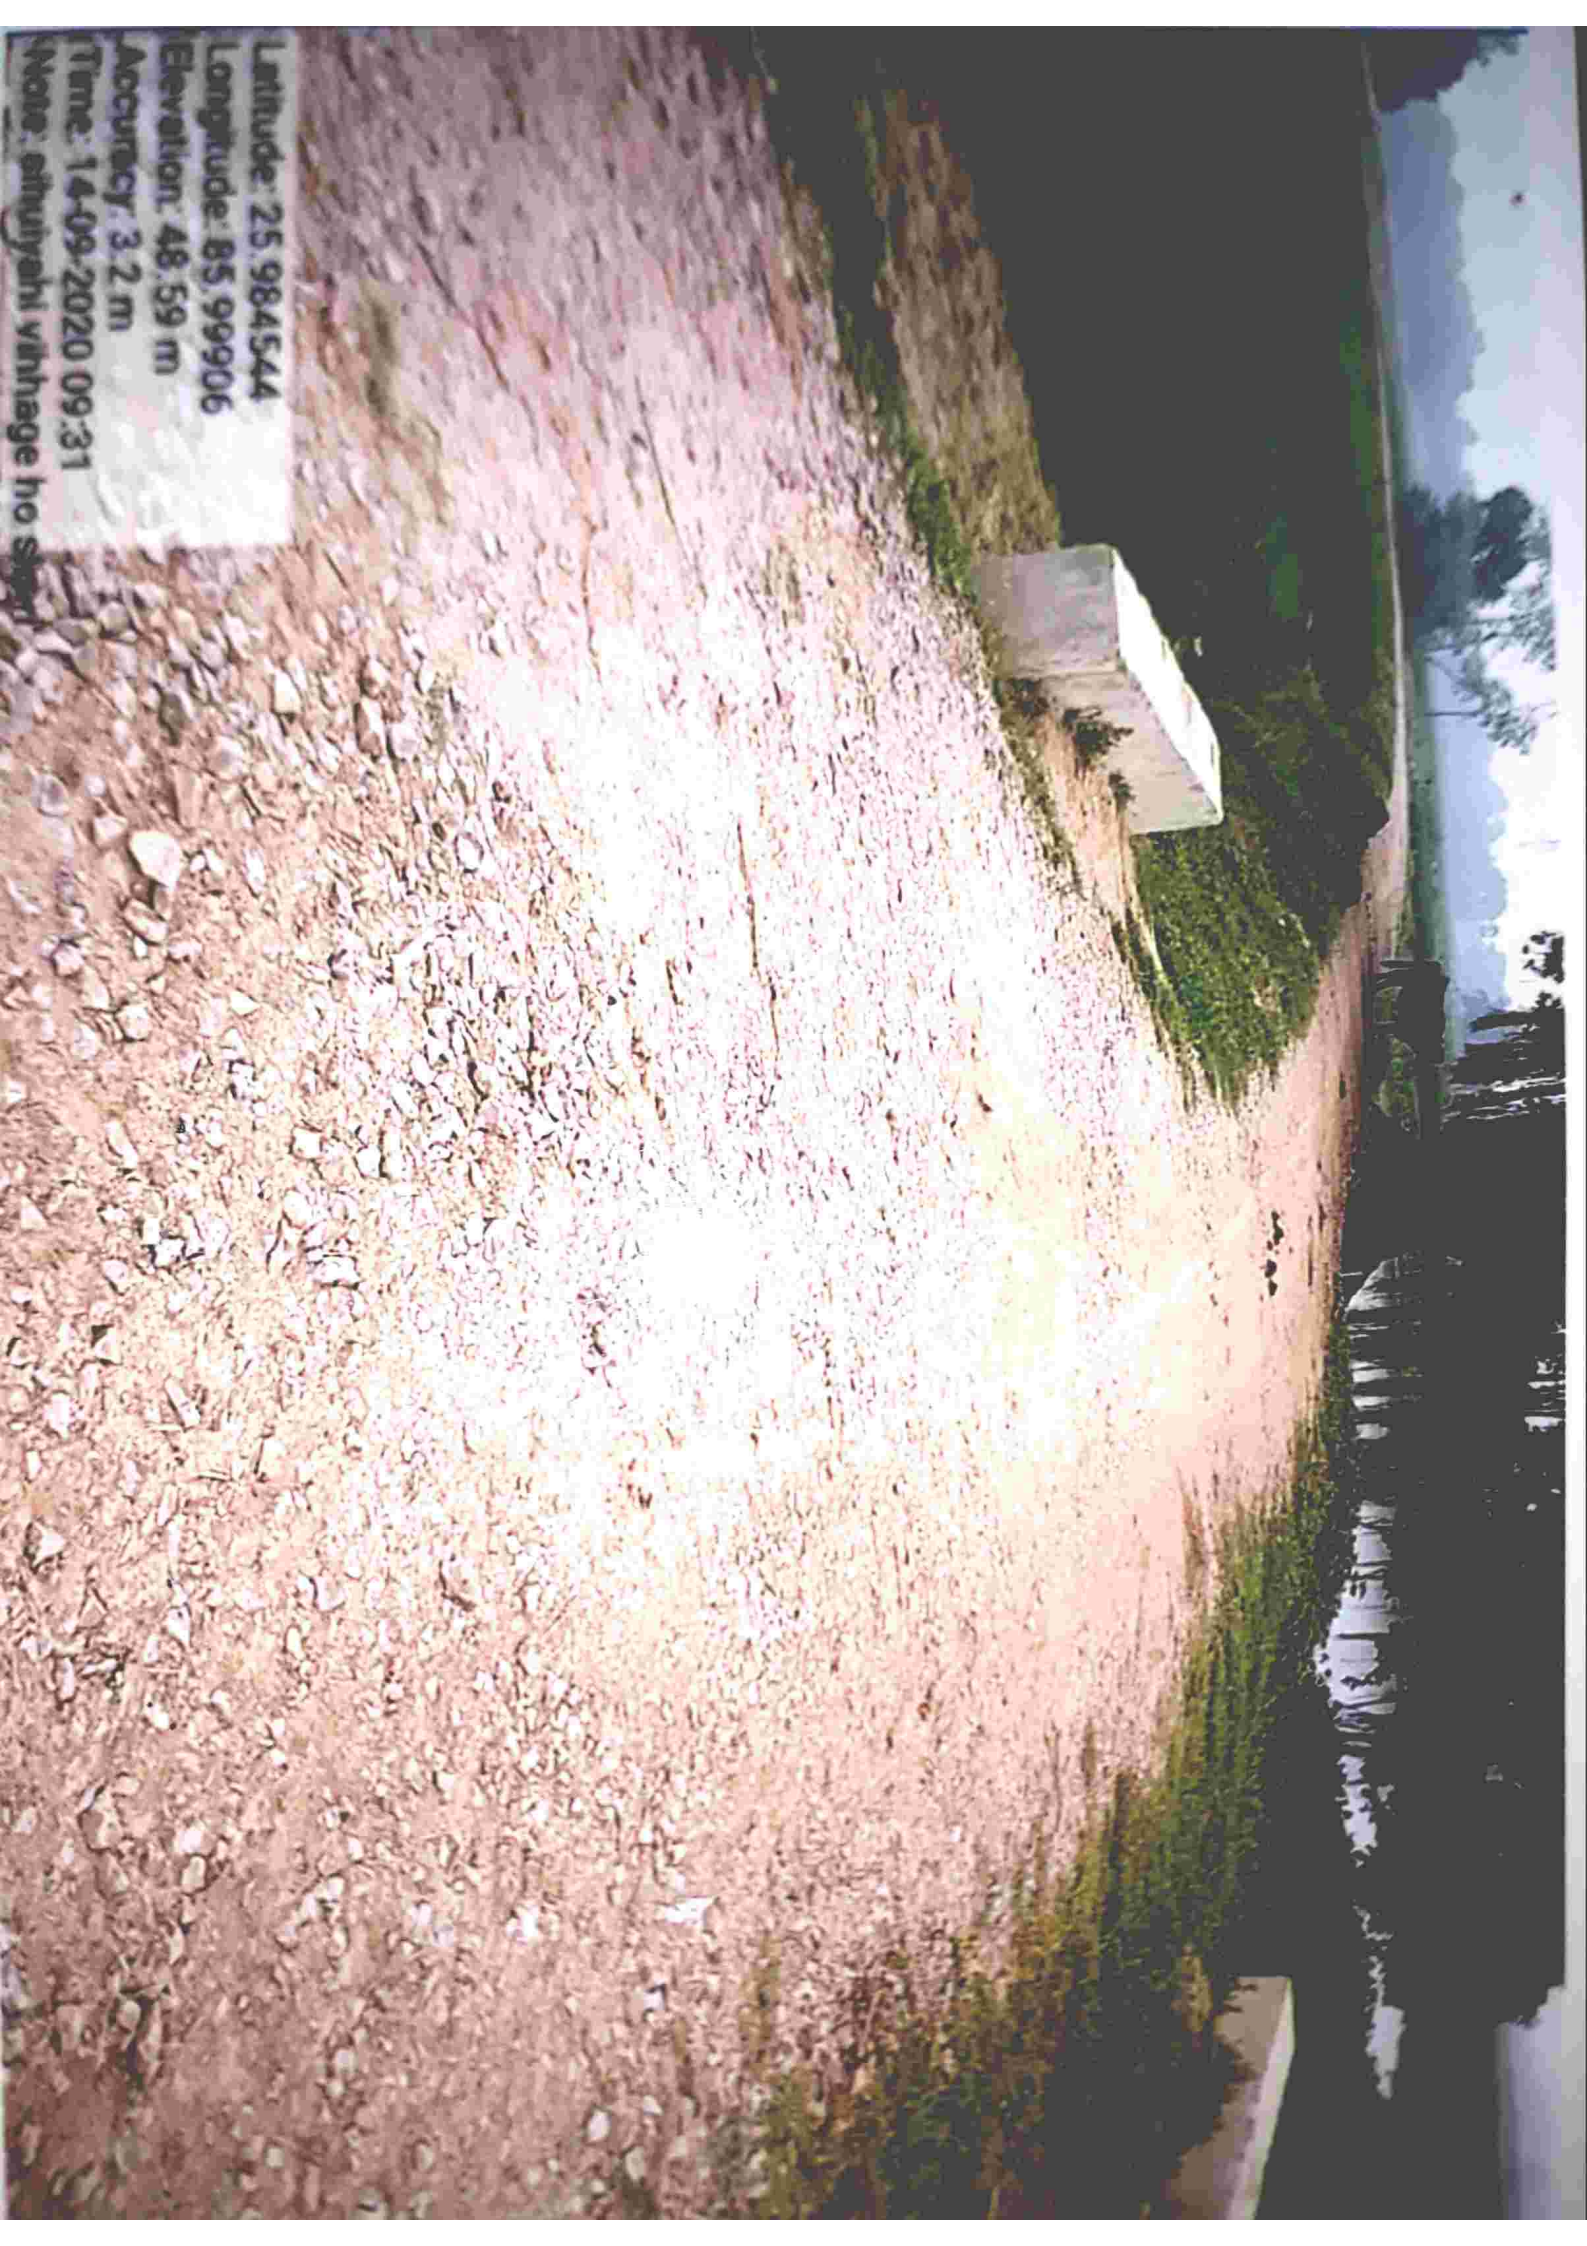

Latitude: 25.984544

Longitude: 85.99906

Elevation: 48.59 m

Accuracy: 3.2 m

Time: 14-09-2020 09:31

More: shtuyahni vihnage ho shtuyahni

Rural Works Department, Govt. of Bihar



Wing:
Circle:
Division:
No. Of Visit:

[Home](#)
[About Us](#)
[Contact Us](#)
[Feedback](#)
[Help](#)
[Privacy Policy](#)
[Terms & Conditions](#)
[Sitemap](#)
[English](#)
[Hindi](#)
[Bhojpuri](#)
[Santali](#)
[Magahi](#)
[Maithili](#)
[Urdu](#)
[Arabic](#)
[Persian](#)
[Pashto](#)
[Kashmiri](#)
[Sinhala](#)
[Tamil](#)
[Telugu](#)
[Kannada](#)
[Malayalam](#)
[Gujarati](#)
[Marathi](#)
[Odia](#)
[Bengali](#)
[Assamese](#)
[Punjabi](#)
[Sanskrit](#)
[Sinhala](#)
[Tamil](#)
[Telugu](#)
[Kannada](#)
[Malayalam](#)
[Gujarati](#)
[Marathi](#)
[Odia](#)
[Bengali](#)
[Assamese](#)
[Punjabi](#)
[Sanskrit](#)

ROADS & HIGHWAYS ROAD (PHYSICAL PROGRESS)

Name of Road (English): SHULIYAH VILLAGE TO SIMRI (On-going)

Financial Approval: Amount: 0.00000

Administrative Approval: Amount: 0.00000

Length(In KM.): 2.465

Maintenance Amt: 11.979860

Upto Last Month: 66.322200

Upto Last Month: 1.000

Upto Last Month: 2.465

Upto Last Month: 0.000

No of Habitations: 0

Fin Year All

Length(In KM.): 0.000

Length(In KM.): 0.000

Tender

Amount: 136.117880

DPR Submitted

Technical Sanction

Length(In KM.): 2.465

Date

Date: 1/1/1900 12

Work Started: Yes

Total: 78.304400 Grand Total

Total: 1.000 Grand Total

Total: 2.465 Grand Total

Total: 0.000 Grand Total

Remarks: BT in Progr

50.09.2010
