

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल समस्तीपुर ।

पत्रांक: 1755285

दिनांक: 07.10.2020

शेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल समस्तीपुर ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी - सह - सचिव
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:- नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत व्यय हेतु आवंटन की मांग ।

महाशय,

उपर्युक्त विषयक नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत व्यय हेतु विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजी जा रही है।

अतः अनुरोध है कि संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने का कृपा की जाए, ताकि किये गये कार्यों का भुगतान किया जा सके । संबंधित संवेदक का इस प्रमंडल में ATR लम्बित नहीं है ।

अनु० :- यथोक्त ।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,

कार्य प्रमंडल समस्तीपुर ।

7.10.2020

Requisition Format for scheme Head : MR(3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and Surface Renewal)

RWD Works Division : Samastipur


Sl No	Package No	Project ID as Per MIS	Name of Road	Administrative Approval (AA) Letter No & Date	Length (Km)	Administrative Amount (In Lakh)	Initial Rectification on with Surface Renewal	Agreement 5 Year Routine Maintenance	Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/km)	Thickness of Bitumen Layer (In MM)	Value of Bitumen Content in	Previous Total Allocated Amount (In Lakh)	Upto date Expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1		NEA220001269	MANNIPUR - DAULATPUR	2173 & 06/07/2019	1.92	65.43570	35.624	18.60497	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3961	25	5.1	32.97792	32.97792	2.49250	BT Complete
2		32010102115	L049 - Chakiafar to Kheraj Gullam (VR49)	2173 & 06/07/2019	2.03	70.00915	38.874	19.32093	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3984	25	5.2	36.31641	36.31641	2.44713	BT Complete
3	RM/SA/S AM/19/00	NEA220001270	MDR T02 TO - DHANIHAR	2173 & 06/07/2019	1.45	43.95000	26.209	12.85000	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3961	25	4.8	24.49075	24.49075	1.71815	BT Complete
4	03	32010102105	X-ROAD L055 - DHURLAKH	2173 & 06/07/2019	0.74	13.07	11.49	5.98066	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3955	25	5.1	0.00000	0.00000	11.48979	BT Complete
5		NEA220001274	MDR T02 - MANIVARPUR	2173 & 06/07/2019	0.85	15.69	13.666	6.58708	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3928	25	5.2	0.00000	0.00000	13.65642	BT Complete
6		32010102092	X-ROAD L029 - BHAGWANPUR	2173 & 06/07/2019	0.56	10.88	9.536	4.57546	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3997	25	5.1	0.00000	0.00000	9.53404	BT Complete
Total															93.78508	93.78508	41.33803	

- 1 Signed Hard Copy and Soft Copy (In Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS


Sr. DAO
RWD (W) Div. Samastipur


Executive Engineer
RWD (W) Div. Samastipur
Vivek
7.10.2020

File :D:\bumpEntegrator\chakjaphar se kheraj gulam.xlsx, Section No. :32, Eqn :test
 Name of Customer :Sri Janak Kishor ray, Name of Work/ Road :L049- Chakjafar to kheraj Gulam, Lab Job number :

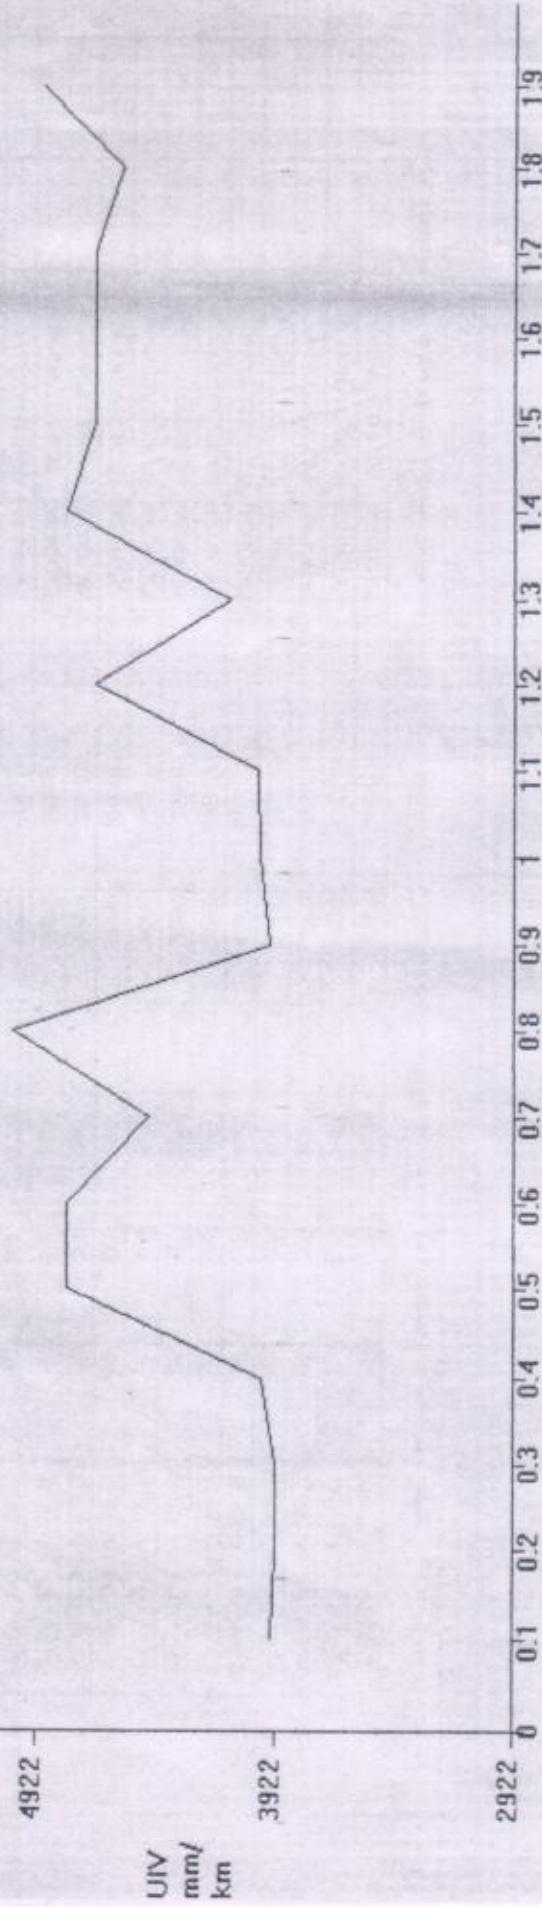

Curve on Speed Breaker के कारण खंबाघर चौक पर सीडीज 4000 से अधिक हो गया है।

 31/8/20
 A.E.
 31.8.20

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$
31/8/20	14:46:0	32	0.1	370	0	3400	3935	G	25.90685	85.80419	Normal	X = 3000
31/8/20	14:46:15	32	0.1	360	20.2	3200	3652	G	25.90647	85.80513	Normal	Y = 3540
31/8/20	14:46:15	32	0.1	360	20.2	3600	3722	G	25.90618	85.80609	Normal	
31/8/20	14:47:0	32	0.1	400	10.1	3500	3776	G	25.90574	85.80608	Normal	
31/8/20	14:47:0	32	0.1	410	20.2	3600	3822	G	25.90482	85.80662	Normal	(R) RURAL ROAD
31/8/20	14:47:25	32	0.1	410	10.1	3500	3776	G	25.90442	85.80721	Normal	Good
31/8/20	14:47:25	32	0.1	380	20.2	3800	4449	A	25.90432	85.80825	Curve	Average
31/8/20	14:48:0	32	0.1	430	10.1	4300	4417	A	25.90444	85.80918	Curve	4001-5000
31/8/20	14:48:0	32	0.1	380	20.2	3800	3649	G	25.90434	85.8102	Normal	Poor
31/8/20	14:48:35	32	0.1	440	20.2	3500	3690	G	25.90423	85.81123	Normal	
31/8/20	14:49:0	32	0.1	340	20.2	3400	3694	G	25.9041	85.81219	Normal	
31/8/20	14:49:11	32	0.1	400	20.2	4000	4676	A	25.90394	85.81318	Curve	
31/8/20	14:49:11	32	0.1	350	10.1	3500	3608	G	25.90424	85.81391	Normal	
31/8/20	14:50:0	32	0.1	410	20.2	3510	3890	G	25.9051	85.81412	Normal	
31/8/20	14:50:0	32	0.1	400	20.2	4000	4576	A	25.90602	85.81431	Curve	
31/8/20	14:50:21	32	0.1	400	10.1	3500	3876	G	25.90638	85.81513	Normal	
31/8/20	14:50:21	32	0.1	400	20.2	3620	4676	A	25.90648	85.81609	Curve	
31/8/20	14:51:0	32	0.1	390	20.2	3500	3962	G	25.9074	85.81626	Normal	
31/8/20	14:51:0	32	0.1	420	20.2	3600	3853	G	25.90827	85.8164	Normal	

Curve एवं Speed Breaker के कारण संबंधित चैनल पर रीडिंग -4000 ले अधिक हो गया है।

31/8/20
A.E.

31/8/20
A.E.

31/8/20

Name of work-

Situation of work-

Agency by which work is executed-

Date of measurement-

No. and date of agreement-

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Record Entry</u>					
<u>N/work - Repair to Road Form</u>					
<u>chakjafaz to kheraj gulam</u>					
<u>Under New Maintenance Policy-2018.</u>					
<u>Agency:- Sri Janak kishor Rai-</u>					
<u>Agmt No - 09 MBD - 2019-20</u>					
<u>Date of Start - 08.01.2020</u>					
<u>Date of Completion:- 07.10.2020</u>					
<u>Actual date of Completion - Ongoing-</u>					

① cleaning and grubbing Road
land - including uprooting -

$$2 \times 1450 \times 1.10 = 3190.00$$

$$2 \times 580 \times 0.75 = 870.00$$

$$4060.00 \text{ m}^2$$

$$\text{In Hect} = \frac{4060.00}{10000} = 0.406$$

$$= 0.41 \text{ Hect}$$

$$0.41 \text{ Hect}$$

② Construction of subgrade -

$$2 \times 1450 \times 1.00 \times 0.20 = 580.00$$

$$2 \times 580 \times 0.50 \times 0.20 = 116.00$$

$$696.00 \text{ m}^3$$

Prep.
24/07/2020
JK

Continuation
25/7/20
A.E.

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	CF Armt - Rs - 3750846 = 00				
(21) Painting two coats each —					
19 Qty vide TMB - P-14 - 82.56 m ²					
82.56 m ² @ Rs - 95.63 / m ²					
					Rs - 7895 = 00
(22) Planting of Tree —					
15 Qty vide TMB - P-14					
66 No @ Rs - 800.30 / Each					
					Rs - 52820 = 00
					Rs - 3811561 = 00
Add GST (12%) - (+) Rs - 457387 = 00					
Add labour (1%) - (+) Rs - 38112 = 00					
					Rs - 4307060 = 00
Less 10% Below (TL) - (-) Rs 430706 = 00					
					Rs - 3876354 = 00
Minus previous Payment vide this MBP-11 (-) 3631641 = 00					
Pay 02/10/2020					2,44,713 = 00
					3/10/20
					A.E.
