

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल समस्तीपुर ।

पत्रांक: 1755298

दिनांक: 07.10.2020

शेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल समस्तीपुर ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी - सह - सचिव
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:- नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत व्यय हेतु आवंटन की मांग ।

महाशय,

उपर्युक्त विषयक नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत व्यय हेतु विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजी जा रही है।

अतः अनुरोध है कि संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने का कृपा की जाए, ताकि किये गये कार्यों का भुगतान किया जा सके । संबंधित संवेदक का इस प्रमंडल में ATR लम्बित नहीं है ।

अनु० :- यथोक्त ।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,

कार्य प्रमंडल समस्तीपुर ।

7.10.2020

Requisition Format for scheme Head : MR(3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and Surface Renewal)

RWD Works Division - Samastipur

Sl No	Package No	Project ID as Per MIS	Name of Road	Administrative Approval (AA) Letter No & Date	Length (Km)	Administrative Amount (In Lakh)	Initial Rectification with Surface Renewal	Agreement 5 Year Routine Maintenance	Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/km)	Thickness of Bitumen Layer (In MM)	Value of Bitumen Content in	Previous Total Allocated Amount (In Lakh)	Upto date Expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1		NEA220001269	MANNIPUR - DAULATPUR	2173 & 06/07/2019	1.92	65.43570	35.624	18.60497	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3961	25	5.1	32.97792	32.97792	2.49250	BT Complete
2		32010102115	L049 - Chakgatar to Kheraj Gulam (VR49)	2173 & 06/07/2019	2.03	70.00915	38.874	19.32093	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3984	25	5.2	36.31641	36.31641	2.44713	BT Complete
3	RM/SA/S AM/19/00 03	NEA220001270	MDR T02 TO - DHANIHAR	2173 & 06/07/2019	1.45	43.95000	26.209	12.85000	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3961	25	4.8	24.49075	24.49075	1.71815	BT Complete
4		32010102105	X-ROAD L055 - DHURLAKH	2173 & 06/07/2019	0.74	13.07	11.49	5.98066	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3955	25	5.1	0.00000	0.00000	11.48979	BT Complete
5		NEA220001274	MDR T02 - MANTYARPUR	2173 & 06/07/2019	0.85	15.69	13.666	6.58708	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3928	25	5.2	0.00000	0.00000	13.65642	BT Complete
6		32010102092	X-ROAD L029 - BHAGWANPUR	2173 & 06/07/2019	0.56	10.88	9.536	4.57546	09(MBD)19-20/ 8.01.2020	7-Oct-20	On Going	3997	25	5.1	0.00000	0.00000	9.53404	BT Complete
Total															93.78508	93.78508	41.33803	

- 1 Signed Hard Copy and Soft Copy (In Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS


Sr. DAO
RWD (W) Div. Samastipur

Executive Engineer
RWD (W) Div. Samastipur

Vivek
7.10.2020

File :D:\bumpIntegrator\chakjaphar se kheraj gulam.xlsx Section No. :34, Eqn :test

Name of Customer :Sri Janak Kishor Ray, Name of Work/ Road :Mannipur - Daulatpur, Lab Job number :

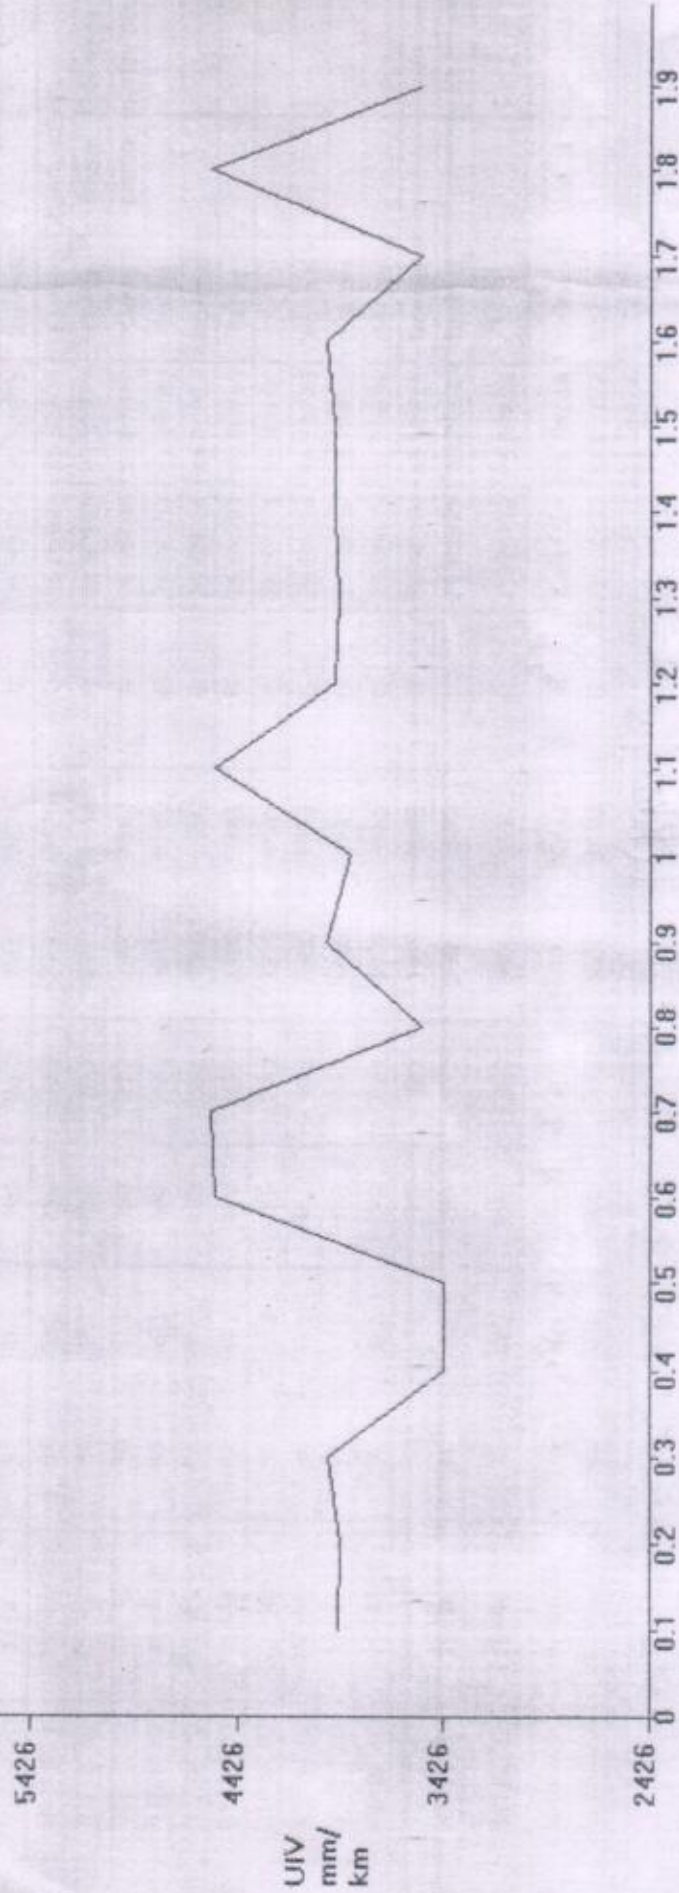

Curve एवं स्पीड ब्रेकर के कारण खंबंधित चैनल पर सीडिंग 4000 से अधिक हो गया है।

Signature
31/8/20
A.E.

31/8/20
SE

31/8/20

date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event		
1/8/20	15:41:15	34	0.1	450	0	3900	3944	G	25.87572	85.80614	$Y = 0 * X^2 + 1.136 * X + 132.5$		
31/8/20	15:41:15	34	0.1	370	20.2	3700	3935	G	25.87659	85.80641	Normal	X = 3000	
31/8/20	15:42:0	34	0.1	340	20.2	3400	3994	G	25.87746	85.80657	Normal	Y = 3540	
31/8/20	15:42:0	34	0.1	290	20.2	2900	3426	G	25.87834	85.80675	Normal		
31/8/20	15:42:25	34	0.1	290	20.2	2900	3426	G	25.87923	85.80704	Curve		
31/8/20	15:42:25	34	0.1	450	20.2	4500	4544	A	25.87989	85.80773	Curve		
31/8/20	15:43:0	34	0.1	390	20.2	3900	4562	A	25.88046	85.80847	Curve	Good	Average
31/8/20	15:43:0	34	0.1	300	20.2	3000	3540	G	25.88131	85.80889	Curve	<4000	4001-5000
31/8/20	15:43:36	34	0.1	490	20.1	3900	3998	G	25.88214	85.80867	Curve		Poor
31/8/20	15:44:0	34	0.1	330	20.2	3300	3881	G	25.88293	85.80813	Normal		
31/8/20	15:44:11	34	0.1	430	20.2	4500	4545	A	25.88371	85.80758	Curve		
31/8/20	15:44:11	34	0.1	440	20.1	3900	3963	G	25.88454	85.80726	Curve		
31/8/20	15:45:0	34	0.1	440	20.2	3500	3945	G	25.88512	85.80652	Normal		
31/8/20	15:45:0	34	0.1	530	20.1	3909	3963	G	25.88469	85.80606	Normal		
31/8/20	15:45:22	34	0.1	520	20.1	3955	3963	G	25.88376	85.80611	Normal		
31/8/20	15:46:0	34	0.1	490	20.2	3900	3998	G	25.88339	85.8054	Normal		
31/8/20	15:46:0	34	0.1	300	20.2	3000	3540	G	25.88292	85.80448	Speed Breaker		
31/8/20	15:46:32	34	0.1	390	20.2	3900	4562	A	25.88229	85.80384	Curve		
31/8/20	15:46:32	34	0.1	300	20.2	3000	3540	G	25.88137	85.80357	Normal		

Curve एवं स्पीड ब्रेकर 3 कारण खोला जायेगा एवं सीमा 4000 से अफिट हो जायेगा।

सि. 31/8/20
R.E.

अभिषेक
31/8/20
R.E.

अभिषेक
31/8/20

Name of work-

Situation of work-

Agency by which work is executed-

Date of measurement-

No. and date of agreement-

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	<u>Record Entry</u>				
<u>N/work</u>	<u>Repairs of Road From</u>				
	<u>Manipur to Daulatpur</u>				
	<u>under new maintenance Policy</u>				
	<u>2018.</u>				
<u>Agency: - Sri Janak Kishor Rai</u>					
<u>Agmt No - 09 MBD, 2019-20</u>					
<u>Date of start - 08.01.2020</u>					
<u>Date of Completion: - 07.10.2020</u>					
<u>Actual date of Comp-</u>					

(1) clearing and grubbing Road
Land --- including ---

$$2 \times 1480.00 \times 1.25 = 3700.00$$

$$2 \times 460.00 \times 0.55 = 506.00$$

$$4206.00 \text{ m}^2$$

$$\frac{4206.00}{10.000} = 0.421 \text{ Hect}$$

$$\text{Limit as Per agreement} = 0.39 \text{ Hect}$$

(2) Construction of subgrade and
earthen shoulder ---

$$2 \times 1480.00 \times 1.00 \times 0.20 = 592.00$$

$$2 \times 460.00 \times 0.50 \times 0.20 = 92.00$$

$$684.00 \text{ m}^3$$

Rs
27/7/2020

Continuation

A.E.

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	BF-Ament - Rs-3390586=00				
(15) RCC-M-15-Bandby Bldg -					
Qty vide MB-P-12					
60 No @ Rs-482.63/Each					
					-Rs-28958=00
(16) Planting of Tree -					
Qty vide MB-P-12					
67 No @ Rs-800.30/Each					
					-Rs-53620=00
(17) Plastering with cement mbr -					
20 Qty vide MB-P-13					
55.04 m ² @ Rs-169.38/m ²					
					-Rs-9323=00
(18) Painting with two coat -					
19 Qty vide MB-P-13					
55.04 m ² @ Rs-95.63/m ²					
					-Rs-5263=00
					<u>Rs-3487750=00</u>
Add 12% GST= (+)					Rs-418530=00
Add 1% Laborm = (+)					Rs-34878=00
					<u>Rs-3941158=00</u>
Less 10% Below (TI) (-)					Rs-394116=00
					<u>Rs-3547042=00</u>
Diduct previous payment vide this MB-P-9-					3297792=00
					<u>Rs-249250=00</u>
Pst 03/10/2020					
JE					
					<u>04/10/20</u>
					A.E.

Continuation
