

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बाढ़

पत्रांक ४३३ अनु / बाढ़ / दिनांक १०/१०/२०२०
प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल बाढ़।

सेवा मे

अधीक्षण अभियन्ता
ग्रामीण कार्य विभाग
कार्य अंचल, पटना।

विषय :- शीर्ष राज्य योजनान्तर्गत Construction of H/L Bridge on Bagdhaiya River between Sobhatika Aatipichhara Mahadalit Tola to Near Dalit Tola under Pandark Block, Dist- Patna तक ब्रीज निर्माण का समय-वृद्धि के संबंध मे।

महाशय,

उपरोक्त विषय के संदर्भ में कहना है कि शीर्ष राज्य योजनान्तर्गत Construction of H/L Bridge on Bagdhaiya River between Sobhatika Aatipichhara Mahadalit Tola to Near Dalit Tola under Pandark Block, Dist- Patna तक ब्रीज निर्माण कार्य का समय-वृद्धि हेतु प्रस्ताव समर्पित किया जाता है।

योजना का बिन्दुवार प्रतिवेदन भेजा जा रहा है -

1. स्थल का फोटोग्राफ।
2. (क) कार्य प्रारम्भ करने की तिथि-09.03.2019 है।
(ख) एकरारनामा के अनुसार कार्य पूर्ण करने की तिथि-08.03.2020 है।
3. माह जुलाई 2019 से सितम्बर 2019 तक नदी में बहुत ज्यादा पानी आ जाने के कारण, मार्च 2020 से अप्रैल 2020 तक लॉकडाउन में मजदूर नहीं मिलने के कारण कार्य में विलम्ब हुआ है, विषयांकित कार्य दिनांक-31.12.2020 तक पूर्ण करने का शपथ पत्र दिया गया है, कार्य प्रगति में है।
4. कार्य विशेष्टियों के अनुरूप किया जा रहा है। अतः दिनांक-31.12.2020 तक समय-वृद्धि की अनुशंसा की जाती है।
अतः अनुरोध है, कि उक्त कार्य का समय-वृद्धि प्रस्ताव की स्वीकृति देने की कृपा की जाय।

अनु०-यथोक्त।

विश्वासभाजन

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बाढ़।

१०/१०/२०

समयवृद्धि हेतु आवेदन-प्रपत्र

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बाढ़

1. अभिकर्ता का नाम : R. K. Construction
2. कार्य का नाम : Constructing & five year maintenance of R.C.C Bridge at Bagdahi Nadi Near Sobhatika Atipichra Mahadasi & Daitola.
3. एकरारनामा सं० : 33/SB01/2018-2019.
4. एकरारनामा अन्तर्गत कार्य का मूल्य : Rs. 2,68,93,867/-
5. प्रशासनिक स्वीकृति की राशि : Rs. 2,97,02,400/-
6. एकरारनामा के अनुसार कार्य प्रारंभ की तिथि : 09/03/2019
7. एकरारनामा के अनुसार कार्य समाप्ति की तिथि : 08/03/2020
8. और अधिक समय जो माँग की जा रही है : upto 31/12/2020
9. तिथि एवं समय जिसमें कार्य संपादन में व्यवधान उत्पन्न हुआ : 16/07/19 to 25/09/19 & 24/03/20 to 20/04/20
10. आवेदन की तिथि तक कार्य पूर्णता का अनुपात : 90 %
11. क्या पूर्व में समय वृद्धि की गयी थी हों तो कब तक तिथि अंकित करें : NO.
12. पूर्व में समय वृद्धि किस कारण दी गयी थी : N/A.
13. अभिकर्ता का हस्ताक्षर : The work has been delayed due to over flow of water in river, Scarcity of labour in lockdown.
14. अनुशंसा की तिथि तक कार्य अधतन की स्थिति : 2 dimensional Superstructure work of main bridge completed G.S.B work in approach road in progress.
15. कनीय अभियंता का अनुशंसा : The matter is true hence time extension granted upto 31/12/20
19/09/20
JE.
16. अवर प्रमंडल पदाधिकारी की अनुशंसा स्पष्ट एवं ठोस कारण सहित : Reasons stated by Contractor is true to best of my knowledge & hence recommended for time extension upto 31.12.2020.
19.09.2020
AE
17. कार्यपालक अभियंता की अनुशंसा स्पष्ट एवं ठोस कारण सहित अपने लिखावट में : T.E. may be granted.
10/10/20
18. अधीक्षण अभियंता की अनुशंसा :

No. 198 Date 3.8.20

भारतीय गैर न्यायिक
एक सौ रुपये Rs. 100

रु. 100



ONE HUNDRED RUPEES

भारत INDIA
INDIAN NON JUDICIAL



बिहार BIHAR

क्रम संख्या 2963 तिथि 03/09/2020 मूल्य 100 x 1 = 100/-

क्रेता का नाम एवं पता राकेश कुमार सलेमपुर जहानाबाद

युगल किशोर प्रसाद
मुद्रांक विक्रेता, समाहरणालय, पटना
ला० नं०-8/77

शपथ - पत्र

मैं राकेश कुमार, पिता श्री गजेन्द्र शर्मा, ग्राम- सलेमपुर, थाना- सफ़ाबाद, जिला- जहानाबाद & बिहार का स्थायी निवासी हूँ
शपथ पूर्वक बयान करता हूँ कि:-

1. यह कि मैं आर.के. कन्स्ट्रक्शन फ़र्म का पार्टनर हूँ।
2. यह कि मैंने राज्य योजना अन्तर्गत बगदाही नदी पर शोशा ठीका अति पिछड़ा महादलित एवं दलित टोला के पास उच्च स्तरीय आर.सी.सी ब्रीज का निर्माण एवं पाँच वर्षीय अनुरक्षण कार्य कर रहा हूँ।
3. यह कि समय वृद्धि स्वीकृत होता है तो शीघ्र में अन्य किसी भी प्रकार का अतिरिक्त राशि का दावा नहीं करूँगा।

यह कि उपरोक्त शपथ पत्र में ली लखी गई सारी बातें मेरी जानकारी में सही एवं सत्य हैं।

Identify the deponents
Signature/L.T.A. who have
affixed in my presence

राकेश कुमार
शपथकर्ता का हस्ताक्षर

Advocate

Shri/Smt. ...
Who is being identified by
advocate solemnly affirms
and declare before me

NATHURA PRASAD
NOTARY (Patna)

19.9.20



Construction Program

Realistic duration.

21025 09/11/16
CONTRACTOR
R K CONSTRUCTION

EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARH

MA BA PA

Schedule XLV-Form No. 134

Name of work → Const of R.C.C. Bridge at Bagdahi Nadi
Near Sobhathia Aitapichae Mandakind

Dalit Tola

Agency → R. R. Constamdn

DIVISION

101. Below

SUB-DIVISION

Dat of Agree + 9.3.2019

Dat of Compl - 8.3.2020

MEASUREMENT BOOK

360

Attest

EXECUTIVE ENGINEER

R.W.D. WORKS DIVISION

BARH

Name to work—
 Situation of work—
 Agency by which work is executed—
 Date of measurement—
 No. and date of agreement.
 (These four lines should be repeated at the commencement of
 the measurements relating to each work.)

1

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Work:-	Construction of RCC Bridge at				
	Bagdani nadi near Sobhathika				
	At Pithra Mahadalit and dalit				
	Jola.				
Agency:-	R.K. Construction, Vill-Salemara				
	Po-Sikandarpur, P.S.-Sakurabad				
	Dist.-Jharkhand.				
Agreement NO.	33/SBD/2018-19				
Date of commencement (as per w/order).	09/03/19				
Date of completion (as per w/order):	08/03/20				

T9.No-05	S/F4 Placing HYSD bar reinforcement in foundation - - - EII			
Abutment Main bar (Bottom)				
25 mm ϕ .				
	$2 \times 22 \times 22.25 \text{ m} = 979.00 \text{ m}$			
L_p	$2 \times 22 \times 1.25 \text{ m} = 55.00 \text{ m}$			
	Total = 1034.00 m			
	@ 3.85 kg/m = 3980.90 kg			
Ring, 8 mm ϕ				
	$2 \times 133 \times 3.40 \text{ m} = 904.40 \text{ m}$			
	Total = 904.40 m			
	@ 0.39 kg/m = 352.72 kg			
20 mm ϕ				
	$2 \times 11 \times 3.54 \text{ m} = 77.88 \text{ m}$			
	@ 2.97 kg/m = 192.36 kg			
	Total = 4525.98			
Continuation		= 4526 MT		

Attended

12/10/20
 EXECUTIVE ENGINEER
 R.W.D. WORKS DIVISION
 BARH

4th main Bill.

dt. 16/09/20

62

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L	B.	D.	
Name of work: Construction of P.C.C. Bridge at					
Bagdahi Nadi near Subhan AHPida.					
2a Mahadeti and dalit tolo.					
Agency: - M/s R.K. Construction					
Agreement No - 33/SKD/2018-19					
Date of commencement (as per work order): 09/03/19					
Date of completion (as per work order): 08/03/20					
Date of actual Completion: - In Progress.					
Abstract of cost:					
T.O.No-01 Earthwork in excavation					
for structures - - - E.I.					
Ordinary soil					
(i) upto 3 m depth.					
Qty V/P-4 L of TMB.					
530.46 m ³ @ Rs. 285.71 per m ³ = Rs. 151558.00					
T.O.No-02 Providing and laying of					
P.C.C. M-15 having coarse - E.I.					
Qty V/P-4 of TMB.					
27.71 m ³ @ Rs. 660.00 per m ³ = Rs. 18300.00					
T.O.No-03 R.C.C. grade M-30 in pile					
foundation - - - E.I.					
Pile cap in R.C.C. M-30					
Qty V/P-4 of TMB.					
305.69 m ³ @ Rs. 8023.82 per m ³ = Rs. 2452802.00					
T.O.No-04 Bored cut in situ M-35 grade					
R.C.C. concrete pile - - - E.I.					
(i) 1200 mm dia.					

Continuation

Total = Rs. 27,87,368.00

Attest. L. d.

10/10/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
1/10/20 BARH

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of aron
	No.	L.	B.	D.	
			8.5	Rs.	2787368.00
Qty V/P-42 of TMB					
452.00 m ³ @ Rs. 17355.60 per m ³					7858291.00
<u>T.2 No-05</u> Supplying fitting & laying					
44 SD bar				- E/I	
Qty V/P-42 of TMB					
69.09 m ³ @ Rs. 73617.32 per m ³					5086225.00
<u>T.2 No-06</u> Providing & constructing					
Temporary earth bund				- E/I	
Qty V/P-42 of TMB					
1 No @ Rs. 53636.45 each					53636.00
<u>T.2 No-07</u> R.C.C grade M-30 in					
Substructure				- E/I	
(i) Up to 5 m height					
154.575 m ³ V/P-42 of TMB					
5.410 m ³ V/P-46 of TMB					
159.985 m ³ @ Rs. 8347.21 per m ³					1335428.00
<u>T.2 No-08</u> R.C.C M-30 grade in					
Substructure				- E/I	
(ii) From 5 m upto 10 m height					
5.76 m ³ V/P-42 of TMB					
14.76 m ³ V/P-47 of TMB					
20.52 m ³ @ Rs. 8501.45 per m ³					174450.00
<u>T.2 No-09</u> R.C.C grade M-35 Substr.					
Structure complete				- E/I	
R.C.C M-35					
(i) From 5 m upto 10 m height					
Qty V/P-42 of TMB					

Continuation

Total = Rs. 172,95,398.00

A. H. S. Red

10/10/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARH

Particulars	Details of actual measurement				Contents of item
	No.	L.	B.	D.	
				DE: 8m	172,95,398.00
9.14 m ² @ 8m	8615.33	Per 2 = 8m			72745.00
<u>T.O. No. 10</u>	Supplying, fitting and				
	Placing 11150 bar reinforcement				
	Cement EIR				
	Qty. v/p-43 of TMB				
22.176 m ² @ 8m	73716.94	MT 3m			1635256.00
<u>T.O. No. 11</u>	Supplying, fitting &				
	fixing POT Cum PTFE				
	bearing EIR				
	9 Nos. v/p-43 of TMB.				
	3 Nos. v/p-47 of TMB				
12 Nos @ 8m	49250.00	each = 8m			590400.00
<u>T.O. No. 12</u>	Supplying, fitting & fixing				
	in position due to line and				
	level elements bearing . . . EIR				
	Qty. v/p-60 of TMB.				
131475.00 Cum @ 8m	6.97	Per Cum = 8m			127531.00
<u>T.O. No. 13</u>	Providing weephole in brick				
	masonry / stone masonry . . . EIR				
	Qty. v/p-43 of TMB.				
144 Nos. @ 8m	145.51	each = 8m			20953.00
<u>T.O. No. 14</u>	Backfilling behind abutment				
	wing wall & return wall . . . EIR				
	Qty. v/p. 61 of TMB.				
140.90 m ² @ 8m	767.73	Per 1 = 8m			107795.00
<u>T.O. No. 15</u>	Providing flying filter				

Continuation

Total = 8,198,56,678.00

Attended

10/10/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARRH
1.18.20

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					B.F. = 178,56,678.00
med to with G.C.C. - - -					El
Dty V/P-60 of TMB.					
69.60 m ³ @ B. 2580.91 Per m ³ = B.					179631.00
<u>T.S. No-16</u> Providing and laying out					
need cement concrete in					
substructure - - -					El
R.C.C.M-30.					
61.20 m ³ V/P-53 of TMB					
61.20 m ³ V/P-58 of TMB					
19.76 m ³ V/P-59 of TMB					
142.16 m ³ @ B. 9031.87 Per m ³ = B.					1283971.00
<u>T.S. No-17</u> Supplying and laying					
HYSD bar reinforcement El					
6.475 M.T. V/P-50 of TMB					
1.246 M.T. V/P-51 of TMB					
2.666 M.T. V/P-53 of TMB					
6.475 M.T. V/P-55 of TMB					
1.246 M.T. V/P-56 of TMB					
2.655 M.T. V/P-58 of TMB					
20.763 M.T. @ B. 74905.92 Per M.T. = B.					1555272.00
<u>T.S. No-18</u> Providing and laying cement					
concrete wearing Course M-30					
Grade - - - - -					El
Dty V/P-60 of TMB.					
20.96 m ³ @ B. 16464.08 Per m ³ = B.					345087.00

Continuation

Total = 232,20,639.00

A. H. H. H.

10/1/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
Wm
1.10-20 BARH

Sch. XLV—Form No. 134

Sch. XLV—Form No. 134					
Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				BF: Rs. 2,32,206.39.00	
<u>T.O.No-21</u>	Construction of P.C.C. railing				
	of M-25 grade E/L				
	Qty. v/p-59 of TMB.				
	86.40 m @ Rs. 4022.77 Per m = Rs. 3,48,177.00				
<u>T.O.No-22</u>	Drainage - spots complete				
	as per drawing E/L				
	Qty. v/p-59 of TMB				
	12 Nos. @ Rs. 667.49 each. = Rs. 8010.00				
<u>T.O.No-23</u>	Providing and laying of a				
	strip seal expansion joint - E/L				
	Qty. v/p-59 of TMB.				
	25.35 m @ Rs. 11792.56 Per m = Rs. 2,99,068.00				
<u>T.O.No-24</u>	Providing & Fixing 20 mm				
	thick compressible fibre				
	board E/L				
	Qty. v/p- of TMB.				
	25.35 m @ Rs. 287.64 Per m = Rs. 7292.00				
<u>T.O.No-25</u>	Providing & Fixing of random				
	20 mm thick precast				
	and filler E/L				
	Qty. v/p- of TMB				
	25.35 m @ Rs. 404.20 Per m = Rs. 1,02,460.00				
<u>T.O.No-28</u>	Clearing and grubbing road				
	land including E/L				
	Qty. v/p- 48 of TMB				
	0.40 Ha @ Rs. 49800.13 Per Ha = Rs. 1,99,200.00				
Continuation					
Total = Rs. 2,39,13,953.00					

A. H. S. Lal

10/10/20
 EXECUTIVE ENGINEER
 R.W.D. WORKS DIVISION
 BARH

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					B.F. Rs. 23913953.00
<u>T.O.No-29</u>	Construction of embankment				
	with materials obtained - E1				
	Qty. V/P-48 of TMB.				
4570.00	m ³	@ Rs. 194.95	Per m ³	= Rs.	890922.00
<u>T.O.No-36</u>	Providing & laying of Logo				
	informatory sign board with				
	logo - - - E/L				
	Qty V/P-46 of TMB				
2 Nos	@ Rs.	9767.24	each	= Rs.	19534.48
<u>T.O.No-39</u>	Construction of embankment				
	with material obtained				
	from borrow pit - - - E/L				
	Qty V/P-46 of TMB				
600.00	m ³	@ Rs. 194.75	Per m ³	= Rs.	116850.00
<u>T.O.No-40</u>	Providing and laying				
	RCC pipe (N.P.) - - - E/L				
	Qty V/P-46 of TMB				
10.00	m	@ Rs. 4781.25	Per m	= Rs.	47813.00
	Total = Rs. 2498907.20				
Less @ 10% below as per tender	agreement - (Rs.) 2498907.00				
	Total = Rs. 22490165.00				
Deduction :-					
Payment upto 3rd on A/c bill					
	V/P-45 of TMB = (Rs.) 1700000.00				
	Net total = Rs. 5490165.00				
Continuation 16.9.2020 S.E.					

Attended

10/10/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARH



राज्य योजनान्तर्गत

योजना का नाम:- वगदाही नदी पर शोभाठिका अतिपिछड़ा महादलित एवं दलित टोला के
पाल् उच्चस्तरीय पुल का निर्माण कार्य

पथ की लम्बाई- 0.634 कि.मी. प्रा.राशि- 288.01 लाख

5 साल तक रख-रखाव की राशि- 3.59 लाख

कार्य प्रारम्भ की तिथि- 09.03.2019

कार्य समाप्ति की तिथि- 08.03.2020

संवेदक का नाम- आर.के. कंसुक्शन, जहानाबाद

कार्यकारी एजेंसी- कार्य.अभि. ग्रामीण कार्य विभाग, कार्य प्रमंडल, बाढ़
ग्रामीण कार्य विभाग, बिहार सरकार द्वारा संपादित

CONSTRUCTION OF RCC BRIDGE NEAR SOBHA THIRA
ATTIPICHA MANDALIT AND DALIT TOLA

Bhramar
18/09/20
J.E.

Shall
18.9.2020
J.E.

C/S

18/09/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARRH

बिहार सरकार



राज्य योजनान्तर्गत

जिला - पटना


प्रखंड - पण्डारक

योजनाका नाम - गंगादी नदी पर शोभाटिका अक्षिपिण्डा महादलित दलित दोला के पास उच्चस्तरीय पुल का निर्माण कार्य

पुल की लम्बाई - 36.12 मीटर

No. Of Span - 2X16.50 M.

पहुँच पथ की लम्बाई 0.634 कि.मी.

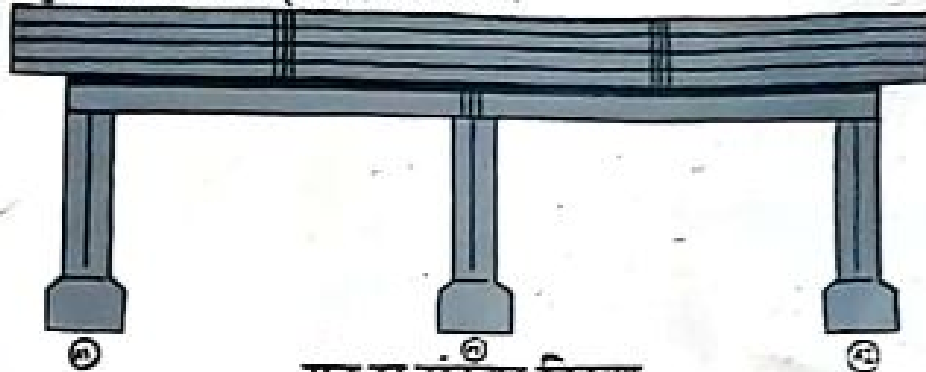

पुल का खंडवार विवरण

पहुँच पथ के पेवमेंट का विवरण

- उप आधार 523.81 घनमी. (185 दक के समतुल्य)
पानी डाल कर रोलर से दबाया हुआ।
मुसम 216 घनमी. (76 दक के समतुल्य)
गिट्टीया नदी की रेत (ग्रेवल) 215.2 घनमी. (दक के समतुल्य)
पत्थर का चूरा 215.2 घनमी. (दक के समतुल्य)
- सीमेंट कंक्रीट पेवमेंट 19 से.मी. मोटा
गिट्टी 23.1 घनमी. (5 दक के समतुल्य)
रेत 11.55 घनमी. (2 दक के समतुल्य)
सीमेंट 333 बैग

3. कुल स्वीकृत राशि - 288.01 लाख

कार्यकारी एंजिनियर कार्य प्रमुख अधिकारी, जिला पंचायत, पटना

CONSTRUCTION OF RCC BRIDGE NEAR SOBHA
THIRA ATIPICHA MAHADAIT AND DALIT TOLA


Bhuvan
18/09/20
J.E.

Yall
18.9.2020
A.E.

CIS

18/09/20

EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARH

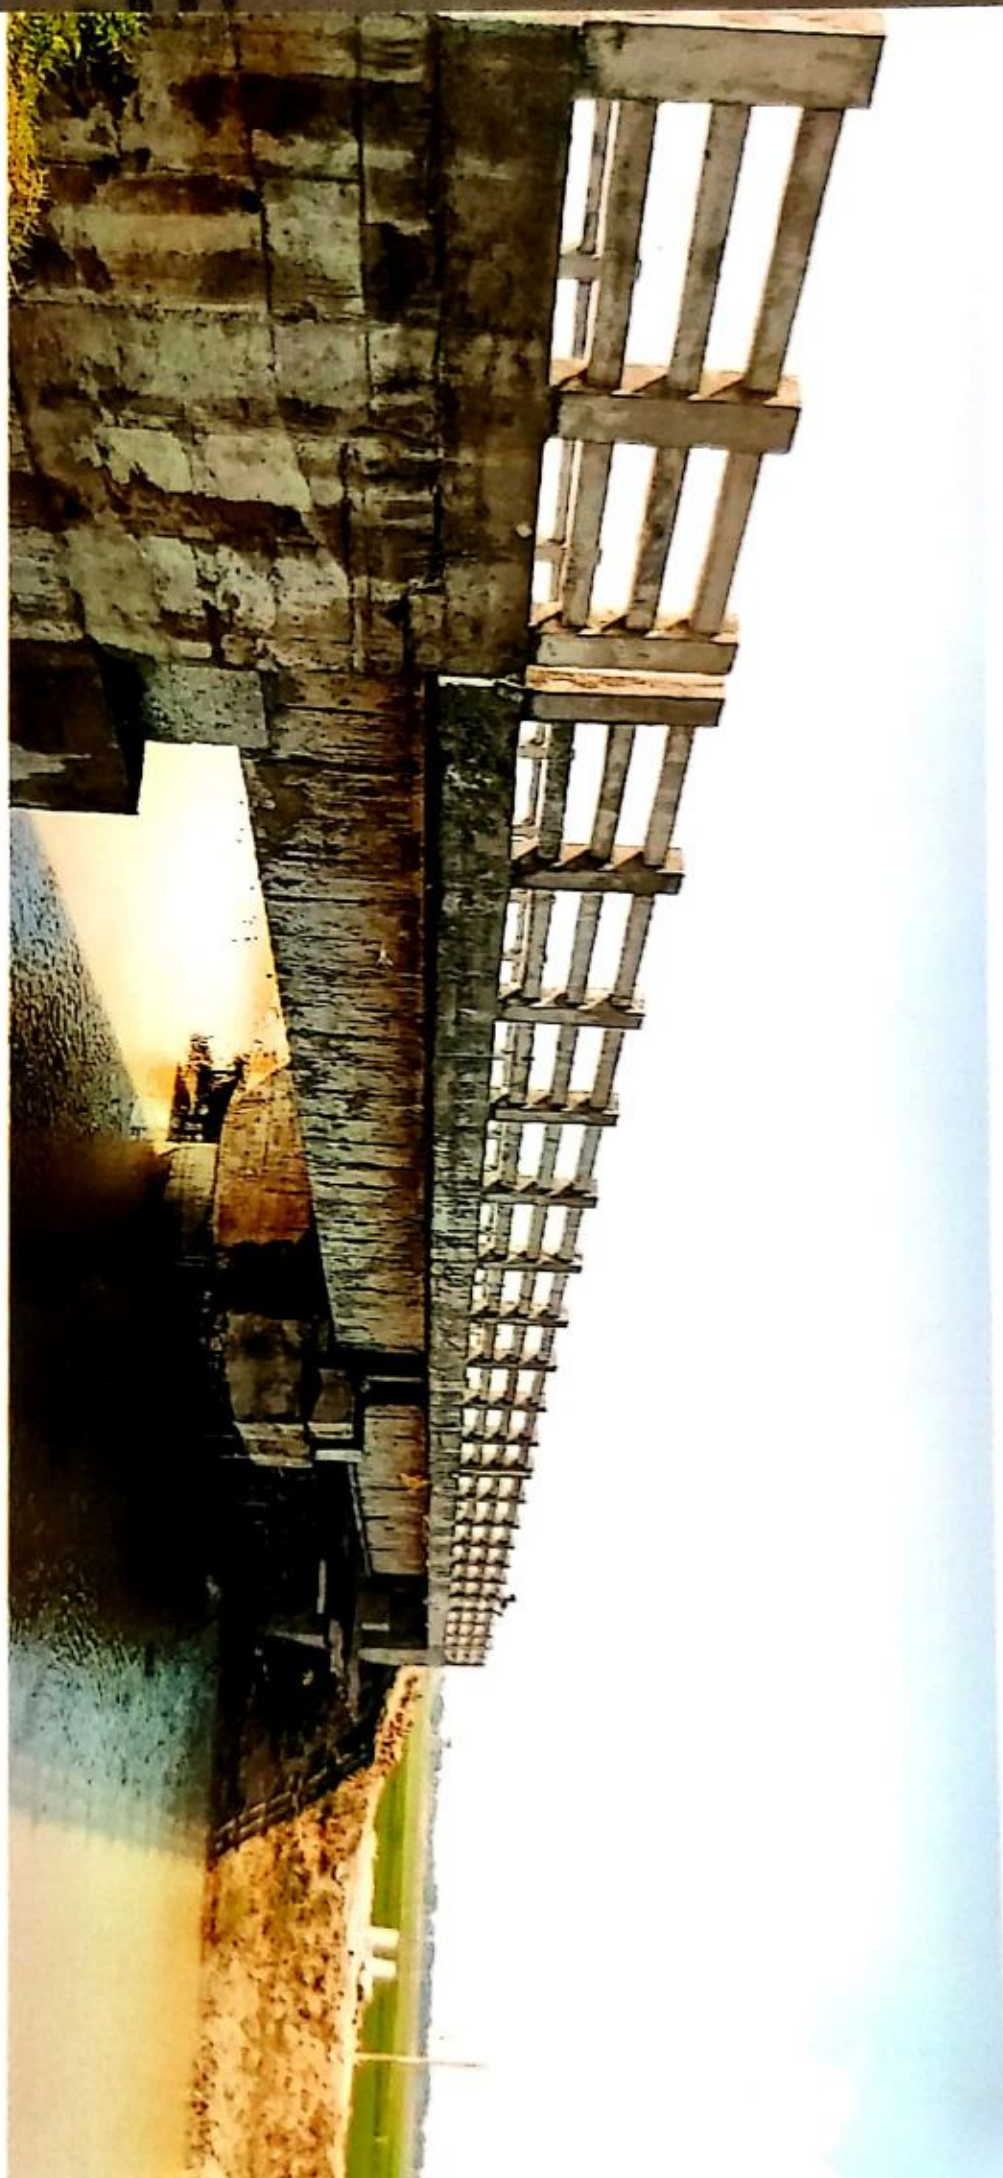

CONSTRUCTION OF ACC BRIDGE NEAR SOBHA THIKRA
ATTACHED MAHA DRAIT AND DRAIT TOLA

Bhumes
18/09/20
J.E

Yall
18.9.20
AE

C/S
18/10/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARRH




CONSTRUCTION OF RCC BRIDGE NEAR SOBHA THIRA
ATTIPICHA MATHA DALIT AND DALIT TALA

B Kumar
18/09/20
J.E

14/9/20
18.9.20
AF

C/S

12/10/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARI

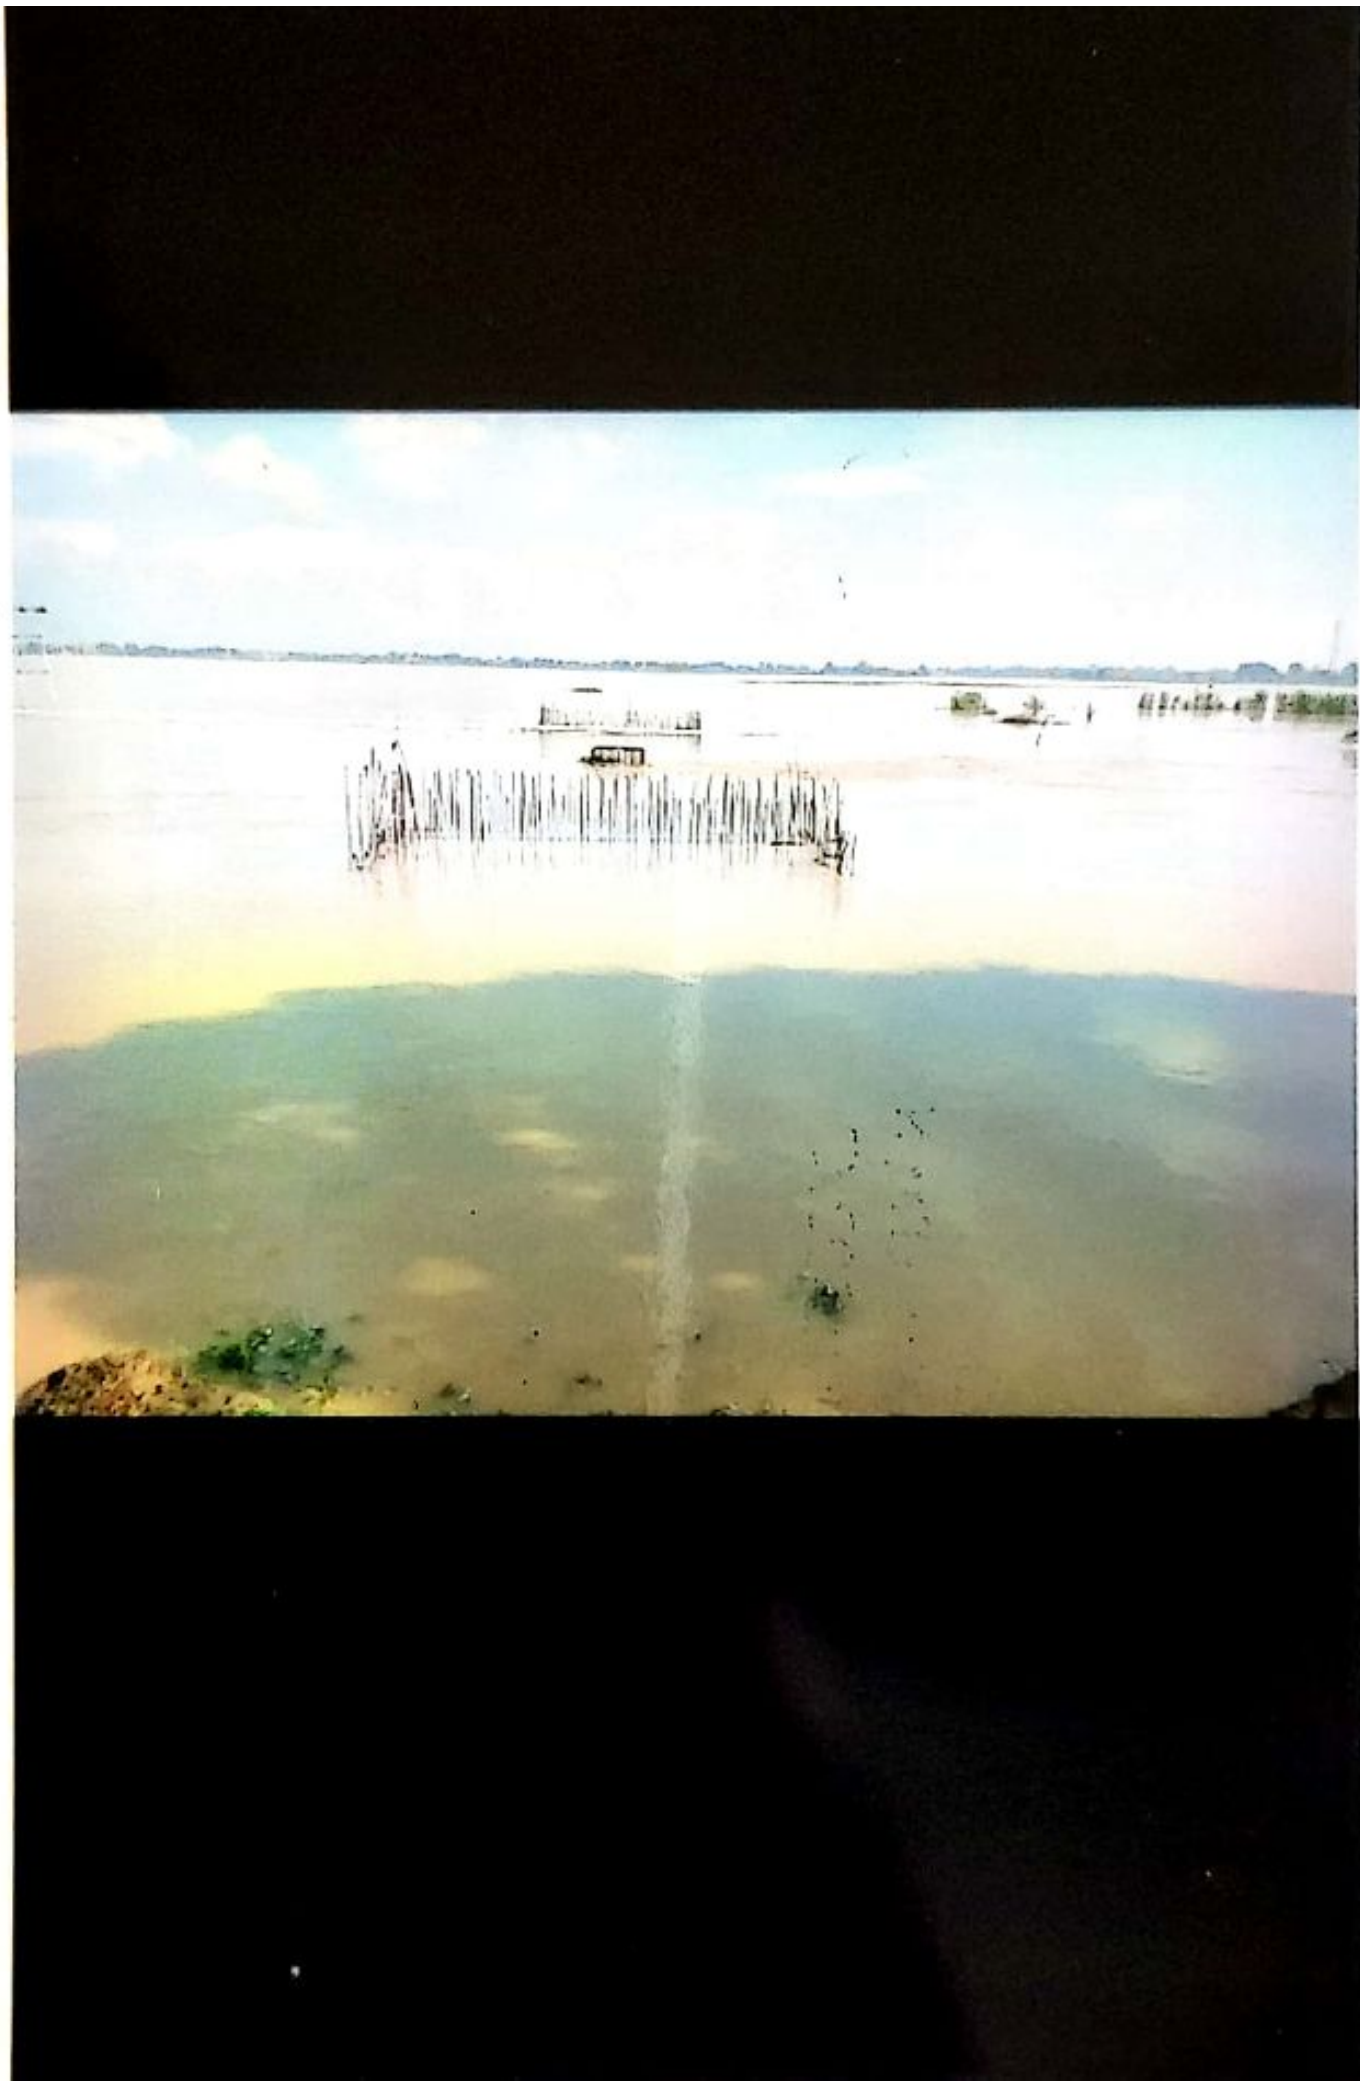

CONSTRUCTION OF RCC BRIDGE NEAR SOBHA
THIRU ATRICHAR MAHADEVI AND DALIT
TOLA

Broum
18/09/20
5:12

18/09/20
18.9.20
18.9.20

C/S

10/10/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARH



CONSTRUCTION OF RCC BAIDUA NEAR SOBHA
THIRU ATIPICHARA MATHADRAIT AND DRAIT
TOLA

Bhumer
18/09/20
J.E

Ball
18.9.2020
AF

C/S

18/09/20

EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARH



CONSTRUCTION OF ACC BRIDGE NEAR SOBHA
THIRA AT PICHHA MAHA DALIT AND DALIT
TOLA

BKumar
18/09/20
J.E

14/9/20
18.9.2020
AF

C/S

18/09/20
EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARH



CONSTRUCTION OF RCC BRIDGE NEAR
SOBHATHIRA ATIPICHRA MAHADALI
AND DALIT TOLA

C/S

Bhumer
18/07/20
J.E.

W. Goll
18.9.2020
J.E.

EXECUTIVE ENGINEER
R.W.D. WORKS DIVISION
BARRH

18/07/20

WRITE X

DVD-RECORDABLE
SPEED 1x - 16x
4.7 GB

PREMIUM QUALITY
DVD-R

Sobhatika Bridge
R.K. Construction
