



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail – eerwd.marhaura@yahoo.com

पत्रांक:- 1803(अनु०)

मढ़ौरा/दिनांक:- 29.12.2020.

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:-शीर्ष MR-3054 योजनान्तर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत स्वीकृत कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु०, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-3054 (MR-3054) अंतर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत **संवेदक में 0 जे०के० एण्ड कम्पनी** द्वारा पूर्ण किये गये पथ का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन हेतु अधियाचना सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये राशि कॉलम सं०-18 के अनुरूप आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक में 0 जे०के० एण्ड कम्पनी द्वारा पूर्ण किये गये पथ में भुगतान किया जा सके।

अनु०-1) अधियाचना प्रपत्र।

2) 19 ए प्रपत्र।

3) मापी पुस्त की छाया प्रति।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

(Handwritten signature)
29/12/2020

FORM GER-19-A

(See Government of India 'S Decision (I) below Rule -150)
Form of Utilization Certificate up to the Month of OCT-2020
PIU:- Executive Engineer RWD Works Division, Marhaura

SL No	Name of Scheme	Sanction No& Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 (New Maintenance Policy-2018)	सचिव ब्राडा के पत्रांक-66 (अनु0) दिनांक-15-09-20	1474.11005	Certified that out of Rs- 1474.11005 Lacs received during the Years, 2018-19 & 2019-20, 2020-21 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 1466.22688 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-7.88317 Lacs remaining unutilized at CFMS the end of the period under report.

29/10/20
Division Accounts Officer
Rural Work Department
Work Division, Marhaura

29/10/20
Executive Engineer
R.W.D. (W) Division Marhaura
29/10/20

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Length (In Km.)	Administrative Approval (AA) Amount of (In Lakh)	Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
							Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 Marhaura/18	L043- MANGURAHAN TO2 TO PILKHI PATH	31306402039	Lt. No-3074 Dt-17-07-19	3.100	102.29300	69.61024	25.93663	07/MR- 3054/MBD /2020-21	25-02-2021	23-10-2020	1431.53	25 mm	5%	0.00000	66.20839	66.20839	Work Completed
2	MR-N/19-20 Marhaura/18	SIRUKAL TO BISHUNPURA PATH	31306402075	Lt. No-3074 Dt-17-07-19	5.415	178.09400	119.22906	47.40333	07/MR- 3054/MBD /2020-21	25-02-2021	29-10-2020	2041.84	25 mm	5%	0.00000	113.01783	113.01783	Work Completed
Total:-																		179.22622

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.


2. Up-to-date Physical Progress has been Uploaded in MIS.

Executive Engineer

Rural Work Department

Work Division, Marhaura

29/11/2020

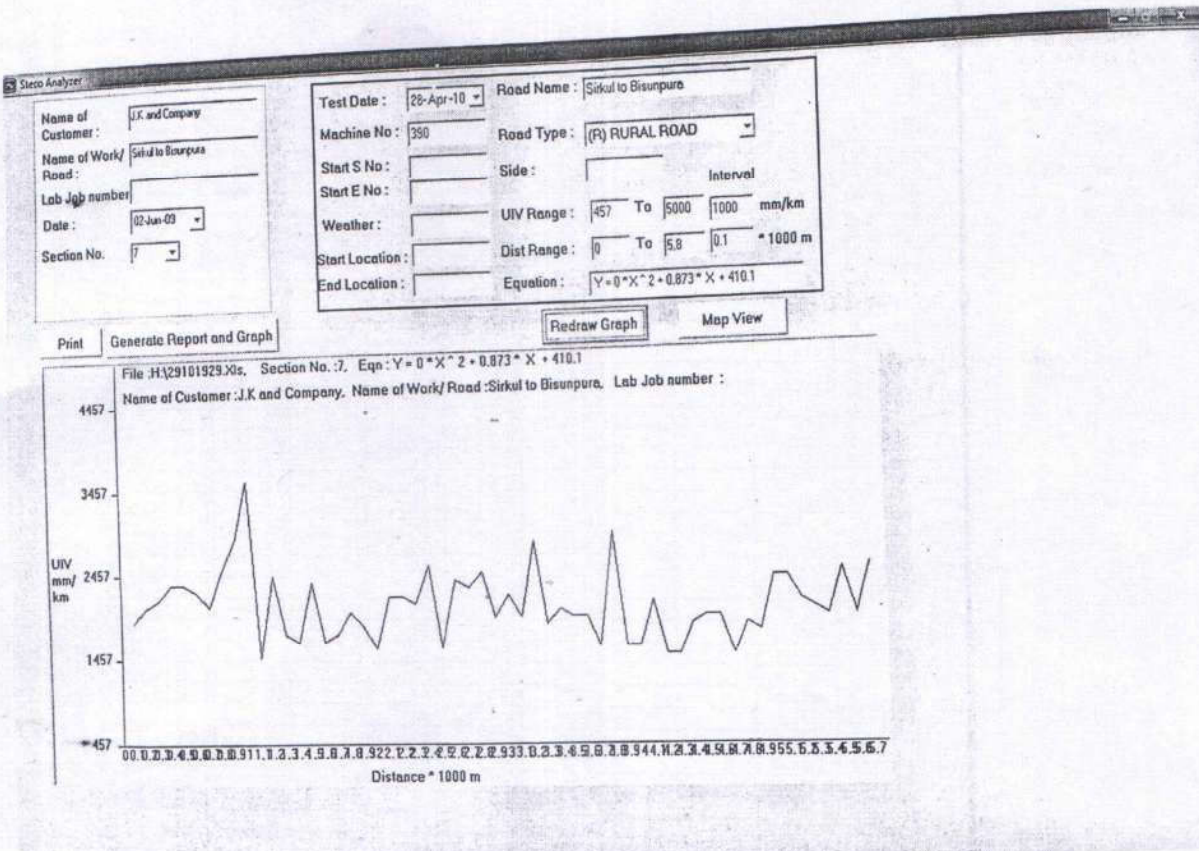

m/29/10/10

कांग्रपालक अभियन्ता
 ग्रा० कार्य वि० कार्य प्रमण्डल
 मदीरा, गरण

Road Name :- Sirkul se Bisunpura

Date Time Section Length Bumps Speed OR IRI (CATEGORY)

Latitude Longitude Event

$$Y = 0 * X^2 + 0.873 * X + 410.1$$

No.		in km	in mm	Rate	mm/km	mm/km	ROAD					
29/10/20	15:21:23	7	0.1	170	0	1700	1894	G		26.10287	84.74749	Normal
29/10/20	15:22:0	7	0.1	190	10.1	1900	2068	G		26.10374	84.747	Curve
29/10/20	15:22:0	7	0.1	200	20.2	2000	2156	G		26.10447	84.74658	Normal
29/10/20	15:22:34	7	0.1	220	20.2	2200	2330	G		26.10533	84.7464	Curve
29/10/20	15:22:34	7	0.1	220	20.2	2200	2330	G		26.10613	84.74672	Normal
29/10/20	15:23:8	7	0.1	210	20.2	2100	2243	G		26.10682	84.74737	Normal
29/10/20	15:23:8	7	0.1	190	20.2	1900	2068	G		26.10752	84.74768	Curve
29/10/20	15:23:43	7	0.1	240	10.1	2400	2505	G		26.10831	84.74808	Normal
29/10/20	15:24:0	7	0.1	280	10.1	2800	2854	G		26.10918	84.74835	Speed Breaker
29/10/20	15:24:19	7	0.1	360	20.2	3600	3552	G		26.11001	84.74862	Normal
29/10/20	15:24:19	7	0.1	120	30.3	1200	1457	G		26.11041	84.74884	Culvert
29/10/20	15:25:0	7	0.1	230	10.1	2300	2418	G		26.11076	84.74806	Normal
29/10/20	15:25:0	7	0.1	150	20.2	1500	1719	G		26.11113	84.74719	Normal
29/10/20	15:25:29	7	0.1	140	20.2	1400	1632	G		26.11114	84.74625	Normal
29/10/20	15:25:29	7	0.1	220	10.1	2200	2330	G		26.11179	84.74539	Normal
29/10/20	15:26:4	7	0.1	140	10.1	1400	1632	G		26.11264	84.74508	Normal
29/10/20	15:26:40	7	0.1	150	10.1	1500	1719	G		26.11314	84.74471	Curve
29/10/20	15:27:0	7	0.1	180	10.1	1800	1981	G		26.1136	84.74391	Culvert
29/10/20	15:27:15	7	0.1	160	10.1	1600	1806	G		26.11379	84.743	Normal
29/10/20	15:27:15	7	0.1	130	10.1	1300	1545	G		26.11399	84.74204	Normal
29/10/20	15:28:0	7	0.1	200	10.1	2000	2156	G		26.1144	84.7412	Normal
29/10/20	15:28:0	7	0.1	200	10.1	2000	2156	G		26.11471	84.74029	Normal
29/10/20	15:28:25	7	0.1	190	10.1	1900	2068	G		26.11471	84.74029	Normal
29/10/20	15:29:1	7	0.1	240	10.1	2400	2505	G		26.11519	84.73948	Speed Breaker
29/10/20	15:29:1	7	0.1	130	30.3	1300	1545	G		26.11562	84.7386	Curve
29/10/20	15:29:36	7	0.1	220	10.1	2200	2330	G		26.1159	84.73832	Curve
29/10/20	15:29:36	7	0.1	210	10.1	2100	2243	G		26.11671	84.73828	Normal
29/10/20	15:30:11	7	0.1	230	10.1	2300	2418	G		26.1175	84.73808	Curve
29/10/20	15:30:11	7	0.1	170	10.1	1700	1894	G		26.11825	84.73744	Curve
29/10/20	15:31:0	7	0.1	200	10.1	2000	2156	G		26.11881	84.73714	Curve
29/10/20	15:31:22	7	0.1	170	10.1	1700	1894	G		26.11917	84.73635	Normal
29/10/20	15:31:22	7	0.1	270	10.1	2700	2767	G		26.11927	84.73537	Normal
29/10/20	15:32:0	7	0.1	160	10.1	1600	1806	G		26.11925	84.73438	Normal
29/10/20	15:32:32	7	0.1	180	10.1	1800	1981	G		26.11875	84.73357	Normal
29/10/20	15:32:32	7	0.1	170	10.1	1700	1894	G		26.11828	84.73279	Normal
29/10/20	15:33:8	7	0.1	170	10.1	1700	1894	G		26.11774	84.73202	Normal
										26.1173	84.7312	Curve

$$X = 2209$$


$$Y = 2338$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

कांतापालक अभियन्ता
ग्रा० कार्य वि० कार्य प्रशा. वि०
मदौरा हरण

29/10/20	15:33:8	7	0.1	130	10.1	1300	1545	G		26.1176	84.73032	Normal
29/10/20	15:34:0	7	0.1	280	10.1	2800	2854	G		26.11761	84.72934	Curve
29/10/20	15:34:18	7	0.1	130	10.1	1300	1545	G		26.11719	84.72847	Normal
29/10/20	15:34:18	7	0.1	130	10.1	1300	1545	G		26.11675	84.72763	Curve
29/10/20	15:35:0	7	0.1	190	10.1	1900	2068	G		26.11626	84.72778	Curve
29/10/20	15:35:0	7	0.1	120	10.1	1200	1457	G		26.11555	84.72818	Normal
29/10/20	15:35:29	7	0.1	120	10.1	1200	1457	G		26.11495	84.72884	Normal
29/10/20	15:36:4	7	0.1	160	10.1	1600	1806	G		26.11429	84.72951	Curve
29/10/20	15:36:4	7	0.1	170	10.1	1700	1894	G		26.11365	84.73019	Normal
29/10/20	15:36:39	7	0.1	170	10.1	1700	1894	G		26.11312	84.73093	Culvert
29/10/20	15:37:0	7	0.1	120	10.1	1200	1457	G		26.1127	84.7318	Curve
29/10/20	15:37:15	7	0.1	160	10.1	1600	1806	G		26.11189	84.73222	Normal
29/10/20	15:37:50	7	0.1	150	20.2	1500	1719	G		26.11118	84.73256	Normal
29/10/20	15:38:0	7	0.1	220	10.1	2200	2330	G		26.11044	84.73306	Normal
29/10/20	15:38:25	7	0.1	220	10.1	2200	2330	G		26.10965	84.73352	Curve
29/10/20	15:39:1	7	0.1	190	10.1	1900	2068	G		26.10879	84.7335	Normal
29/10/20	15:39:1	7	0.1	180	10.1	1800	1981	G		26.10791	84.73	Normal
29/10/20	15:39:36	7	0.1	170	10.1	1700	1894	G		26.10711	84.73306	Normal
29/10/20	15:40:11	7	0.1	230	10.1	2300	2418	G		26.10622	84.73288	Curve
29/10/20	15:40:11	7	0.1	170	10.1	1700	1894	G		26.10543	84.73318	Normal
29/10/20	15:41:0	7	0.076	180	10.1	2368	2477	G		26.10499	84.73375	Normal


 कार्यपालक अभियन्ता
 प्रा० कार्य वि० कार्य प्रम-७७
 मढौरा गरण

Name of work—
 Situation of work—
 Agency by which work is executed—
 Date of measurement—
 No. and date of agreement.
 (These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
IS+ on A/c Bill.					
Name of work -	M/R to Serkaub to				
	Paishunpora path				
Agency.	M/s T.K. and company				
	vill - Karm Kudarkh,				
	P.O. Dumarisen Bhangra				
	P.S. Malsakh, Dist Sargu				
Ag No.	/MR-3054/MBD/2020-21				
Const cost -	1, 19, 22 906 = rs				
Date of start -	26-05-2020				
Date of completion -	25-02-2021				

Details of measurement.					
(+)	Clearing and grubbing				
	road land.				
	2x10x	30Mx	1.0	=	600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓
	2x	10x	30Mx	1.0	= 600M ² ✓

Continuation

[illegible]

ABSTRACT OF COST

(Est en W.C. Bu)

$$\left(\frac{1}{T}\right)$$

clearing anal

grubbing road land

Alg. Mat. TMBP. 02

1.08 Hec. @ 49496.70/Hec. = 53456 = 10

$$\left(\frac{2}{3}\right)$$

Construction of granular

Subsided with well

graded material table

(4vo. 1)

olympics P. 04

112.259

$$112.25 \text{ m}^3 @ 2392.08 / \text{m}^3 \quad 268533 = \infty$$
$$\left(\frac{3}{4}\right)$$

W.B.M. Grade - 2

p/v laying spreading

Continuation

Continuation

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(13) (13)	Direction of place identification sign				
	note TMB	P- 14			
	1.92 M ²	Cts 12384.75/m ²			23779 =
(14) (14)	Retro-reflectorised Traffic sign				
	note TMB	P- 14			
32 Nos	Cts 3679.31 Each				117738 =
(15) (15)	600 mm encircler				
	note TMB	P- 15			
8 Nos	Cts 3778.66 Each				30220 =
(16) (16)	600 mm x 450 mm rectangle				
13 Nos	Cts 3649.54 Each				47444 =
(17) (17)	Boundary pillar / Guard pillar				
	note TMB	P- 15			
48 Nos	Cts 510.91 Each				24524 =
(18) (18)	printing new letters and figures of any shape				
	note TMB	P- 15			
352 Nos	Cts 0.51 each				180 =
(19) (19)	planting of tree and their maintenance				
	note TMB	P- 15			
271 Nos	Cts 800.30 Each				216881 =

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(20) (20)	Road marking with				
	Hot applied Thermoplastic				
	note TMB P- 15				
1083 M ²	Rate 735.40/M ²				796438 =
(21) (21)	Placing and fixing of				
	logs of maintenance				
	project -				
	note TMB P- 15				
4 Nos	Rate 9386.95 Each -				37548 =
(22) (22)	Brick masonry in				
	cm(1:3) in parallel -				
	note TMB P- 15				

11.52 M ³	Rate 5102.55/M ³	58781=00
(23) (23)	plastering with cement mortar (1:4)	
	Note TMB P- 15	
80.64 M ²	Rate 150.50/M ²	12136=00
(24) (24)	painting two coats on new concrete surface	
	Note TMB P- 16	
234.24 M ²	Rate 95.63/M ²	22400=00
		<u>1000/579 = 0</u>
	11. Labour	1000/5 = 00
	12. GST	1200/89 = 00
	GT	<u>11301783 = 00</u>
	29.10.20	
		IN

Continuation

WP
29.10.20
