

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

पत्रांक :- 1312-21/मुज0,

दिनांक :- 15/09/20

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम।

सेवा में,
नोडल पदाधिकारी,
नई अनुरक्षण नीति-2018 (3054),
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- शीर्ष नई अनुरक्षण नीति-2018 (MR) अन्तर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषयक शीर्ष नई अनुरक्षण नीति-2018 (MR) अन्तर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन संलग्न विवरणी के अनुसार रु0 56.56390 (छप्पन लाख छप्पन हजार तीन सौ नब्बे) रुपये मात्र का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि किये गये कार्य का भुगतान किया जा सके।

अनुलग्नक- 1. विहित प्रपत्र में अधियाचना।

विश्वासभाजन

15/09/20

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur West																		
S.N.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	MR-N/19-20 Muzaffarpur West/14	Daudpur PWD Road To Bhajapatti		06 07 2019	2.840	92.0900	55.36100	23.86373	203MBD/2 019-20	27 09 2020	SDBC Complete	0.000	25mm	5.00	0.00000	0.00000	49.96433	MB Copy Attached
2	MR-N/19-20 Muzaffarpur West/19	house of Sri Bindeshwan Singh Teacher (Before Rly Gumti) to NH-28 Via School and Yadav Tola	31507201043	06 07 2019	3.050	72.0900	40.20800	23.2952	161MBD/2 019-20	27 09 2020	Work Complete	4000.000	25mm	5.00	38.00000	38.00000	1.31557	MB Copy Attached
3	MR-N/19-20 Muzaffarpur West/19	Madhuban Gram Ka PWD Path To via Kameshwar Pandey ka Ghar Hote Hue Kalwan Chai Tak	31507203013	06 07 2019	1.800	96.69000	30.45400	12.88233	161MBD/2 019-20	27 09 2020	Work Complete	2640.000	25mm	5.00	29.00000	29.00000	1.16126	MB Copy Attached
4	MR-N/19-20 Muzaffarpur West/19	Barka Gawan Shine PMGSY Sadak me Bangal Pati Shine More To Singar Sadak Helth Center	31507301002	06 07 2019	1.300	66.17000	19.13000	10.13637	161MBD/2 019-20	27 09 2020	Work Complete	1239.000	25mm	5.00	18.00000	18.00000	0.89895	MB Copy Attached
5	MR-N/19-20 Muzaffarpur West/20	PWD To Sonbarsa	31507202240	06 07 2019	1.740	53.53400	29.22900	12.91609	160MBD/2 019-20	12 09 2020	Work Complete	2275.000	25mm	5.00	28.50000	28.50000	0.01385	MB Copy Attached
6	MR-N/19-20 Muzaffarpur West/20	Kanti San Road To Bahura	31507202150	06 07 2019	1.390	70.15600	21.06800	10.41972	160MBD/2 019-20	12 09 2020	Work Complete	1759.000	25mm	5.00	18.00000	18.00000	1.36861	MB Copy Attached
7	MR-N/19-20 Muzaffarpur West/20	NH-28 To Akuraha Khargi via Kishunnaagar Ganj Cold Storage	31507202212	06 07 2019	2.030	53.11000	28.25100	15.40944	160MBD/2 019-20	12 09 2020	Work Complete	1495.000	25mm	5.00	26.00000	26.00000	0.59837	MB Copy Attached
8	MR-N/19-20 Muzaffarpur West/21	Harchanda Path To Bahua Chowk Via Bhariyahi Salona Village	31507201012	06 07 2019	2.810	84.18300	53.65300	21.89039	162MBD/2 019-20	27 09 2020	Work Complete	1113.000	25mm	5.00	50.00000	50.00000	0.35291	MB Copy Attached
9	MR-N/19-20 Muzaffarpur West/21	Handaspur Aarapur Mukhya Mantri Sadak To Mann Lahladpur	31507301023	06 07 2019	4.000	112.370	71.42500	28.77208	162MBD/2 019-20	27 09 2020	Work Complete	1563.000	25mm	5.00	69.00000	69.00000	0.88945	MB Copy Attached
															276.50000	276.50000	56.56390	

Executive Engineer
 RWD Works Division
 Muzaffarpur West

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
N/A: - Construction of Road from Barua Gopin shine p.m.s.y sadar me Bangal patti shine more to Singar health centre M/R-N/19-20 muz. west/19					
Name of Agency: - Anandh milita construction pvt Ltd Baranagar motipur muzafarpur					
Agreement No - 16/MAD/2019-20					
Date of work order: - 28-12-2019					
Date of completion: - 27-09-2020					
Actual date of completion: - 24-08-2020					
Measurement - 1.51					
ABSTRACT OF COST					
(1/29) clearing and grubbing road land including uprooting cu.ft. - do - do comp vide TMB page NO-06 0.260 ha @ 49496.90 = 12869.00					
(2/29) WBM Gr-3 providing & laying spreading & compacting stone agg regates - do - do comp vide TMB page NO-06 17.0870 @ 3374.48 = 57636.00					
Total = 70505.00					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					B.F = 1847967.00
(19/45) plastering with cement mortar (1:4) 15mm thick on B/C - - do - - do comp					
vide TMB page no - 16					
					40.32 m ² @ 169.46 = 6833.00
(20/46) painting two coats including primer coat after filling with surface - - do - - do comp					
vide TMB page no - 16					
					40.32 m ² @ 86.94 = 3504.00
					Total = 1858304.00
Add 1% labour & cess Rs					(+) 18583.00
Add 12% GST - Rs					(+) 222996.00
					Hence Total Rs = 2099883.00
					Less 10% below as per Agmt = (-) 209988.00
					Total Rs = 1889895.00
Less previous payment					
TMB page no - 118 22					
					1459338 + 340662 = (-) 1800000.00
					Hence To be pay Rs = 89895.00
					Anyamale 57-09-2020 JE

Name of Road :- Barka Gawan Shine PMGSY Sadak me Bangal Patti Shine More To Singar Sadak Health Center

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY ROAD	IRI	Latitude	ongitude	Event
13/5/20	16:11:0	16	0.1	160	0	1600	1568 G	2.26	26.18263	85.22123	Normal
13/5/20	16:11:17	16	0.1	90	20.2	900	876 G	1.34	26.18241	85.22221	Normal
13/5/20	16:11:17	16	0.1	130	20.2	1300	1272 G	1.87	26.18218	85.22318	Normal
13/5/20	16:12:0	16	0.1	170	20.2	1700	1667 G	2.38	26.18192	85.22414	Normal
13/5/20	16:12:0	16	0.1	130	20.2	1300	1272 G	1.87	26.18168	85.22508	Normal
13/5/20	16:12:27	16	0.1	160	20.2	1600	1568 G	2.26	26.18157	85.22606	Normal
13/5/20	16:12:27	16	0.1	150	20.2	1500	1469 G	2.13	26.1815	85.22704	Normal
13/5/20	16:13:1	16	0.1	200	10.1	2000	1964 G	2.76	26.18161	85.22798	Normal
13/5/20	16:13:1	16	0.1	150	20.2	1500	1469 G	2.13	26.18195	85.22882	Normal
13/5/20	16:13:37	16	0.1	120	20.2	1200	1173 G	1.74	26.18171	85.22956	Curve
13/5/20	16:14:0	16	0.1	110	20.2	1100	1074 G	1.61	26.18189	85.23044	Normal
13/5/20	16:14:12	16	0.1	90	20.2	900	876 G	1.34	26.18169	85.23143	Normal
13/5/20	16:14:12	16	0.1	80	20.2	800	777 G	1.21	26.1814	85.23239	Normal
13/5/20	16:14:47	16	0.1	160	10.1	1600	1568 G	2.26	26.18046	85.23237	Normal
13/5/20	16:14:47	16	0	0	181.8	0	-14 G	2.26	26.18045	85.23237	Normal
AVG :-								1239			


(R) RURAL ROAD
Good <4000
Average 4001-5000
Poor >5001

$$Y = 0 * X^2 + 0.989 * X - 13.59$$

X = 0
Y = -14

13/5/20

File : E:\Software\Bump Indicator Software\Reports\14.05.2020\13051616.Xls, Section No. : 16, Eqn : $Y = 0 * X^2 +$
 Name of Customer : Shree Awadh Mithila, Name of Work/ Road : Barka Gawan Shine PMGSY Sadak me Bangal Patti

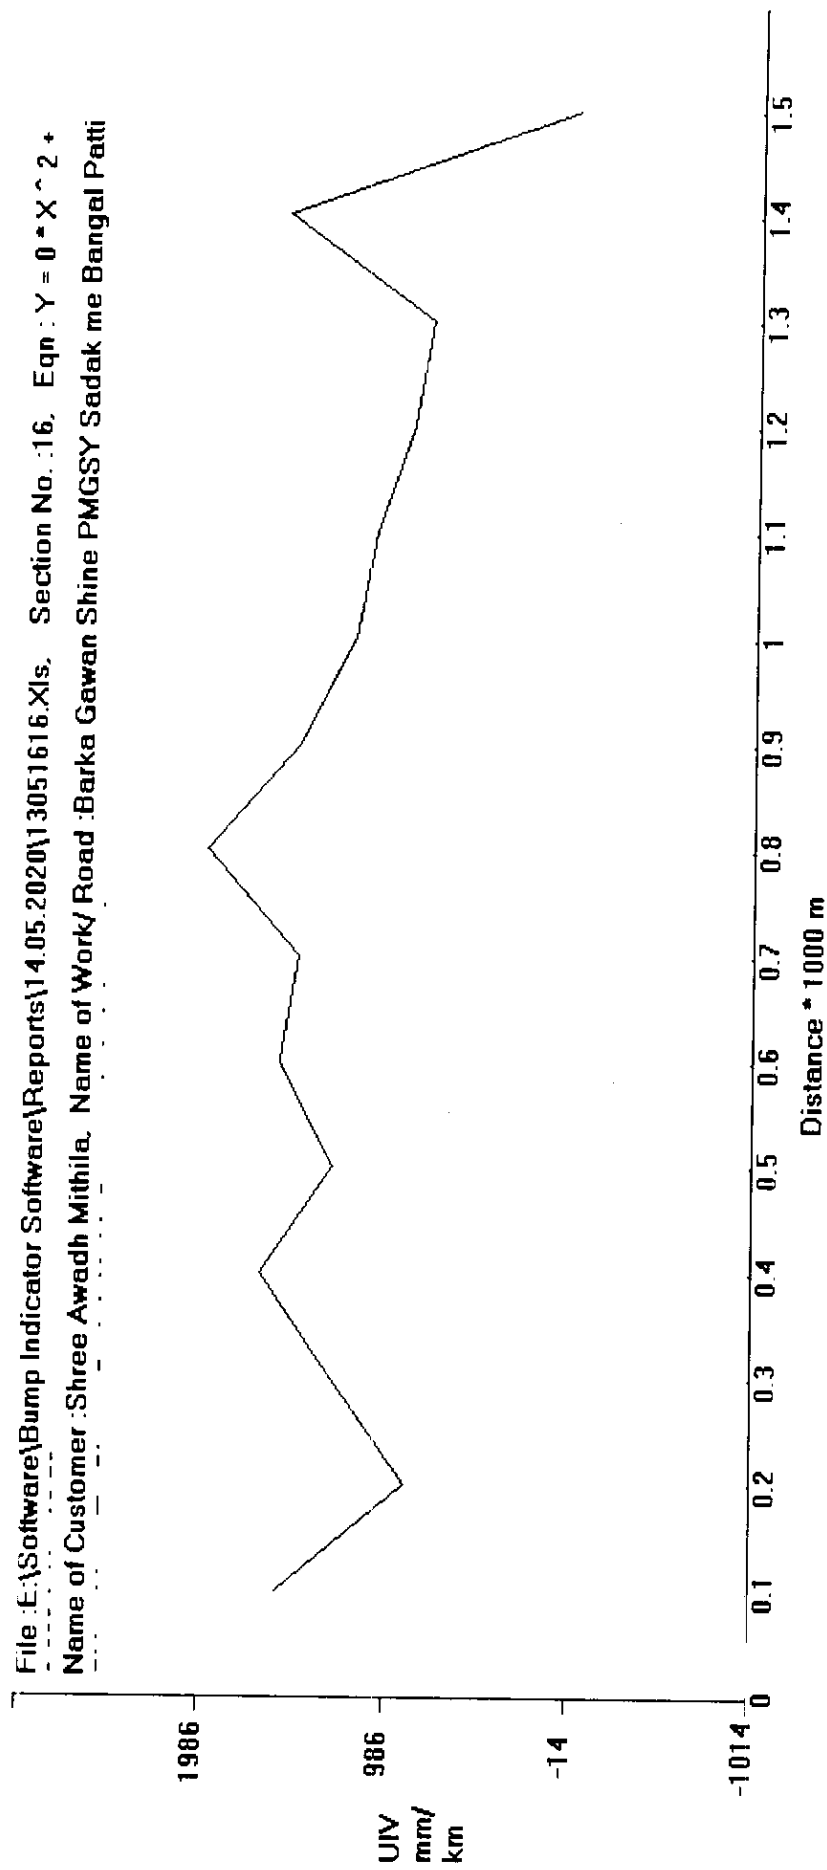

Signature
