

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सिवान-2

पत्रांक...1276..... सिवान, दिनांक...12-8-21.....

प्रेषक,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सिवान-2

सेवा में,
सचिव-सह-प्राधिकृत पदाधिकारी
बिहार ग्रामीण पथ विकास एजेन्सी
भूमि विकास बैंक भवन
बुद्ध मार्ग, पटना।

विषय:- योजना शीर्ष नई अनुरक्षण निति 2018 MR/3054 अन्तर्गत पथों में मरम्मत हेतु
अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के आलोक में कहना है कि योजना शीर्ष नई अनुरक्षण
निति 2018 MR/3054 अन्तर्गत संलग्न विहित प्रपत्र में 177.05420 लाख (एक करोड सतहतर
लाख पाँच हजार चार सौ बीस) रुपये मात्र आवंटन देने की कृपा की जाय।

अनु0-अधियाचना पत्र, Bump Integrator Equipment Report की छाया प्रति,
एकरारनामा की छाया प्रति,

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
सिवान-2
12.8.21

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- RWD, WORKS DIVISION, SIWAN-2																		
S.N.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance Maint. (in Lakh)										
1	MR-N/19-20 Siwan-2/02	Guthani to Sohagra	31406708029	1877/24.06.2019	11.00	454.1160	284.94236	94.81598	139MBD/19-20 16.01.20	30.12.2020	30.12.2020	Good	25 mm	5.031	273.325	273.325	0	Complete
2		Guthani Darauli Salarao Road to Harpur	31406701003	1877/24.06.2019	2.800	94.5320	58.00427	21.17897	139MBD/19-20 16.01.20	30.12.2020	30.12.2020	Good	25 mm	5.038	40.855	40.855	0	Complete
3		Sohagra Road to Bakulari	31406701006	1877/24.06.2019	1.70	59.8580	36.12334	13.84236	139MBD/19-20 16.01.20	30.12.2020	30.12.2020	Good	25 mm	5.037	36.12334	36.12334	0	Complete
4	MR-N/19-20 Siwan-2/01	Makarwar to Anoni Path	31406701019	1877/24.06.2019	1.800	62.4230	38.17403	14.14724	141MBD/19-20 15.02.20	31.12.19	30.12.2020	Good	25 mm	5.036	34.03423	34.03423	0	Complete
5		PWD Road to Bisawaniya	220001242	1877/24.06.2019	4.40	155.6160	94.14988	36.41117	141MBD/19-20 15.02.20	31.12.19	30.12.2020	Good	25 mm	5.032	93.90567	93.90567	0	Complete
6		Aasawa to kampakar path	31406701011	1877/24.06.2019	4.500	155.7750	94.46653	35.81914	141MBD/19-20 15.02.20	31.12.19	30.12.2020	Good	25mm	5.031	93.17	93.16954	0.00	Complete
7		CMDG PWD Road to Pihuli	31406701002	1877/24.06.2019	2.500	87.4850	52.32609	21.10208	141MBD/19-20 15.02.20	31.12.19	30.12.2020	Good	25mm	5.032	52.05	52.06	0.00	Complete
8	MR-N/19-20 Siwan-2/05	PWD Marera - Garwar	31406602034	1877/24.06.2019	5.200	179.1250	109.46012	40.5255	141MBD/19-20 15.02.20	31.12.19	30.12.2020	Good	25mm	5.036	108.46	108.46476	0.00	Complete
9		T02 Sarai Via Safi Tola to Amarpur	31406702047	5139/24.09.2019	3.20	111.2009	65.47033	32.86766	105MBD/20-21 17.09.20	16.06.21	30.12.2020	0.00	0	0.000	0.00	0.00	0	
10		PWD Path Se Tarwan Taruwani	31406602033	5139/24.09.2019	3.90	135.8480	80.10775	40.04263	105MBD/20-21 17.09.20	16.06.21	01.11.2020	Good	25 mm	5.031	79.14848	79.14848	0	Complete
11		CMDG Road to Bishwaniya Via Balhu	314671033666	6132/20.11.2019	7.00	254.6024	155.25400	69.47072	105MBD/20-21 17.09.20	16.06.21	30.12.2020	0.00	0	0.000	0.00	0.00	0	
12	MR-N/19-20 Siwan-2/10	Babhanauli to Bargawa Tak Via Kathauliya	31406602016	5139/24.09.2019	6.10	205.2256	125.29266	60.69045	104MBD/20-21 17.09.20	16.06.21	30.12.2020	Good	25 mm	5.031	124.40	124.41	0.00	Complete
13		L026 to Nautan to Kurnauta (VR10)	31406702033	5139/24.09.2019	2.50	84.4215	51.33843	25.15108	104MBD/20-21 17.09.20	30.12.2020	01.11.2020	Good	25 mm	5.034	50.8059	50.8059	0	Complete

OR

14	MR-N/19-20 Siwan-2/03	Akolohi to Valuhi Via Sishani	31406701001	1877/24.06.2019	3.30	104.8720	64.0953	23.79127	140MBD/19-20 15.02.20	14.11.2020	30.11.2020	0.00	0	0	0.00	0.00	0	
15		Guthani Balua to Mamur Path	31406701014	1877/24.06.2019	2.50	82.9270	51.4269	17.9899	140MBD/19-20 15.02.20	14.11.2020	09.11.2020	Good	25 mm	5.034	51.41	51.41	0.00	Complete
16		Guthani Darauli Road to Damodara	31406701004	1877/24.06.2019	1.46	48.5180	29.0178	11.53854	140MBD/19-20 15.02.20	14.11.2020	30.11.2020	Good	25 mm	5.033	26.6948	26.6948	0	Complete
17		Guthani Mairwa (Takaniya) to Chavariya Path	31406701015	1877/24.06.2019	2.50	80.4920	49.581	17.73496	140MBD/19-20 15.02.20	14.11.2020	30.11.2020	Good	25 mm	5.032	49.32	49.32	0.00	Complete
18		Guthani Nainjore Via Sematar Chilmara	31406701005	1877/24.06.2019	1.40	55.3266	28.7748	21.02097	140MBD/19-20 15.02.20	14.11.2020	06.11.2020	Good	25 mm	5.032	28.77226	28.77226	0	Complete
19		Guthani Mairwa Path to Kolharua to Bhagwanpur via Baheliya	31406701023	1877/24.06.2019	2.40	82.5300	50.2353	18.88126	140MBD/19-20 15.02.20	14.11.2020	06.11.2020	Good	25 mm	5.031	47.0038	47.0038	0	Complete
20	MR-N/19-20 Siwan-2/12	Harpur to Bikaur	31406602023	5139/24.09.2019	5.90	196.7360	123.665	18.21068	142 MBD 2020-21 24.09.20	22.06.21	16.02.2021	Good	25 mm	5.032	63.25061	109.4058	0	Complete
21		Maniya to Santhu	31406602024	5139/24.09.2019	5.30	148.0130	0	0	142 MBD 2020-21 24.09.20	22.06.21		Good	25 mm	0.000	0	0	0	Complete
22		T05 to Repura	31406702037	5139/24.09.2019	1.30	42.3709	0	0	142 MBD 2020-21 24.09.20	22.06.21		Good	25 mm	0.000	0	0	0	Complete
23	MR-N/19-20 Siwan-2/04	Andar Pari Via Kathwar More	314671033668	6132/20.11.2019	10.10	353.3995	217.79937	97.79881	98 MBD 2020-21 15.09.20	14.06.21	03.06.2021	Good	25 mm	5.038	0	145.9809	0	Complete
24		Katware To Sahasrao	314671033669	6132/20.11.2019	3.200	114.6904	70.63089	31.73409	98 MBD 2020-21 15.09.20	14.06.21	06.04.2021	Good	25 mm	5.031	70.50399	70.50399	0	Complete
25	MR-N/19-20 Siwan-2/13	Jurkan to Chapiya Tak	31406702028	661/10.02.2020	2.80	85.0828	50.72727	25.23595	153MBD 2020-21 10.12.20	10.06.21	03.06.2021	Good	25 mm	5.032	0.00	50.46837	50.46837	Complete
26		Habibnagar to Gangauli Tak	NEA220001393	661/10.02.2020	6.40	215.0490	127.09373	65.04209	153MBD 2020-21 10.12.20	10.06.21	01.06.2021	Good	25 mm	5.036	0.00	126.58583	126.58583	Complete
27		T02 SH to Dhumnagar Tak	314671033879	661/10.02.2020	1.500	81.5530	56.54297	5.47467	153MBD 2020-21 10.12.20	10.06.21	0	0.00	0	0.000	0.00	0	0	
													1323.2476	1692.44218	177.05420			

प्रमुख कार्य विभाग, कार्य प्रबंधक,
सिवान-2

Executive Engineer
RWD Works Division
Siwan-2
13/08/21
17.8.21

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate up to 12th August 2021
NEW MAINTENANCE POLICY (2018)

Sl.No	Name of Scheme	Sanction No.& Date with Amount, (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural roads under NEW MAINTENANCE POLICY (2018)	24/19.03.2020 59/18.08.2020 78/29.10.2020 82/13.11.2020 86/11.12.2020 05/12.01.2021 17/26.02.2021 20/19.03.2021 26/15.04.2021	309.44834 40.85500 127.93990 129.95438 140.17554 246.86987 257.50061 46.15519 70.50399	Certified that out of Rs 1111.90221 lacs received during the years 2021-22 in favour of Ex. Engineer, RWD, Works Division, siwan-2 Bihar, a sum of Rs 1065.74702 Lacs has been utilized for the purpose of NEW MAINTENANCE POLICY-2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs 46.15519 lacs remaining unutilized at the end of the period under.
Total :			1111.90221	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

3. **Physical Progress achieved :-**

- Construction of Road works.
- Construction of CD works.

DAO

RWD, WORKS DIVISION
SIWAN-2

EXECUTIVE ENGINEER
RWD, WORKS DIVISION

B.K. SIWAN-2
12/08/21 12-8-21

Road name:- Habib nagar to Gangauly tak

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	ongitude	Event
7/8/21	12:0:7	45	0.1	220	0	2200	2330	G	26.18276	84.31626	Normal
7/8/21	12:0:43	45	0.1	100	20.2	1000	1283	G	26.18317	84.31441	Normal
7/8/21	12:1:18	45	0.1	50	10.1	500	846	G	26.18364	84.31251	Normal
7/8/21	12:1:53	45	0.1	260	10.1	2600	2679	G	26.18345	84.31168	Normal
7/8/21	12:2:0	45	0.1	210	10.1	2100	2243	G	26.18365	84.31077	Normal
7/8/21	12:2:29	45	0.1	190	20.2	1900	2068	G	26.18377	84.30983	Normal
7/8/21	12:2:29	45	0.1	170	20.2	1700	1894	G	26.18397	84.30891	Normal
7/8/21	12:3:4	45	0.1	200	20.2	2000	2156	G	26.18415	84.30798	Normal
7/8/21	12:3:4	45	0.1	90	20.2	900	1195	G	26.18438	84.30704	Normal
7/8/21	12:3:39	45	0.1	210	10.1	2100	2243	G	26.18464	84.30608	Normal
7/8/21	12:4:0	45	0.1	140	10.1	1400	1632	G	26.18466	84.30519	Curve
7/8/21	12:4:14	45	0.1	170	10.1	1700	1894	G	26.18432	84.30451	Normal
7/8/21	12:4:14	45	0.1	230	20.2	2300	2418	G	26.1845	84.30355	Normal
7/8/21	12:5:0	45	0.1	230	20.2	2300	2418	G	26.18455	84.30259	Normal
7/8/21	12:5:0	45	0.1	260	20.2	2600	2679	G	26.18461	84.30163	Normal
7/8/21	12:5:25	45	0.1	240	10.1	2400	2505	G	26.18516	84.30111	Normal
7/8/21	12:6:0	45	0.1	190	10.1	1900	2068	G	26.18519	84.30015	Normal
7/8/21	12:6:0	45	0.1	310	10.1	3100	3116	G	26.18534	84.29928	Normal
7/8/21	12:6:36	45	0.1	240	10.1	2400	2505	G	26.18556	84.29837	Speed Breaker
7/8/21	12:7:0	45	0.1	70	30.3	700	1021	G	26.18583	84.298	Normal
7/8/21	12:7:11	45	0.1	30	20.2	300	672	G	26.1861	84.298	Normal
7/8/21	12:8:21	45	0.1	150	0	1500	1719	G	26.18694	84.29823	Normal
7/8/21	12:9:0	45	0.1	160	10.1	1600	1806	G	26.18773	84.29837	Normal
7/8/21	12:9:32	45	0.1	120	10.1	1200	1457	G	26.18861	84.2985	Normal
7/8/21	12:10:0	45	0.1	160	10.1	1600	1806	G	26.18928	84.29801	Normal
7/8/21	12:10:43	45	0.1	360	0	3600	3552	G	26.18942	84.2971	Normal
7/8/21	12:11:18	45	0.1	320	0	3200	3203	G	26.19022	84.29689	Normal
7/8/21	12:12:0	45	0.1	270	0	2700	2767	G	26.19085	84.29744	Normal
7/8/21	12:12:28	45	0.1	160	10.1	1600	1806	G	26.19164	84.29774	Normal
7/8/21	12:13:0	45	0.1	240	10.1	2400	2505	G	26.19182	84.2987	Normal
7/8/21	12:13:4	45	0.1	220	10.1	2200	2330	G	26.19183	84.29958	Curve
7/8/21	12:13:39	45	0.1	270	10.1	2700	2767	G	26.1927	84.29956	Speed Breaker
7/8/21	12:14:14	45	0.1	90	10.1	900	1195	G	26.19315	84.29894	Normal
7/8/21	12:14:50	45	0.1	110	10.1	1100	1370	G	26.19323	84.29803	Normal
7/8/21	12:15:0	45	0.1	180	10.1	1800	1981	G	26.19328	84.29709	Normal

$$Y = 0 * X^2 + 0.873 * X + 410.1$$

$$X = 2963$$

$$Y = 2996$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

7/8/21	12:15:25	45	0.1	210	10.1	2100	2243	G		26.19335	84.29611	Normal
7/8/21	12:15:25	45	0.1	70	10.1	700	1021	G		26.19367	84.29525	Normal
7/8/21	12:16:0	45	0.1	160	10.1	1600	1806	G		26.19394	84.29429	Normal
7/8/21	12:16:35	45	0.1	150	10.1	1500	1719	G		26.19441	84.29365	Normal
7/8/21	12:17:0	45	0.1	110	10.1	1100	1370	G		26.19518	84.29345	Normal
7/8/21	12:17:46	45	0.1	270	0	2700	2767	G		26.19579	84.29293	Normal
7/8/21	12:18:0	45	0.1	240	10.1	2400	2505	G		26.19649	84.29256	Normal
7/8/21	12:19:0	45	0.1	380	0	3800	3727	G		26.19733	84.29229	Normal
7/8/21	12:20:0	45	0.1	360	0	3600	3552	G		26.19788	84.29175	Normal
7/8/21	12:20:7	45	0.1	180	10.1	1800	1981	G		26.19844	84.2913	Normal
7/8/21	12:20:42	45	0.1	200	10.1	2000	2156	G		26.19923	84.29114	Normal
7/8/21	12:21:18	45	0.1	240	0	2400	2505	G		26.19965	84.29039	Normal
7/8/21	12:21:53	45	0.1	190	10.1	1900	2068	G		26.20044	84.29015	Normal
7/8/21	12:22:0	45	0.1	180	10.1	1800	1981	G		26.20068	84.28933	Normal
7/8/21	12:22:28	45	0.1	220	10.1	2200	2330	G		26.20148	84.28966	Normal
7/8/21	12:23:0	45	0.1	170	10.1	1700	1894	G		26.20232	84.28978	Normal
7/8/21	12:23:3	45	0.1	210	10.1	2100	2243	G		26.20303	84.28956	Normal
7/8/21	12:23:39	45	0.1	240	10.1	2400	2505	G		26.20337	84.28877	Normal
7/8/21	12:24:0	45	0.1	190	20.2	1900	2068	G		26.20376	84.28795	Normal
7/8/21	12:24:14	45	0.1	190	10.1	1900	2068	G		26.20452	84.28758	Normal
7/8/21	12:24:49	45	0.1	160	10.1	1600	1806	G		26.20498	84.28692	Normal
7/8/21	12:25:0	45	0.1	180	10.1	1800	1981	G		26.20587	84.287	Normal
7/8/21	12:25:25	45	0.1	290	10.1	2900	2941	G		26.2066	84.28636	Normal
7/8/21	12:26:0	45	0.1	270	10.1	2700	2767	G		26.20722	84.28655	Normal
7/8/21	12:26:0	45	0.1	210	10.1	2100	2243	G		26.20783	84.2871	Normal
7/8/21	12:26:35	45	0.1	280	20.2	2800	2854	G		26.20868	84.28734	Normal
7/8/21	12:27:10	45	0.1	210	10.1	2100	2243	G		26.20924	84.28791	Curve
7/8/21	12:27:10	45	0.1	180	10.1	1800	1981	G		26.21007	84.28805	Normal
7/8/21	12:27:10	45	0.1	200	10.1	2000	2156	G		26.21041	84.28886	Normal
7/8/21	12:28:0	45	0.1	200	10.1	2000	2156	G		26.2105	84.28907	Normal
7/8/21	12:28:0	45	0.021	30	50.5	1429	1657	G				

7/8/21
5.8

20
8/8/21
AE


Name of Customer : Balindra Chaudhary
 Name of Work/ Road : Habibnagar to Gangauly tal.
 Lab Job number :
 Date : 02-Jun-08
 Section No : 45

Test Date : 26-Apr-10 Road Name : Habibnagar to Gangauly tal.
 Machine No : 390 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : IIV Range : -32% To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 6.6 10.1 * 1000 m
 End Location : Equation : $Y = 0.000000 X^2 + 0.873000 X + 410.1$

Print Generate Report and Graph

Redraw Graph

Map View

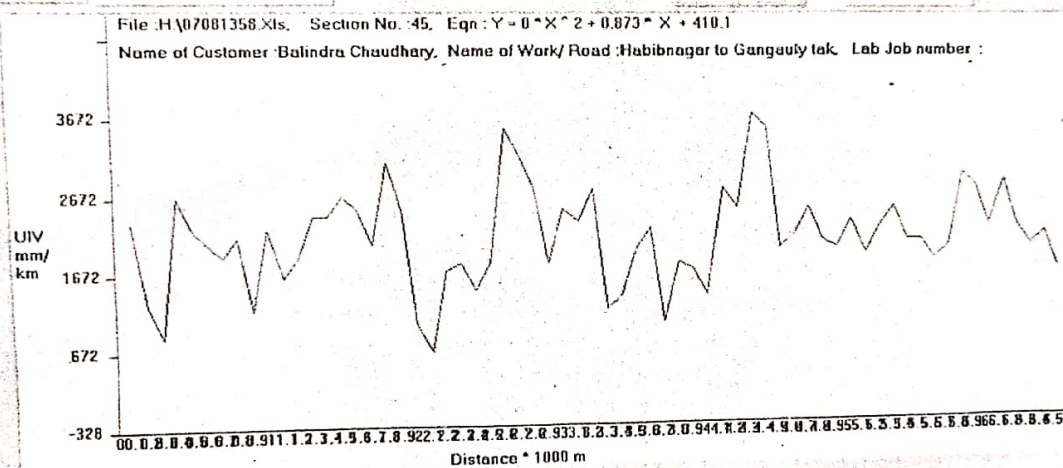

Handwritten signature
 08/08/21
 J.E

Handwritten signature
 8/8/21
 AE

भारतीय गैर न्यायिक INDIA NON JUDICIAL

एक हजार रुपये

रु.1000

ONE THOUSAND RUPEES

Rs.1000

बिहार BIHAR

2378

16-9-20 1000/-
श्री. प्र. चौधरी (110 मा. 19. 509/11)
श्री. प्र. चौधरी (110 मा. 19. 509/11)
(A) Standard Form of Agreement

Notes on Standard Form of Agreement

The Agreement should incorporate any correction or modification to the Bid resulting from corrections of errors (Instructions to Bidders, Clause 26)

Work Start Date:- 11.09.20
Work End Date:- 17.06.21

Standard Form: Agreement

(Below-4.77%)

Agreement No. 153 MBD, MR/3054 of 2020-21

This agreement, made the 10 day of 12 2020 between EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, SIWAN-2 [name and address of Employer] (hereinafter called "the Employer") of the one part, Balinder Chaudhary, VIL.- Lakhraw, Siwan. [name and address of Contractor] (hereinafter called "the Contractor" of the other part).

Whereas the Employer is desirous that the Contractor execute under MR/3054 (New Maint. Policy 2018) in Block-Hussainganj, Dist- Siwan of Const. of Road From MR-N/19-20 Siwan-2/13, (Tender ID.-93115) (BID ID- 403315) from Length of 10.700 Km and Construction Cost Rs. 23473140.00 + Maintenance Cost for Five Years Rs. 1541552.00 [name and identification number of Contract] (hereinafter called "the Works") and the Employer has accepted the Bid by the Contractor for the execution and completion of such works and the remedying of any defects therein at a cost of Rupees Total 34014692.00 (Three Corer Forty Lacs Fourteen Thousand Six Hundred Ninety Two Only).

EXECUTIVE ENGINEER
RWD, WORKS DIVISION,
SIWAN

16.12.2020

