

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, टिकारी।

पत्रांक:- 25153-नु०

/टिकारी,

दिनांक:- 14.12.21

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, टिकारी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण, पटना।


विषय- 3054/MR New Maintenance Policy-2018 अंतर्गत आवंटित राशि का उपयोगिता प्रमाण पत्र तथा आवंटन अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि इस प्रमण्डल अंतर्गत **3054/MR New Maintenance Policy-2018** अंतर्गत Nishur Pur to Chhatma पथ में चल रहे कार्यों के भुगतान हेतु उपयोगिता प्रमाण पत्र विहित प्रपत्र में संलग्न करते हुए आग्रह है कि माँग पत्र के अनुसार योजना में रुपये **1,00,18,771.00** (एक करोड़ अठारह हजार सात सौ इकहत्तर रुपये) मात्र का आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल, टिकारी।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION TEKARI.**

Requisition Format for Scheme Head:- MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Tekari																		
Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	Up to date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
MR-N/19-20 Tekari/-14		Nishur Pur to Chhatma	15221033217	LT-5546 Dt. 23.10.19	3.100	134.22100	100.18771	31.13867	42/MBD/3054/MR/2020-21	19.04.2021	-	4.1070	25 mm	5.06%	0	0	100.18771	RI का कार्य बंद
Total																	100.18771	

Amount in Word:- One Crore Eighteen Thousand Seven Hundred Seventy Only Only.

[Signature]
Sr. D.A.O.,
RWD, Works Division, Tekari

[Signature]
Executive Engineer
RWD, Works Division, Tekari

FORM GFR 19-A

(See Government of India's Decision (1) below Rule 150)
Form of Utilization Certificate up to the Month of **14-DECEMBER-2021**

S. No	Name of Scheme	Sanction No. & Date with Amount (In Rs.lacs)	Amount Received (in Rs.Lacs)	Particulars
1	Bihar Rural Roads New Maint. Policy 2018	Lt. No. 47/Encl. Dated 24.06.2020	98.21031	Certified that out of Rs. 2047.90156 Lakh received during the Financial Year 2021-22 (14-DECEMBER-21) in favour of Executive Engineer, RWD (W) Division, Tekari, Gaya, Bihar out of which a sum of Rs. 1898.85919 Lacs has been utilized for the purpose of New Maintenance Policy 2018 Under MR3054 Scheme as given in the margin for which it was sanctioned and that the balance of Rs. 149.04237 Lacs remaining unutilized at the end of the said period.
2		Lt. No. 82/Encl. Dated 13.11.2020	148.49067	
3		Lt. No. 84/Encl. Dated 26.11.2020	199.17599	
4		Lt. No. 05/Encl. Dated 12.01.2021	65.81907	
5		Lt. No. 17/Encl. Dated 26.02.2021	10.83516	
6		Lt. No. 22/Encl. Dated 24.03.2021	95.70700	
7		Lt. No. 26/Encl. Dated 15.04.2021	78.50000	
8		Lt. No. 27/Encl. Dated 15.04.2021	334.32100	
9		Lt. No. 30/Encl. Dated 21.05.2021	462.46838	
10		Lt. No. 52/Encl. Dated 24.08.2021	203.89921	
11		Lt. No. 58/Encl. Dated 27.10.2021	84.52200	
12		Lt. No. 60/Encl. Dated 09.11.2021	265.95277	
			2047.90156	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


Kind of Checks exercised :-

- Works have been supervised by Executive Engineers/Superintending Engineer.
- Periodic inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

Physical Progress achieved :-

- Construction of Road Works
- Construction of CD Works


Sr. Divisional Accounts Officer,
Rural Works Department,
Works Division, Tekari.


Executive Engineer,
Rural Works Department,
Works Division, Tekari.



बिहार BIHAR

AH 199597

Agreement

Rate Approved by C.E.-1, RWD, Bihar, Patna Letter No. 2841 (We) Dt. 24.06.2020

rate below (-) :- 0.10% (Rs. Zero Point One Zero Percent Below)

Construction Rs. 1,66,33,050.00

Maintenance Rs. 53,89,289.00

Agreement Value Rs. 2,20,22,339.00

Original copy

Executive Engineer
RWD, Works Division

Tekari, Gaya

Agreement No. ... 27/MBD/3054/MR/2020-21

42/MBD/3054/MR/2020-21

This agreement, made the ... 20th ... Day of ... July 2020 ... between Executive

Engineer, R.W.D., Works Division, Tekari. ("The E/I") of the one part, and Shreekanth

Kumar, Village- Kaudiya, Post- Iguna, PS- Konch, Gaya [Name and address of Contractor]

("The Contractor") of the other Part. Whereas the Employer is desirous that the Contractor execute Output and performance based Rural Road Contact for the Maintenance Roads MR-N/19-20 Tikari/14, [Tender 88405] (Under MR Policy-2018) Length 5.300 km. (hereinafter called "The Works") and the Employer has accepted the Bid by the contractor

for the execution of such work and the remedying of any defects therein, at a contract price of Rs. 2,20,22,339.00 (Two Crore Twenty Lakh Twenty Two Thousand Three Hundred Thirty Nine Only). The Commencement of work is ... 20.7.20 ... and Completion of date upto

one year i.e. ... 19.7.21 (9 months)

03.07.21

Executive Engineer
RWD, Works Division

Tekari, Gaya

24/7/20

Work Details					
Sl.No.	Name of Road	Length (in Km)	Construction Cost	Maintenance Cost	Total
1	Tekari Bela path Bhawanpur pul to Harna	2.200	66.14279	22.75422	88.89701
2	Nishurpur to Chhatma	3.100	100.18771	31.13867	131.32638
Total----		5.300	166.33050	53.89289	220.22339

Agreement Amounts :- 220.22339

NOW THIS AGREEMENT WITNESSETH and the Parties hereto agree as follows :

1. In this Agreement, words and expressions shall have the same meanings as are respectively assigned to them in the General conditions hereinafter referred to, and they shall be deemed to form and be read and construed as part of this Agreement.
2. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the works and remedy any defects therein in conformity in all aspects with the provisions of the Contract.
3. The Employer hereby covenants to pay the Contractor in consideration of the execution and completion of the Works and the remedying the defects wherein the Contract Price or such other sum as may become payable under the provisions of the contract at the times and in the manner prescribed by the contract.
4. The following documents shall be deemed to form and be read and construed as part of this Agreement, viz :
 - (i) Letter of Acceptance;
 - (ii) Contractor's Bid;
 - (iii) Section VI- General Conditions,
 - (iv) Section VII- Particular Conditions
 - (v) Section V- Technical Specifications, (General and Supplementary Technical Specifications)
 - (vi) Appendix A- Drawings
 - (vii) Section IV- Works Schedule
 - (viii) Quality Plan for output and Performance Based Road Contract as per Clause A14.1 of the Technical Specifications.
 - (ix) Appendices to the Contract .
 - (x) Addenda issued during bid period.

Executive Engineer
RWD, Works Division
Tekari, Gaya

सहायक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य अवर प्रमंडल, टिकारी।

पत्रांक:- ८२

दिनांक:- ०९/१२/२१


जाँच प्रतिवेदन

प्रखण्ड का नाम	योजना का नाम	पथ की लम्बाई (कि०मी०)	S.D.B.C परत की मोटाई	बिटुमिन Content की मात्रा	BUMP INTEGRATOR का Reading	अभियुक्ति
Tekari	Nishur Pur to Chhatma	3.100	25MM	5.06	Reading Attached	Satisfactory

Subd
09/12/21
VB

A-1
09/12/21
सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, टिकारी।

Name of Customer: Shreekant Kumar, Machine no: 19211, Road: Nishur Par To Chhatma, Date: 10-12-21, Section No: 1, Equation: $Y=0.931X+333$.

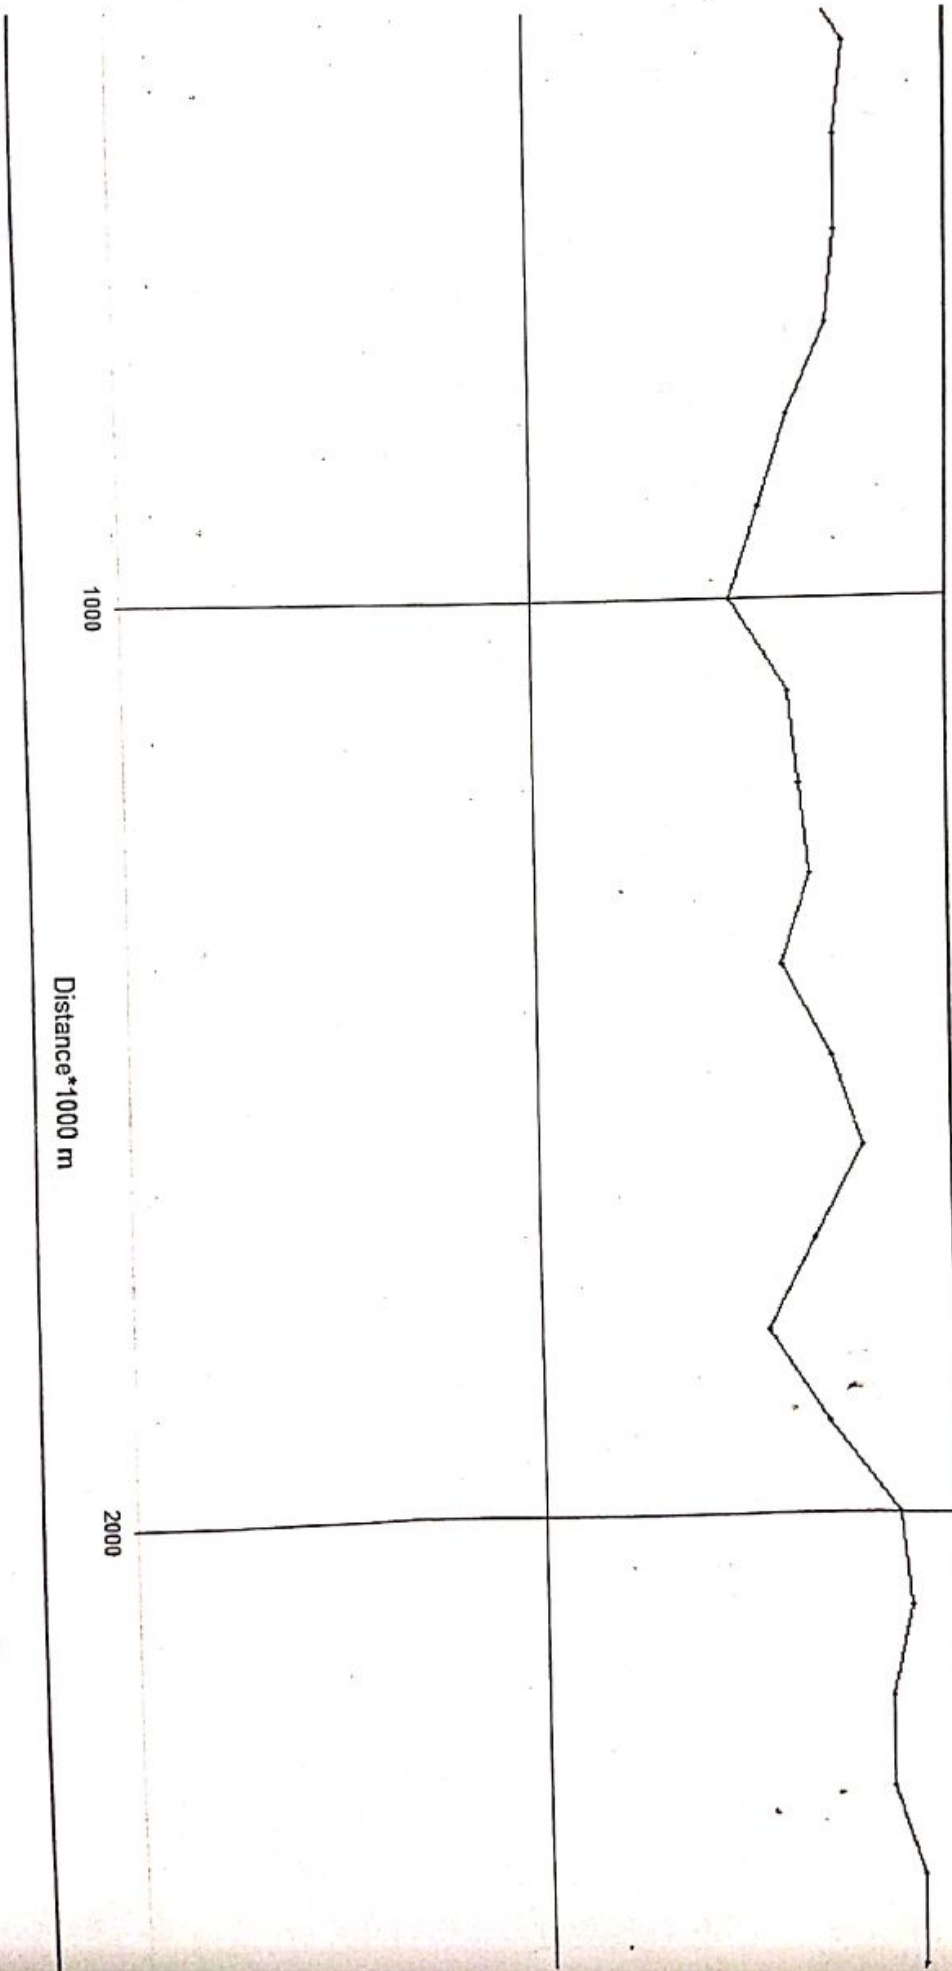

Shreekant Kumar
06/12/21
E.E

Shreekant Kumar
06/12/21
E.E

Shreekant Kumar
E.E

Name of the work: Nushur Pur to Chhatma

Name of Contractor :- Shreekant Kumar

Date	Time	Test No	Distance (meter)	Total Distance (meter)	BUMP (cm)	Speed (km/hr)	UI (mm/km)	Corrected UI (mm/km)	IRI	Status	Latitude	Direction	Longitude	Direction 1	Remark
12-09-21	15:37:37	5	100	100	29.0 cm	1.0 Km/Hr	2900.0 mm/Km	3033.5	4.069	Good	24.94228	N	84.83206	E	Normal
12-09-21	15:38:03	5	100	200	36.0 cm	13.5 Km/Hr	3600.0 mm/Km	3665.2	4.841	Good	24.94223	N	84.83096	E	Normal
12-09-21	15:38:24	5	100	300	25.0 cm	17.1 Km/Hr	2500.0 mm/Km	2661.1	3.62	Good	24.94292	N	84.8307	E	Normal
12-09-21	15:38:44	5	100	400	31.0 cm	18.5 Km/Hr	3100.0 mm/Km	3219.7	4.291	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:39:07	5	100	500	30.0 cm	15.6 Km/Hr	3000.0 mm/Km	3126.6	4.18	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:39:23	5	100	600	30.0 cm	21.3 Km/Hr	3000.0 mm/Km	3126.6	4.18	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:39:39	5	100	700	29.0 cm	22.5 Km/Hr	2900.0 mm/Km	3033.5	4.069	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:39:54	5	100	800	25.0 cm	24.4 Km/Hr	2500.0 mm/Km	2661.1	3.62	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:40:08	5	100	900	22.0 cm	26.4 Km/Hr	2200.0 mm/Km	2381.8	3.279	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:40:21	5	100	1000	19.0 cm	27.2 Km/Hr	1900.0 mm/Km	2102.5	2.933	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:40:36	5	100	1100	25.0 cm	23.9 Km/Hr	2500.0 mm/Km	2661.1	3.62	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:40:59	5	100	1200	26.0 cm	16.2 Km/Hr	2600.0 mm/Km	2754.2	3.733	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:41:14	5	100	1300	27.0 cm	22.6 Km/Hr	2700.0 mm/Km	2847.3	3.845	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:41:29	5	100	1400	24.0 cm	24.9 Km/Hr	2400.0 mm/Km	2568	3.506	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:41:45	5	100	1500	29.0 cm	22.7 Km/Hr	2900.0 mm/Km	3033.5	4.069	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:41:59	5	100	1600	32.0 cm	24.6 Km/Hr	3200.0 mm/Km	3312.8	4.402	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:42:14	5	100	1700	27.0 cm	24.1 Km/Hr	2700.0 mm/Km	2847.3	3.845	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:42:29	5	100	1800	22.0 cm	24.7 Km/Hr	2200.0 mm/Km	2381.8	3.279	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:42:43	5	100	1900	28.0 cm	25.7 Km/Hr	2800.0 mm/Km	2940.4	3.957	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:43:00	5	100	2000	35.0 cm	20.0 Km/Hr	3500.0 mm/Km	3592.1	4.732	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:43:15	5	100	2100	36.0 cm	24.5 Km/Hr	3600.0 mm/Km	3685.2	4.841	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:43:29	5	100	2200	34.0 cm	24.9 Km/Hr	3400.0 mm/Km	3499	4.622	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:43:44	5	100	2300	34.0 cm	24.6 Km/Hr	3400.0 mm/Km	3499	4.622	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:44:11	5	100	2400	37.0 cm	13.4 Km/Hr	3700.0 mm/Km	3778.3	4.95	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:44:25	5	100	2500	37.0 cm	24.7 Km/Hr	3700.0 mm/Km	3778.3	4.95	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:44:44	5	100	2600	33.0 cm	19.2 Km/Hr	3300.0 mm/Km	3405.9	4.512	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:45:01	5	100	2700	27.0 cm	21.3 Km/Hr	2700.0 mm/Km	2847.3	3.845	Good	24.94358	N	84.8307	E	Normal
12-09-21	15:45:17	5	100	2800	31.0 cm	22.0 Km/Hr	3100.0 mm/Km	3219.7	4.291	Good	24.95063	N	84.80778	E	Normal
12-09-21	15:45:34	5	100	2900	32.0 cm	21.6 Km/Hr	3200.0 mm/Km	3312.8	4.402	Good	24.95086	N	84.80684	E	Normal



SAS GROUP

LABORATORY FOR TESTING OF ALL CIVIL ENGINEERING MATERIAL & GEO-TECH

(AN ISO 9001 : 2015 & ISO/IEC 17025 :2017 CERTIFIED NABL ACCREDITED LAB)

Plot No 2503, Rambhag Estates, Gandhinagar Patilputra

Station, P.O.- Ashiyana Nagar Patna 800025



TEST REPORT

Test Report Issued To: The Assistant Engineer Rural Work Department Work Division Tekari		Report No.: 2021-FINITY/REP-0496/C-i			
		Sample Job Order No.: FINITY-JO-21-0496			
		Booking Date: 06/12/2021			
		Period of Testing:- 07/12/2021 to 09/12/2021			
		Reporting Date: 10/12/2021			
Name of Customer:		Rural Work Department Work Division Tekari			
Customer Ref No.:		Letter-00		Date-04/12/2021	
Customer-Client Agreement No.					
Sample Description:		MSS (Mix Seal Surfacing);			
Name of Work/Subject:		Maintenance of Roads of Nishurpur to chhatma.(Lentgh3.100km)			

S.No.	Tests	Test Method	Results	Requirement Rate of Spray (Bitumen-VG-10) (KG/m ²)	Requirement Ref. IS No.
1.	Bituminous surface (Chainage 900m)	IS:1195: 2002	0.42	0.40 to 0.50	IRC: SP:78-2008
2.	Bituminous surface (Chainage 2200m)	IS:1195:2002	0.45	0.40 to 0.50	IRC:SP:78-2008

--Page 01 of 01--

P. K. Singh

Checked By

Remarks:

- The result (s) listed in the report refer only to the item(s) tested and it's Parameters(s). Endorsement of products is neither inferred nor implied.
- Sample will be destroyed after 30 days from the date of issue of test report unless otherwise specified.
- Report refer to the sample as received and not drawn by us unless mentioned otherwise
- The report shall not be reproduced exception full, without the approval of the laboratory and cannot be used as evidence in the Court of law and should not be used in any advertising media without our special permission in writing.

SAS GROUP
Authorized Signatory

Mob.- 6203263339, 7903718229

Email-sasbihar01@gmail.com



SAS GROUP

LABORATORY FOR TESTING OF ALL CIVIL ENGINEERING MATERIAL & GEO-TECH

(AN ISO 9001 : 2015 & ISO/IEC 17025 :2017 CERTIFIED NABL ACCREDITED LAB)

Plot No 2503, Rambhag Estates, Gandhinagar Patliputra
Station, P.O.- Ashlyana Nagar Patna 800025



TEST REPORT

Test Report Issued To: The Assistant Engineer Rural Work Department Work Division Tekari		Report No.:	2021-FINITY/REP-0496/C-ii		
		Sample Job Order No.:	FINITY-JO-21-0496		
		Booking Date:	06/12/2021		
		Period of Testing:	07/12/2021 to 09/12/2021		
		Reporting Date:	10/05/2021		
Name of Customer:		Rural Work Department Work Division Tekari			
Customer Ref No.:		Letter-00		Date-04/12/2021	
Customer-Client Agreement No.					
Sample Description:		S.D.B.C. (Semi Dense Bituminous Concrete); Grade-2			
Name of Work/Subject:		Maintenance of Roads of Nishurpur to chhatma.(Lentgh3.100km)			
S.No.	Tests	Test Method	Results	Requirement	Requirement Ref. IS No.
1.	Bitumen Content, % (Chainage 900m)	IS:1195: 2002	5.06	5.0 min.	IRC:111-2009
2.	Bitumen Content, % (Chainage 2200m)	IS:1195:2002	5.03	5.0 min.	IRC:111-2009

--Page 01 of 01--

[Signature]

Checked By

Remarks:

- The result (s) listed in the report refer only to the item(s) tested and it's Parameters(s). Endorsement of products is neither inferred nor implied.
- Sample will be destroyed after 30 days from the date of issue of test report unless otherwise specified.
- Report refer to the sample as received and not drawn by us unless mentioned otherwise
- The report shall not be reproduced exception full, without the approval of the laboratory and cannot be used as evidence in the Court of law and
- should not be used in any advertising media without our special permission in writing.



Authorized Signatory

Mob.- 6203263339, 7903718229

Email-sasbihar01@gmail.com
