



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail - eerwd.marhaura@yahoo.com

पत्रांक:- 2528(अ-3) मढ़ौरा/दिनांक:- 14.12.21.

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:- शीर्ष MR-3054 योजनान्तर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु0, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-3054 (MR-3054) अंतर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत संवेदक अभय कन्स्ट्रक्शन के द्वारा पथों में किये गये कार्य का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अधियाचना-पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं0-18 के अनुरूप पथों में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथों में किये गये कार्य का भुगतान किया जा सकें।

अनु0-1) अधियाचना प्रपत्र।

2) 19 ए प्रपत्र।

3) मापी पुस्त की छाया प्रति संलग्न।

4) BOMP Indicator Report संलग्न।

विश्वासभाजन

Handwritten signature


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

Handwritten date and initials
14/12/21

FORM GER-19-A

(See Government of India 'S Decision (I) below Rule -150)
Form of Utilization Certificate up to the Month of DECEMBER-2021
PIU:- Executive Engineer RWD Works Division, Marhaura

SL No	Name of Scheme	Sanction No& Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 (New Maintenance Policy-2018) (Ledger ID-7069)	सचिव ब्राडा के पत्रांक-39(अनु०) दिनांक- 11-06-2021 एवं पत्रांक:-64, दिनांक:- 06-12-2021	5715.65458	Certified that out of Rs- 5715.65458 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 5510.63947 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-205.01511 Lacs remaining unutilized at CFMS the end of the period under report.


Divisional Account Officer
R.W.D. (W) Division Marhaura

14/12/2021


Executive Engineer
R.W.D. (W) Division Marhaura

14/12/21

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (in Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MIR-N/19-20 Marhaura/12	Repura Rasulpur Road To Bansadhi Path	31306202092	Lt- No-3074 Date-17-07-2019	1.38000	49.87000	29.67718	13.98136	17/MR-N-3054/MBD/2020-21 05-02-2021	04-11-2021	04-11-2021	2638.21	25mm	5%	0.00000	0.00000	29.62079	Work Completed
Total:-																	29.62079	


1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.

2. Up-to-date Physical Progress has been Uploaded in MIS.


 Executive Engineer
 Rural Work Department
 Work Division, Marhaura


 17/10/20

File : E:\BUMP\Abhay Const\REPURA Rasulpur Rd - Bansdih\04111637.Xls, Section No. : 76, Eqn : $Y = 0 \cdot X^2 +$
 Name of Customer : Abhay Const., Name of Work/ Road : REPURA Rasulpur Rd - Bansdih, Lab Job number : 76

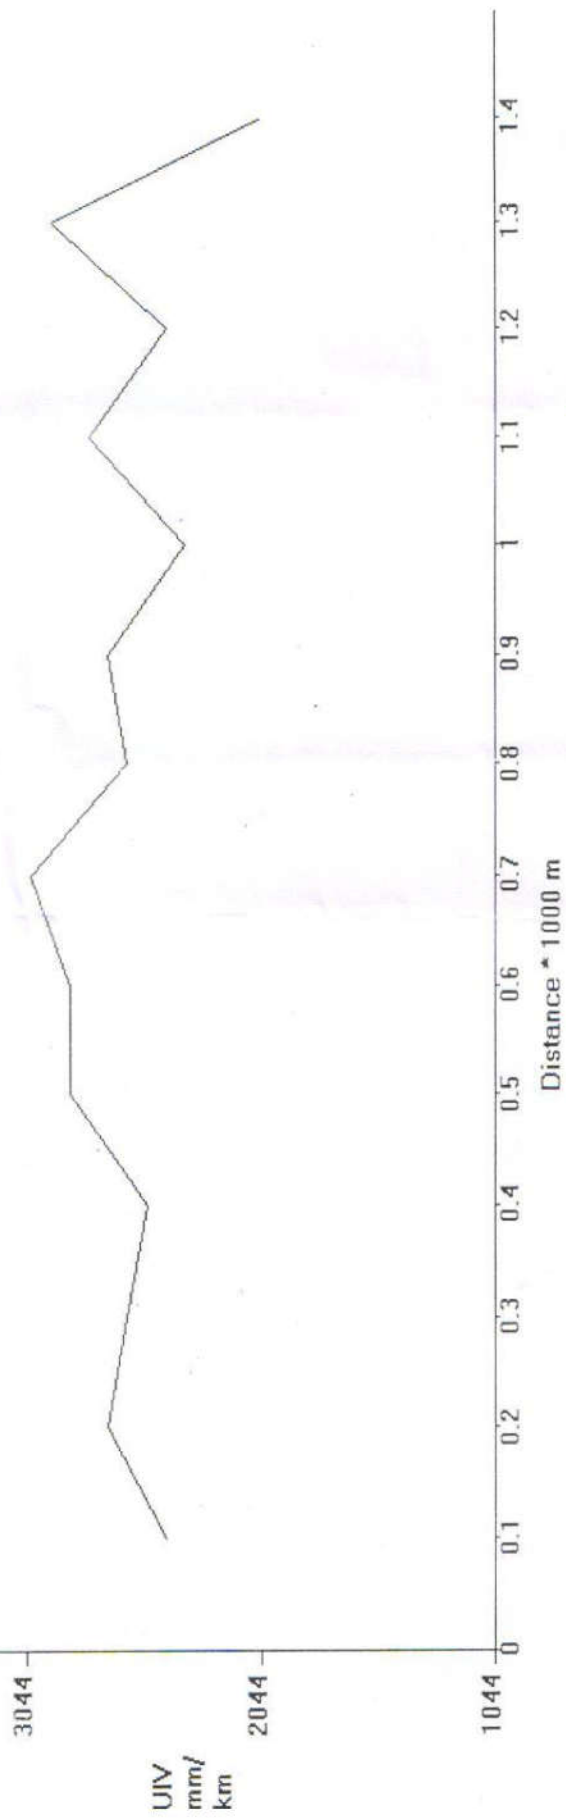

Signature
 Executive Engineer
 Rural Works Department
 Works Division, Marhaura
18/11/19

Signature

Signature
18/11/19

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY ROAD	Latitude	ongitude	Event
3/11/21	16:31:46	76	0.1	270	10.1	2700	2452 G	25.8756	84.87258	0 Normal
3/11/21	16:32:56	76	0.1	300	0	3000	2696 G	25.87629	84.87204	Curve
3/11/21	16:33:0	76	0.1	290	10.1	2900	2615 G	25.87722	84.87212	Normal
3/11/21	16:33:31	76	0.1	280	10.1	2800	2533 G	25.87802	84.87259	Normal
3/11/21	16:34:6	76	0.1	320	0	3200	2860 G	25.87886	84.873	Normal
3/11/21	16:35:0	76	0.1	320	10.1	3200	2860 G	25.87974	84.87345	Normal
3/11/21	16:35:16	76	0.1	340	10.1	3400	3023 G	25.88067	84.87365	Normal
3/11/21	16:36:0	76	0.1	290	10.1	2900	2615 G	25.88156	84.87391	Normal
3/11/21	16:36:27	76	0.1	300	10.1	3000	2696 G	25.8819	84.87458	Normal
3/11/21	16:36:27	76	0.1	260	10.1	2600	2370 G	25.88156	84.87547	Normal
3/11/21	16:37:2	76	0.1	310	10.1	3100	2778 G	25.88124	84.8765	Normal
3/11/21	16:37:37	76	0.1	270	10.1	2700	2452 G	25.88124	84.87749	Normal
3/11/21	16:38:0	76	0.1	330	10.1	3300	2941 G	25.88182	84.8782	Normal
3/11/21	16:38:48	76	0.1	220	10.1	2200	2044 G			

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 2800$$

$$Y = 2533$$

(R) RURAL ROAD

Good <4000
Average 4001-5000
Poor >5001

div
8/11/21

Executive Engineer
Rural Works Department
Works Division, Marhaura

(These four lines should be repeated at the commencement of the measurements relating to each work.)

5.40.024 Construction of subgrade
and another shoulder
Construction of subgrade

$8 \times 2 \times 30 \times 0.73 \times 0.30 = 105.12$ (A ₁)	
$11 \times 2 \times 30 \times 0.70 \times 0.30 = 138.60$ (A ₁)	
$16 \times 2 \times 30 \times 0.71 \times 0.32 = 218.112$	

461.832

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Abstract of Cost</u>					
J.40.02:-	Clearing and grubbing				
	Road (on lot at Comp. H.				
	Vide P.No.1 in T.4.B.				
0.276	H.R.	49496=70	H.R.	13661=00	
J.40.03:-	Construction of Subgrade				
	and earthen shoulders				
	with approved material				
	at -- Comp. H.				
	Vide P.No.02 in T.4.B.				
575-2327	2 R.	176=96	1 R.	101793=00	
J.40.04:-	Construction of G.S.B. by				
	providing well graded				
	material at -- Comp. H.				
	Vide P.No.02 in T.4.B.				
37-1487	2 R.	2281=71	1 R.	77916=00	
J.40.05:-	Providing laying & spreading				
	and compacting stone				
	aggregate (W.B.M. II)				
	at -- Comp. H.				
	Vide P.40.03 in T.4.B.				
38-596	4 R.	4243=90	1 R.	163798=00	
J.40.06:-	Providing laying & spreading				
	and compacting stone				
	aggregates of specific				
	sizes to water bound				
	Macadam seal (Gr. III)				

Continuation

R-357168=00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					R- 357168=00
Vide P.No. 04 in T. 4 B.					
52-9964 ² R ₁ - 3793 = 254 ² R ₂ -					201027=00
J.No. 07:- Providing & applying primer coat with bitumen emulsion					
(SS-1) et - Comp to G.					
Vide P.No. 04 in T. 4 B.					
706.613 4 ² R ₁ - 41 = 21 4 ² R ₂ -					29120=00
J.No. 08:- Providing and applying Jack Coat with bitumen emulsion et. G.					
Vide P.No. 04 in T. 4 B.					
706.613 4 ² R ₁ - 13298 4 ² R ₂ -					9878=00
J.No. 09:- Providing laying and rolling of close graded premix surfacing material of 20 mm R et. - G.					
Vide P.No. 04 in T. 4 B.					
706.613 4 ² R ₁ - 222 = 01 4 ² R ₂ -					156875=00
J.No. 10:- Providing & applying Jack Coat with bitumen emulsion using et. G.					
Vide P.No. 05 in T. 4 B.					
5175.00 4 ² R ₁ - 11 = 72 4 ² R ₂ -					60651=00
J.No. 11:- Providing & laying Semi dense bituminous Concrete with - 100-120 TPH					

Continuation

R- 814719=00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
batch type HMP powder					R-814719=00
at - comp - Id.					
Vide P. No. 05 in T.Y.B.					
129.375 $\times$ 2 R - 10881 = 7243 R - 1407823 = 00					
J. 40.12 - Reinforced Cement					
Concrete H/S Good 6 km					
local stone of standard					
et - comp - Id.					
Vide P. No. 05 in T.Y.B.					
(II) km stone					
02 Nos 2 R - 2295 = 724 N R - 4591 = 00					
J. 40.13 - (III) 200 m stone.					
06 Nos 2 R 633 = 42 Bath R - 3799 = 00					
J. 40.14 - Retro Reflectors					
Traffic signs Powder					
and erecting at - Id.					
Vide P. 40.05 in T.Y.B.					
1.924 $\times$ 2 R - 12356 = 264 $\times$ 2 R - 23724 = 00					
J. 40.15 - Powdering & fixing of retro					
reflectors of cautionary					
mandatory and informative					
et - comp - Id.					
Vide P. No. 06 in T.Y.B.					
30 Nos 2 R - 3657 = 95 Nos R - 109738 = 00					
J. 40.16 - 600 mm Circular					
Vide P. 40.06 in T.Y.B.					
08 Nos R - 3757 = 30 Nos R - 30058 = 00					

Continuation

R-2394452=00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
4					R- 2394452=0
J. No. 17:- 600mm x 450mm rect. gully					
Vide P. No. 06 in T. Y. B.					
13 Nos. rd - 3628 = 18 Each R - 47166 = 00					
J. No. 18:- Reinforced Cement					
Concrete M/S grade boundary					
Pillars/Local Stone and					
Standard etc. - Comp. etc.					
Vide P. No. 06 in T. Y. B.					
23 Nos. rd - 507 = 19 / Each R - 11665 = 00					
J. No. 19:- Planting of trees					
and their maintenance					
of One year - Planting					
of trees by the road					
Side (Avenue Trees) in					
etc. - Comp. etc. - 100					
Vide P. No. 06 in T. Y. B.					
68 Nos. rd - 800 = 30 / Each R - 54420 = 00					
J. No. 20:- Providing & laying out					
of dot applied from plate					
Compound 2.50m at 16.					
Vide P. No. 06 in T. Y. B.					
276.00 yds - 735 = 40 yds R - 202970 = 00					
J. No. 21:- Providing and fixing of					
Typical H.M. 951 in 10m x 4					
Vide P. No. 06 in T. Y. B.					
04 Nos. rd - 9344 = 21 / Each R - 37377 = 00					

Continuation

R - 2748050 = 00

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					R-2748050=00
S. 40.22/- :- Bridge Masonry work	13				
C/T (1/2) in P.C.C.					
Vide P. No 07 in T.Y.B.					
5.76 Y ² R - 5102 = 55 / 4 ² R - 29391 = 00					
S. 40.23/- :- Plastering with Cement	24				
mortar (1:4) at 1/6					
Vide P. No 07 in T.Y.B.					
40.32 Y ² R - 148 = 384 ² R - 5983 = 00					
S. 40.24/- :- Painting two Coats	25				
including Primer Coat					
et - - Comp Job.					
Vide P. No 07 in T.Y.B.					
91.68 Y ² R - 95 = 63 Y ² R - 8767 = 00					
					R-2792191=00
Add 12% G.S.T.					R-335063=00
Add 1% Labor Cess					R-27922=00
					R-3155176=00
Less 6.12% Below					R-193097=00
					R-2962079=00
Certified that work has been completed as per specification and direction of A.E.					8/11/14 BZ
Date 04/11/21 J.R. Amman.					

Continuation
