

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल-दाउदनगर।

पत्रांक:- 5188(6/10)

दाउदनगर/दिनांक:- 28/12/2021

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दाउदनगर।

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार।

विषय:- गैर योजना मद शीर्ष MR 3054(Bihar Rural Road New Maintenance Policy-2018)
के तहत कार्यान्वित पथों में उपयोगिता प्रमाण पत्र एवं अधियाचना समर्पित करने के संबंध
में।

महाशय,


उपयुक्त विषय के संबंध में कहना है कि ग्रामीण कार्य विभाग, कार्य प्रमंडल दाउदनगर
के अंतर्गत गैर योजना मद शीर्ष MR 3054(Bihar Rural Road New Maintenance Policy-
2018) के तहत चल रहे कार्य पूर्ण हो चुका है। उपयोगिता प्रमाण पत्र एवं अधियाचना विहित प्रपत्र
में संलग्न कर समर्पित किया जाता है।

आग्रह है कि सूची के अनुसार संवेदको का नाम प्राधिकार पत्र में शामिल
करने एवं अधियाचित राशि रु0त्र 1,31,72,576=00(एक करोड़ ऐकतीस लाख बहतर हजार पाँच सौ
छेहतर रुपये) मात्र आवंटन उपलब्ध कराने की कृपा करना चाहेंगे। ताकि भुगतान किया जा सके।

अनु०:-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दाउदनगर।



FORM GFR 19-A

(Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate as on 06.12.2021
MR 3054(Bihar Rural Road New Maintenance Policy-2018)

STATE-BIHAR

PIU - E.E,RWD (W), Div.- Daudnagar

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under MR 3054 (Bihar Rural Road New Maintenance Policy-2018)	F.Y 2020-2021 & 2021-2022 Vide Lt.no. -64 dated-06.12.2021	4115.34159	Certified that out of Rs 4115.34159 Lacs received during the years 2020-2021 in favour of Ex. Engineer, RWD (W), Div.- Daudnagar, Bihar, a sum of Rs3974.61480 Lacs has been utilized for the purpose of MR Policy (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs140.72679Lacs remaining unutilized at the end of the period under.
			4115.34159	

I Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Supertending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Supertending Engineer.
- Construction materials have been tested
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

Memo No-

Dated:-

Copy forwarded to Secretary Cum- Empowered Officer(BRRADA),Patna for taking necessary action.

Div. Accounts Officer
R.W.D Works Division
Daudnagar

Executive Engineer
R.W.D Works Division
Daudnagar

Office of The Executive Engineer, Rural Works Department, Works Division Daudnagar
Requisition formate for Scheme Head- MIR-3054 Under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification with Surface Renewal)

Sl.No.	Package No	Name of Road	Project ID As per MIS	A.A. Letter No & Date	Administrative Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of FRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-Date Expenditure as per MIS (in lakh)	Requisition against work done (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance										
1	1	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AU/DAU/19/0020	Const of Rd from Groh Daudnagar Rd to Muihar Kanhi Bankur Rd	Project ID- 10602801010	2164 06/07/2019	3.0	109.13	64.89800	26.54977	08/MBD/2019-2020	03.12.2021	25.12.2021	3125.37	25	5.00	0.00000	0.00000	60.29887	Complete
2	RM/AU/DAU/19/0020	Phatepur Devhara Road to Khuthan	Project ID- 10602801032	2164 06/07/2019	3.6	124.27	72.56800	31.43568	08/MBD/2019-2020	03.12.2021	25.12.2021	3123.83	25	5.00	0.00000	0.00000	71.42689	Complete

28-12-20
Sr. Divisional Accounts Officer
Rural Works Department,
Works Division, Daudnagar

28-12-20
Executive Engineer,
Rural Works Department,
Works Division, Daudnagar

Name of Contractor- Kamlesh Kumar Prop. Shashi Kumari

Name of Work- Const. of Rd from Goh Daudnagar Rd to Muijhar Kaithi Bankut Rd

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI in mm/km	CATEGORY ROAD	IRI	Latitude	Longitude	Event
		No.										
25/12/21	11:50:37	50	0.1	290	0	2900	2924	G	3.93	25.4492	84.553552	Normal
25/12/21	11:51:12	50	0.1	320	10.1	3200	3212	G	4.28	25.4155	84.552878	Normal
25/12/21	11:51:12	50	0.1	340	10.1	3400	3404	G	4.5	25.3292	84.552473	Normal
25/12/21	11:52:0	50	0.1	300	10.1	3000	3020	G	4.05	25.2442	84.55212	Normal
25/12/21	11:52:0	50	0.1	330	20.2	3300	3308	G	4.39	25.163	84.551665	Normal
25/12/21	11:52:23	50	0.1	350	20.2	3500	3500	G	4.62	25.988	84.550942	Normal
25/12/21	11:52:58	50	0.1	300	10.1	3000	3020	G	4.05	25.413	84.55037	Normal
25/12/21	11:53:0	50	0.1	320	10.1	3200	3212	G	4.28	24.99938	84.551178	Normal
25/12/21	11:53:34	50	0.1	310	10.1	3100	3116	G	4.16	24.9993	84.551665	Normal
25/12/21	11:53:34	50	0.1	270	20.2	2700	2731	G	3.7	24.998375	84.551278	Normal
25/12/21	11:54:9	50	0.1	320	20.2	3200	3212	G	4.28	24.997603	84.551278	Normal
25/12/21	11:54:9	50	0.1	350	10.1	3500	3500	G	4.62	24.99685	84.550773	Normal
25/12/21	11:54:44	50	0.1	370	10.1	3700	3692	G	4.84	24.996557	84.551598	Normal
25/12/21	11:55:0	50	0.1	270	10.1	2700	2731	G	3.7	24.995797	84.551598	Normal
25/12/21	11:55:19	50	0.1	290	20.2	2900	2924	G	3.93	24.994955	84.551295	Speed Breaker
25/12/21	11:55:19	50	0.1	310	20.2	3100	3116	G	4.16	24.994062	84.55148	Normal
25/12/21	11:55:55	50	0.1	230	20.2	2300	2347	G	3.23	24.99318	84.55148	Normal
25/12/21	11:56:0	50	0.1	220	20.2	2200	2251	G	3.11	24.992377	84.551093	Normal
25/12/21	11:56:0	50	0.1	260	20.2	2600	2635	G	3.58	24.991807	84.55042	Normal
25/12/21	11:56:30	50	0.1	300	20.2	3000	3020	G	4.05	24.991068	84.55007	Normal
25/12/21	11:57:5	50	0.1	370	10.1	3700	3692	G	4.84	24.990187	84.55008	Normal
25/12/21	11:57:5	50	0.1	330	10.1	3300	3308	G	4.39	24.989818	84.550925	Normal
25/12/21	11:57:41	50	0.1	360	20.2	3600	3596	G	4.73	24.989048	84.551515	Speed Breaker
25/12/21	11:58:0	50	0.1	350	20.2	3500	3500	G	4.62	24.988437	84.551143	Normal
25/12/21	11:58:16	50	0.1	360	10.1	3600	3596	G	4.73	24.988638	84.550202	Normal
25/12/21	11:58:16	50	0.1	240	20.2	2400	2443	G	3.35	24.988838	84.549258	Normal
25/12/21	11:59:0	50	0.1	260	20.2	2600	2635	G	3.58	24.98845	84.548	Normal
25/12/21	11:59:0	50	0.1	360	10.1	3600	3596	G	4.73	24.98778	84.547793	Normal
25/12/21	11:59:26	50	0.1	330	10.1	3300	3308	G	4.39	24.987118	84.547945	Normal
25/12/21	12:3:33	50	0.1	320	10.1	3200	3212	G	4.28	24.986902	84.548063	Normal
Length-			3.0									
					Total IRI	93761						
					Average IRI	3125.37						

$$y = 0 * x^2 + 0.961 * x + 137.3$$

$$x = 3200$$

$$y = 3212$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

J.E

A.E

E.E

Sharma
28.12.21

Sharma
28/12/21

Sharma
28.12.21

Name of Customer :	kamlesh kumar Prop Shashi Kuri
Name of Work/ Road :	Const. of Rd from Goh Daudnagar
Lab Job number	10602801010
Date :	25-Dec-21
Section No.	50

Test Date :	28-Apr-10	Road Name :	Const of Rd from Goh Daudnagar
Machine No :	398	Road Type :	(R) RURAL ROAD
Start S No :	0.000	Side :	Haspura
Start E No :	3.000	Interval	
Weather :	Normal	UIV Range :	1251 To 5000 mm/km
Start Location :	25.449284.553	Dist Range :	0 To 3.1 0.1 * 1000 m
End Location :	24.986902845	Equation :	$Y = 0 * X^2 + 0.961 * X + 137.3$

Print


Generate Report and Graph

Redraw Graph

Map View

File : E:\kaithi\25121229.Xls, Section No. : 50, Eqn : $Y = 0 * X^2 + 0.961 * X + 137.3$

Name of Customer : kamlesh kumar Prop. Shashi Kuri, Name of Work/ Road : Const. of Rd from Goh Daudnagar Rd

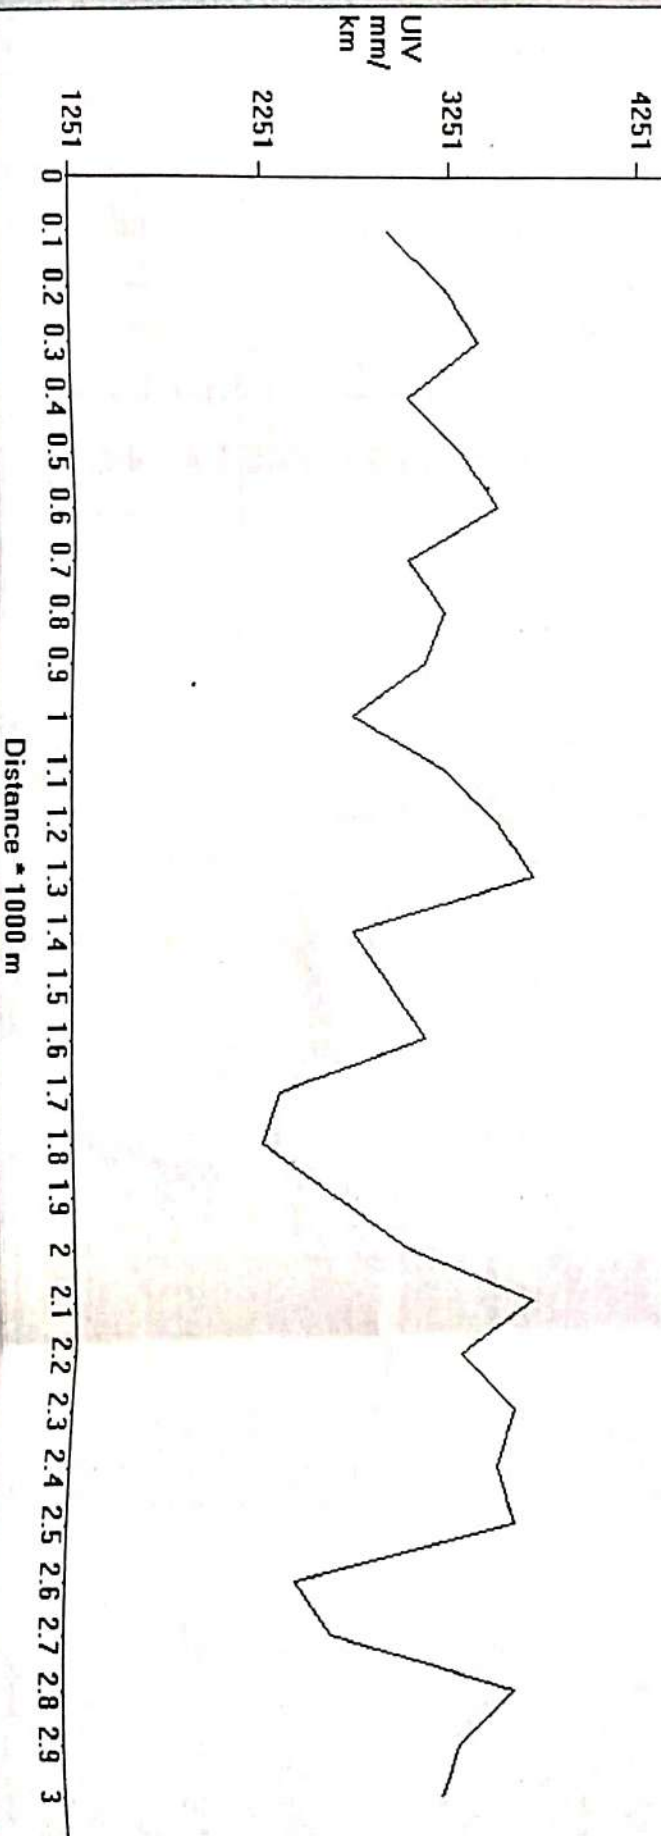

Sharma
28.12.21
js

js
28/11/21

js
28/12/21

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल-दाउदनगर।

प्रमाण पत्र

प्रमाणित किया जाता है कि संवेदक- श्री कमलेश कुमार प्रो० शशी कुमारी

पता- S/O- Ramashish Sharma, behind Khadi Bhandar, Lakhibag, Manpur
Gaya-823003 जिला-गया के द्वारा बिहार अनुरक्षण नीति-2018 के तहत ग्रुप
सं०-RM/AUD/DAU/19/0020 में दो पथों का SDBC का कार्य जिसका Project_ID-
10602801010 and 10602801032 का कार्य प्राक्कलन के अनुसार विष्टियों एवं गुणवत्ता के
अनुरूप पूर्ण कर दिया गया है।

Sharma
28.12.21
JB

Sharma
28/12/21
JB

विश्वासभाजन

Sharma
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दाउदनगर।

M/R

STC 61876921 < H 4902C

Schedule XLV-Form No. 134

B-A 49742

Stamp No

CHRYSLER ENGINE, WITH AN 80-612544C DIVISION

GENERAL INVESTIGATIVE DIVISION SUB-DIVISION
EGGT

MEASUREMENT BOOK

763

21923 →

1st on A/C Bill

1.

Name of work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work	Repair of road				
	from Goh Daudh Nagar road to				
	Mujhar Kaiithi Bankat road.				
Agency - M/S	Kamlesh Kumar				
	Prop. Shashi Kumari.				
Agreement NO.	08/MBD/2021-22				
Date of commencement	27-5-21				
Date of completion	03-12-2021				

Record Measurement

Date of measurement - 1-11-21

(1) Clearing & grubbing

$$2 \times 3000m \times 2.00m = 1.20 \text{ Ha.}$$

(2) Scarifying B.T. surface

$$300m \times 3.75m = 1125.00 m^2$$

(3) Providing G. S. B. gr-II...

$$10 \times 15.0m \times 4.05m \times 0.175m = 106.31$$

$$10 \times 5.0m \times 4.05m \times 0.175m = 35.43$$

$$10 \times 2.25m \times 2.0m \times 0.175m = 7.87$$

$$10 \times 5.0m \times 4.05m \times 0.175m = 35.43$$

$$10 \times 2.25m \times 2.0m \times 0.175m = 7.87$$

$$192.91 m^2$$

Sharma
7.11.21
JE

Continuation
4/11/21
AR

ABSTRACT OF COST

8

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
① Clearing & grubbing					
1.20 Ha P-1					
@ 49496 = 70/Ha-3					59,396 = 00
② Scarifying P.T. roller					
1125.00 m ² P-1					
@ 15.40/m ² - 3					17,325 = 00
③ Concrete of cushion shoulder					
2250.0 m ³ P-6					
@ 176 = 75/m ³ - 3					397,688 = 00
④ Providing C.P. 38...					
192.91 m ³ P-1					
@ 1940 = 94/m ³ - 3					374,427 = 00
⑤ Providing W.B. masonry-II					
178.65 m ³ P-2					
@ 3406 = 76/m ³ - 3					608,618 = 00
⑥ Providing W.B. masonry-III					
212.95 m ³ P-2					
@ 3177 = 25/m ³ - 3					676,595 = 00
⑦ Prime coat					
2839.33 m ² P-3					
@ 41 = 25/m ² - 3					117,122 = 00
⑧ Tack coat					
2840.00 m ² P-3					
@ 13 = 99/m ² - 3					39,732 = 00
					2290903 = 00

Continuation

2290903=00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(9) Patch work with 20mm P.M.C.					
2840.00 m ² P-3					
@ 179=48/m ² = ₹				509,723=00	
(10) Trck cont					
11350.00 m ² P-5					
@ 11=73/m ² = ₹				133,135=00	
(11) Binding SDBC					
283.75 m ³ P-5					
@ 7683=58/m ³ = ₹				21,80,216=00	
(12) 4mm stone					
4 Nos. P-5					
@ 2099=46 each = ₹				8,398=00	
(13) 200mm stone					
10 Nos. P-5					
@ 603=87 each = ₹				6,039=00	
(14) Directional placement					
0.96 m ² P-5					
@ 12956=60/m ² = ₹				12,438=00	
(15) Traffic cone					
10 Nos. P-6					
@ 1225=59 each = ₹				12,256=00	
(16) Traffic sign					
@ 600mm eq Triangle					
15 Nos. P-6					
@ 3736=43 each = ₹				56,046=00	
				52,09,154=00	

Continuation

5209154=00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(17) 600mm circular.					
8 Nos. P-6					
@ 3904=97 each- ₹					31,240=00
(18) 600mm x 450mm rectangular.					
5 Nos. P-6					
@ 3765=15 each- ₹					18,826=00
(19) Planting of Tree.					
90 Nos. P-6					
@ 799=08 each- ₹					71,917=00
(20) Road marking					
600.00m ² P-6					
@ 735=40/m ² - ₹					441,240=00

(21) Guard stone.					
40 Nos. P-6					
@ 495=02 each- ₹					19,801=00
(22) B/W in CM (1:3)					
20.16 m ² P-5					
@ 5072=91/m ² - ₹					102,270=00
(23) Plastering with CM (1:4)					
141.12 m ² P-5					
@ 149=87/m ² - ₹					21,150=00
(24) Painting on parapet					
141.12 m ² P-5					
@ 95=63/m ² - ₹					13,495=00

(0.5) 5929093=00
Continuation

[illegible]
