

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, अरवल।

पत्रांक: 13.....अरवल

दिनांक 05/01/2021...../

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, अरवल।

सेवा में,

अधीक्षण अभियंता
ग्रामीण कार्य विभाग,
कार्य अंचल, औरंगाबाद।

विषय:-

एम0एम0जी0एस0वाई0 योजना अन्तर्गत Sikanderpur Dhewai to Rupsagar Bigha पथ
निर्माण कार्य का समय वृद्धि स्वीकृति के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि वर्णित पथ का कार्य पूर्ण है। समय वृद्धि की
स्वीकृति हेतु विहित प्रपत्र में अनुशंसा के साथ फोटों, शपथ पत्र, मापीपुस्त की छाया प्रति सहित
समर्पित किया जा रहा है।

अतः अनुरोध है कि उक्त पथ का समय वृद्धि की स्वीकृति देने की कृपा की जाय।

अनु0यथांवात्।

विश्वासभाजन

कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमण्डल, अरवल।

05/01/21

APPLICATION FOR EXTENTION OF TIME

1. Name of contractor :- Arbind Kumar
2. Name of work :- Const. of Road Five year maintenance sikanderpur
Dhewai to Roop Sagar Bigha.
(Head of Expenditure) MMGSy
3. Agreement Number :- 06/SBD/MMGSy/2019-2020
4. Agreement Value :- 55,66,308.00
5. Date of Commencement of Work :- 15-07-2019
6. Date of Completion Stipulated in The Agreement :- 14-04-2020
7. Period for Which Extension Has Been Given Previously :- NO
8. Work Done in % :- 100%
9. Period For Which Extension Now Applied for :- 20-06-2020
10. Reason For Extension of Time :- Land Disturbed & Covid-19
11. Recommendation By J.E :- Land Disturbed & Covid-19 unlock.
has
20/6/20
12. Whether Programme of Work Approved :- YES
13. Whether Fund Available :- NO
14. If Spill Over From Previous Financial Year Whether Year Included in the Current
Work Programme or not :- NO (work is completed)
15. Recommendation by S.D.O यू.पी. बिनाद एवं कोविड 19 के अनलॉक के कारण कार्य
रूक जाने में विलम्ब हुआ है।
20/6/20
16. Recommendation by Executive Eng :- 20/6/20
20-7-2021
E.E.
17. Recommendation by S.E :-



Vijay Kumar Paswan
Notary Public
Arwal (Bihar)

शपथ - पत्र

1898 6.11.2020
No. Date

मैं अरबिन्द कुमार, पिता- शारदानन्द सिंह, ग्राम-बन्धु बिगहा, पो0 उसरी-थाना-मेहन्दिया, जिला- अरवल शपथ पत्र के माध्यम से सत्य एवं निष्ठा पूर्वक निम्नांकित बातों की उदघोषण करता हूँ :-

1. यह कि मैं उपरोक्त पते का स्थायी निवासी हूँ।
2. यह कि मैं सिकन्दरपुर धेवई से रूपसागर बिगहा (MMGSY) योजना अन्तर्गत कार्य दिनांक 20.06.2020 को पूर्ण रूप से कर लिया हूँ।
3. यह कि उक्त योजना का एकरानामा सं0 06/SBD/MMGSY (SC) 2019-20 एवं एकरारनामा की राशि रू0 55,66,308.00 रू0 है।
4. यह कि दिनांक 20.06.2020 तक समय वृद्धि हेतु न्यायालय के समक्ष शपथ-पत्र दायर कर रहा हूँ।
5. यह कि समय वृद्धि मिलने के बाद किसी अन्य तरह के भुगतान का दावा मैं नहीं करूँगा।


सत्यापन

मैं अरबिन्द कुमार, पिता- शारदानन्द सिंह, ग्राम-बन्धु बिगहा, पो0 उसरी-थाना-मेहन्दिया, जिला- अरवल घोषणा करता हूँ कि कंडिका 1 से 5 तक में दी गई सभी बातें मेरे जानकारी में सत्य व सही हैं।

अधिवक्ता *Vijay Kumar Paswan*
07.11.2020

उपरोक्त अरबिन्द कुमार

अधिवक्ता करते हैं।



जिनकी *Vijay Kumar Paswan*

sub Rule-4 of Notaries act 195

Vijay Kumar Paswan
NOTARY
ARWAL (BIHAR)
06.11.2020

CH/11

HS 0000977335

GOVERNMENT OF BIHAR
e-Court Fee



DATE & TIME :

09-NOV-2020 11:17:27

NAMES OF THE ACC/ REGISTERED USER :

SREI INFRASTRUCTURE FINANCE LIMITED

LOCATION :

Civil Court Arwal

e-COURT RECEIPT NO :

BRCT0908K2003L114

e-COURT FEE AMOUNT :

₹ 90

(Rupees Ninety Only)



₹10

BIHAR COURT FEE
BRCT0634134K20240
06-NOV-2020



BRCT0908K2003L114

Statutory Alert : The authenticity of this e-Court fee receipt should be verified at www.shcilestamp.com. Any discrepancy in the details on this receipt and as available on the website renders it invalid. In case of any discrepancy please inform the Competent Authority. This receipt is valid only after verification & locking by the Court Official.

Reg. No. - 3160315

Mob. : 852194

ARBIND KUMAR

Civil Contractor
Bandhu Bigha (Arwal)

Ref. :

Date : 11-01-2020

सेवा में:

कार्मपालक अभियंता
ग्रामीण कार्य विभाग
कार्म प्रमंडल अरवल

विषय :- मुख्यमंत्री ग्राम सड़क योजना (MMSY) अंतर्गत
सिमंदरपुर चौक से रूपसागर बिरा पंच में जमीनी
विवाद के संबंध में,

दिनांक
11-01-2020

महोदय,


सविनय निवेदन है कि मेरा स्करानामा संख्या
06/SBD/MMSY (SC) 2019-20 है। इस पंच में कार्य
करने की तिथि 15-07-2019 से आरम्भ करना था
जो वर्षा ऋतु का समय था। अब जब मैं वर्षा ऋतु समाप्त
होने के बाद कार्य प्रारम्भ किया हूँ, तब जगह-जगह
पर जमीनी विवाद हो रहा है। इसके चलते कार्य
करने में रुकावट हो रही है।

अतः श्रीमान, व नम्र निवेदन है कि
जमीनी विवाद को जल्द से जल्द निपटारा किया
जावे ताकि खसमम कार्य पूर्ण हो सके।

आपका विचारी
Arbind Kumar



by
20/6/2020
me

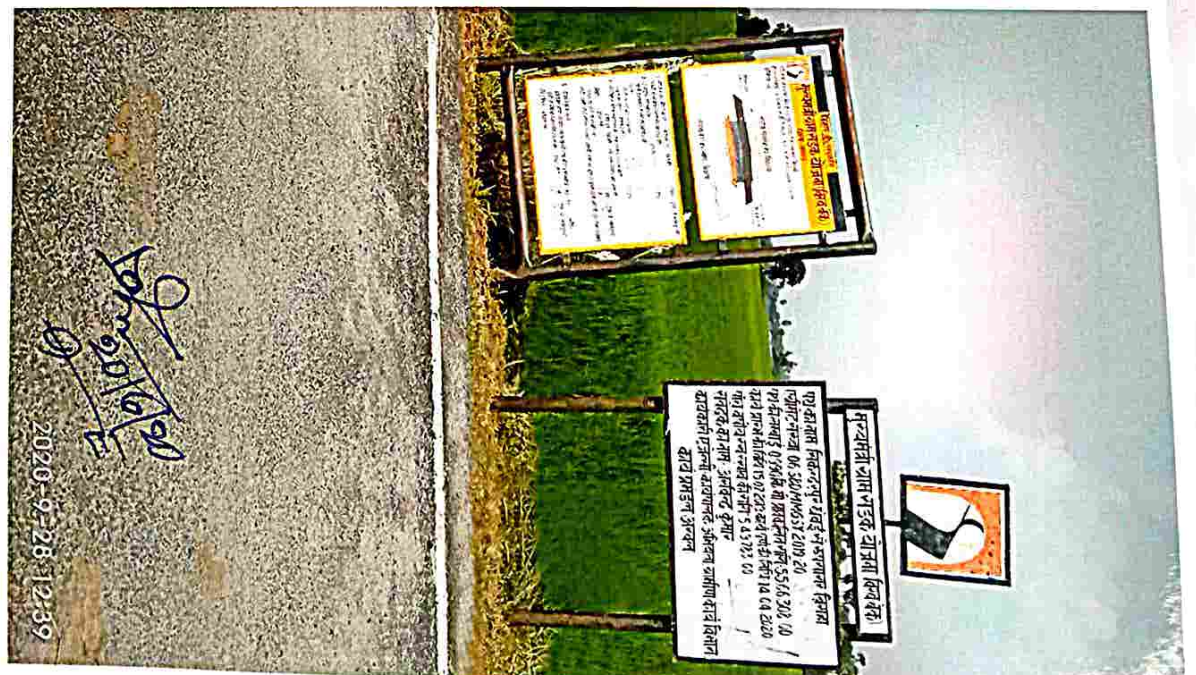

by
20/6/2020
me

by
20/6/2020
me



JSC
 20/6/2020
 JSC

JSC
 20/6/2020
 JSC

JSC
 20/6/2020
 JSC



2016/11/01
 2016/11/01



2016/11/01
 2016/11/01

2016/11/01
 2016/11/01



20/10/20
2020-10-3 11:55

20/10/20
2020-10-3 11:55



20/10/20

2020-9-27 13:27

20/10/20
2020-9-27 13:27

20/10/20
2020-9-27 13:27



for
20/6/2020
SC



for
20/6/2020
SC

for
20/6/2020
SC

प्रमाणित किया जाता है कि इस मापी
पुस्त में कुल मुद्रित पृष्ठ 100 (एक सौ फने)
है, जो सहायक अभियंता मो अपरान अकाद
सहायक अभियंता कार्य अवर प्रमंडल
~~कलेक्टर~~
~~अधिकारी~~ के नाम से निर्णित किया जाता है।

30/5/19
Executive Engineer
R.W.D. (W) Division
Arwal
30/5/19

Sch. XLV - Form No. 134

_____ DIVISION

_____ SUB-DIVISION

Measurement Book

No. 542

186910 BLM

Recessed measurement

1

Name of Work-

Situation of Work-

Agency by which work is executed-

Date of Measurement-

No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work	Construction of road from				
	Sikanderpur Dhewai to				
	Roopsagar Bigha.				
Name of Agency	Arvind Kumar				
Agreement no.	06/560/MMG/SY/2010-20				
Date of commencement	15/07/2010				
Date of completion	14/04/2020				
Date of measurement	20/2/2020, 4/3/2020, 17/3/2020				

1. Setting out pillars p/v 2 -

fixing bench mark pillars

to 500

1 nos

2. Setting out pillars p/v 2

fixing of reference mark

pillars to 500

4 nos

3. clearing and grubbing road

land (62 manual years) inch

to 500

$10 \times 30.00 \times 3.50 = 1050.00 \text{ m}^2$

$10 \times 30.00 \times 3.50 = 1050.00 \text{ m}^2$

3rd 4th 5th 6th 7th 8th 9th 10th 11th 12th 13th 14th 15th 16th 17th 18th 19th 20th 21st 22nd 23rd 24th 25th 26th 27th 28th 29th 30th 31st 32nd 33rd 34th 35th 36th 37th 38th 39th 40th 41st 42nd 43rd 44th 45th 46th 47th 48th 49th 50th 51st 52nd 53rd 54th 55th 56th 57th 58th 59th 60th 61st 62nd 63rd 64th 65th 66th 67th 68th 69th 70th 71st 72nd 73rd 74th 75th 76th 77th 78th 79th 80th 81st 82nd 83rd 84th 85th 86th 87th 88th 89th 90th 91st 92nd 93rd 94th 95th 96th 97th 98th 99th 100th

Recast measurement

16

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:-	Construction of road				
	from Sikan for Dhawai				
	to Rook Cagar Bika.				
Name of Agency:-					
Agreement no:-	06/ SRD/Amrasi/101320				
Date of completion:-	15/7/2019				
Date of certification:-	14/4/2020				
Date of measurement:-	12/10/2020				

1. Earthwork in excavation for structure - 50

$$2 \times 6.50 \times 1.40 \times 1.50 = 27.30 \text{ m}^3$$

$$1 \times 4.25 \times 1.53 \times 0.30 = 1.95 \text{ m}^3$$

$$= 29.25 \text{ m}^3$$

2. P.V fixed class type 15 wall constructed local sand 50

$$1 \times 4.25 \times 1.53 \times 60 = 3.90 \text{ m}^3$$

3. P.V concrete for bh - 12 inch concrete in open foundation 50

$$2 \times 6.50 \times 1.40 \times 0.15 = 2.73 \text{ m}^3$$

4. P.V brick masonry work in cement mortar (1:4) 50

$$2 \times 6.30 \times \frac{1.25 + 0.40}{2} \times 2.50 = 25.99 \text{ m}^3$$

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
abblint h... ..					
CC					
2x4x30.00 x 0.10 = 24.00m ²					
= 24.00m ²					
9. Plv Reinforced Cement concrete					
M/S grade fibro meshing					
(i) Km store ———— 2 nos					
(ii) 200mm store ———— 4 nos					
10. Plv at fixing of steel					
rebarised Cautioning					
(i) 600mm square ———— 4 nos					
(ii) 600mm circular ———— 2 nos					
11. 600mm x 450mm rectangular					
————— 2 nos					
1. Plv at fixing of typical					
masonry base					
————— 1 nos					
22. Plv Reinforced Cement concrete					
M/S grade boundary					
————— 8 nos					
Dr					
20/6/2020					
E					
Dr					
20/6/2020					
A					
E					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
28. 85-1 @ B 55 38.093 / 1-1 B.					1,59,774 = 00
29. Plv at large Rec bite					
NP3 (1x1000 - 1/2 in 1/2)					
8th with item no. (5) Part 12					
					± 5.00m
					@ B 4363.096 / 1-1 B
29. Plv at large with 1m					21,815 = 00
(1.14) - 1/2 in 1/2					
8th with item no. (7) Part 12					
					± 28.57 m
					@ B 16,373 / 1-1 B
					4182 = 00
					B 47, 44,399 = 00
less 0.03% below of					
B.O.G rate (-)					1423 = 00
					R 47,42,976 = 00
allotment					25,00,000 = 00
less previous bill					B 22,24,177 = 00
					R 18,18,795 = 00
					B 22,42,976 = 00
15/9/2020					15/9/20
JS					E
Attended					
Executive Engineer					
R.W.D (W). Division					
Arwal.					
21/11/21					

Continuation
