

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, किशनगंज-1

पत्रांक:- 22अनु०

प्रेषक:- कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, किशनगंज-1

सेवा में,

Addl. CEO-Cum-Secretary-Cum empowered officer
Bihar Rural Road Development Agency 3rd floor, Land Development
Bank Bhawan Budh Marg Patna.

किशनगंज / दिनांक ०८/०१/२०२१

विषय:- MR (3054) New Maintenance Policy-2018 के अंतर्गत वर्ष 2019-20 एवं 2020-21 के पथों में अधियाचना के संबंध में।

महाशय

उपर्युक्त विषय के संबंध में कहना है कि MR (3054) New Maintenance Policy-2018 अंतर्गत वर्ष 2019-20 एवं 2020-21 के निम्नलिखित पथों में कराये गये कार्य के भुगतान हेतु कुल 2,35,09049.00 (दो करोड़ पैंतीस लाख नौ हजार उनचास) मात्र रुपये के अधियाचना मरम्मत मद में की जा रही है।

अतः अनुरोध है कि अधियाचित राशि विमुक्त करने की कृपा की जाय।

अनुलग्नक:-यथोक्त ।

विश्वासभाजन

Clear
8/1/21
कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, किशनगंज-1
8/1/21

Utilization Certificate-up to January-2021 For MR (3054) New Maintenance Policy-2018 office of the Executive Engineer RWD Work Division, Kishanganj-1

From

Name of PIU/Executive Engineer RWD, Work Division, Kishanganj-1

To

Secretary cum Empowered Officer,
BRRDA (MR-3054), Patna (Bihar).

Sl. N o.	Name Scheme	Sanction No. & Date with Amount	Amount Received (in Lacs Rs.)	Particular
1	2	3	4	5
1	Constructi on of Rural roads under MR (3054) New Maintenance Policy-2018	Secretary cum Empowered Officer, BRRDA (MR-3054), Patna (Bihar). Total Amounting Rs. 2609.73530 (Twenty Six Crore Nine Lakh Seventy Three Thousand Five Hundred Thirty) only.	Total Amounting Rs. 2609.73530 (Twenty Six Crore Nine Lakh Seventy Three Thousand Five Hundred Thirty)only.	Certified that out of Rs. 2609.73530 (Twenty Six Crore Nine Lakh Seventy Three Thousand Five Hundred Thirty) only. of grants in aid sanctioned during and up to year 2020-21 in favor of officer-in-charge/PIU/E.E, RWD work Division, Kishanganj-1. A sum of Rs. 2576.18844 (Twenty Five Crore Seventy Six Lakh Eighteen Thousand Eight Hundred Forty Four) only. has been utilize for the purpose of MR-3054 State Share as given in the margin for which it was sanctioned and that the balance of Rs. 16.77343 (Sixteen Lakh Seventy Seven Thousand Three Hundred Forty Three) Only. remaining unutilized as the end of the period under report.

Certified that I have satisfied myself that the condition on which the grants in-aid was sanction have been only fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which in was sanctioned.

Kind of Check Exercised:-

- Works have been supervised by Executive Engineer/Superintend Engineer.
- Periodic Inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction Material have tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer.
- All other codas formalities have been observed.

Physical Progress achieved.

- Construction of road works.
- Construction of CD works.

Divisional Accounts Officer
RWD works division, Kishanganj-1

Signature of PIU/Executive Engineer
RWD works division,
Kishanganj-1

Clear
8/1/21

8/1/21

Sl. No	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (in KM)	Amount of (In Lakh)	Initial Rectification with Surface renewal (In Lakh)	5 Year Routine Maintenance In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR/KI/KIS/19/0010	Kathalhari to Kumhartoli road	21205901005	2050/3-7-19	4.250	182.952	110.134	40.688	58/3054/MBD/2020-21	27-09-2020	0-09-2020	3418.55	25mm	5.03	0.00000	0.00000	124.45000	WIP
2	MR/KI/KIS/19/0010	Murmala Chowk to Bishanpur Road	21205901012	2050/3-7-19	2.580	110.257	74.569	28.064	58/3054/MBD/2020-21	27-09-2020	0-09-2020	3747.15	25mm	5.02	70.16755	70.16755	4.26616	WIP
3	MR/KI/KIS/19/0010	PWD Road to Lohiakandar Road	21205901003	2050/3-7-19	3.100	150.303	94.17616	29.401	58/3054/MBD/2020-21	27-09-2020	0-09-2020	3670.52	25mm	5.06	0.00000	0.00000	106.37433	WIP
			TOTAL=														235.09049	

8/11/21

Clear
8/11/21
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रगंडल, किरानगंज-1
8/11/21

Road Name- PWD Road to Lohiakandar Road

Contractor's Name- Dayanand Kumar


Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	ATEGORY ROAD	Latitude	Longitude	Event
30/12/20	11:40:36	41	0.1	390	0	3900	3839	G	26.24982	87.948198	Culvert
30/12/20	11:41:0	41	0.1	500	10.1	5000	4844	A	26.25008	87.947272	Curve
30/12/20	11:41:11	41	0.1	350	20.2	3500	3473	G	26.24983	87.946295	Normal
30/12/20	11:41:11	41	0.1	480	20.2	4800	4661	A	26.24976	87.945318	Curve
30/12/20	11:42:0	41	0.1	300	10.1	3000	3016	G	26.24948	87.94441	Normal
30/12/20	11:42:22	41	0.1	440	10.1	4400	4296	A	26.24953	87.94345	Speed Breaker
30/12/20	11:42:22	41	0.1	360	10.1	3600	3564	G	26.2497	87.94244	Normal
30/12/20	11:43:0	41	0.1	230	20.2	2300	2376	G	26.24983	87.94148	Normal
30/12/20	11:43:0	41	0.1	360	20.2	3600	3564	G	26.24992	87.940505	Normal
30/12/20	11:43:32	41	0.1	410	10.1	4100	4021	A	26.25006	87.939477	Speed Breaker
30/12/20	11:43:32	41	0.1	440	10.1	4400	4296	A	26.25004	87.938518	Curve
30/12/20	11:44:8	41	0.1	430	10.1	4300	4204	A	26.25052	87.93803	Curve
30/12/20	11:44:8	41	0.1	450	20.2	4500	4387	A	26.25142	87.938063	Curve
30/12/20	11:44:43	41	0.1	230	10.1	2300	2376	G	26.25219	87.937743	Curve
30/12/20	11:45:0	41	0.1	360	20.2	3600	3564	G	26.25265	87.936918	Curve
30/12/20	11:45:18	41	0.1	400	20.2	4000	3930	G	26.25297	87.93601	Curve
30/12/20	11:45:18	41	0.1	300	20.2	3000	3016	G	26.253	87.9351	Normal
30/12/20	11:45:18	41	0.1	290	20.2	2900	2925	G	26.25385	87.934258	Normal
30/12/20	11:46:0	41	0.1	360	20.2	3600	3564	G	26.25465	87.933687	Curve
30/12/20	11:46:0	41	0.1	450	20.2	4500	4387	A	26.25537	87.933635	Curve
30/12/20	11:46:29	41	0.1	440	20.2	4400	4296	A	26.25611	87.93343	Curve
30/12/20	11:46:29	41	0.1	300	30.3	3000	3016	G	26.25621	87.932457	Normal
30/12/20	11:46:29	41	0.1	350	20.2	3500	3473	G	26.25637	87.93148	Normal
30/12/20	11:47:4	41	0.1	620	10.1	6200	5941	P	26.25639	87.930487	Speed Breaker
30/12/20	11:47:4	41	0.1	230	10.1	2300	2376	G	26.2563	87.929493	Normal
30/12/20	11:47:39	41	0.1	350	20.2	3500	3473	G	26.25631	87.928502	Curve
30/12/20	11:48:0	41	0.1	410	20.2	4100	4021	A	26.25691	87.927962	Curve
30/12/20	11:48:15	41	0.1	390	10.1	3900	3839	G	26.2576	87.927642	Curve
30/12/20	11:49:0	41	0.1	360	10.1	3600	3564	G	26.25842	87.927558	Curve
30/12/20	11:49:0	41	0.1	250	20.2	2500	2559	G	26.25915	87.927357	Curve
30/12/20	11:50:36	41	0.1	290	10.1	2900	2925	G	26.26007	87.927592	Normal

$$Y = 0 * X^2 + 0.914 * X + 274.50$$

30.12.20
JE

Arg - 3670.516
30/12/20
m

Clear
30/12/20

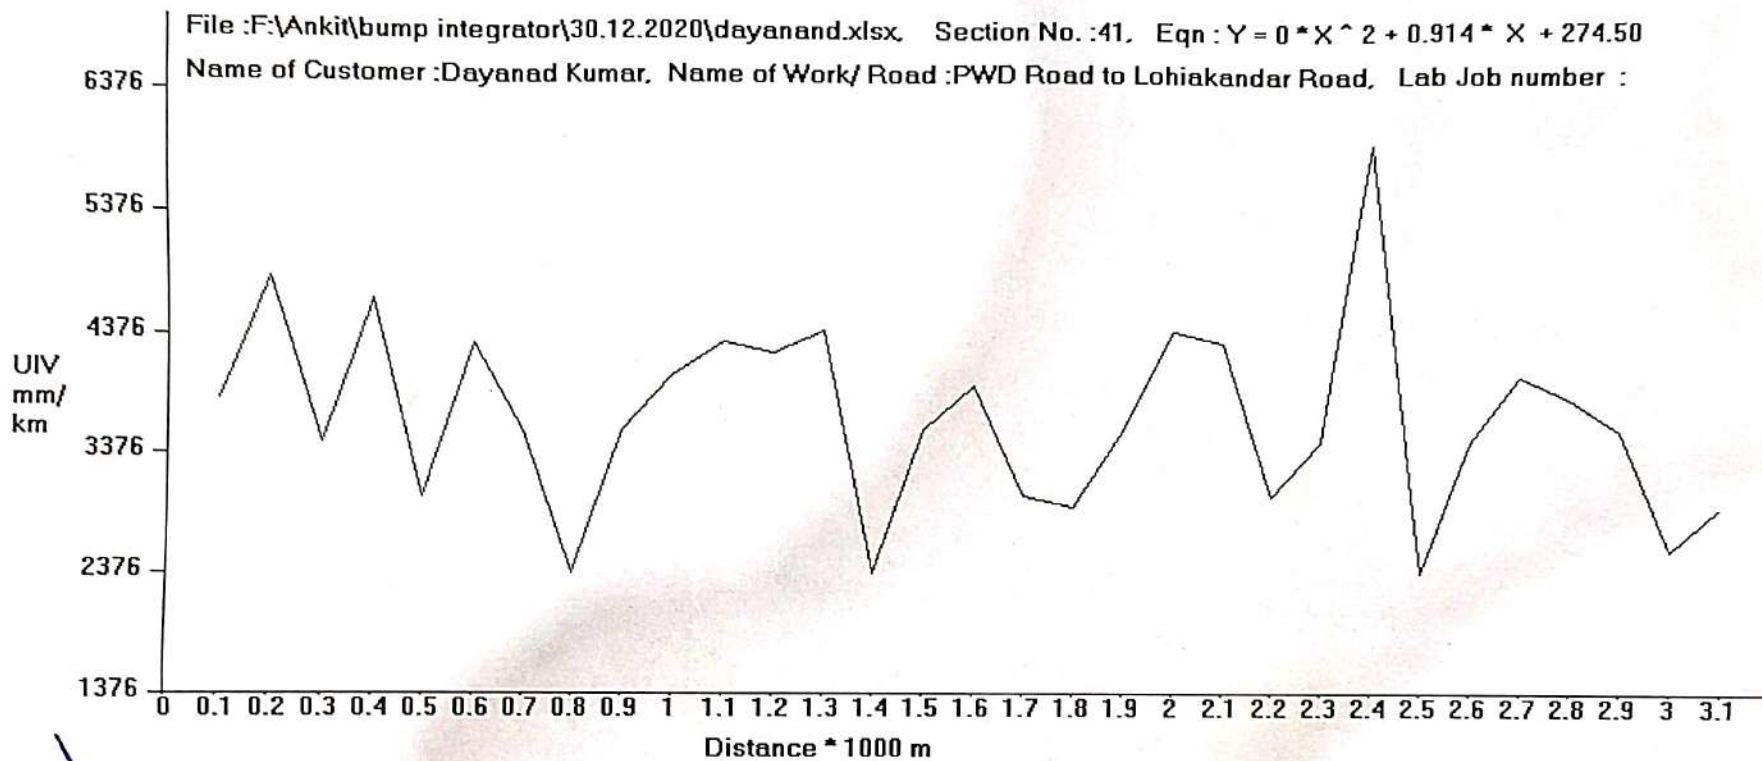

[Signature]
30.12.2020
JE

[Signature]
30/12/2020
RE

[Signature]
30/12/20

Name of work—
 Situation of work—
 Agency by which work is executed—
 Date of measurement—
 No. and date of agreement.
 (These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work—					vertical recti-
					bication and surface
					renewal of road from
					PWD road to Lohiyakanday
					road.
Assessment—	58/3054/M80/2019-20.				
Assessed by—	Dr. Anand Kumar				
Date of survey—	28.12.2019				
Date of completion—	27.09.2020.				

Record measurement

① Clearing and grubbing road					
land included—					
$2 \times 86 \times 30.00 \times 1.00 = 5160.00 \text{ m}^2$					
$2 \times 1 \times 20.00 \times 1.00 = 40.00 \text{ m}^2$					
Total— 5200.00 m^2					
$\approx 0.52 \text{ Hec.}$					
② E/W calculation—					
Chaining	Fill	Mean	Area	Area	Fill
10. male	Area	Area	Area	Area	Volume
(M)	(M ²)	(M ²)	(M)	(M)	(M ³)
0	0.194	—	20	—	14.2
50	0.356	0.280	50	—	12.50
100	0.488	0.422	50	—	21.10
Continuation					
150	0.125	0.307	50	—	15.33
200	0.655	0.390	50	—	19.50
250	0.454	0.555	50	—	27.73

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
58-560 m ² (under mbr-22)					
@ Rs. 92.32 / m ² = Rs. 540600.5 / -					
Total 22 - Rs. 9423080.00 / -					
Add GST @ 12% :- (+) Rs. 1130770.00 / -					
Add LC @ 1% :- (+) Rs. 94231.00 / -					
					Rs. 10648081.00 / -
Less 0.1% eg contract (-) Rs. 10648.00 / -					
					Rs. 10637433.00 / -
 08.01.021 JE			 8/1/2021 AR		
					DAO CSP 21/1/21
