

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, खगडिया।

पत्र संख्या 4.10.2020 खगडिया, दिनांक 12.1.2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, खगडिया।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:— शीर्ष Maintenance Policy-2018 under MR-3054 योजना अन्तर्गत राशि का अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि 3054(MR) योजना अन्तर्गत राशि—67.21197 Lakh (सरसठ लाख इक्कीस हजार एक सौ सन्तान्वे) Only उपलब्ध कराने की कृपा की जाए। इस पत्र के साथ विहित प्रपत्र में अधियाचना राशि समर्पित की जा रही है।

सूचनार्थ सादर समर्पित।

अनु०— यथोक्त

विश्वासभाजन


12.1.21

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

कार्य प्रमण्डल, खगडिया

12/1/21

Application Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
 Name of Works Division :- Khagaria

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requestion against work done (in Lakh)	Remarks
					Length (In km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/KH/KHA/19/0010	Khagaria Bakhri PWD Road se Belaganj tak	29451032310	Lt No.- 3679 Dated 28.08.2019	1.55	94.786	74.2350	12.05230	05 MBD/2020-21 22-6-2020	21-03-21	In progress	3695	25,000	5.00	0.00	0.00	67.21197	

Total 67.21197

Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
 Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer

MRD, Works Division

12/1/21 12/1/21

FROM GFR 19-A
(See Government of India's Decision (1) below Rule-150)
Form of utilization Certificate up to the Month of 11.01.2021

PIU

Executive Engineer,
R.W.D. Works Division,
Khagaria.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	MR(3054) under Bihar Rural Road Maintenance Policy - 2018	Up to Letter No.35 Dt 21-05-2020 Letter No.78 Dt.29-10-2020	30.10422 127.63299	Certified that out of Rs. 157.73721 Lacs received upto date 11/01/2021 in favour of Executive Engineer, RWD, Khagaria sum of Rs. 157.73721 Lacs has been utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy - 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.0.0 remaining unutilized at the end of the period under.
	Total		157.73721	


2 Certified that I have satisfied myself that the conditions on which the grants-in-aid wa sanctioned have been duly

Kind of Checks excercised :-

- (i) Works have been supervised by Executive Engineer/Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- (iii) Construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant.
- (v) All other codal formalities have been observed.

3 Physical Progress achieved :

- (i) Construction of Road Works.
- (ii) Construction of CD Works.


12.1.21
Executive Engineer,
R.W.D. Works Division
Khagaria. 

Steco Analyzer

Name of Customer : shree Narayan Construction
 Name of Work/ Road : Khagaria Bakhari PWD Path to Belaganj
 Lab Job number :
 Date : 19-12-2020
 Section No. : 19


Test Date : 19-12-2020	Road Name : Bakhari PWD Path to Belaganj
Machine No : 403	Road Type : (A) ASPHALTIC
Start S No :	Side :
Start E No :	Interval :
Weather :	UIV Range : 1628 To 5000 1000 mm/km
Start Location :	Dist Range : 0 To 1.6 0.1 * 1000 m
End Location :	Equation : test

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\Shantnu Kumar\Desktop\bump Integrator 19-12-2020\19121925.Xls. Section No. 19. Eqn : test
 Name of Customer : shree Narayan Construction, Name of Work/ Road : Khagaria Bakhari PWD Path to Belaganj.

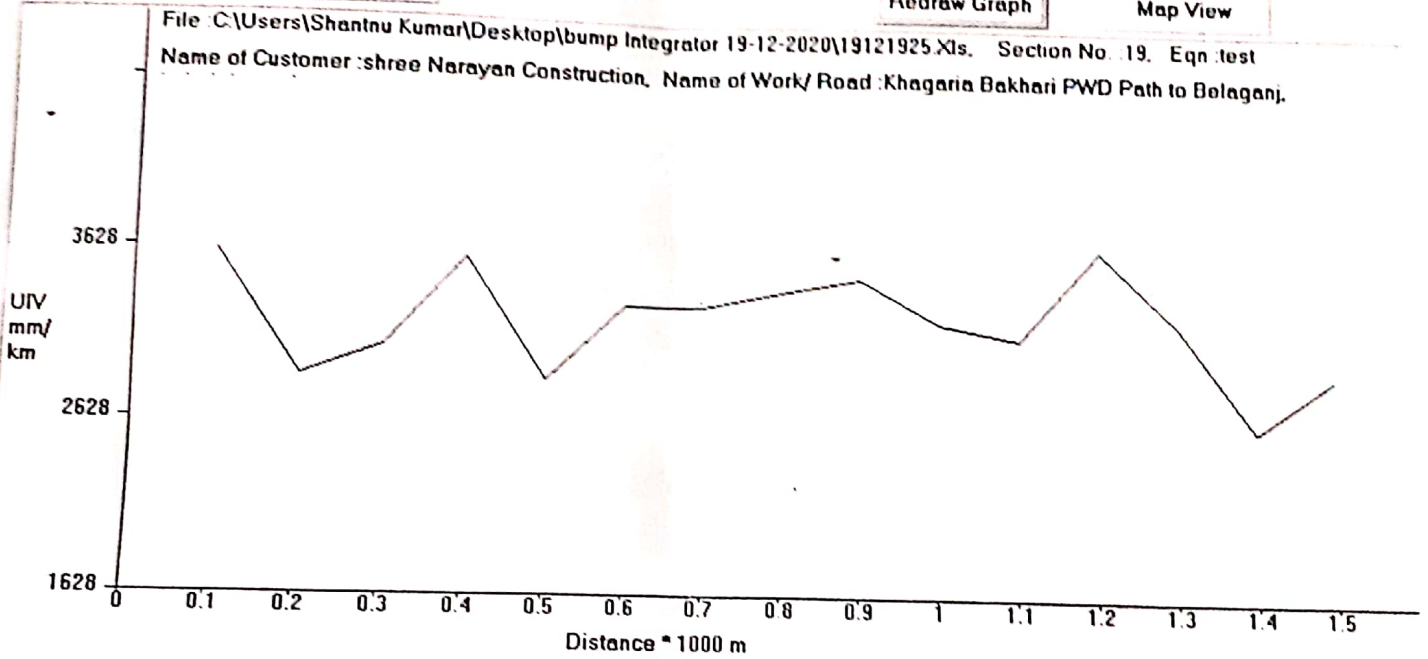

Signature
 19/12/2020
 Khagaria

Signature
 19-12-2020
 A.B
 Khagaria

Signature
 19.12.20
 EC

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
19/12/20	16:10:33	19	0.1	380	0	3800	3606	G	25.52988	86.30173	Normal
19/12/20	16:11:9	19	0.1	300	10.1	3000	2895	G	25.53077	86.3018	Normal
19/12/20	16:11:9	19	0.1	320	20.2	3200	3073	G	25.53127	86.302608	Normal
19/12/20	16:11:44	19	0.1	380	20.2	3800	3606	G	25.53161	86.303552	Normal
19/12/20	16:12:19	19	0.1	300	10.1	3000	2895	G	25.53185	86.304393	Curve
19/12/20	16:12:19	19	0.1	350	10.1	3500	3339	G	25.53205	86.305168	Normal
19/12/20	16:12:19	19	0.1	350	10.1	3500	3339	G	25.532	86.30611	Normal
19/12/20	16:13:30	19	0.1	360	10.1	3600	3428	G	25.53221	86.307087	Normal
19/12/20	16:13:30	19	0.1	370	10.1	3700	3517	G	25.53262	86.307677	Normal
19/12/20	16:14:4	19	0.1	340	10.1	3400	3250	G	25.53356	86.30776	Normal
19/12/20	16:16:25	19	0.1	330	0	3300	3161	G	25.53439	86.307625	Normal
19/12/20	16:19:0	19	0.1	390	0	3900	3695	G	25.53507	86.30712	Normal
19/12/20	16:19:21	19	0.1	340	10.1	3400	3250	G	25.53596	86.306885	Normal
19/12/20	16:19:21	19	0.1	270	20.2	2700	2628	G	25.53687	86.30702	Normal
19/12/20	16:20:0	19	0.078	240	10.1	3077	2963	G	25.5375	86.30744	Normal

$$Y = 0 \cdot X^2 + 0.889 \cdot X + 228.2$$

$$X = 2800$$

$$Y = 2717$$

(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

19/12/20
 Khagand

19/12/20
 E

19-12-2020
 A-E
 Khagand

Est on A/c Bill

Name of work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:- Repair and maintenance of Road from Khyagaria Bakhri PWD Road to Belgamj Tal. (MR-3053)					
Agency:- Sri Nityananda Construction, Gola Road, Patna					
Agreement no- 05 MED/2020-21					
Date of commencement:-					
22.06.20					
Date of completion:- 21.03.2021					

1) Clearing and grubbing m-					
ad land (By manual work)					
including uprooting material					
2x	20x	30.0x	1.00	=	1200.0m ²
2x	20x	30.0x	1.00	=	1200.0m ²
2x	10x	30.0x	1.00	=	600.0m ²
Total					3000.0m ²
=					0.30 Hec.

2) Construction of granular					
sub-base by providing					
well graded material					
1x	12.0x	1.00x	0.150	=	180 m ³
1x	7.50x	0.75x	0.150	=	0.84 m ³

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(vi) Providing and applying dense bituminous concrete with bitumen seal as per technical specifications					
	2x	30.0x	3.75x		225.00 m ²
	3x	30.0x	3.75x		337.50 m ²
	1x	27.00x	3.75x		101.25 m ²
					$5.0x(3.75+5.0)/2 = 21.88 \text{ m}^2$
					$5.0x(5.0+3.75)/2 = 28.00 \text{ m}^2$
					Total: 713.63 m²
(vii) Providing and laying semi dense bituminous concrete with 100-120 mm base layer					
	2x	30.0x	3.75x	0.025x	5.63 m ³
	3x	30.0x	3.75x	0.025x	8.44 m ³
	1x	27.0x	3.75x	0.025x	2.53 m ³
					$5.0x(3.75+5.0)/2x0.025 = 0.55 \text{ m}^3$
					$5.0x(5.0+3.75)/2x0.025 = 0.70 \text{ m}^3$
					Total: 17.85 m³
(viii) Providing and fixing 'legs' of maintenance project as per technical specifications					
					= 2 Nos.
(ix) Road marking with hot applied thermoplastic compound with reflectorising.					

Continuation

Continuation

Scanned by CamScanner

