

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल बेलसंड।

पत्रांक- 943 / बेलसंड दिनांक- 25/01/2021 /

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बेलसंड

संज्ञा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण, पटना।
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय -

MR-3054-BIHAR RURAL ROAD NEW MAINTENANCE POLICY-2018 योजना
अंतर्गत निर्माण कार्य की राशि के अधियाचना के संबंध में।

महोदय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054-BIHAR RURAL ROAD
NEW MAINTENANCE POLICY-2018 योजना अंतर्गत संलग्न सुची के आधार पर पथ में निर्माण
कार्य की राशि का आवंटन उपलब्ध कराने की कृपा की जाए।

अंग्रेजी - यथावत।

विश्वासभाजन

 25/1/21

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेलसंड

 25/01/21

FORM GFR 19-A

(See Government of India;s Decision (IO below Rule-150)

Form of Utilisation Certificate up to the Month of Jan- 2021

Sl.No.	Name of Schemes	Sanction No.& Date with Amount (in Lacs Rs.)	Amount Received (in Lacs Rs.)	Particulars
1	Construction or Rural Roads under MR-3054 New Maintenance Policy.	MR-3054-New Maintenance Policy-2018		Certified that out of Rs 224.87958 Lacs of grants-in-aid
		BRRDA	224.87958	Sanctioned during the year in favour of Executive
		Expenditure	224.70042	Engineer R.W.D Works Div. Belsand a Sum of Rs
				224.70042 lacs has been utilised for the purpose of
		Balance Total	0.17916	New Maint. Policy-2018 Schemes as given in the margin
				for which it was Sanctioned and that the balance of Rs.
				0.17916 lacs remaining utilized at the end of the period
				under report.

Certified that I have satisfied my self that the conditions on which the grant-in aid was sanctioned have been dully

Kind of check exercised

- 1 Work have been supervised by Executive Engineer/ Superintending Engineer
- 2 Periodical inspection has been conducted by Excutive Engineer/Superintending Engineer.
- 3 Contruction Material have been tested.
- 4 Measurment have been recorded in the MBs and test check conducted by the Assistant Engineer/ Excutive Engineer
- 5 Other codal formalities have been observed.

Physical progress achieved

- 1 Contruction of Road works.
- 2 Contraction of CDs works .


Divisional Accounts Officer
Rural Works Department
Works Division Belsand


Executive Engineer
Rural Works Department
Works Division Belsand


25/01/21

Requisition for Scheme Head- MIR(3054) under Bihar Rural Road Maintenance Policy-2018.

Name of Division- RWD (W) Division Beland																			
Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date.	Administrative Approval (AA)		Agreement Amount (In Lakh)			Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	Up-to date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 years Routine Maintenance (In Lakh)											
1	2		4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
		RNI/S/BE L/19/0002	JAMMUA BAZAR TO DIANGAR TOLA	NEA22000 1739	2174 Did 06.07.2019	1.580	58.50100	34.90376	12.98723	69 MBD/2020- 21 Did. 07.08.2020	06.05.2021	23.12.2020	3183	25	5%	19.77000	19.77000	13.62926	Completed
		RNI/S/BE L/19/0002	Hashima to Pachtaki Jaddu	NEA2200017 46	2174 Did 06.07.2019	2.000	72.72800	44.85665	15.91157	69 MBD/2020- 21 Did. 07.08.2020	06.05.2021	21.12.2020	3403	25	5%	25.80600	25.80600	17.44592	Completed
		RNI/S/BE L/19/0002	MARPA TO AKITA TOLA	31608102099	2174 Did 06.07.2019	2.300	83.66800	50.28378	18.71836	69 MBD/2020- 21 Did. 07.08.2020	06.05.2021	19.12.2020	3267	25	5%	0.00	0.00000	36.84181	Completed
Total:-																45.57600	45.57600	67.91699	


 Executive Engineer
 R.W.D. (W.) Division
 Beland
 25/11/21

Name of Customer :	RAJESH KUMAR
Name of Work / Road :	HASHIMA TO PACHTAKI JADU
Lab Job number :	394
Date :	24-12-2020
Section No. :	20


Test Date :	24-12-2020	Road Name :	HASHIMA TO PACHTAKI JADU
Machine No. :	394	Road Type :	(R) RURAL ROAD
Start S No. :		Side :	
Start E No. :		Interval	
Weather :		UV Range :	1854 To 5000 1000 mm/km
Start Location :		Dist Range :	0 To 2.1 0.1 * 1000 m
End Location :		Equation :	$Y = 2700 * X^2 + 0.989 * X - 13.58$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BPRDA116\OneDrive\Desktop\HASIMA TO PACHTAKI JADDU.Xls, Section No. : 20, Eqn : $Y =$
 Name of Customer : RAJESH KUMAR, Name of Work / Road : HASHIMA TO PACHTAKI JADDU, Lab Job number

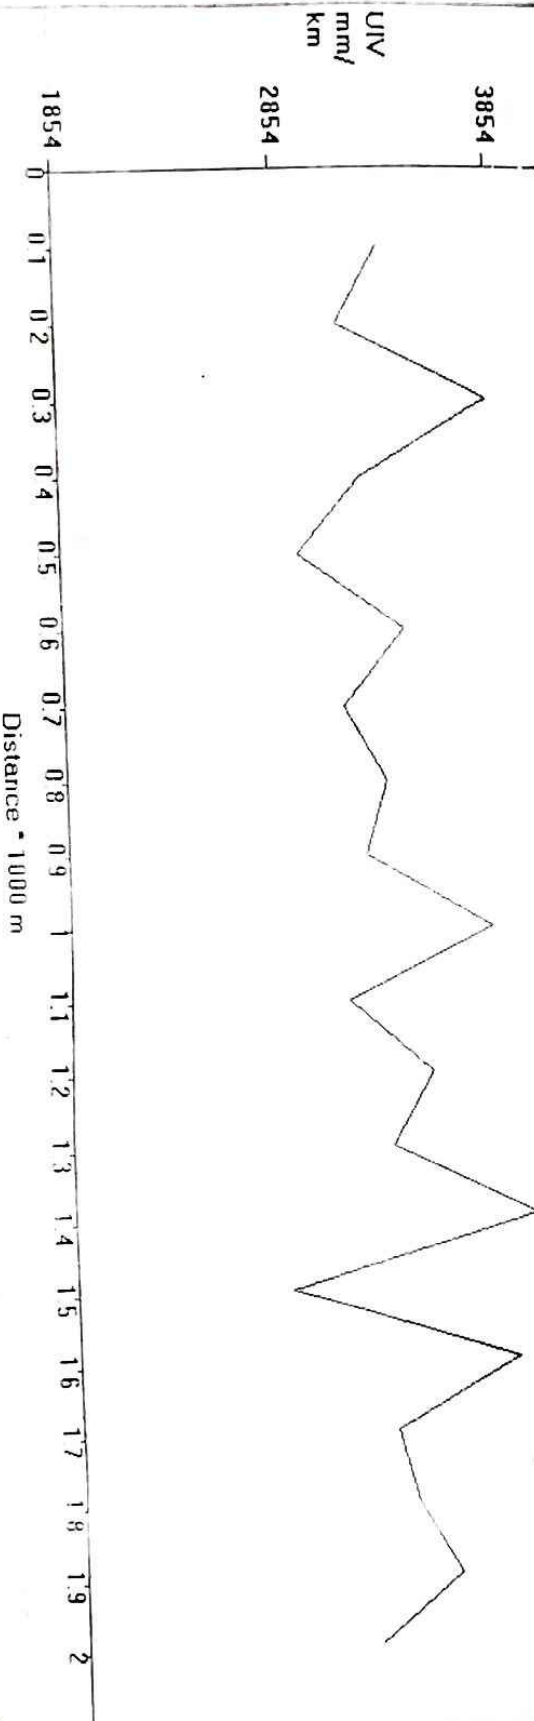

Sagib

24.12.2020

S.E

24.12.2020
Sagib

24/12/20

Executive Engineer
R. W. D. Works Division
Belsand

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	TEGORY ROAD	IRI	Latitude	ongitude	Event
24/12/20	14:41:0	20	0.1	340	10.1	3400	3349 G	4.44	26.70511	85.27389	Normal	
24/12/20	14:41:12	20	0.1	320	30.3	3200	3151 G	4.2	26.70437	85.27333	Normal	Y = 2700 * X ^ 2 + 0.989 * X - 13.58 X = 3300 Y = 3250
24/12/20	14:41:12	20	0.1	390	30.3	3900	3843 G	5.02	26.70349	85.27293	Normal	
24/12/20	14:41:47	20	0.1	330	30.3	3300	3250 G	4.32	26.70258	85.27274	Normal	
24/12/20	14:42:0	20	0.1	300	30.3	3000	2953 G	3.97	26.7017	85.27241	Normal	(R) RURAL ROAD
24/12/20	14:42:0	20	0.1	350	30.3	3500	3447 G	4.55	26.7009	85.27195	Normal	Good
24/12/20	14:42:0	20	0.1	320	30.3	3200	3151 G	4.2	26.7001	85.27114	Normal	<4000
24/12/20	14:42:22	20	0.1	340	40.4	3400	3349 G	4.44	26.69942	85.27069	Normal	Average
24/12/20	14:42:22	20	0.1	330	40.4	3300	3250 G	4.32	26.69879	85.26987	Normal	Poor
24/12/20	14:42:22	20	0.1	390	30.3	3900	3843 G	5.02	26.6983	85.26902	Curve	
24/12/20	14:43:0	20	0.1	320	40.4	3200	3151 G	4.2	26.69779	85.26816	Normal	
24/12/20	14:43:32	20	0.1	360	40.4	3600	3546 G	4.67	26.69722	85.26731	Normal	
24/12/20	14:43:32	20	0.1	340	30.3	3400	3349 G	4.44	26.6967	85.2665	Curve	
24/12/20	14:44:0	20	0.1	410	30.3	4100	4041 A	5.25	26.69605	85.26572	Bridge	
24/12/20	14:44:7	20	0.1	290	30.3	2900	2854 G	3.85	26.69529	85.2652	Normal	
24/12/20	14:44:7	20	0.1	400	30.3	4000	3942 G	5.13	26.69452	85.26458	Normal	
24/12/20	14:44:42	20	0.1	340	30.3	3400	3349 G	4.44	26.69373	85.26406	Normal	
24/12/20	14:44:42	20	0.1	370	30.3	3700	3645 G	4.79	26.69296	85.26343	Bridge	
24/12/20	14:49:0	20	0.1	350	30.3	3500	3447 G	4.55	26.69036	85.26091	Normal	
24/12/20	14:49:7	20	0.1	330	40.4	3300	3250 G	4.32	26.68949	85.26044	Normal	
AVERAGE							3408					

24/12/2020
S.E

24/12/2020
S.E

Executive Engineer
R. W. D. Works Division
Belsand

ABSTRACT OF COST :-

24

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
① clearing and grubbing road land ---					
Qty. vide TMBP (15)					
Item no :- ① = 0.39 Ha					
@ Rs 494.96.70/Ha					Rs 19303.00
② Construction of subgrade					
② and earthen shoulders with approved material --- as per specification					
Qty. vide TMBP (15)					
Item no :- ② = 319.0 m ²					
@ Rs 176.75 m ²					Rs 144752.00
③ construction of granules					
③ sub base --- as per specification					
Qty. vide TMBP (15)					
Item no :- ③ = 200.343 m ³					
@ Rs 2154.29/m ³					Rs 431596.00
④ P/L and spreading					
④ and compacting --- (cum gr-2) ---					
Qty. vide TMBP (15)					
Item no :- ④ = 85.276 m ²					
@ Rs 3890.89/m ²					Rs 331799.00
				C/o	Rs 927456.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑤ P/L, Spreading and					
⑤ Compacting -					
WBM gr-3 - - -					
Qty. vide Tms P ⑫					
Item no:- ⑤ = 128.45m ³					
@ R 3591.44/m ³					R 461320.00
⑥ Providing and					
⑥ Supplying primer					
Coat with bitumen					
Emulsion (SS-1) - -					
Qty. vide Tms P ⑫					
Item no:- ⑥ = 1712.86m ²					
@ R 4140/m ²					R 70904.00
⑦ P/A tack Coat					
⑦ with bitumen					
Emulsion - - -					
Qty. vide Tms P ⑫					
Item no:- ⑦ = 1787.66m ²					
@ R 14.04/m ²					R 25098.00
⑧ P/L and rolling of					
⑧ close graded premix					
Surfacing - - -					
Qty. vide Tms P ⑫					
Item no:- ⑧ = 1787.66m ²					
@ R 206.82/m ²					R 369723.00
					C/P 1854501.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑨ Providing and applying					
⑨ tack coat with bitu-					
men emulsion - -					
as per specification					
Qty. vide TMBP ⑦					
Item no:- ⑨ = 7372.0m ²					
@ Rs 11.77/m ²					Rs 86768.00
⑩ P/L Semi dense					
⑩ bituminous Concrete					
- - as per spec.					
Qty. vide TMBP ⑦					
Item no:- ⑩ = 184.30m ²					
@ Rs 10358.49/m ²					Rs 1909069.00
⑪ R.C.C m-15 grade					
⑫ kilometre local					
Stone - - as per spec.					
Qty. vide TMBP ⑦					
Item no:- ⑪ = 3 nos.					
@ Rs 2353.25/no.					Rs 7059.00
⑬ 200m Stone					
⑬ Qty. vide TMBP ⑦					
Item no:- ⑬ = 8 nos.					
@ Rs 629.93/no.					Rs 5119.00
⑮ P/F of retro refl-					
⑮ ectronised - -					
Qty. vide TMBP ⑦					
Item no:- ⑮ = 4 nos.					
@ Rs 3686.83/no.					Rs 14747.00
c/o					Rs 3877263.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(14) 600mm circular					
(15) Qty. vide Tmbf (18)					
Item no:- (14) = 2 nos.					
@ Rs 3786.18/no.					Rs 7572.00
(15) 600mm X 450mm					
(17) rectangular					
Qty. vide Tmbf (18)					
Item no:- (15) = 2 nos.					
@ Rs 3657.06/no.					Rs 7314.00
(16) RCC m15 grade					
(18) boundary pillar					
- as per spec.					
Qty. vide Tmbf (18)					
Item no:- (16) = 24 nos.					
@ Rs 509.10/no.					Rs 12218.00
(17) P/L of hot applied					
(21) thermoplastic --					
2.5mm thick --					
Qty. vide Tmbf (18)					
Item no:- (17) = 390.0m ²					
@ Rs 735.40/m ²					Rs 286806.00
(18) P/F of typical					
(22) masonry infomatory					
Sign board --					
Qty. vide Tmbf (18)					
Item no:- (18) = 2 nos.					

Continuation

@ Rs 9401.98/no.

Rs 18803.00

C/o Rs 4209976.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(19) Brick masonry work					
(23) in Cement mortar					
1:3 in parapet --					
Qty. vide TMBF (19)					
Item no:- (19) = 5.042 m ³					
@ Rs 266.93/m ³					Rs 2655.00
(20) plastering with					
(24) Cement mortar					
(1:4) --					
Qty. vide TMBF (19)					
Item no:- (20) = 40.296 m ²					
@ Rs 173.28/m ²					Rs 6982.00
(21) Painting two					
(25) coats including					
primer coat --					
Qty. vide TMBF (19)					
Item no:- (21) = 98.096 m ²					
@ Rs 95.63/m ²					Rs 9380.00
					Rs 4252893.00
Less 10% as per agreement (-)					Rs 425289.00
					Rs 3827604.00
Add 1% labour cess (+)					Rs 38276.00
Add 12% GST (+)					Rs 459312.00
					Rs 4325192.00
Less as per last allotment (-)					Rs 2580600.00
S.A.O.					Rs 1744592.00

Continuation

Sagunb

23.01.2021

B.R.

25/1/21

23.01.2021
