

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल समस्तीपुर ।

पत्रांक: 5623/90

दिनांक:- 4-03-2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल समस्तीपुर ।

सेवा मे,

अपर मुख्य कार्यपालक पदाधिकारी - सह - सचिव
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:- नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत व्यय हेतु आवंटन की मांग ।

महाशय,

उपर्युक्त विषयक नई अनुक्षण नीति 2018 शीर्ष MR-3054 योजना मद अंतर्गत व्यय हेतु
विहित प्रपत्र मे अधियाचना पत्र संलग्न कर भेजी जा रही है।

अतः अनुरोध है कि संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने का कृपा की जाए,
ताकि किये गये कार्यो का भुगतान किया जा सके ।

अनु० :- यथोक्त ।

विश्वासभाजन

कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमंडल समस्तीपुर ।

4-3-2021

FROM GFR 19-A
(See Government of India's Division (I) below Rule- 150)

Form of Utilization Certificate Up To 02.03.2021
PIU- E.E., R.W.D. Works Division, Samastipur

S.N.	Name of Scheme	Sanction No.& Date with Amount	Amount Received	Particulars
1	Construction of Rural Road under 3054 (M/R)	Secretary cum Empowered Officer BRRDA Bihar Patna vide up to	95399814.00	Certified that out of Rs.95399814.00 received Upto 02.03.2021 in favour of Executive Engineer R.W.D. Works Division Samastipur a sum of Rs.68776488.00 has been utilized for the purpose of MR-3054 Maintenance Repairs Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 26623326.00 remaining unutilized at the end of period under report.
			95399814.00	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have

Kind of Checks exercised:-

- i Works have been supervised by Executive/Superintending engineer.
- ii Periodical inspection has been conducted by Executive/Superintending engineer.
- iii Construction materials have been tested.
- iv Measurements have been recorded in the MB's and test check conducted by Assistant Engineer/Executive
- v All other codal formalities have been observed.

3 Physical Progress achieved:-

- i Construction of Road work.
- ii Construction of CD works.

[Signature]
SR. Divisional Account Officer
R.W.D (W) Division Samastipur

[Signature]
Executive Engineer
Works Division Samastipur
Rural Works Dipartment

[Signature]
4.3.2021

Requisition Format for scheme Head : MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Sl No	Package No	Project ID as Per MIS	Name of Road	Administrative Approval (AA) Letter No & Date	Administrative		Agreement		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in MM)	Value of Bitumen Content in Percent	Previous Total Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal	5 Year Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SA/S AM/19/0 014	32010102096	X-ROAD L039 - JAGDISHPUR	2173 & 06/07/2019	1.4	50.46	29.699	13.267	11(MBD)19 -20/ 26.2.2020	7-Oct-20	On- Going	3940.2	25	5.1	28.69900	28.69900	0.61474	Work Complete
2	RM/SA/SA M/19/0007	32010102061	SH - CHANDHARPUR	2173/ 07.06.19	1.64	17.18	34.207	15.20719	12(MBD)201 9- 20/26.02.20	07.10.202	OnGoing	3016.68	25	5.1	17.1035	0	14.60097	BT Complete
3	RM/SA/SA M/19/0012	32010102034	CHATURABAHUARA - KHATUAHA	2173/ 07.06.19	0.73	17.92	15.941	6.37047	14(MBD)201 9- 20/02.03.20	07.10.2020	Ongoing	3135.57	25	5.1	4.462	0	11.479	BT Complete
4	RM/SA/SA M/19/0007	32010102030	Tara chok - Bhato chowk	2173/ 07.06.19	7.0	150.57	133.583	66.90639	12(MBD)201 9- 20/26.02.20	7-Oct-20	Ongoing	3326.85	25	5.1	60.11235	0	73.3252	BT Complete
5	RM/SA/ SAM/19 /0006	NEA220005 69	MAIN ROAD TO - BHINDI	2173 & 06/07/2019	4.0	89.27	78.287	34.5465	14(MBD)20- 21/02.06.202	01.03.2021	On-Going	3593.15	25	5.2	0	0	78.19987	Work Complete
Total						325.40000	291.71700	136.29755									178.21978	


1 Signed Hard Copy and Soft Copy (In Excel) of recorded IRI is enclosed.
2 Up-to-date Physical Progress has been uploaded in MIS

Sr. Divisional Account Officer
R.W.D (W) Division Samastipur

Executive Engineer
RWD (W) Div. Samastipur

4.3.2021

File D:\bumpf\integrator\X-ROAD\1039 - JAGDISHPUR.xls, Section No. 35, Eqn. Test
 Name of Customer: Bhola kumar, Name of Work/Road: X-ROAD 1039 - JAGDISHPUR, Lab Job number :

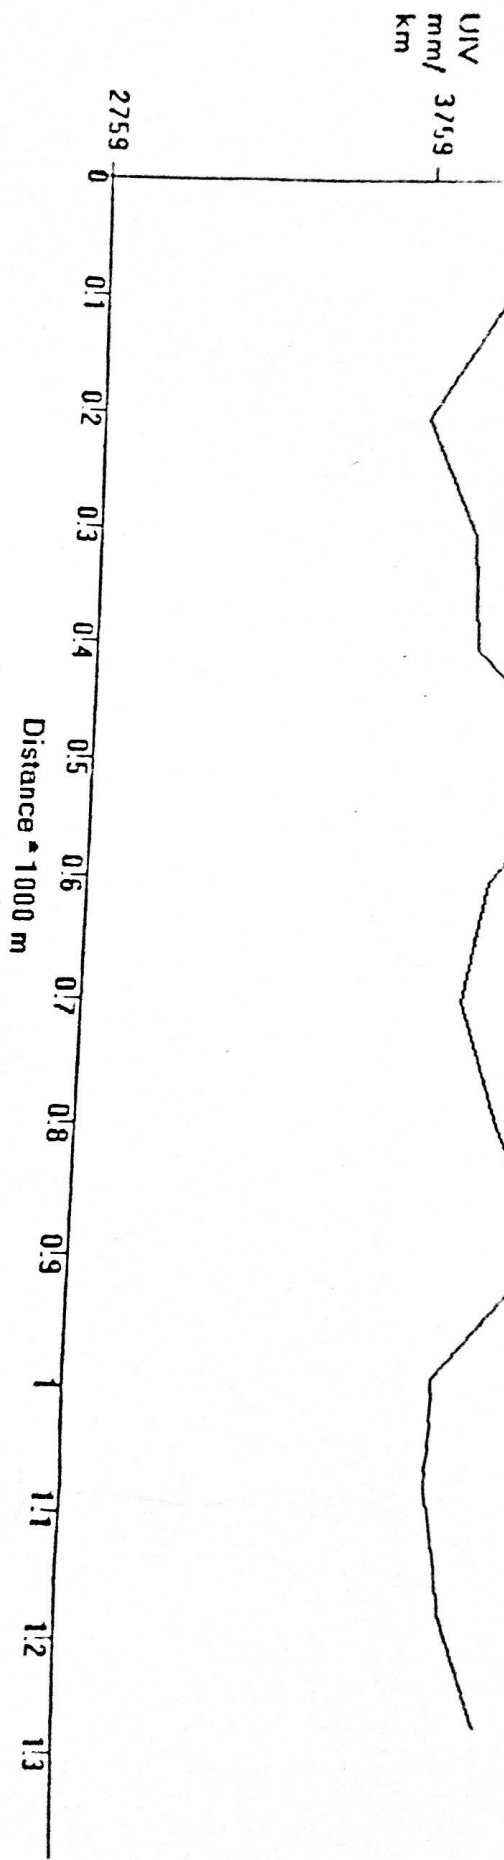

Curve 2nd Speed Breaker test of 2nd section after 9000 of center

[Signature]
 12/10/2020
 J.E. Puda-1
[Signature]
 12/10/2020
 A.E. Puda-1

[Signature]
 16/10/20

