

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, दानापुर।

पत्रांक:- 1555 अगु०

दानापुर/दिनांक:- 03/09/21

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल दानापुर।

सेवा में,

अधीक्षण अभियंता
ग्रामीण कार्य विभाग,
कार्य अंचल, पटना।

विषय:- शीर्ष-3054, जानीपुर फुलवारी मेन रोड बभनपुरा मोड़ मिशन तक पथ निर्माण कार्य का समय-वृद्धि के संबंध में।

महाशय,

उपर्युक्त विषय के संदर्भ में कहना है कि योजना शीर्ष-3054, जानीपुर फुलवारी मेन रोड बभनपुरा मोड़ मिशन तक पथ निर्माण कार्य का समय-वृद्धि हेतु प्रस्ताव समर्पित किया जाता है।

योजना का विन्दुवार प्रतिवेदन भेजा जा रहा है।

1. स्थल विडियो ग्राफी का सीडी
2. (1) कार्य प्रारंभ करने की तिथि-18.11.2019 है।
(2) एकरारनामा के अनुसार कार्य पूर्ण करने की तिथि-17.05.2020 था।
(3) कोविड-2019 के कारण लॉकडाउन एवं संवेदक के परिवार में कोविड हो जाने के कारण कार्य बन्द हो गया, इसलिए समयवृद्धि की आवश्यकता है। संवेदक द्वारा दिनांक-14.07.2021 तक कार्य पूर्ण कर देने का शपथ पत्र दिया गया है।

अतः अनुरोध है कि उक्त कार्य का समय-वृद्धि प्रस्ताव की स्वीकृति देने की कृपा की जाय।

अनु०:- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल दानापुर।

03/09/21

APPLICATION FORM FOR EXTENSION OF TIME

1. Name of Contractor:- **BRICK VALUE PUT LTD**

2. Name of Work:- **construction of five year old Flood from Janipur to hulumaimai Road Bobhamra more to misham (MR 3054)**

(Head of Expenditure)

3. Agreement No.:- **11/SBD/2019-2020**

4. Agreement Value:- **1,26,68,088 = -**

5. Date of Commencement of Work:- **18/11/2019**

6. Date of Completion stipulated in the Agreement:- **17/05/2020**

7. Period of Which Extension has been given Previously:-

8. Work done of %:- **100 %**

9. Period for Which Extension now Applied for :- **14/07/21**

10. Reason for extension of time:- **कोविड के कारण**

11. Recommendation by J.E. :- **संवैदक के परिणाम में कोविड से प्रभावित एवं कोविड-19 के लंबी के कारण कार्य बाधित रहा, अतः समय-वृद्धि दिया जा सकता है।**

12. Whether Programme of work approved :-

**24/08/21
J.E.**

13. Whether fund available:-

14. If spill over from previous financial Year whether included in the current work programme or not:-

15. Recommendation of S.D.O.:-

**Recommended
24/8/21
A.B.**

16. Recommendation of Executive Engineer:-


3/9/21

17. Recommendation of S.E.:-

18. Recommendation of C.E.:-

Deponent's Signature
Deponent's Name
Deponent's Address
Deponent's Profession
Deponent's Date of Birth
Deponent's Date of Signature

22/08/21



शपथ-पत्र

मैं श्रीकस्त भैल्यू प्राणलिंग, वार्ड नं०-21 भवानीपुर जिरात, बियर रोबींग कल्ब, मोतीहारी।

शपथ पूर्वक घोषणा करता हूँ।

1. यह कि मैं शीर्ष-3054, जानीपुर फुलवारी मेन रोड बभनपुरा मोड़ मिशन तक पथ निर्माण कार्य

अन्तर्गत एकरारनामा संख्या-11SBD वर्ष 2019-20 का संवेदक हूँ। कोविद-2019 के कारण

लॉकडाउन हो जाने के कारण परिवार में कोविद हो जाने के फलस्वरूप कार्य को बन्द हो

गया दिनांक-14.07.2021 तक समयवृद्धि की आवश्यकता है।

2. विषयाकित कार्य दिनांक-14.07.2021 तक कार्य पूर्ण कर दिया गया है।

यह कि समय वृद्धि की स्वीकृति के उपरांत भुगतान के अलावे अन्य किसी प्रकार के बड़े हुए


दर का कोई दावा मैं पेश नहीं करूंगा।

यह कि उपरोक्त बातें हमारी जानकारी में सही व सत्य है।



Shikva
शपथकर्ता का हस्ताक्षर

I, Identify the deponent
who, Signed in my presence
22.8.21

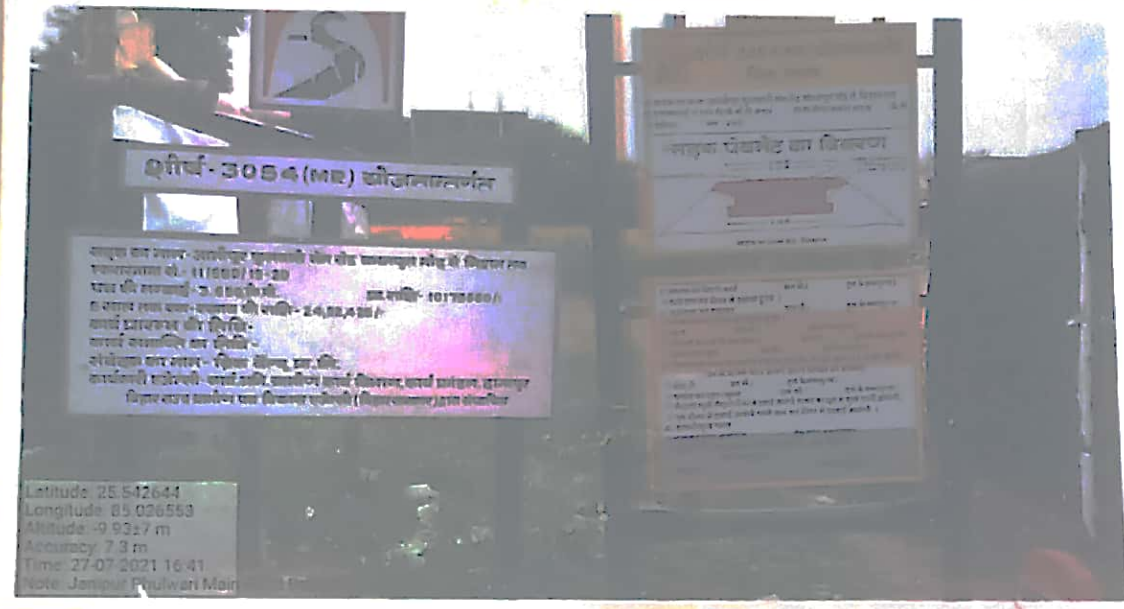

3054 5212 11773 23 7912 1802 424
954481 473 14517 15 2114246
P9 5428 289 11919

Schedule XLV-Form No.-134

EXECUTIVE ENGINEER
DANAPUR. DIVISION

PHULWARISARAI SUB-DIVISION
Brick value pvt Ltd

MEASUREMENT BOOK

MBNO-1349

2 x 5 x 0.4 x 0.6 = 2.4 m²

⑧ Guarding Scaffolding (1:1)

on brickwork on 4 sides

all complete job.

$$2 \times 2 \times 5.00 \times 0.600 = 12.000 \text{ m}^2$$

$$2 \times 5.00 \times 0.400 = 4.000 \text{ m}^2$$

$$4 \times 0.400 \times 0.600 = 0.960 \text{ m}^2$$

$$\text{Total Qty.} = 16.960 \text{ m}^2$$

M
14/7/21
AB

Signed
14/07/21
J. R.

Continuation

Particulars	Details of actual measurement				of area
	No.	L.	B.	D.	

Abstract of Cost.

(1) Providing clearing and grubbing of Road bed
 ----- do ----- do -----
 ----- all complete job.

V.T.M.B.P. ----- (13)

Qty. ----- 0.47 Hec

@ Rs. 42244.52/Hec. - Rs. 23145.01

(2) Providing Box Cutting of Road across in Soil
 ----- do ----- do -----
 ----- all complete job.

V.T.M.B.P. ----- (13)

Qty. ----- 317.100 m²

@ Rs. 8199/m² - Rs. 25979.01

(3) Providing Const. of Subgrade and Earthen Shoulders
 ----- do ----- do -----
 ----- all complete job.

V.T.M.B.P. ----- (17)

Qty. ----- 1728.800 m³

@ Rs. 194.91/m³ - Rs. 33696.30

(4) Const. of granular Sub-base by providing well graded material. ----- do -----
 ----- do ----- all complete job.

V.T.M.B.P. ----- (14)

Qty. ----- 486.493 m³

@ Rs. 2391.07/m³ - Rs. 1163677.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑤ Providing, laying, spreading and Compacting Stone aggregates of specific sizes to W.B.M. on - III material					
do do					
all Compleat Job.					
V.T.M.B.P.	(14)				
Qty.		680.908	m ³		
@Rs. 4160.60/m ³					Rs. - 2832986=00
⑥ Providing Prime Coat with bitumen emulsion (SS-1) on prepared granular surface					
do do					
all Compleat Job.					
V.T.M.B.P.	(14)				
Qty.		7335.125	m ²		
@Rs. 50.23/m ²					Rs. - 368443=00
⑦ Providing Tack Coat with bitumen emulsion (RS-1) on the prepared granular surface					
do do					
all Compleat Job.					
V.T.M.B.P.	(14)				
Qty.		7335.125	m ²		
@Rs. 17.03/m ²					Rs. - 124917=00
⑧ Providing 20mm thick Min. Seal Surfacing material					
do do					
all Compleat Job.					
V.T.M.B.P.	(14)				
Qty.		7335.125	m ²		

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(12) Providing Const. of non-reinforced Plain Cement Concrete (M30) Pavement material ——— do ——— do ———					
--- all Complet. Job.					
V.T.M.B.P. ——— (15)					
Qty. ——— 286.200 m ³					
@ Rs. 7851.32/m ³ ——— Rs. 2247048 = 001					
(13) Laying bricks Soling layer on prepared sub-grade with bricks on end edging ——— do ——— do ———					
--- all Complet. Job.					

V.T.M.B.P. ——— (17)					
Qty. ——— 227.350 m ²					
@ Rs. 563.36/m ² ——— Rs. 128080 = 001					
(14) Providing and fixing Kilometre Stone ——— do ———					
--- do --- all Complet. Job.					
V.T.M.B.P. ——— (18)					
(1) Km Stone ——— 5 Nos.					
@ Rs. 2470.64/Each ——— Rs. 12353 = 001					
(2) 200m Stone ——— 14 Nos.					
@ Rs. 692.42/Each ——— Rs. 9694 = 001					
(17/12) Providing and fixing of Traffic Signs ——— do ———					
--- all Complet. Job.					
V.T.M.B.P. ——— (19)					
(1) 600mm equilateral triangle ——— 4 Nos.					
@ Rs. 1696.81/Each ——— Rs. 6787 = 001					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(13/13) Providing Road Marking with Hot applied thermoplastic Compound — do —					
— do — all complet Job.					
V.T.M.B.P. — (18)					
Qty. — 377.000 m ²					
@ Rs. 941.14/m ² — Rs. 354810 = 00/-					
(14/14) Providing and fixing of typical MMSY informatory sign board with Logo — do —					
— do — all complet Job.					
V.T.M.B.P. — (5) — Qty. — 2 Nos.					
V.T.M.B.P. — (17) — Qty. — 2 Nos.					
Total Qty. — 4 Nos.					
@ Rs. 10758.24/Ech. — Rs. 43036 = 00/-					
(15/15) Providing Brick Masonry in C.M.(1:2) in Scrapel well — do —					
— do — do —					
— all complet Job.					
V.T.M.B.P. — (18)					
Qty. — 2.400 m ³					
@ Rs. 7767.84/m ³ — Rs. 18643 = 00/-					
(16/16) Providing Plastering (1:4) on brick work — do —					
— all complet Job.					
V.T.M.B.P. — (18)					
Qty. — 16960 m ²					
@ Rs. 181.24/m ² — Rs. 3079 = 00/-					
1508 = 00/-					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
B/Gl. —				53 0546	
Rs. —				9402348	= 00/-
Total Rs.				53 0546	= 00/-
Less 10% Below Agreement (-)				940235	= 00/-
Total Rs.				8462113	= 00/-
Less Previous Paid Amount (-)				8459512	= 00/-
				3588570	= 00/-
Net Payable Amount —				4873543	= 00/-
Satisfied Measurement —				4873542	= 00/-
✓ Vignar (S/O)				19/07/21	J. D.
14/07/21					
संबंधित द्वारा एक शहनामा के अनुकूल कार्य पूर्ण कर दिया गया					
				14/07/21	
