

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, दानापुर।

पत्रांक:- 1554 अशु०

दानापुर/दिनांक:- 03/09/21

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल दानापुर।

सेवा में,

अधीक्षक अभियंता
ग्रामीण कार्य विभाग,
कार्य अंचल, पटना।

विषय:- शीर्ष-3054, बगड़ा मुख्य पथ से बेतौड़ा तक पथ निर्माण कार्य का समय-वृद्धि के संबंध में।
महाशय,

उपर्युक्त विषय के संदर्भ में कहना है कि योजना शीर्ष-3054, बगड़ा मुख्य पथ से
बेतौड़ा तक पथ निर्माण कार्य का समय-वृद्धि हेतु प्रस्ताव समर्पित किया जाता है।

योजना का विन्दुवार प्रतिवेदन भेजा जा रहा है।

1. स्थल विडियो ग्राफी का सी0डी0

2. (1) कार्य प्रारंभ करने की तिथि-28.10.2019 है।

(2) एकरारनामा के अनुसार कार्य पूर्ण करने की तिथि-27.02.2020 था।

(3) पूर्व में दिनांक-30.03.2020 तक का समयवृद्धि लिया गया था। कोविड-2019 के कारण
लॉकडाउन एवं संवेदक के परिवार में कोविड हो जाने के कारण कार्य बन्द हो गया,
इसलिए समयवृद्धि की आवश्यकता है। संवेदक द्वारा दिनांक-15.07.2021 तक कार्य
पूर्ण कर देने का शपथ पत्र दिया गया है।

अतः अनुरोध है कि उक्त कार्य का समय-वृद्धि प्रस्ताव की स्वीकृति देने की कृपा की
जाय।

अनु०:- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल दानापुर।



APPLICATION FORM FOR EXTENSION OF TIME

1. Name of Contrator:- *Brick Value Pvt. Ltd.*
2. Name of Work:- *Construction and five years maint of Road from Bagada main Road To Betwada (MR 3054)*

(Hread of Expenditure)

3. Agreement No.:- *10/SB7/2019-2020*
4. Agreement Value:- *60,32,586 =*
5. Date of Commecement of Work:- *28/10/2019*
6. Date of Completion stipulated in the Agreement:- *27/02/2020*
7. Period of Which Extension has been givev Previously:-
8. Work done of %:- *100%.*
9. Period for Which Extension now Applied for :- *15/07/21*
10. Resion for extention of time:- *कोविड के कारण*

11. Recomandation by J.E. :- *सर्वेदक के परिवार में कोविड से ग्रस्त एवं कोविड-19 के बंदी के कारण कार्य बाधित रहा/ अतः समय वृद्धि किया जा सकता है।*
Signed 24/08/21
S. D.
12. Whether Programme of work approved :-

13. Whether fund available:-

14. If spill over from previous financial Year whether included in the current work programme or not:-

15. Recommendation of S.D.O.:-

Recommended
AB
24/08/21

16. Recommendation of Executive Engineer.:-

3/9/21

17. Recommendation of S.E.:-

18. Recommendation of C.E.:-

3rd/5th... N 1455
Deponent's Signature/L. T.
Identified by...
Advocate, Solely affirmed and
Declared before me.

D.K. SINHA
NOTARY PUBLIC



शपथ-पत्र

मैं ब्रीक्रस भैल्यू प्रा0लि0, वार्ड नं0-21 भवानीपुर जिरात, निधर-सेबींग कल्ब, मोतीहारी।


शपथ पूर्वक घोषणा करता हूँ।

1. यह कि मैं शीर्ष-3054, बगड़ा मुख्य पथ से बेटौड़ा तक पथ निर्माण कार्य अन्तर्गत एकरारनामा संख्या-10SBD वर्ष 2019-20 का संवेदक हूँ। इस कार्य में 31.03.2020 तक का समयवृद्धि दिया गया था। कोविद-2019 के कारण लॉकडाउन हो जाने एवं परिवार में कोविद ग्रसित होने के कारण कार्य को बन्द हो गया दिनांक-15.07.2021 तक समयवृद्धि की आवश्यकता है।
2. विषयांकित कार्य दिनांक-15.07.2021 तक कार्य पूर्ण कर दिया गया है।
3. यह कि समय वृद्धि की स्वीकृति के उपरांत भुगतान के अलावे अन्य किसी प्रकार के बड़े हुए दर का कोई दावा मैं पेश नहीं करूंगा।

यह कि उपरोक्त बातें हमारी जानकारी में सही वो सत्य है।



Brickvalue
शपथकर्ता का हस्ताक्षर

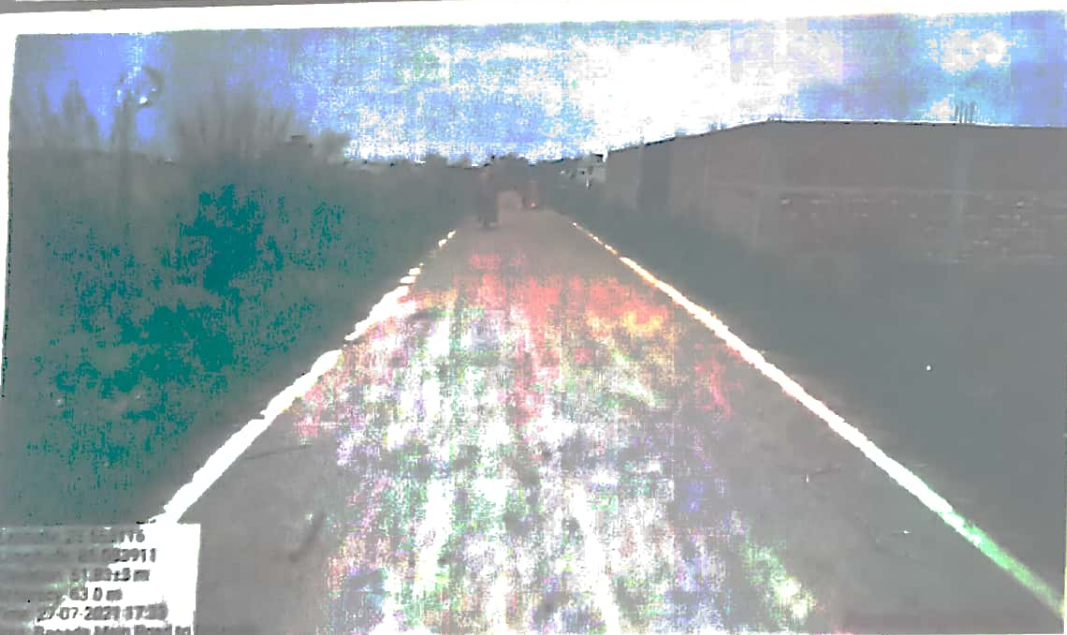

21/8 2054 अन्तर्गत कांस्टाबल पुराणा
५५ से कांस्टाबल ५५
॥ हरमोहि ५५५

Schedule XLV-Form No.-134

EXECUTIVE ENGINEER

DANAPUR DIVISION

PHULWARISHARIF SUB-DIVISION

MEASUREMENT BOOK

ग्रोक गेहा

M.B NO-1346

3rd ^{and final} ~~on~~ ~~AG~~ Bill.

Name of Work—Const. of Road
from Bagda Main Road to
Betaura. (Old M/R-3054)

Agency - Brick Valua Pvt. Ltd,
Ward No. - 21, Bhawanipur Zirat,
Near Rowing Club, Motikazi,
Bihar.

No. and Date of Agreement —
10/SBD/2019-2020 (28/10/19)

Date of measurement - 15/07/20

① Laying brick Soling layer on prepared sub grade with bricks on end edging — do — do — all complet Job.

~~$2 \times 300.00 \times 0.250 = 150.00 \text{ m}^2$~~

$$(211.00 + 136.00) \times 0.250 = 86.750 \text{ m}^2$$

Continuation

Plastic Compound. — do —
— do — all complet Job.
 $2 \times 851.00 \times 0.10 = 170.200 \text{ m}^2$
⑤ Providing and fixing of
Typical MMSY Informatory
Sign board with 'Logo' —
— do — do — all complet Job
 $1 \times 1 = 1 \text{ Nos.}$

Amrigonda
15/07/21

सर्वे वक्तुं शक्यं सन्तुष्टास्तु नृणां कुरु
अनुष्ठानं चैव पूजितं कुरु विद्यायाश्चैव

Catibid
15/07/21

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Abstract of Cost.</u>					
① Providing Clearing and grubbing of Road Land					
do do do					
all complet Job.					
V.T.M.B.P.				(10)	
Qty.				0.24 Hac.	
@Rs. 49244.52/Hac.				11819 = 00/-	
② Providing Box Cutting of Soil at the Road way					
do do do					
all Complet Job.					
V.T.M.B.P.				(10)	
Qty.				150.150 m ²	
@Rs. 81.99/m ²				Rs. 12311 = 00/-	
③ Const. of Subgrade and earthen Shoulders					
do do do					
all Complet Job.					
V.T.M.B.P.				(13)	
Qty.				948.200 m ³	
@Rs. 194.91/m ³				Rs. 183839 = 00/-	
④ Const. of granular sub-base by Providing well graded material					
do do do					
all Complet Job.					
V.T.M.B.P.				(10)	
Qty.				233.055 m ³	

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(10) Providing, Laying, Spreading and Compacting stone aggregates of specific sizes to W.B.M. Gr. - III material					
do do do					
all complete Job.					
V.T.M.B.P.				(11)	
Qty.				335.182 m ³	
@ Rs. 4028.18/m ³					Rs. 1350173 = 00/-
(11) Providing and applying Primer Coat with bitumen emulsion (SS-1) on prepared surface of granular base					
do do					
all complete Job					
V.T.M.B.P.				(12)	
Qty.				3309.625 m ²	
@ Rs. 50.17/m ²					Rs. 166044 = 00/-
(12) Providing and applying Tack-Coat with bitumen emulsion (RS-1) on the prepared granular surface					
do do					
all complete Job.					
V.T.M.B.P.				(13)	
Qty.				3309.625 m ²	
@ Rs. 17.00/m ²					Rs. 56264 = 00/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑧ Providing, Laying and rolling of graded premix surfacing material					
do					
all Complet Job.					
V.T.M.B.P.					⑤
Qty.					3309.625 m ²
@ Rs. 228.32/m ²					Rs. 755654 = 00/-
⑨ Providing Const. of un-reinforced plain cement concrete (M80) pavement material					
do					
all Complet Job.					
V.T.M.B.P.					⑪
Qty.					181.800 m ³
@ Rs. 7727.03/m ³					Rs. 1404774 = 00/-
⑩ Laying Bricks Soling Layer on prepared sub-grade with brick on end edging					
do					
all Complet Job.					
V.T.M.B.P.					⑬
Qty.					86.750 m ²
@ Rs. 563.36/m ²					Rs. 48871 = 00/-
⑪, ⑫ Providing and fixing of Kilometer Stone					
do					
all Complet Job.					
V.T.M.B.P.					⑯
① Km Stone					2 Nos.
@ Rs. 2426.65/Each					Rs. 4853 = 00/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(12/13) Providing and fixing of Traffic Signs					do
do					all complete job.
V.T.M.B.P.	(16)				
(1) 600mm equilateral triangle					4 Nos.
@ Rs. 1680.92/Each					Rs. 6724.00
(11) 600mm x 450mm rectangular					5 Nos.
@ Rs. 1743.33/Each					Rs. 8717.00
(12/15) Providing and laying Road Marking with hot applied thermoplastic compound					do
do					do
do					all complete job.
V.T.M.B.P.	(16)				
Qty.					170.200 m ²
@ Rs. 941.14/m ²					Rs. 160182.00
(14/16) Providing and fixing of typical M.M.A.S.V. informative sign board with 'Logo'					do
do					do
do					all complete job.
V.T.M.B.P.	(11)				Qty. 2 Nos.
V.T.M.B.P.	(16)				Qty. 1 Nos.
Total Qty.					3 Nos.
@ Rs. 10727.16/Each					Rs. 32181.00
Total Rs.					474769.00
Less 10% Below Agreement (-)					47476.90
					427292.10
