

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक 1141 ~~अनु~~ बिहारशरीफ, दिनांक 5-8-22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:- नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।
महाशय,


उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अधियाचना पत्र समर्पित की जा रही है।

अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।


अनु०:- यथोक्त।

विश्वासभाजन


04/08/22


4/8/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ


4/08/2022

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 04-08-2022

(New Maintenance Policy 2018)

Year-2022-23

PIU- BIHARSHARIF


Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	latter no. 43 dated 08-04-2022	2037.01263	Certified that out of Rs 2037.01263 received & balance during the years 2022-23 in favour of Ex. Engineer, R.W.D. Works Division Bihar Sharif, sum of Rs 1998.73739 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 38.27524 lacs remaining unutilized at the end of the period under 04-08-2022
	Total Rs.		2037.01263	


2 Certified that I have satisfied myself that the conditions on which the grants-in- aid was Kind of Checks exercised :-


- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works


4/08/22
Divisional Accounts Officer
Rwd, Works Division
Bihar Sharif


4/8/22
Executive Engineer
Rwd, Works Division
Bihar Sharif


9/08/2022

Office Division :- BIHARSHARIF

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Length (in km)	Administrative Approval (AA) Amount of (in Lakh)	Agreement Amount (in Lakh)	Initial Rectification on Surface	5 Years Routine Maintenance (in Lakh)	Agreement at No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allowed Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Increase in Allotment	Remarks
1	RM/NA/BIH/20/0004	Alipur road to Village Gajipur, Block - Bind	10200701001	1043 02-03-2022	0.665	28.5107	19.56044	7.68188	MBD-02 02/2020-21	6-Apr-21	28-03-2022	26.51	25	5.4	0.00000	19.35504	19.35504		
3	RM/NA/BIH/20/0004	L068-T02 to Rasulpur (VR46)	10200602030	1013 03-03-2020	0.965	40.732	19.433	10.89966	MBD-02 20-21	4/6/2021	24-01-2022	34.38	25.00	5.40	18.00000	17.92195	5.44880		
3	RM/NA/BIH/20/0004	Benar-saksohra road to village Nigriyan	10200701026	1043 02-03-2022	1.3	60.9288	49.20928	8.73445	MBD-02 02/2020-21	6-Apr-21			30.89	25	5.4	0.00000	0.00000	7.96034	
4	RM/NA/BIH/19/0005	Const. of road from Venda More of Sonsa Path to Village Sondih via Chand Bathan Chhlika.	10200605003	5268 04-10-2019	2.39	47.546	54.777	23.66314	MBD-07 20-21	6/7/2021	10/6/2022	89.95	25.00	5.40	40.06725	40.06725	8.53074		
				TOTAL															
				58.06725 77.34424 41.28692															

1. Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
2. Up-to-date Physical Progress has been uploaded in MIS.

Divisional Accounts Officer
Rwd, works Division Biharsharif

Executive Engineer
Rwd, works Division

Name of Road:- Venda More of Sounsa Path To Village Sosandi Chand Bathan
Name of Contractor:- M/S Uday Shankar Prasad

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY	IRI	Latitude	Longitude	Event
		No.						ROAD				
5/12/21	9: 26: 40	57	0.1	290	0	2900	2982	G	4	25.290752	85.61071	Normal
5/12/21	9: 27: 0	57	0.1	320	20.2	3200	3251	G	4.32	25.290825	85.6117	Normal
5/12/21	9: 27: 15	57	0.1	310	30.3	3100	3161	G	4.22	25.290855	85.61274	Normal
5/12/21	9: 27: 15	57	0.1	280	30.3	2800	2892	G	3.89	25.290938	85.61375	Normal
5/12/21	9: 27: 15	57	0.1	250	30.3	2500	2622	G	3.57	25.291045	85.61475	Normal
5/12/21	9: 27: 51	57	0.1	210	30.3	2100	2263	G	3.13	25.2914	85.61567	Normal
5/12/21	9: 28: 0	57	0.1	220	30.3	2200	2353	G	3.24	25.291435	85.61665	Normal
5/12/21	9: 28: 0	57	0.1	250	30.3	2500	2622	G	3.57	25.29133	85.61763	Normal
5/12/21	9: 28: 0	57	0.1	310	30.3	3100	3161	G	4.22	25.29124	85.61862	Normal
5/12/21	9: 28: 26	57	0.1	210	40.4	2100	2263	G	3.13	25.291242	85.61975	Normal
5/12/21	9: 28: 26	57	0.1	280	40.4	2800	2892	G	3.89	25.291242	85.62064	Normal
5/12/21	9: 28: 26	57	0.1	260	40.4	2600	2712	G	3.68	25.29123	85.622	Normal
5/12/21	9: 28: 26	57	0.1	240	40.4	2400	2533	G	3.46	25.291228	85.62271	Normal
5/12/21	9: 29: 1	57	0.1	260	40.4	2600	2712	G	3.68	25.29121	85.62374	Normal
5/12/21	9: 29: 1	57	0.1	220	30.3	2200	2353	G	3.24	25.291227	85.62483	Normal
5/12/21	9: 29: 1	57	0.1	270	20.2	2700	2802	G	3.79	25.29173	85.62547	Curve
5/12/21	9: 29: 37	57	0.1	330	20.2	3300	3341	G	4.43	25.292562	85.62571	Normal
5/12/21	9: 30: 0	57	0.1	280	20.2	2800	2892	G	3.89	25.293215	85.62643	Normal

$Y = 0 * X^2 + 0.898 * X + 377.8$		
$X = 2471$		
$Y = 2596$		
(R) RURAL ROAD		
Good	Average	Poor
<4000	4001-5000	>5001

Executive Engineer
R.W.D. (W)
 Division Biharsharif (Nalanda)

[Signature]
 24/12/21

[Signature]
 24/12/21

Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UTV	ROAD				
5/12/21	9:30:12	57	0.1	220	20.2	2200	2353	G	3.24	25.293893	85.62704	Speed Breaker
5/12/21	9:30:12	57	0.1	250	10.1	2500	2622	G	3.57	25.294737	85.62744	Normal
5/12/21	9:36:5	57	0.1	240	0	2400	2533	G	3.46	25.294547	85.62729	Normal
5/12/21	9:36:5	57	0.1	300	10.1	3000	3071	G	4.11	25.293682	85.6269	Normal
5/12/21	9:36:40	57	0.1	310	20.2	3100	3161	G	4.22	25.293012	85.62626	Normal
5/12/21	9:37:0	57	0.09	290	20.2	2900	2982	G	4	25.292363	85.62566	Normal
Total			2.390	6400	606	64000	66529		89.95			

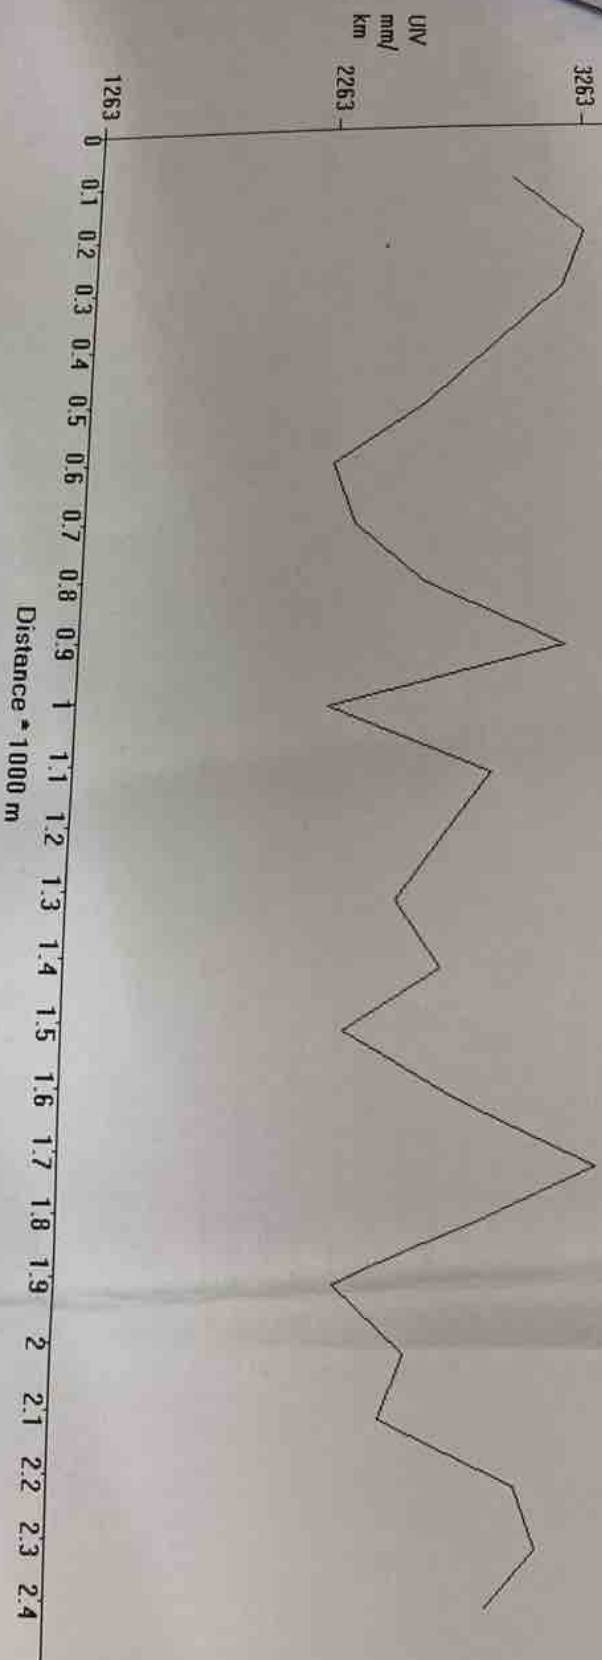

 24/12/21
 AD

Executive Engineer
 R.W.D. (W)
 Division Biharsharif (Nalanda)


 24/12/21

File : F:\19121130.Xls. Section No. 57. Eqn : $Y = 0 \cdot X^2 + 0.898 \cdot X + 377.8$

Name of Customer : MS Uday Shankar Prasad. Name of Work/ Road : Venda More of Sonsa Path to Village Sosandi



DM
24/11/21
AB

DM
24/11/21

Executive Engineer
R.W.D. (W)
Division Bilharsnarfi (Nalanda)

प्रमाणित किया जाता है कि इस माप-
पत्रिका में मशीन से ७०० पैज- १००
एड को पूरा है जिसे श्री रामरुद्राचल २५५६
हिंदू खारुड अभियन्ता, माओन कार्य विभाग
कार्य प्रमण्डल, बुद्धि ३-१११- निरीत-
किया- जाता है।
(90m)
3-18/20

कार्यपालक अभियन्ता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल, बिहार शरीक

Seyin
3-18/20

Re-issued to Sri Binod Kumar Singh,
J.B. Rehui
11/11/20
AB

Sch, XLV-Form No. 134

विहार ३

DIVISION

२३३

SUB-DIVISION

Measurement Book

No. 2990

Name of Officer

श्री रामरुद्राचल २५५६ हिंदू २५५६

Date of first entry

11/11/20

Date of last entry

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2nd/and final Bill					
Name of work — Maintenance of road					
from vanda more of Songa Path					
to village SoSando via chanel Bathan					
Head —	3054				
Agency —	M/S Velay Shankar Prasad				
Agreement No —	MBD — 07/2020-21				
Work start date —	08/09/2020				As per
Date of completion —	07/06/2021				Agreement
Date of Actual completion —	10/6/22				
Date of entry —	10/6/22				
1) construction of Subgrade					
and earthen shoulders					
--- all complete job					
2x	2x30.10x	1.10x	0.30=	39.60m ³	
2x	1x28.10x	1.10x	0.30=	16.48m ³	
2x	2x30.10x	1.05x	0.25=	31.50m ³	
2x	3x30.10x	1.10x	0.25=	49.50m ³	
2x	2x30.10x	1.15x	0.20=	27.60m ³	
2x	3x30.10x	1.20x	0.30=	64.80m ³	
2x	2x30.10x	1.10x	0.25=	33.00m ³	
2x	4x25.10x	1.20x	0.25=	60.00m ³	
2x	2x30.10x	1.10x	0.25=	30.00m ³	
2x	2x30.10x	1.10x	0.20=	24.00m ³	
1x	25.10x	1.10x	0.30=	7.50m ³	
1x	24.10x	1.10x	0.30=	7.20m ³	
				391.18m ³	

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>ABSTRACT OF COST</u>					
($\frac{1}{400}$) clearing and grubbing road level — all complete job					
Qty wide TMB Page 14 = 0.5225 Hec					
@ Rs 52970.33/Hec = Rs					27677.2
($\frac{2}{402}$) construction of Subgrade and earthen shoulders — all complete job					
Qty wide TMB Page 17 = 391.18 m ³					
@ Rs 176.66/m ³ = Rs					69106.2
($\frac{3}{403}$) construction of GSB spreading II — all					
Qty wide TMB Page 14 = 86.534 m ³					
@ Rs 1635.74/m ³ = Rs					141547.2
($\frac{4}{404}$) Providing, Laying, Spreading and compacting WBM 2 — all complete job					
Qty wide TMB Page 14 = 107.74 m ³					
@ Rs 2858.43/m ³ = Rs					307967.2
($\frac{5}{405}$) Providing, Laying, Spreading and compacting WBM 3 — all complete job					
Qty wide TMB Page 14 = 146.07 m ³					
@ Rs 2579.90/m ³ = Rs					376846.2
					Rs 923143.2

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					8F A 4267526.4
Add GST @ 12%					= (+) R 512103.4
Add Labour Charges @ 1%					= (+) R 42675.4
					R 4822304.4
Add <u>Seigniorage fee</u>					
(i) Subgrade					
Qty wide TMB Page 20					= 391.18 m ³
@ R 23.78 x $\frac{10}{100}$ / m ³					= R 930.40
(ii) G.S.B					
Qty wide TMB Page 20					= 86.534 m ³
@ R 439.34 x $\frac{10}{100}$ / m ³					= R 3802.40
(iii) W.B.M 2					
Qty wide TMB Page 20					= 107.74 m ³
@ R 620.16 x $\frac{10}{100}$ / m ³					= R 6682.40
(iv) W.B.M 3					
Qty wide TMB Page 20					= 146.07 m ³
@ R 637.37 x $\frac{10}{100}$ / m ³					= R 9310.40
(v) M.S.S					
Qty wide TMB Page 21					= 2023.55 m ²
@ R 12.69 x $\frac{10}{100}$ / m ²					= R 2568.40
(vi) S.D.B.C					
Qty wide TMB Page 21					= 197.835 m ³
@ R 717.93 x $\frac{10}{100}$ / m ³					= R 14203.40
Less Percentages paid amount wide TMB Page 16					R 4859799.00 = (-) R 4006725.40
					R 853074.40
