

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, गोगरी।
E-mail ID.- eerwdgogri@gmail.com**

पत्रांक 1469(उत्तर) प्र0गोगरी, दिनांक 08-08-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, गोगरी ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-

शीर्ष New Maintenance Policy-2018 under MR-3054 योजना अन्तर्गत राशि का अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 under MR-3054 योजना अंतर्गत कुल मो0 24.15650 लाख (चौबीस लाख पन्द्रह हजार छः सौ पचास) रुपये मात्र उपलब्ध कराने की कृपा की जाए। इस पत्र के साथ विहित प्रपत्र में अधियाचना राशि समर्पित की जा रही है।

सूचनार्थ सादर समर्पित।

अनु0- यथोक्त

विश्वासभाजन

Mumai
8/8/22
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, गोगरी।

Elev
8/8/22

08-08-22

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilization Certificate up to the 21 April 2022
RWD, Works Divisio, Gogri

Sl. No	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural roads Maintenance Policy-2018 under MR-3054	Previous Allotment	Rs. 1512.55447 Lakh	Certified that out of Rs. 2318.25319 lacs of grants-in-aid sanctioned during the years 2019-20 in favors of E-in-C, RWD Bihar, Patna a sum of Rs. 2318.25319 lacs has been utilized for the purpose of MR(3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 0.00 Lacs remaining unutilized at the end of the period under report.
		01. Letter No-26, Date -15.04.21	Rs. 126.73585 Lakh	
		02. Letter No-30, Date -21.05.21	Rs. 211.26975 Lakh	
		03. Letter No-60, Date -09.01.21	Rs. 83.54087 Lakh	
		04. Letter No-02, Date -03.01.22	Rs. 185.7605 Lakh	
		05. Letter No-05, Date -25.01.22	Rs. 66.66837 Lakh	
		-----	Rs.-11.03089 Lakh	
		06. Letter No-20, Date -14.03.22	Rs. 103.32400 Lakh	
		07. Letter No-22, Date -16.03.22	Rs. 17.36849 Lakh	
		Total :-	Rs.- 2318.25319 Lakh	

18. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

19. Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD works

[Signature]
8/8/22

D.A.O.
RWD Works, Division, Gogri

[Signature]
8/8/2022
Executive Engineer
RWD Works, Division, Gogri
09.08.22

Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
Works Division :- Gogri

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/20-21 Gogri/02	Pastraha market to Hari Tola Dina Chakla	29461039629	Lt No.- 1098Dated 31.03.2021	0.450	19.91	14.81239	4.16921	15NMBD /2021-22 16.11.2021	15.08.2022	On-Going	3440.833	5.06	25.00	0.00	0.00	13.63767	On-Going
1	MR-N/20-21 Gogri/02	Haripur Chauk to G.N Bandh	29461033491	Lt No.- 1098Dated 31.03.2021	0.600	21.42	11.43804	5.25938	15NMBD /2021-22 16.11.2021	15.08.2022	On-Going	3569.167	5.06	25.00	0.00	0.00	10.51883	On-Going
Total :-																	24.15650	

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.

Murali
 Executive Engineer
 RWD, Works Division,
 Gogri
 09.03.22

Road Name-Haripur Chawk to G.N Bandh Haripur Sirniya Bandh Tola, Contractor-Bidhanchandra Kumar

Project ID-29461033491

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGO	Latitude	Longitu	Event
		No.	in km	in mm	Rate	mm/km	mm/km	RY		de	
1/8/22	18:13:19	74	0.1	420	0	4200	3962 G	ROAD	25.38544	86.68945	Normal
1/8/22	18:13:54	74	0.1	370	30.3	3700	3517 G		25.38476	86.68918	Normal
1/8/22	18:14:29	74	0.1	320	30.3	3200	3073 G		25.3849	86.68803	Normal
1/8/22	18:15:5	74	0.1	360	20.2	3600	3428 G		25.38471	86.68666	Normal
1/8/22	18:15:40	74	0.1	380	30.3	3800	3606 G		25.38482	86.6862	Normal
1/8/22	18:16:15	74	0.079	320	20.2	4051	3829 G		25.38534	86.68523	Normal
							Total IRI				
							21415				
							Average IRI				
							3569.167				

$$Y = 0 * X^2 + 0.889 * X + 228.2$$

$$X = 4051$$

$$Y = 3829$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

[Signature]
07-08-22
JE


[Signature]
07-08-22
AE

[Signature]
07-08-22
Executive Engineer
Rural Works Department
Works Division Gogri

Name of Customer : Bidhanchandra Kumar
 Name of Work/Road : Indh Haripur Sirmiya Bandh Tola
 Lab Job number : 29461033491
 Date : 01-08-2022
 Section No. : 74

Test Date : 01-08-2022
 Machine No : 403
 Start S No : 0.00 KM
 Start E No : 0.600 KM
 Weather : Normal
 Start Location :
 End Location :
 Road Name : Indh Haripur Sirmiya Bandh Tola
 Road Type : (R) RURAL ROAD
 Side :
 UIV Range : 2073 To 5000 mm/km
 Dist Range : 0 To 0.7 * 1000 m
 Equation : $Y = 0 * X^2 + 0.889 * X + 228.2$

File : C:\Users\BRRDA45\OneDrive\Desktop\Haripur Chawk to G.N Bandh Haripur Sirmiya Bandh Tola.Xls, Section
 Name of Customer : Bidhanchandra Kumar, Name of Work/Road : Haripur Chawk to G.N Bandh Haripur Sirmiya

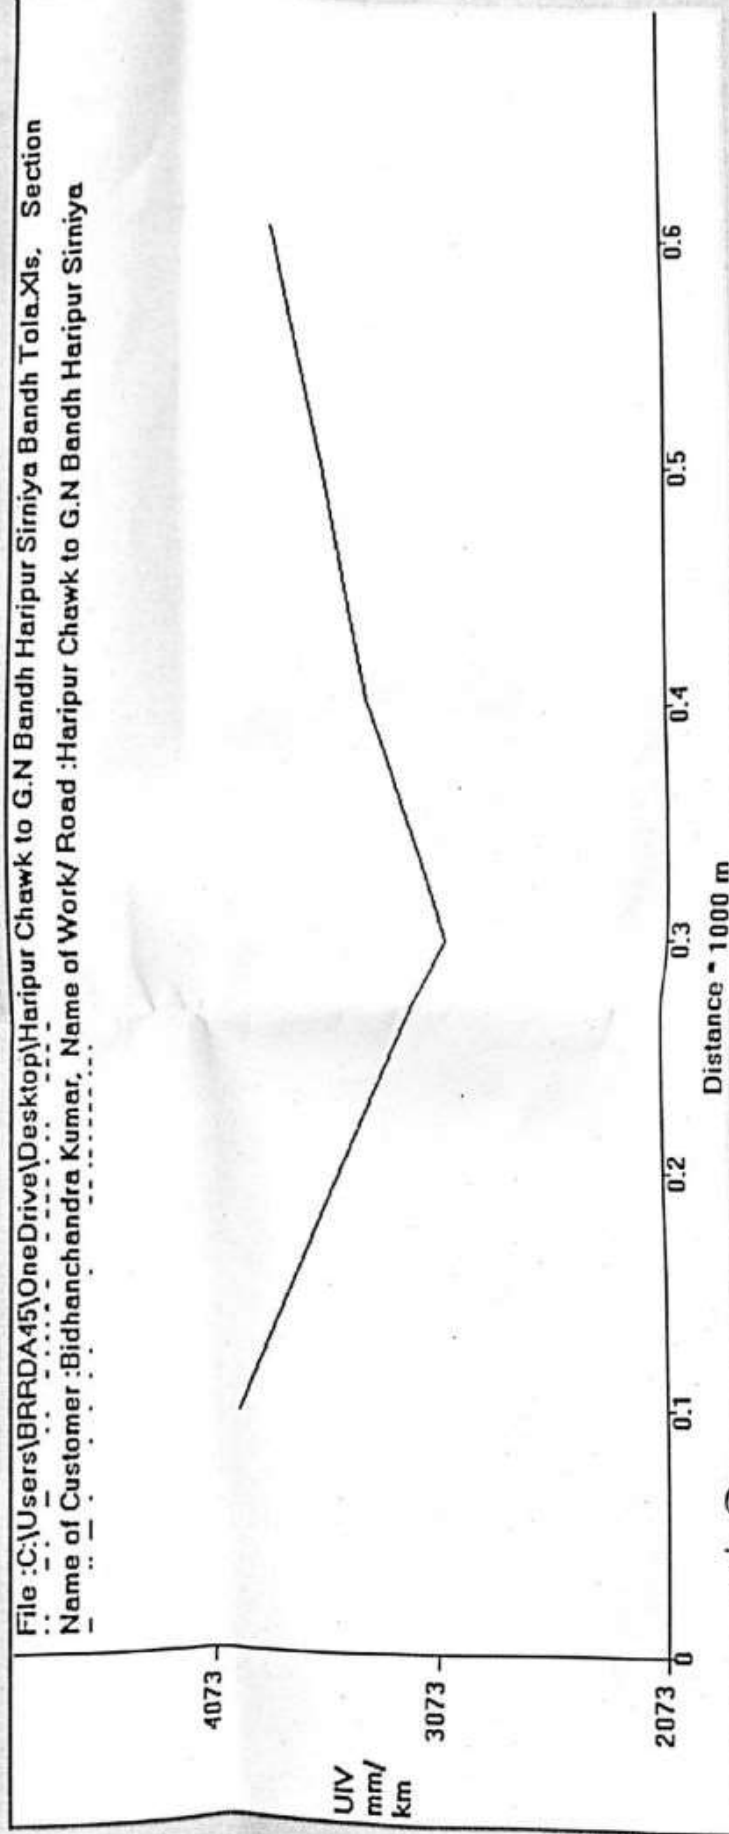

02.08.22
J.E

01.08.22
AB

01.08.22
AB

MR.3054 (new)

M.B.No-518
21-22

Schedule XLV Form No. 134.

Haripur Chauk To GN Bondh

Yash. Dhoti DIV GN

3700 Yash. Dhoti SUB-DIV. GN

Measurement Book

प्रमाणित किया जाता है कि इस
मापी व पुस्तक में मशीन द्वारा अंकित
कुल - 100 (एक सौ) पन्ने हैं जिस
की श्रेष्ठ कुमार सरा. सहायक
अभियंता. ग्रामीण कार्य विभाग.
कार्य अवर प्रमंडल, गोगरी का
निर्गत किया जाता है।

Arund
Executive Engineer
R.W.D. Works Div.
Gogri -
Basky
18.11.21

Sch. XLV - Form No. 134

प्रमंडल, गोगरी DIVISION

अवर प्रमंडल, गोगरी SUB-DIVISION

Measurement Book

No. 518

Name of Officer _____

Date of first entry _____

Scanned with CamScanner

Name of Work—
 Situation of Work—
 Agency by which work is executed—
 Date of Measurement—
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work—	Haripur chowk				
	70 G.N. Bandh				
Name of Agency—	Bidhanchand 29				
	Kumar At - Azeiya, Porbatta				
	Distt - Khagaria,				
Agreement No:—	15/MBD/2021-22.				
Date of Start:—	09.11.2021				
Date of completion:—	15.02.2022				

Record measurement

1. clearing & grubbing

Road land (by manual means) including uprooting wild vegetation, grass, bushes etc—do do.

all comp. job —

$$2 \times 5 \times 30.0 \times 1.0 = 300.0 \text{ m}^2$$


$$2 \times 5 \times 30.0 \times 1.0 = 300.0 \text{ m}^2$$

$$2 \times 5 \times 30.0 \times 1.0 = 300.0 \text{ m}^2$$

$$2 \times 5 \times 30.0 \times 1.0 = 300.0 \text{ m}^2$$

$$1200.0 \text{ m}^2$$

$$= 0.12 \text{ Ha.}$$

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
13. Pvg. & fixing of typical masonry in laboratory signboard with logo etc-do do all comp job					
4.07 Ha.					
					
30.07.22					
J.E					

1st of A/C Bill
 ABSTRACT OF COST
 Date - 02.08.22

1. clearing & grubbing
 Road land (By manual means) including uprooting wild vegetation, grass, bushes etc-do do-all comp job

74. vide T.M.B.P. (1)
 0.12 Ha.

QPR 53,879 = 81/Ha. ← R. 6.465

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2. Const. of subgrade & earthen shoulders with cast approved materials obtained from approved pits etc-do-do-all comp. job					
2+y. vide T.M.B.P. (2)					
397.925 m ³					
Q.P.S. 192 = 10/m ³				Rs	76,441/-
3. Pvg. & applying tack					
3+y. Cast with bitumen emulsion using pressure distributor etc-do-do-all comp. job					
2+y. vide T.M.B.P. (4) - 549.0 m ²					
2+y. vide T.M.B.P. (5) - 1849.05 m ²					
2398.05 m ²					
Q.R. 16 = 43/m ²				Rs	39,400/-
4. Pvg. laying & rolling of close graded premix surfacing etc-do-do-all comp. job					
2+y. vide T.M.B.P. (5)					
549.0 m ²					
Q.P.S. 214 = 42/m ²				Rs	1,17,716/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
5. Paving & laying semi dense bituminous concrete with 100-120 TPH etc - do-do-all comp. job - 7.4 y. vide T.M.B.P. (6) 46.19 m ²					
Q.R. 11,092 = 05/m ² — R. 5,12,342-					
6. Reinforced cement concrete, mis-gade kilometre local stone. Ob standard design etc - do-do-all comp. job — 7.4 y. vide T.M.B.P. (6)					
i) Km stone - 2.070 m					
Q.R. 2161 = 71/108 — R. 4,323-					
ii) 200m stone - 2.070 m					
Q.R. 630 = 94/108 — R. 1,262-					
7. Relao - reflectorised traffic signs providing & erecting direction & place identification etc - do-do-all comp. job - 7.4 y. vide T.M.B.P. (7) 1.92 m ²					
Q.R. 12,265 = 44/m ² — R. 23,550-					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
8. Pvg. & binding of Ret-20. - reflecting Cautionary mandatory and informationary Lignature of do-do-all comp. job					
Qty. vide T.M.B.P. (7)					
i) 600mm equilateral & triangle - 6.0 nos.					
QR. 2470 = 05/100. - R. 20.820					
ii) 600mm circular - 4 nos.					
QR. 3737 = 23/100. - R. 14.949					
iii) 600 x 400 x 50mm - 4 nos.					
iv) Rubble Strip 3505 = 59/100. - R. 14.422					

a) Thermoplastic paint - 6.0m ²					
QR. 721 = 98/100. - R. 4.332					
b) Road Strip - 20.0m ²					
QR. 223 = 24/100. - R. 4.465					

9. Reinforced cement concrete M15 grade boundary pillars etc - do-do-all comp. job					
Qty. vide T.M.B.P. (8)					
24.0 nos.					
QR. 532 = 25/100. - R. 12.774					

10. planting of trees by the

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
road side, in			0.60m		
dia holes etc-do do-all					
comp job					
qty. vide T.M.B.P. (8)					
25.0 nos.					
QR=8.55=50/90s.				QR	21,387~
11. Pvg. & Laying of hot applied thermoplastic compound 2.5 mm thick etc-do do-all comp. job					
qty. vide T.M.B.P. (8)					
1240 m ²					
QR=721=98/m ²				QR	89,525~
12. Pvg. & Laying of typical masonry infill masonry signboard with logo etc-do do-all comp. job					
qty. vide T.M.B.P. (9)					
4.0 nos.					
QR=9384=34/100s.				QR	37,537~
				QR	10,01,710~
Add 12% GST + 1% C.C. R.					1,30,222~
				C.V. R.	11,31,932~

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			8.7	88.11	31932 ~
					(A)
<u>Seigniorage fee</u>					
10.1.01 material cost					
i) E/w - 397.925 m ³					Rs.
QR. 34 = 81/m ³				Rs.	13852 ~
ii) 13.2 mm to 0.09 mm - 1647 m ³					
QR. 523 = 37/m ³				Rs.	8,620 ~
iii) 9.5 to 4.75 mm - 38.33 m ³					
QR. 582 = 80/m ³				Rs.	22,339 ~
iv) 4.75 mm & below - 27.71 m ³					
QR. 251 = 35/m ³				Rs.	6,965 ~
v) c-sand - 0.54 m ³					
QR. 175 = 80/m ³				Rs.	95 ~
vi) 40 mm aggregate - 0.54 m ³					
QR. 494 = 15/m ³				Rs.	267 ~
vii) 20 mm aggregate - 0.38 m ³					
QR. 604 = 91/m ³				Rs.	230 ~
viii) 10 mm - 0.04 m ³					
QR. 668 = 80/m ³				Rs.	27 ~
				Rs.	52,395 ~
10.1. S.f. i.e.				Rs.	5,239 ~
					(B)
<u>Total cost</u>					
(A)				Rs.	11,31932 ~
(B)				Rs.	5,239 ~
					c.u. Rs. 11,37,171 ~

[illegible]
