

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल बेनीपट्टी।

पत्रांक...1619 अनु

दिनांक 29/08/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेनीपट्टी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह- सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-

शीर्ष NEW MAINTENANCE POLICY - 2018 (MR - 3054) में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष NEW MAINTENANCE POLICY - 2018 (MR - 3054) अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताक संवेदक का भुगतान किया जा सके।

अनु०:-

1. अध्याचना प्रमाण पत्र 1 पृष्ठ में।
2. उपयोगिता प्रमाण पत्र एक प्रति।

विश्वसभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेनीपट्टी।

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate Upto the month of 31 July 2022

New Maintenance policy - 2018

PIU – Executive Engineer, R.W.D (W) Division, Benipatti

SL. No	Name of Gen.heme	Sanction No. & Date with Amount (In Rs. lacs)	Amount Received (In Rs. lacs)	Particulars
1	Construction of Rural roads under New maintenance policy - 2018	Authorization letter No. 03 we dt- 08.06.2022 Rs.46.55787	964.68887	Certified that out of Rs.964.68887 Lakh received during the years up to 2022-23 (31 July 2022) in favour of Ex. Engineer, RWD (W) Division Benipatti, Madhubani, Bihar, a sum of Rs. 964.08041 Lakh has been utilized for the purpose of New maintenance policy-2018 as given in the margin for which the balance of Rs 0.60846 Lakh remaining unutilized at the end of the period under.


2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


Divisional Account Officer,
R.W.D (W) Division
Benipatti


Executive Engineer
R.W.D (W) Division
Benipatti

Formate of Requisition under Head New Maintenance policy - 2018 (MR- 3054) for the month of August- 2022

Name of Division :- Benipatti

SI No.	Package No.	Name of road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MIR-N/19-20 Benipatti/03	Loha Paraul Dighia Pokhar to Village Jhonjh	31910001030	1859/ 24.06.2019	1.360	57.36630	34.14121	12.85946	17MBD/21-22 23.09.2021	22.09.2022	—	3150	25	5	0.00	0.00	33.00139	Work Completed
Total					1.360	57.36630	34.14121	12.85946	—	—	—	3150	25	5	0.00000	0.00000	33.00139	

Divisional Account Officer
R.W.D(W)Div. Benipatti

Executive Engineer
R.W.D(W)Div. Benipatti

Name of work : Loha Parau Dighia Pokhar To Village Jhonjhi

Name of customer : Susheel kumar chaudhari

(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

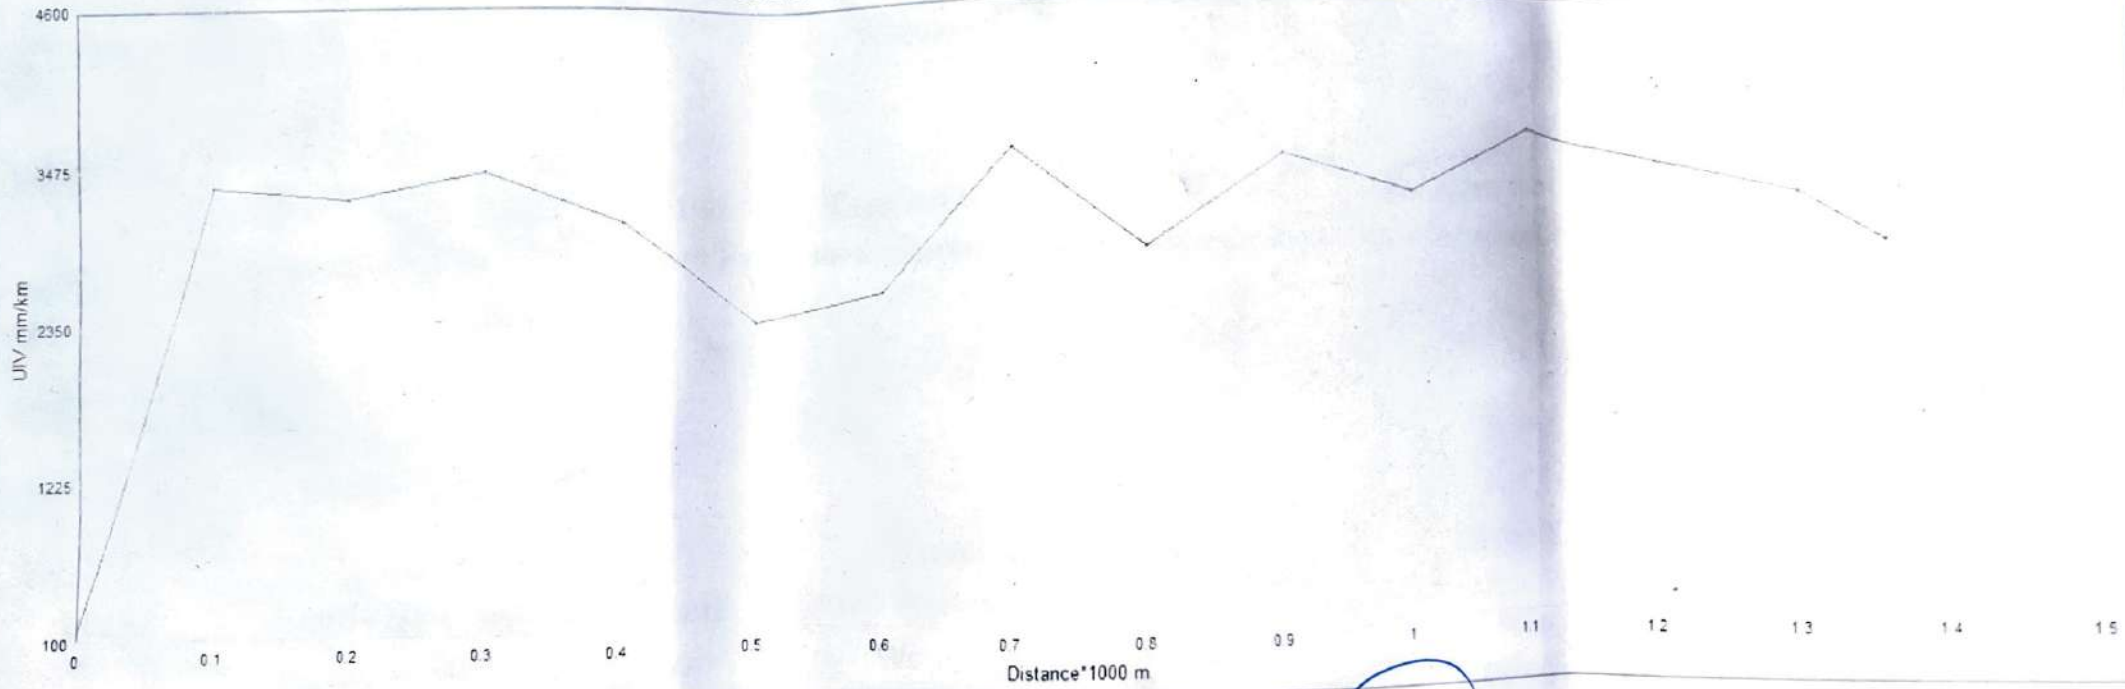
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
18/08/22	14:13:52	55	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	196	0.35	Good	26.4422865	N	86.0332193	E	Normal
18/08/22	14:14:24	55	100	100	34.0 cm	2.2 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.4423723	N	86.0324717	E	Normal
18/08/22	14:14:44	55	100	200	33.0 cm	17.8 Km/Hr	3300.0 mm/Km	3255	4.33	Good	26.4424410	N	86.0317697	E	Normal
18/08/22	14:15:05	55	100	300	35.0 cm	17.5 Km/Hr	3500.0 mm/Km	3441	4.55	Good	26.4426203	N	86.0308313	E	Normal
18/08/22	14:15:25	55	100	400	31.0 cm	17.8 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.4422865	N	86.0296564	E	Normal
18/08/22	14:15:47	55	100	500	23.0 cm	16.3 Km/Hr	2300.0 mm/Km	2328	3.21	Good	26.4422865	N	86.0296564	E	Normal
18/08/22	14:16:06	55	100	600	25.0 cm	18.4 Km/Hr	2500.0 mm/Km	2514	3.44	Good	26.4423876	N	86.0275736	E	Normal
18/08/22	14:16:23	55	100	700	36.0 cm	21.8 Km/Hr	3600.0 mm/Km	3534	4.66	Good	26.4423799	N	86.0267267	E	Normal
18/08/22	14:16:38	55	100	800	28.0 cm	23.9 Km/Hr	2800.0 mm/Km	2792	3.78	Good	26.4429693	N	86.0257502	E	Normal
18/08/22	14:16:53	55	100	900	35.0 cm	23.4 Km/Hr	3500.0 mm/Km	3441	4.55	Good	26.4434290	N	86.0249338	E	Normal
18/08/22	14:17:08	55	100	1000	32.0 cm	24.4 Km/Hr	3200.0 mm/Km	3163	4.22	Good	26.4442644	N	86.0251474	E	Normal
18/08/22	14:17:22	55	100	1100	37.0 cm	25.2 Km/Hr	3700.0 mm/Km	3626	4.77	Good	26.4451742	N	86.0251627	E	Normal
18/08/22	14:17:37	55	100	1200	34.0 cm	24.5 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.4460573	N	86.0253077	E	Normal
18/08/22	14:17:59	55	100	1300	31.0 cm	15.8 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.4470949	N	86.0254908	E	Normal
18/08/22	14:17:59	55	60	1360	27.0 cm	13.6 Km/Hr	2700.0 mm/Km	2699	3.67	Good	26.4470949	N	86.0254908	E	Normal

Shif. 19.8.22
JE.

19-8-2022
AE.

3236
29/8/22
ER

Name of Customer: Susheel kumar chaudhari , Machine no: 19195 , Road: Loha Parau Dighia Pokhar To Village Jhonjhi , Date: 18/08/22 , Section No: 55 , Equation: $Y = 0.927 X + 196.3$



[Signature]
19.8.22
JE

[Signature]
19-8-2022

[Signature]
29/8/22
RR

OFFICE OF THE EXECUTIVE ENGINEER
RWD WORKS DIVISION, Benipatti

Name of Scheme:- Improvement of Road from Loha Paraul Dighia Pokhar to Village Jhonjhi., Package No. -
RM/MA/BEN/19/0003,


Project ID - 31910001030

Certified that all item wise 100%
measurement has been taken by
me


19.8.22


Junior Engineer
RWD Work Section Benipatti
Works Division Benipatti

Certified that all item wise 50%
measurement has been Cheked by
me


29-8-2022

Assistant Engineer
RWD Work Sub Division Benipatti
Works Division Benipatti

Certified that all item wise 10%
measurement has been Cheked by
me


29/8/22

Executive Engineer
RWD Works Division
Benipatti

1
 Name of work—
 Situation of work—
 Agency by which work is executed—
 Date of measurement—
 No. and date of agreement.
 (These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1st on A/C Bill					
N/W:- Maintenance of road & CD					
WORK-RR-N/19-20 ^{Loha} Poraul Dighiya					
Pokhar To Village Jhathi					
N/A:- Shushil Kumar Chowdhary					
Agg. No:- 17MBD/2021-22					
D.O.S:- 23.09.2021					
D.O.C. 1- 22.09.2022 (As per Agg.)					
Record Entry					
Measurement					

① clearing and grubbing road land including uprooting wild vegetation --- do --- dir of E/T
 $2 \times 1360 \times 1.500 = 4080 \text{ m}^2$
 $= 0.408 \text{ Hec}$

② Construction of granular sub base by providing well graded material --- do --- as per tech. specs.

$$1 \times 11.00 \times 1.750 \times 0.10 = 1.925 \text{ M}^3$$

$$1 \times 8.00 \times 2.30 \times 0.10 = 1.840 \text{ M}^3$$

$$1 \times 6.00 \times 2.10 \times 0.10 = 1.260 \text{ M}^3$$

$$1 \times 8.00 \times 2.50 \times 0.100 = 2.00 \text{ M}^3$$

$$\text{C/O} = 7.025 \text{ M}^3$$

20.8.22
 JE

Continuation

20.8.22
 A.C.

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			B.F. Rs =	5,16,961 = 00	
(5/5) P&A primer coat with bitumen emulsion SS-1					
---do--- as per tech. sp.					
Qty vide TMB PNO-(5)					
647.35 M ² @ Rs 41.25/M ² Rs =				26,703 = 00	
(6/6) Providing, laying & rolling of close graded premix ---do--- sp.					
Qty vide TMB PNO-(6)					
1027.50 M ² @ Rs 213.08/M ²					
			Rs =	2,19,515 = 00	
(7/7) P&A tack coat with bitumen emulsion					
RS-1 ---do--- specs.					
Qty vide TMB PNO-(7)					
6168.50 M ² @ Rs 13.99/M ²					
			Rs =	86,297 = 00	
(8/8) P&L semi dense bituminous concrete					
with ---do--- tech. sp.					
Qty vide TMB PNO-(9)					
128.518 M ³ @ Rs 10704.74/M ³					
			Rs =	13,75,752 = 00	
			/		
			C/O Rs =	22,25,228 = 00	

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					B.F. Rs = 22,25,228=00
(9/9) P&F RCC M-15 grade					
K.M. stone --- do ---					
Qty vide TMB PNo - (11)					
2.00 Nos @ Rs 2373.47/Each					
					Rs = 4747=00
(10/10) P&F RCC M-15					
grade 200mm stone					
--- do --- tech. spec.					
Qty vide TMB PNo - (11)					
6.00 Nos @ Rs 639.02/Each					
					Rs = 3834=00
(11/11) P&F Retro reflec.					
Place identification					
sign board --- do ---					
Qty vide TMB PNo - (11)					
1.920 M ² @ Rs 12511.07/M ² Rs = 24021=00					
(12/12) P/F of retro. ref.					
cautionary, mandatory					
sign board --- do ---					
(i) 600 mm equilateral					
& triangle.					
Qty vide TMB PNo - (11)					
35.00 Nos @ Rs 3716.01/Each					
					Rs = 1,30060=00
					/
					C/O Rs = 23,87,890=00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	Q.	
(13/B) (11) 600mm circular Qty vide TMB PNO-(11) 21.00 NOS @ Rs 3849.72/Each Rs = 80,844.00					
(14/B) (11) 600mm x 450mm Rectangular. Qty vide TMB PNO-(11) 9.00 NOS @ Rs 3719.32/Each Rs = 33474.00					
(15/B) (14) 900mm octagonal stop Board. Qty vide TMB PNO-(11) 6.00 NOS @ Rs 7752.04/Each Rs = 46512.00					
(16/B) P/L Rumble strip with man studs & thermo plastic --- --- do --- tech. sp. Qty vide TMB PNO-(12) 7.50 M ² @ Rs 735.40/M ² Rs = 5516.00					
(17/B) P&F RCC M15 grade Boundary pillar --- --- do --- tech. sp. Qty vide TMB PNO-(12) 90.00 NOS @ Rs 529.93/Each Rs = 47694.00					

Continuation
C/O Rs = 26,01,930.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					R.F.R. = 26,01,930.00
(18/19) Planting of tree by road side --- --- do --- tech spec.					
Qty vide TMB PNO- (12)					
60.00 Nos @ Rs 800.30/each					
					Rs = 48,01,800.00
(19/20) P&F of hot applied thermoplastic comp. --- do --- tech spec.					
Qty vide TMB PNO- (12)					
272.00 m ² @ Rs 735.40/m ²					Rs = 2,00,02,800.00
(20/21) P&F of typical MMGSY informatory sign board --- tech spec.					
Qty vide TMB PNO- (12)					
2.00 Nos @ Rs 11158.14/each					
					Rs = 22,316.00
(21/22) Brick masonry with cement mortar --- do --- tech spec.					
Qty vide TMB PNO- (9)					
23.16 m ³ @ Rs 5714.05/m ³					Rs = 1,32,337.00
					1
					C/O Rs = 30,04,629.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					B.F. Rs = 30,04,629=00
22/23 Plastering with cement mortar --- --- do --- tech. sp.					
Qty vide TMB P No. (9)					
214.40 M ² @ Rs 173.07/M ²					
					Rs = 37,106=00
23/24 Providing 1.5 mm cement putty including curing --- do --- tech. specs.					
Qty vide TMB P No. (10)					

214.40 M² @ Rs 44.99/M² Rs = 9646=00

Rs = 30,51,381=00

Add GST @ 12% Rs = 3,66,166=00

Add L/c @ 1% Rs = 30,514=00

Rs = 34,48,061=00

Less 4.29% below
sch. Rate.

Rs = 147,922=00

Rs = 33,00,139=00

20.8.22
JE

20.8.22
A.L.

Continuation
