

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग कार्य प्रमंडल, महाराजगंज।**

पत्रांक 2003अनु०

महाराजगंज,

दिनांक 14/12/2022

प्रेषक :-

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महाराजगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह— सचिव बिहार ग्रामीण पथ विकास एजेंसी
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:

नई अनुरक्षण नीति 2018 शीर्ष 3054 अन्तर्गत व्यय हेतु आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक ग्रामीण कार्य विभाग, कार्य प्रमंडल महाराजगंज के अधीन नई अनुरक्षण नीति 2018 शीर्ष 3054 अन्तर्गत कराए कार्य के विरुद्ध संलग्न विवरणी के अनुसार भुगतान हेतु रु०— 83,25,065=00(तिरासी लाख पच्चीस हजार पैंसठ) मात्र का आवंटन उपलब्ध कराने की कृपा की जाय ताकि किए गए कार्य का भुगतान किया जा सके।

अनु०— यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, महाराजगंज।

From GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of Utilization Certificate up to the month of December 2022

Rural Road Maintenance Policy-2018 under MR 3054

1. RWD, Works Division, Maharajganj

S.No.	Name of Scheme	Sanction No. with amount (In Rs. Lacs)	Amount Received (In Rs. Lacs)	Particulars
1	Rural Road Maintenance Policy-2018 under MR 3054			
	Letter No.	Date	Amount	
1	42 WE-	04-06-20	321.29600	✓ Certified that out of Rs. 5071.68083 lacs received till October 2022 in favor of Ex. Engineer R.W.D., Works Division, Maharajganj, a sum of Rs 4899.87773 lacs has been utilized for the purpose of Rural Road Maintenance Policy-2018 under MR 3054 Schemes for which it was sanctioned and the balance of Rs 171.80310 lacs remaining unutilized at the end of the period .
2	64 WE	03-09-20	26.37	
3	77 WE	14-10-20	27.09100	
4	80 WE	05-11-20	243.700	
5	82 WE	13-11-20	418.794	
6	84 WE	26-11-20	101.95	
7	86 WE	11-12-20	401.076	
8	05 WE	12-01-21	556.75256	
9	17 WE	26-02-21	541.18495	
10	20 WE	19-03-21	213.04560	
11	26 WE	15-04-21	37.34449	
12	27 WE	04-05-21	87.13221	
13	30 WE	21-05-21	122.65500	
14	32 WE	28-05-21	33.32400	
15	34 WE	04-06-21	209.64778	
16	36 WE	07-06-21	58.54493	
17	40 WE	14-06-21	108.84119	
18	58 WE	27-10-21	5.26470	
19	02 WE	03-01-22	56.94891	
20	05 WE	25-01-22	148.39890	
21	20 WE	14-03-22	49.27450	
22	43 WE	24-03-22	16.50	
23	44 WE	30-03-22	109.93135	
24	46 WE	13-04-22	299.40405	
25	51 WE	28-04-22	26.35	
26	01 WE	20-05-22	249.58677	
27	03 WE	08-06-22	227.14938	
28	22 WE	08-08-22	193.59758	
29	35 WE	13-10-22	14.28911	
30	44 WE	18-11-22	166.23587	

2. Certified that I have satisfied myself that the conditions which the grants—in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

DAO
R.W.D., Works Division
Maharajganj

Executive Engineer
R.W.D., Works Division
Maharajganj



Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification and Surface Renewal)

1. Signed Hard Copy and Soft Copy (In excel) of recorded IRI is enclosed .
2. Up-to-date Physical Progress has been uploaded in MIS

RWD. Works Division, Maharajganj


RWD Works Division, Maharajgarh

Name of Customer: **PRUTHI PRIVATE LIMITED**
 Name of Work Road: **PRUTHI VIA DEVA PIPRABADI**
 Lab Job Number: **0812022**
 Date: **08/12/22**
 Sample No: **3**

Test Date:	08-12-2022	Field Name:	
Machine No:		Road Type:	(A) ASPHALT
Start S No:		Sign:	
Weather:		UV Range:	75/ T ₂ E ₂₀₀₀ 1100 m/min
Start Location:		Dist Range:	0 T ₂ 31 101 1000 m
End Location:		Equation:	test

File: G:\0812\22\B.Ma. Section No. 03. Egn test

Name of Customer: YUGALBHAI CONSTRUCTION PRIVATE LIMITED. Name of Work Road: BHAGAWANPUR

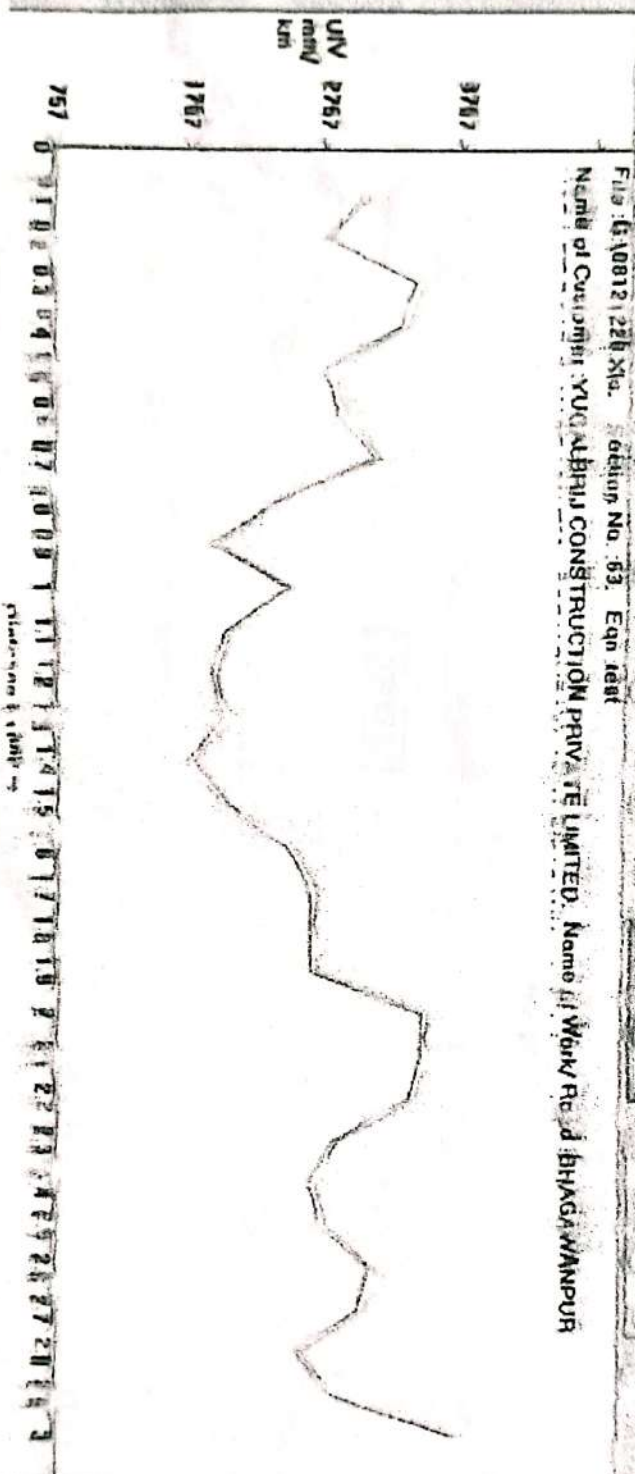

Reduce Graph

Map View

Handwritten signature
08/12/22

Handwritten signature
08/12/22
SE

Handwritten signature
08/12/22
SE

Handwritten signature
08/12/22

Assd. 15 Manager
(R.D/V.D) Maheshwari

of Road - BHAGAWANPUR MORA BT ROAD SAHASRAON 103 - GOPALPUR VIA ARUA PIPARAHIA

Date	Time	Section	No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
8/12/22	12:12:0	63	0.1	320	0	3200	3054		G	26.94663	84.67345	Normal
8/12/22	12:12:0	63	0.1	290	20.2	2900	2776		G	26.94613	84.672473	Normal
8/12/22	12:12:25	63	0.1	360	20.2	3600	3424		G	26.94552	84.671463	Culvert
8/12/22	12:12:25	63	0.1	350	20.2	3500	3331		G	26.94555	84.67047	Normal
8/12/22	12:13:1	63	0.1	290	20.2	2900	2776		G	26.94637	84.669477	Normal
8/12/22	12:13:1	63	0.1	300	20.2	3000	2868		G	26.94932	84.668535	Normal
8/12/22	12:13:1	63	0.1	330	20.2	3300	3146		G	26.95292	84.667575	Normal
8/12/22	12:13:36	63	0.1	250	20.2	2500	2405		G	26.96198	84.667525	Normal
8/12/22	12:14:0	63	0.1	200	20.2	2000	1942		G	26.97057	84.667288	Normal
8/12/22	12:14:11	63	0.1	260	20.2	2600	2498		G	26.9742	84.666497	Normal
8/12/22	12:14:11	63	0.1	210	20.2	2100	2035		G	26.97913	84.665673	Normal
8/12/22	12:14:46	63	0.1	200	20.2	2000	1942		G	26.9832	84.66478	Normal
8/12/22	12:15:0	63	0.1	210	30.3	2100	2035		G	26.9858	84.663872	Normal
8/12/22	12:15:22	63	0.1	180	30.3	1800	1757		G	26.99047	84.662945	Normal
8/12/22	12:15:22	63	0.1	210	20.2	2100	2035		G	26.9944	84.66202	Normal
8/12/22	12:15:22	63	0.1	260	30.3	2600	2498		G	26.9967	84.661043	Normal
8/12/22	12:15:22	63	0.1	280	30.3	2800	2683		G	26.99865	84.66002	Normal
8/12/22	12:16:0	63	0.1	280	10.1	2800	2683		G	26.99993	84.659023	Normal
8/12/22	12:16:32	63	0.1	280	10.1	2800	2683		G	26.10015	84.65803	Normal
8/12/22	12:17:8	63	0.1	370	10.1	3700	3517		G	26.10031	84.657037	Normal
8/12/22	12:17:8	63	0.1	360	20.2	3600	3424		G	26.10079	84.656212	Normal
8/12/22	12:17:43	63	0.1	300	20.2	3000	2868		G	26.10151	84.655992	Normal
8/12/22	12:18:0	63	0.1	280	20.2	2800	2683		G	26.10225	84.655723	Normal
8/12/22	12:18:18	63	0.1	290	20.2	2900	2776		G	26.10303	84.655735	Normal
8/12/22	12:18:18	63	0.1	330	20.2	3300	3146		G	26.10378	84.654628	Normal
8/12/22	12:18:53	63	0.1	320	20.2	3200	3054		G	26.10453	84.654157	Normal
8/12/22	12:19:0	63	0.1	270	20.2	2700	2591		G	26.10541	84.654308	Culvert
8/12/22	12:19:0	63	0.1	300	20.2	3000	2868		G	26.10631	84.654528	Normal
8/12/22	12:19:29	63	0.01	40	40.4	4000	3794		G	26.10772	84.654813	Normal

$$Y = 0 * X^2 + 0.926 * X + 90.84$$

$$X = 909$$

$$Y = 932$$

(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

08/12/22
 A-1.1.1.1

08/12/22
 SE

08/12/22

26.10772

1

Name of Work—
 Situation of Work—
 Agency by which work is executed—
 Date of Measurement—
 No. and date of agreement—
 (These four lines should be repeated at the commencement
 of the measurement relating to each work)

Measurement relating to each work)					
Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work - Maintenance/Repair of road from Bhagwanpur mora BT road To Sahasraon to Gopalpur via Arua Piprahia					
Agency:- M/s Yugal brij Construction Pvt. Ltd #- Champur Charihara, Ra-Madhya					
App. No- 81/MBD./2021-22 dated-26.07.22					
Date of Commencement = 22.12.2021					
Date of Completion - 21.09.2022					
Actual date of Completion:- —					
Date of Measurement :- 19.09.2022					
1. Clearing and Grubbing road land (by manual means) including uprooting wild vegetation, grass, bushes shrubs. Sapling and trees of girth etc.					
	2X	30X	30X	1.00	= 1800
	2X	30X	30X	1.00	= 1800
	2X	30X	30X	1.00	= 1800
	2X	6X	30X	1.00	= 360
	2X	1X	20X	1.00	= 40
					5800 m ²
Continuation					

Continuation

0.58 Hectare



Abstract of cost

1. clearing and grubbing road land (by manual means).

Qty vide TMB page no - 01
and item no - 1.

0.58 Hectare @ Rs. 60884.19/hect Rs. 35313/-

② Construction of Subgrade
and earthen shoulder with
approved material obtained
from borrow pit

Qty vide TMB page no - 26 and
item no - 02

1000.71 m³ @ Rs. 217.07/m³ Rs. 217224/-

Continuation

Rs. 252537/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
③ Construction of granular Sub base by providing Well graded Material, spreading in Uniform layers with motor grader.					
Qty vide TMB Page no-8 and 9 of item no. $\frac{22}{3}$					
158.57 m³@Rs. 2891.32/m³ Rs. 458476/-					
④ Providing, laying, Spreading and Compacting Stone aggregate of Specific Size to water bound macadam WBM Gr-II					
Qty vide TMB page no- 9, 10 and 11 of item no. $\frac{23}{4}$					
125.20 m³@Rs. 4532.99/m³ Rs. 567530/-					
⑤ WBM Gr-III. Providing, laying spreading and Compacting Stone aggregate of Specific Size to water bound macadam.					
Qty vide TMB Page no- 12, 13 and 14 of item no. $\frac{24}{5}$					
189.62 m³@Rs. 4771.58/m³ Rs. 904787/-					
⑥ Prime coat: Providing and applying primer coat with bitumen Emulsion (SS-1) on Prep. Sub.					
Qty vide TMB page no- 15, 16, 17 item no. $\frac{25}{6}$					
2528.20 m²@Rs. 54.07/m² Rs. 136700/-					

Continuation

Rs. 2320030/-

B/Rs. 232 0030/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(7) Tack Coat: Providing and applying tack coat with bitumen Emulsion using emulsion pressure distributor					
Qty vide TMB page no - 18					
and item no - 26/7.					
2528.20 m ² @ Rs. 18.25/m ²					Rs. 46139/-
(8) Providing, laying and rolling of close-graded premix surfacing material of 20 mm thickness.					
Qty vide TMB page no - 18,					
19, 20, 21 & item no - 27/8.					
2528.20 m ² @ Rs. 249.58/m ²					Rs. 630988/-
(9) Tack coat					
Providing and applying tack Coat with bitumen Emulsion (RS-1) using emulsion pressure distributor					
Qty vide TMB page no - 21					
of item no - 28/9					
10050 m ² @ Rs. 15.81/m ²					Rs. 158890/-
(10) SDBC: - Providing and laying semi dense bituminous concrete with 100-120 TPH batch type etc.					
Qty vide TMB page no - 21, 22					
of item no - 29/10					
251.25 m ³ @ Rs. 13850.36/m ³					Rs. 3479903/-

Continuation

Rs. 6635950/-

Continuation

Rs. 6635950/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑪ WBM Gr-III for put in PCC position					
Providing, laying, Spreading and Compacting stone aggregate of specific size to WBM.					
Qty vide TMB page no - 22, 23					
and item no - $\frac{30}{11}$					
20.53 m ³ @ Rs. 4771.58/m ³ to Rs. 97960/-					
⑫ Cement Concrete Pavement					
Construction of Un-reinforced Cement Concrete thickness as					
Per design, over a prepared subgrade					
Qty vide TMB page no - 23					
and item no - $\frac{31}{12}$					
132.0 m ³ @ Rs. 8090.07/m ³ to Rs. 1067889/-					
⑬ Km Stone					
Qty vide TMB page no - 26					
and item no - $\frac{33}{14}$					
4 nos @ Rs. 2925.57/each - Rs. 11702/-					
⑭ 200 m Stone					
Qty vide TMB Page no - 27 and					
item no - $\frac{34}{15}$					
12 nos @ Rs. 785.67/each - Rs. 9428/-					
⑮ Direction and place identification					
Signs with size more than					

Continuation

Rs. 7822929/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
0.9 sqm Soge board					
Qty vide TMB page no-27					
and item no - $\frac{25}{16}$					
1.32 nos @ Rs. 13548.56/m ² Rs. 26013/-					
(17) Bowditch and fixing of retro-reflectorsed Cautionary, mandatory and informatory sign					
600 mm equilateral triangle					
Qty vide TMB page no-27					
of item no - $\frac{26}{17}$ $\frac{36}{17}$					
12 nos @ Rs. 4051.22/each Rs. 48614/-					
(18) 600 mm Circular.					
Qty vide TMB page no-27					
and item no - $\frac{37}{18}$ $\frac{18}{18}$					
6 nos @ Rs. 4272.52/each Rs. 25635/-					
(19) 600 mm X 450 mm rectangular					
Qty vide TMB page no-27					
and item no - $\frac{38}{19}$ $\frac{38}{19}$					
6 nos @ Rs. 4132.01/each Rs. 24792/-					
(20) Reinforced Cement Concrete					
M15 grade boundary pillar					
Qty vide TMB page no-27					
and item no - $\frac{39}{20}$					
64 nos @ Rs. 636.74/each Rs. 40751/-					
					Rs. 7988734/-

Continuation

B.R. 7988734/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(22) Planting of trees and their Maintenance for one year.					
Qty vide TMB page no 27					
and item no -			48	22	
134 nos @ R. 964.48/each					129240/-
(23) Road marking with hot applied thermoplastic					
Qty vide TMB page no - 27					
and item no -			48	23	
580 m ² @ R. 815.83/m ²					473181/-
(24) Ponding and fixing					
'Logo' of Maintenance project.					
Qty vide TMB page no - 28 and					
item no -			48	24	
4 nos @ R. 11229.65/each					44918/-
(25) Brick masonry in C.M.					
in parapet.					
Qty vide TMB page no - 28					
and item no -			48	25	
15.84 m ³ @ R. 5754.82/m ³					91156/-
(26) Plastering with Cement mortar in brick work in substructure.					
Qty vide TMB page no -			44	26	
120.96 m ² @ R. 170.54/m ²					20628/-
					R. 8747857/-

Continuation

BRR 2747 857/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(27) Painting two coats on new concrete surface.					
Qty vide TMB pageno- 28, 29					
of item no- 45/27.					
211.2 m ² @ Rs. 114.46/m ²					Rs. 24174/-
(28) Earthwork in excavation for foundation of structure.					
Qty vide TMB pageno- 2					
and item no- 2/28					
29.798 m ³ @ Rs. 320.85/m ³					Rs. 9560/-
(29) Providing M15 PCC as levelling course in foundation.					
Qty vide TMB pageno- 2					
of item no- 3/29					
2.96 m ³ @ Rs. 6537.51/m ³					Rs. 19351/-
(30) Brick masonry work in C.M (1:4) in head wall complete as per drawing.					
Qty vide TMB pageno- 2 and item no- 3/30					
27.654 m ³ @ Rs. 6132.52/m ³					Rs. 169588/-
(31) Providing and laying RCC Pipe NP4 for Culvert.					
Qty vide TMB pageno- 2 and item 5/31					
7.50 m @ Rs. 3706.5/m					Rs. 27799/-

Continuation

Rs 8998329/-

BBK 8998329/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(32) Plastering with Cement mortar (1:4) on brick work in Substructure					
Qty vide TMB page no - 3					
and item no - 6/32.					
41.633 m ² @ Rs. 170.54/m ² Rs. 7100/-					
(33) Providing 1.5 mm Cement punning including cutting Carriage of water etc.					
Qty vide TMB page no - 3					
and item no - 7/33.					
13.26 m ² @ Rs. 52.94/m ² Rs. 702/-					
(34) E/W in excavation for structure as per drawing and technical specification					
Qty vide TMB page no - 3					
and item no - 8/34					
95.546 m ³ @ Rs. 320.85/m ³ Rs. 30656/-					
(35) Sand filling in foundation trenches as per drawing & tech. spec.					
Qty vide TMB page no - 4					
and item no - 9/35					
2.02 m ³ @ Rs. 560.57/m ³ Rs. 1132/-					
(36) Providing ACC M15 Concrete for plain concrete in open foundations complete as					

Continuation

Continuation

BBK 9037919/-

Rs. 9037913/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
per drawing and Technical Specification					
Qty vide TMB page no - 4					
and item no - $\frac{10}{26}$					
13.68 m ³ @ Rs. 6537.51/m ³ Rs. 89433/-					
(37) Brick masonry work in Cement mortar in foundation					
Qty vide TMB page no - 4					
and item no - $\frac{11}{37}$					
52.298 m ³ @ Rs. 5875.01/m ³ Rs. 307251/-					
(38) Brick masonry work in cement mortar in					
Substructure and field complete					
Qty vide TMB page no - 4					
and item no - $\frac{12}{38}$					
26.71 m ³ @ Rs. 6132.52/m ³ Rs. 163799/-					
(39) Plain/reinforced Cement Concrete (M20) in Substructure					
Complete as per drawing and Technical Specification					
Qty vide TMB page no - 4 x 5					
8 item no - $\frac{13}{39}$					
4.428 m ³ @ Rs. 6909.80/m ³ Rs. 30596/-					
(40) Powdering bitumen painting over top surface of Abut' emb.					
Qty vide TMB page no - 5 item no - $\frac{14}{40}$					
15 m ² @ Rs. 18.25/m ² Rs. 274/-					
Continuation					
Rs. 9629272/-					

B.R. 3629272/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(41) R.C.C. 12.5 in Deck slab bonding and laying reinforced Cement concrete in Superstructure Qty vide MB page no-5 and item no- $\frac{16}{41}$ 8.01 m ³ @ Rs. 7567.16/m ³ Rs 60613/-					
(42) Supplying, fitting and placing HYSD bar reinforcement in Super structure. Qty vide MB page no-5 and item no- $\frac{15}{42}$ 1.16 MT @ Rs. 63525.61/MT Rs 73690/-					
(43) Bonding and fitting joint Sealing Compound as per drawing and Technical specification Qty vide MB page no-6 and item no- $\frac{17}{43}$ 15 m @ Rs. 44.08/m Rs 661/-					
(44) Brick masonry work in Cement mortar 1:3 in parapet excluding pointing and plastering. Qty vide MB page no-6 and item no- $\frac{18}{44}$ 4.32 m ³ @ Rs. 5754.82/m ³ Rs 24861/- Rs 9789097/-					

Continuation

