

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल बिहारशरीफ

पत्रांक 1918(819) बिहारशरीफ, दिनांक 15-12-22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:- नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।
महाशय,

उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अधियाचना पत्र समर्पित की जा रही है।


अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन


15/12/22

 15/12/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
 15/12/22

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 15.12.2022

(New Maintenance Policy 2018)

FIU- BIHARSHARIF

Year-2022-23

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	latter no. 35 dated 13-10-2022	2246.65000	Certified that out of Rs 2246.65000 received & balance during the years 2022-23 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 2121.19924 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 125.45076 lacs remaining unutilized at the end of the period under 15.12.2022
	Total Rs.		2246.65000	

2 Certified that I have satisfied myself that the conditions on which the grants-in- aid was Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works


15/12/2022
Divisional Accounts Officer

Rwd, Works Division
Biharsharif


15/12/2022
Executive Engineer
Rwd, Works Division
Biharsharif

Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
Roads Division :- Bihar Sharif

Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) & Letter No	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Alloted (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Increase in Allotment	Remain
				Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	RM/NA/BI H/20/0002	NH-82 Barass To Ghaulachak	1013 03.03.2020	1.100	46.10900	35.17500	15.35970	MBD-04/2020-21 04.08.2020	03.05.2021	0	2563	25.00	5.40	0.0000	0.0000	16.42358	
2	RM/NA/BI H/21/0001	Kemar Kala Main Road To Tower Hote Huye Devi Mandir Path	073 11.01.2021	0.81	64.737	49.28	5.96612	MBD-01/2021-22 23.03.2021	22.12.2021	06.10.2021	1583	25.00	5.40	40.81056	40.81056	1.04229	
Total =				17.46587													
				TOTAL													

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


 15/12/2022
 Divisional Accounts Officer
 Rwd, works Division Bihar Sharif


 15/12/22
 Executive Engineer
 Rwd, works Division Bihar Sharif

Name of Road:- Kenar Kala Main Road to Tower Hote Huye Devi Mandir Path Nirman
Name of Contractor:- Probes Construction

Date	Time	Section		Length in km	Bumps in mm	Speed Rate	OR mm/km	CATEGORY		IRI	Latitude	Longitude	Event
		No.						ROAD					
5/7/21	8:51:0	39		0.1	200	0	2000			3.02	25.29419	85.73070	Normal
5/7/21	8:51:25	39		0.1	140	30.3	1400			2.34	25.29432	85.730813	Normal
5/7/21	8:51:25	39		0.1	180	30.3	1800			2.79	25.29449	85.738753	Normal
5/7/21	8:51:25	39		0.1	110	20.2	1100			1.99	25.29523	85.738585	Normal
5/7/21	8:52:0	39		0.1	90	40.4	900			1.76	25.29619	85.738787	Normal
5/7/21	8:52:0	39		0.1	90	10.1	900			1.76	25.2967	85.73847	Normal
5/7/21	8:52:0	39		0.1	10	40.4	100			0.77	25.29689	85.737473	Normal
5/7/21	8:52:35	39		0.1	10	40.4	100			0.77	25.29711	85.736447	Normal
5/7/21	8:52:35	39		0.01	0	50.5	0			0.63	25.29721	85.735975	Normal
Total=				0.810	830	262.6	8300			10850			15.83

$Y = 0 + X + 2 - 0.898 * X - 3.777 * X$			
X = 0			
Y = 377			
(R) RURAL ROAD			
Good	Average	Poor	
<4000	4001-5000	>5001	

2K
05/07/21

Executive Engineer
R.W.D. (W)
Division Biharsharif (Nalanda)


5/13/11

File : F:\05070853.Xls.

Section No. : 39.

Eqn : $Y = 0 - X^2 + 0.898 \cdot X + 377.8$

Name of Customer : Probes Construction, Name of Work/ Road : Kenar Kala Main Road to Tower Hole Huye Devi

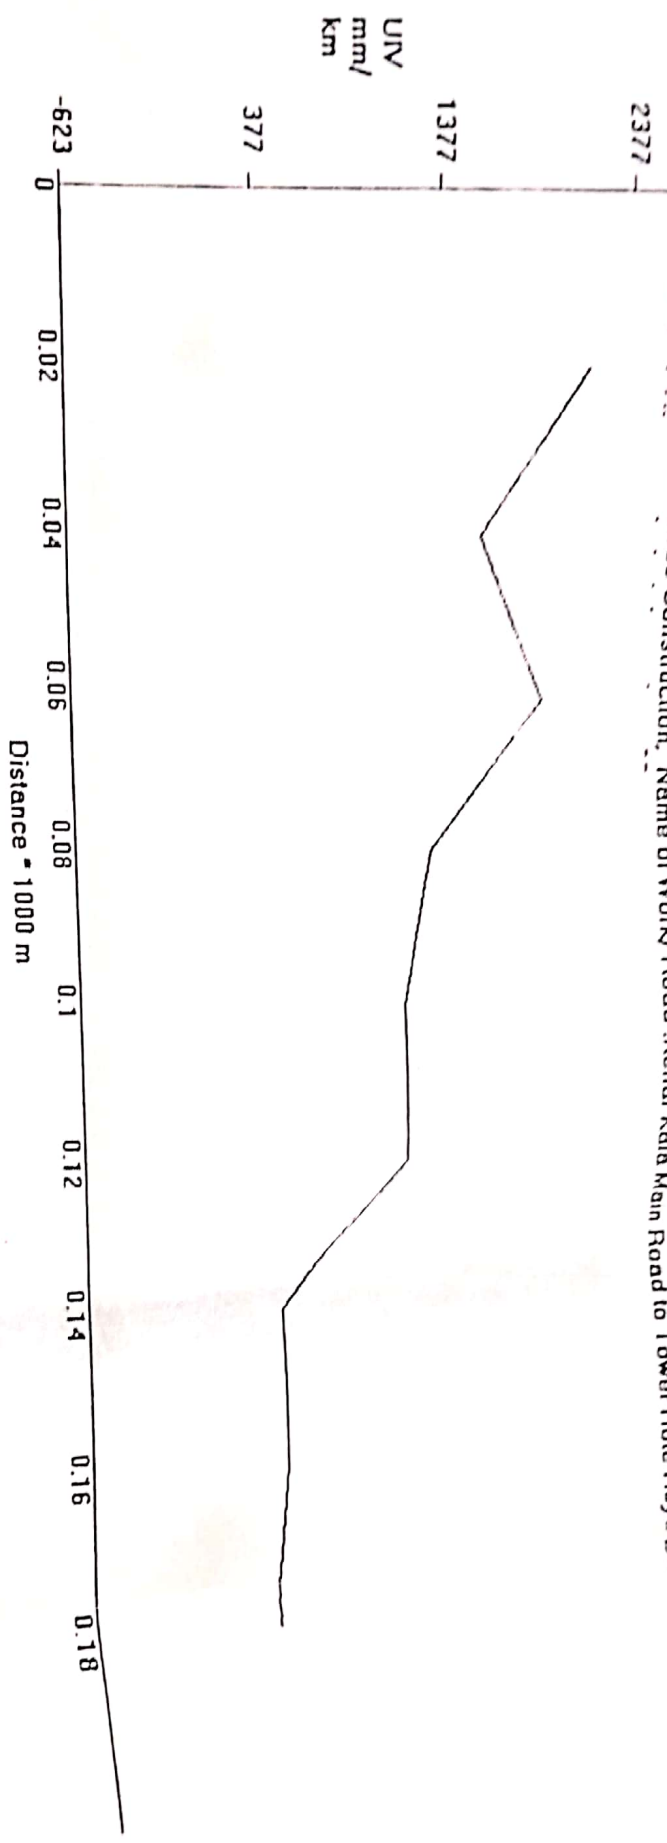

24/12/17
05/12/17

gm
5-12-17

Executive Engineer
R.W.D. (W)
Division Biharsharif (Nalanda)

New Maintenance Policy ~~2018~~ 2018

1 KENIA R KALLA

Measurement Book

Schedule XLY-Form No. 134

Road Name - Keras Kala. Main Road to Apurva hole lake

Dev. provided.

DIVISION

102/102/102/102

SUB-DIVISION

102/102/102/102

Com - Probable Cons. 2011

3011

1
 Name of Work -
 Situation of work -
 Agency by which work is executed -
 Date of measurement -
 No. and date of agreement -
 (These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1st on 30th bill					
Name of work - M/R to road from Kenar Kala Main Road to Tower hote hwe					
Devi Mandir Path Nirman					
Agency - Probase Construction India P.L					
F-101, Maurya Vihar, Kumbhar, Patna.					
Block - Sammera					
Agreement No. - MBD-01/2021-2022					

Work started date - 23-03-2021
 Date of completion - 22-12-2021
 Actual date of completion - ~~02-07-2021~~ ^{work in progress}

600mm dia H.P. Culvert
 (1/32) Earthwork in excavation
 for foundⁿ of structure do-do
 all complete
 H.K.L. - $2 \times 3.90 \times 1.15 \times 1.50 = 13.455$
 Below pipe - $1 \times 5.35 \times 1.15 \times 0.365 = 2.246$
 15.701 m^3
 (2/33) Providing M-15 Pcc (1:2.5:5)
 as levelling course in foundⁿ
 do-do all complete

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>2nd on Sirsi Boli</u>					
Name of work - M/E to road from Kaner Kala main road to tower hote					
here Den Mandir Path Nirman					
Agency - Probate Construction India P.L.					
F-101, Maurya Vihar, Kumbhari, Patna.					
Block - Sarmera					
Agreement No. - MBD-01/2021-22					
Work started date - 23-03-2021					
Date of completion - 22-12-2021					
Actual date of completion - 06-10-2021					
06/10/2021					

$\frac{1}{10}$ Const ⁿ of PCC un-reinforced expansion M 30 do do all					
Complete					
	13.60	$\frac{5.60 + 3.10 + 2.70}{2}$	$\times 0.160$	=	8.269
	6	$\frac{3.60 + 4.40}{2}$	$\times 0.160$	=	3.840
	15	$\frac{4.40 + 3.90}{2}$	$\times 0.160$	=	9.960
	15	$\frac{3.90 + 3.60}{2}$	$\times 0.160$	=	8.280
	15.60	$\frac{3.60 + 3.60}{2}$	$\times 0.160$	=	6.528
	12.10	$\frac{3.60 + 2.50}{2}$	$\times 0.160$	=	5.324
	12.20	$\frac{2.30 + 2.20}{2}$	$\times 0.160$	=	4.392
	12.30	$\frac{2.20 + 2.20}{2}$	$\times 0.160$	=	4.330
	9.10	$\frac{2.70 + 2.10 + 2.25}{3}$	$\times 0.160$	=	4.392
	7.25	$\frac{3.10 + 3.60}{2}$	$\times 0.160$	=	3.538
	3.10	3.150	$\times 0.160$	=	1.562
	10.70	$\frac{1.75 + 2.60}{2}$	$\times 0.160$	=	3.724
					64.139
Continuation					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					3707122.00 P.F. Rs 4051469.00
2.050m ³ Pg No. - (27)					
@ Rs 4658.37/m ³ - Rs 9550.20					
(48/66) Providing RCC M-20 (1:2:4)					
as cover slab do do all					
Completed					
7.006m ³ Pg No. - (28)					
@ Rs 4658.37/m ³ - Rs 32637.20					
(49/62) Supplying, fitting, placing					
TMT bar reinforcement in					
Suba-str. do do all					
Completed					
0.287 m.T. Pg No. - (28)					
@ Rs 49979.09/m.T. - Rs 14344.20					
Add 12% G.S.T (+) Rs 1721.30					
Add 1% L.Cess (+) Rs 1434.42					
Add Seigniorage fee (+) Rs 1434.42					
less 3% below (-) Rs 429.42					
Rs 18528.50					
less previous amount (-) Rs 40810.56					
Rs 10422.90					
16/11/21 J.E					
18/11/21 J.E					
20/11/21					
Work has been completed as per specification and direction of M.P.					
Nothing due against the contractor.					
Continuation					
16/11/21 J.E					
