

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल बिहारशरीफ

पत्रांक 1968 अनु० / बिहारशरीफ, दिनांक 26.12.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:— नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।
महाशय,

उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अधियाचना पत्र समर्पित की जा रही है।

अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।


अनु०:— यथोक्त।


26/12/22

विश्वासभाजन


26/12/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ


26/12/22

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 26.12.2022

(New Maintenance Policy 2018)

PIU- BIHARSHARIF

Year-2022-23

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	latter no. 35 dated 13-10-2022	2246.65000	Certified that out of Rs 2246.65000 received & balance during the years 2022-23 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 2121.19924 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 125.45076 lacs remaining unutilized at the end of the period under 26.12.2022
	Total Rs.		2246.65000	


2 Certified that I have satisfied myself that the conditions on which the grants-in- aid was Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works


26/12/22
Divisional Accounts Officer
Rwd, Works Division
Biharsharif


26/12/22
Executive Engineer
Rwd, Works Division
Biharsharif

Requisition Formate for Scheme Head - MIB(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Works Division :- Bihar Sharif

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Alloted (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Increase in Allocation	Remarks
					Length (In km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/NAB/HH/19/0005	NH-31 Dhannauli More to Desobhiga Gaigampur, Shrivasthiga, Garabigha Dousai	10200701010	5268 04-10-2019	1.89	46.439	47.847	19.22609	MIBD-07 20-21	07-06-2021	07 10 20 22	70.98	25.00	5.40	27.30219	27.30219	7.74164	
2	RM/NAB/HH/19/0005	Somsa Chhannuchak Road to Chandaura Road	10200601027	5268 04-10-2019	0.63	13.926	15.574	6.05637	MIBD-07 20-21	07-06-2021	10 10 20 22	23.55	25.00	5.40	8.71697	8.71697	6.64738	
3	RM/NAB/HH/19/0005	Band Alipur Road to Sonsikara	10200701039	5268 04-10-2019	0.63	13.014	13.562	5.90747	MIBD-07 20-21	07-06-2021	06 10 20 22	25.61	25.00	5.40	8.40134	8.40134	3.40246	
TOTAL																		

Total = 17.79148

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.

Divisional Accounts Officer
Rwd. works Division Bihar Sharif

Executive Engineer
Rwd. works Division Bihar Sharif

New maintenance Policy

Sanga chunchunchak Road to Chenduravara

Measurement Book

Schedule XLV-Form No. 134

DIVISION

C
19/12/21/21/15

SUB-DIVISION

235

2989

M/S Uday Shankar Prasad

प्रमाणित किया जाता है कि इस सामी प्रतिको
से मशीन से छपे कुल 100 (सौ) पृष्ठ हैं जिस
में रामरत्नकवल प्रसाद सिंह मादव सहायक
आयोगता, ग्रामीण कार्य विभाग कार्य अवर
प्रमंडल, रहुई के नाम निर्गत किया जाता है।

30/8/20

कार्यपालक अभियन्ता

ग्रामीण कार्य विभाग

कार्य प्रमंडल, बिहार शरीफ

30/8/20

Re-issued to Sri Binod Kumar Singh,
J.B. Rahui

28/10/20
AB

Sch, XLV-Form No. 134

बिहार शरीफ DIVISION

रहुई SUB-DIVISION

Measurement Book

No. 2989

Name of Officer श्री रामरत्नकवल प्रसाद सिंह मादव

सहायक आयोगता अवर प्रमंडल, रहुई

Date of first entry 28/10/20

Date of last entry

Name of Work -
 Situation of work -
 Agency by which work is executed -
 Date of measurement -
 No. and date of agreement -
 (These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Record Entry</u>					
Name of work - Maintenance of Road					
from Sankh chun chun chak road					
to Chandwari					
Heed - 3054					
Agency - M/S Uday Shankar Prasad					
Agreement No - MBD-07/2020-21					
Agreement Rate - 0.01% Below of Govt Rate					
Agreement Amount -					
Work start Date - 08/07/2020					
Date of completion - 07/06/2021					
Date of entry - 28/10/20					
(1/194) Clearing and grubbing road					
Land - - all complete RB					
By	$2 \times 30 \times 30 \times 1 =$				180 m^2
	$2 \times 40 \times 30 \times 1 =$				240 m^2
	$2 \times 20 \times 30 \times 1 =$				120 m^2
	$2 \times 10 \times 23 \times 1 =$				46 m^2
	$2 \times 10 \times 28 \times 1 =$				56 m^2
	$2 \times 30 \times 30 \times 1 =$				180 m^2
	$2 \times 20 \times 30 \times 1 =$				120 m^2
	$2 \times 10 \times 24 \times 1 =$				48 m^2
					990 m^2
					$= 0.099/100$
(2/219) Provisioning and turning					
Informative sign board - - 124					
Complete RB					
					240

By 28/10/20

Continuation
 21/11/20
 AB

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Final Bill					
Name of work					Maintenance of road
from	Sansa	Chunmehat			road to
Chandwarh					
Agency	M/s. Vda. Shankar Prasad				
Agreement No.	MBD-07/2020-21				
Agreement Rate	As per PoR Rate				
Work Start Date	08/09/2020				
Date of Completion	07/06/2021				
Date of Actual Completion	10/10/22				
Date of entry	10/10/22				
①	Provided and applied				
201	Tack coat				

Complete 002					
1x	30.00	3.75			112.50 m ²
(2/202) Provided and Laying Semi					
dense bituminous concrete					
--- all complete 006					
1x	30.00	3.75	0.025		42.50 m ²
					2.813 m ³
(3/195) Construction of Subgrade					
and earthen shoulders					
All complete 007					
2x6x	30.00	1.20	0.70		302.40 m ³
2x4x3	0.60	1.00	0.70		168.00 m ³
2x2x30.00	0.90	0.75			81.00 m ³
2x2x30.00	0.80	0.75			72.00 m ³
2x1x30.00	0.60	0.75			27.00 m ³
2x1x20.00	0.50	0.75			15.00 m ³
2x1x30.00	1.00	0.70			42.00 m ³
Continuation					707.40 m ³

Sch. XLV-Form No. 134					
Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>ABSTRACT OF COST</u>					
(1/194) Clearing and grubbing road land -- all complete job					
Qty vide TMB Page 10 = 0.099 Hec					
@ 52970.33/Hec =					5244.00
(2/195) Construction of subgrade and earthen shoulders --					
All complete job					
Qty vide TMB Page 13 = 707.40 m ³					
@ 176.66/m ³ =					124969.00
(3/196) Construction of G.S.B grading II -- all complete job					
Qty vide TMB Page 10 = 20.81 m ³					
@ 1608.01/m ³ =					33463.00
(4/197) Provision, laying, spreading and compacting WBM 2 --					
All complete job					
Qty vide TMB Page 10 = 17.76 m ³					
@ 2745.70/m ³ =					48764.00
(5/198) Provision, laying, spreading and compacting WBM 3 --					
All complete job					
Qty vide TMB Page 10 = 26.62 m ³					
@ 2522.93/m ³ =					67160.00
(6/199) Provision and application of binder coat -- all complete job					
Qty vide TMB Page 10 = 355.15 m ²					
@ 42.85/m ² =					15218.00

Continuation

Total 294818.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				Bf Pf	1348725.10
(22/222) Painted two coats					
including primer coat					
all Comp Code sub					
44.16 TMB Page 15 = 25.70 m ²					
Qd 110.76/m ²				= R	2590.10
				R	1351315.10
Add GST @ 12%				= (4) R	162158.10
Add Labour @ 10%				= (4) R	13513.10
				R	1526986.10
Add Sundry charges					
(2) Subgrade - 707.40 m ³					
Qd 23.78 x 10/100/m ³				= R	1682.10
(3) GSB - 20.81 m ³					
Qd 4 39.34 x 10/100/m ³				= R	914.10
(4) WBM2 - 17.76 m ³					
Qd 6 20.16 x 10/100/m ³				= R	1101.10
(5) WBM3 - 26.62 m ³					
Qd 6 37.37 x 10/100/m ³				= R	1697.10
(6) MSS - 355.15 m ²					
Qd 1 2.69 x 10/100/m ²				= R	451.10
(7) SDBC - 50.196 m ³					
Qd 7 17.93 x 10/100/m ³				= R	3604.10
(8)				R	1536435.10
Less Provision for Road					
Vide TMB Page 12				= (4) R	871697.10
				R	664738.10
10/10/12					
10/10/12					

Continuation

Name of Road:-Sonsa Chunchunchak Road To Chandwara

Name of Contractor:- M/S Uday Shankar Prasad

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
		No.										
5/12/21	10:20:14	61	0.1	220	0	2200	2353	G	3.24	25.280068	85.61094	Normal
5/12/21	10:20:14	61	0.1	240	30.3	2400	2533	G	3.46	25.28002	85.6119	Normal
5/12/21	10:20:49	61	0.1	210	10.1	2100	2263	G	3.13	25.279898	85.61296	Normal
5/12/21	10:21:0	61	0.1	220	10.1	2200	2353	G	3.24	25.27901	85.61293	Normal
5/12/21	10:21:25	61	0.1	230	0	2300	2443	G	3.35	25.278298	85.61268	Normal
5/12/21	10:22:0	61	0.1	200	30.3	2000	2173	G	3.02	25.278345	85.612	Normal
5/12/21	10:22:0	61	0.03	300	30.3	3000	3071	G	4.11	25.278312	85.61066	Normal
Total			0.630	1620.00	111.10	16200.00	17189.00		23.55			

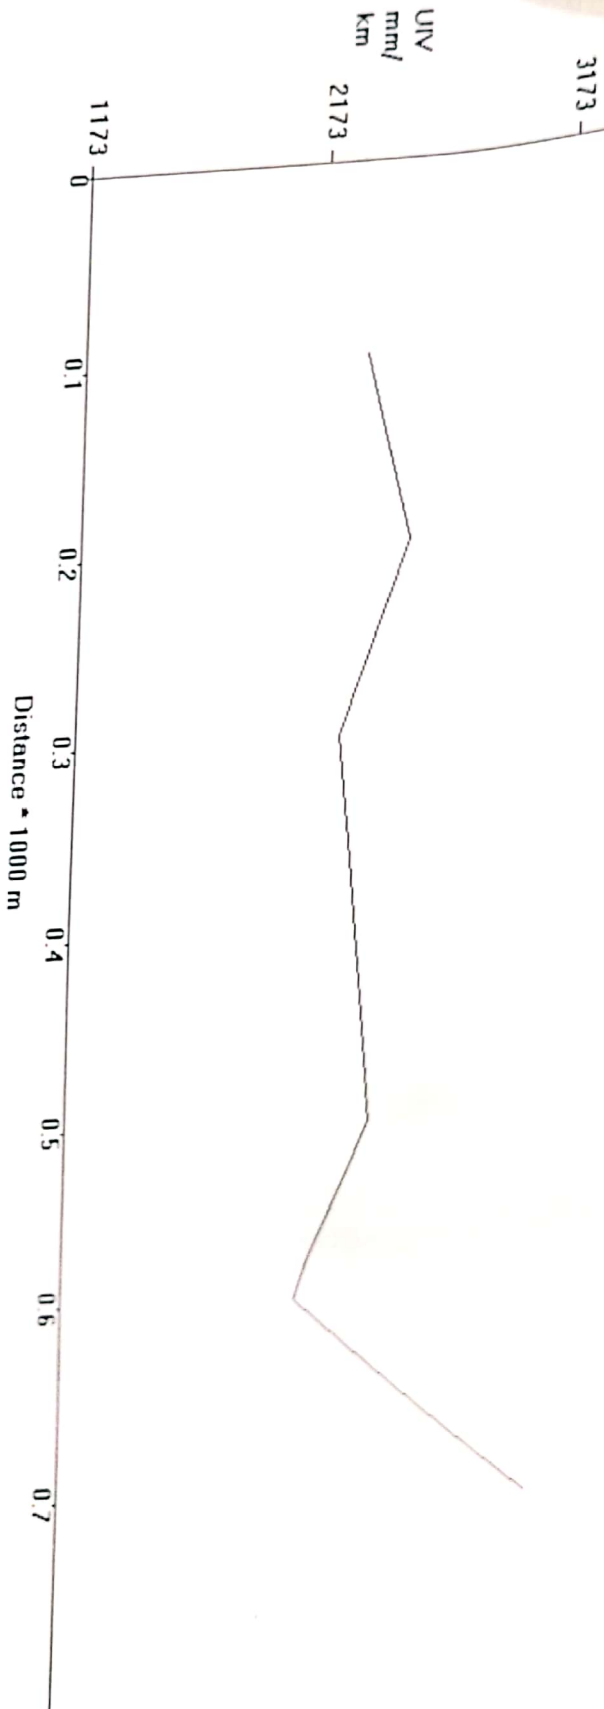
SPV
24/11/21
APR

$Y = 0 * X^2 + 0.898 * X + 377.8$		
X = 2471		
Y = 2596		
(R) RURAL ROAD		
Good	Average	Poor
<4000	4001-5000	>5001

Executive Engineer
R.W.D. (W)
Division Biharsanif (Nalanda,

24/11/21

File : F:\19121130.Xls. Section No. : 61. Eqn : $Y = 0 \cdot X^2 + 0.898 \cdot X + 377.8$
 Name of Customer : MS Uday Shankar Prasad, Name of Work/ Road : Sonsa Chunnuchak Road to Chandaura. Lab



SK
24/11/21

Hy
24/11/21
PAB

QPM
24/11/21

Executive Engineer
 R.W.D. (V)
 Division Biharsharif (Nalanda),
