

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक:- 274 (अनु०)

पालीगंज/दिनांक:- 12/2/22

प्रेषक :

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

विशेष सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- शीर्ष-MR (3054) Under Bihar Rural Road Maintenance Policy-2018 के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष-MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का अधियाचना का मॉग विहित प्रपत्र में तैयार कर Signed Hard Copy of Recorded IR1 के साथ अधियाचना हेतु भेजी जा रही है।

अतः आप से अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाये, ताकि संवेदक का भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

12/2/22
06/02/22

Requisition Form for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification and surface Renewal)

Name Of Work division - Paliganj				Administrative		Agreement Amount															
Sl	Package No	Name Of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Length (in KM)	Amount of (in lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Year Routine Maintenance (in lakh)	Agreement no & Date	Date of completion as per Agreement	Actual Date of completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Shown Content in Percentage	Previous Total Allocated Amount (in lakh)	Up-to-date expenditure as per MIS (in lakh)	Requisition against work done (in lakh)	Remarks			
1	MR-N/19-20	SAIDASAD MASUD-SARDA CHAPRA PATH	NEA22000897	13.12.2019	1.0	40.58600	30.95700	10.47190	05/MBD/2020-21 & 18.06.2020	17.03.2021	-	2.57800	25 mm (SDBC)	5.01%	0.00	0.00	17.32894	Work has been completed as per specification and verification of 80% percent measurement by resident engineer and 20% percent by Executive Engineer has been done.			

for 9/2/22
Sr. Divisional Accounts Offi
Rural Work Department
Works Division Paliganj

for 9/2/22
Executive Engineer:
Rural Works Deptt.
Works Division Paliganj
09/2/22

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the end of January.2022

PIU: RWD Works Division , Paliganj

Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Bihar Rural road Maintenance Policy 2018- Under MR 3054	64we dt 06.12.2021	158574627.00	Certified that out of Rs 158574627.00 received during the years January 2022 in favour of Ex. Engineer, RWD, Works Div. Paliganj Bihar a sum of Rs 157585023.00 has been utilized for the purpose of Bihar Rural Road Maintenance policy 2018- Under MR 3054 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 989604.00 remaining unutilized at the end to the period under
Total			158574627.00	

2. Certified that I have satisfied myself that the conditions of which the grants sanction Sanctioned have been duly fulfilled/are being fulfilled and I have exercised the checks to see the money was actually utilised for the purpose for which it was sanctioned.

Kishor 9/1/22
Sr. Divisional Accounts Offi
Rural Work Department
Works Division Paliganj

12/1/22
Executive Engineer
Rural works Deptt.
Works Division, Paliganj
09/1/22
09/12/2022

Name of work : Saicabad Masjid -Sarda :Thapra Path

Name of customer : SANTOSH KUMAR

(R)Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000


Date	Time	Test No	Distance(m)	Total Distance(m)	BUMPI(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction?	Remarks
29/01/22	19:02:44	9	100	100	25.0 cm	5.5 Km/Hr	2500.0 mm/Km	2380	3.28	Good	25.4165817	N	84.7935038	E	Breaker
29/01/22	19:03:13	9	100	200	21.0 cm	12.1 Km/Hr	2100.0 mm/Km	2012	2.82	Good	25.4174032	N	84.7924967	E	Breaker
29/01/22	19:03:33	9	100	300	26.0 cm	17.2 Km/Hr	2800.0 mm/Km	2473	3.39	Good	25.4174032	N	84.7924967	E	Breaker
29/01/22	19:03:49	9	100	400	14.0 cm	22.9 Km/Hr	1400.0 mm/Km	1366	2	Good	25.4159021	N	84.7913904	E	Normal
29/01/22	19:04:04	9	100	500	13.0 cm	24.1 Km/Hr	1300.0 mm/Km	1274	1.88	Good	25.4159021	N	84.7913904	E	Normal
29/01/22	19:04:20	9	100	600	14.0 cm	22.9 Km/Hr	1400.0 mm/Km	1366	2	Good	25.4149580	N	84.7906122	E	Normal
29/01/22	19:04:35	9	100	700	15.0 cm	24.3 Km/Hr	1500.0 mm/Km	1458	2.12	Good	25.4149580	N	84.7906122	E	Normal
29/01/22	19:04:50	9	100	800	12.0 cm	23.4 Km/Hr	1200.0 mm/Km	1182	1.75	Good	25.4149580	N	84.7906122	E	Normal
29/01/22	19:05:10	9	100	900	31.0 cm	18.1 Km/Hr	3100.0 mm/Km	2934	3.95	Good	25.4149580	N	84.7906122	E	Normal
29/01/22	19:05:53	9	100	1000	19.0 cm	8.8 Km/Hr	1900.0 mm/Km	1827	2.59	Good	25.4149580	N	84.7906122	E	Normal

5.2.22
ISA

Shri. Santosh Kumar

12/2
E.E.

NT Group Access Control
No. of Customer: SANTOSH KUMAR . Machine no: 19206 . Road: Saidabad Masjid -Sarda Chappa Path . Date: 04-02-22 . Section No: 09 . Equation: $y=0.922x-75.3$

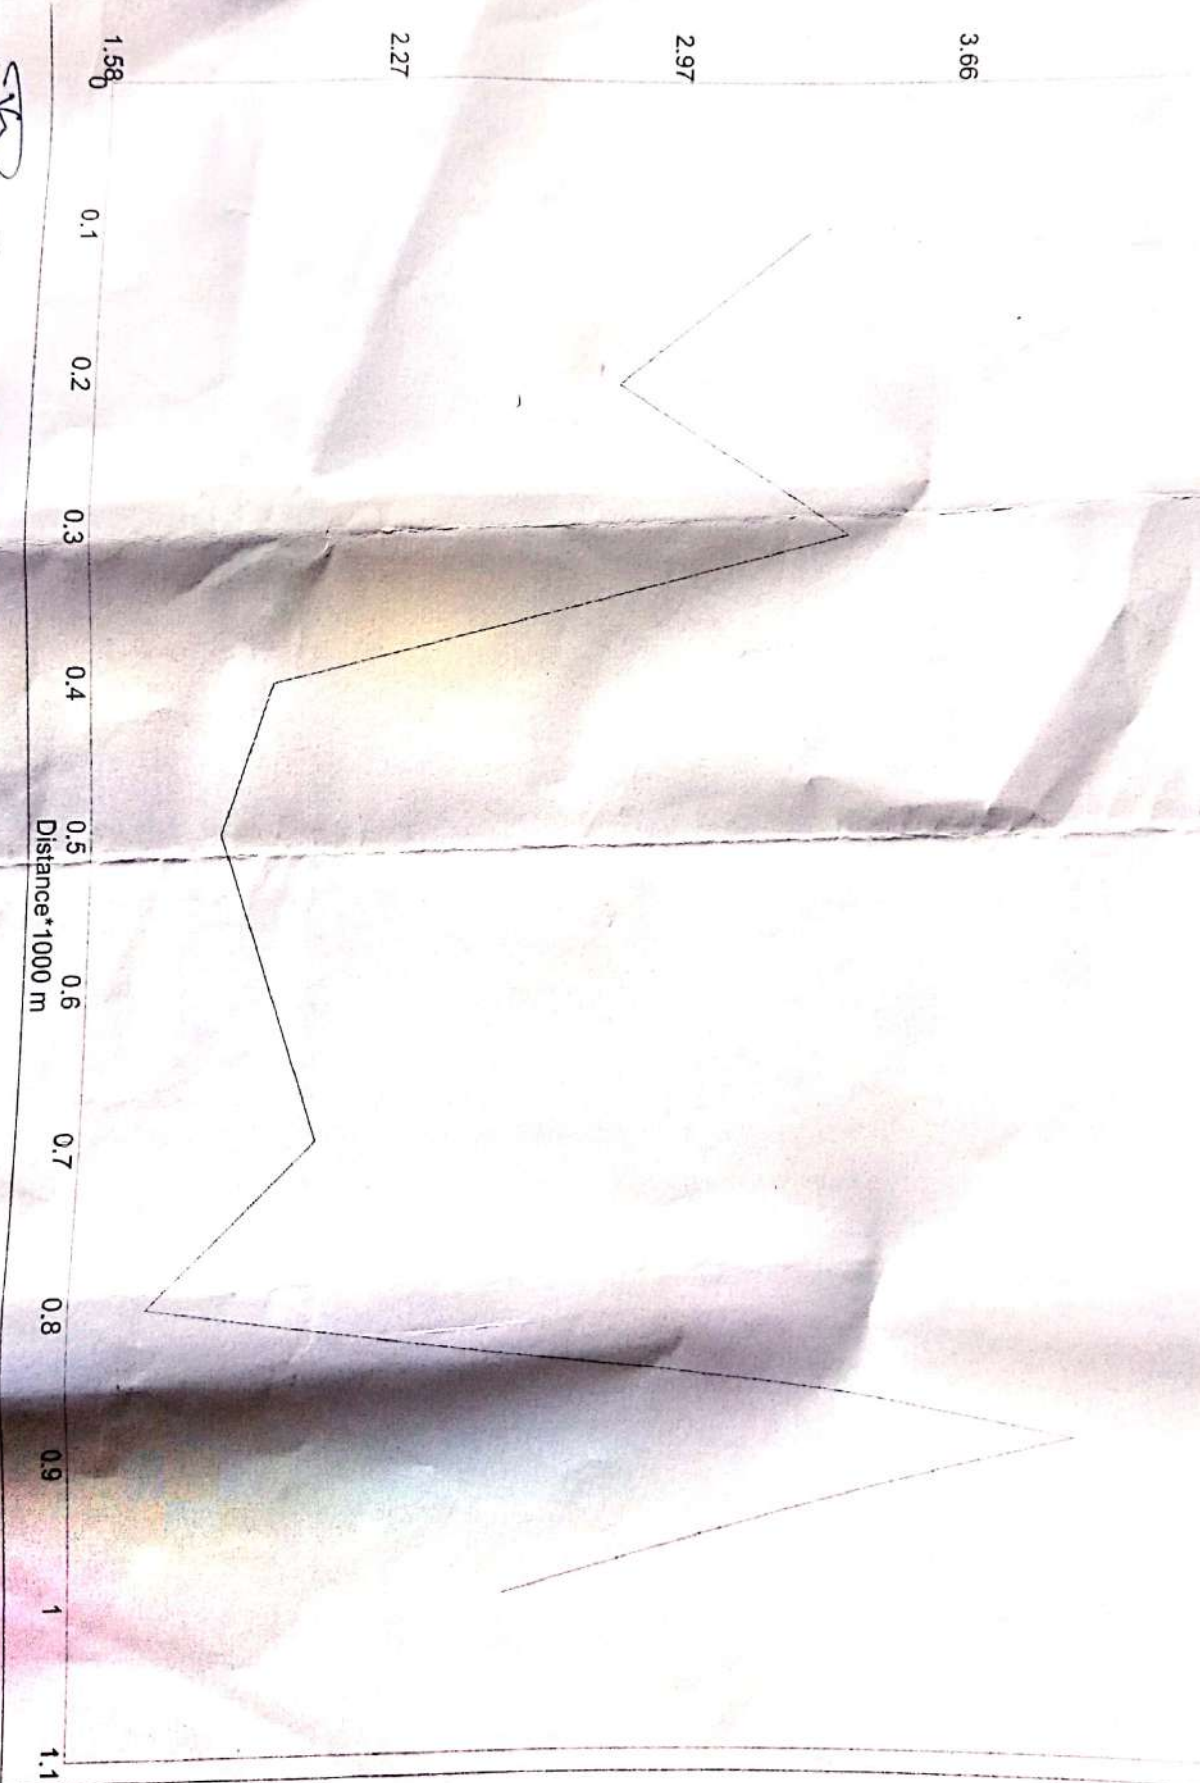

[Signature]
4.02.22
S.K.

[Signature]
S.K.

[Signature]
S.K.

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग , क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना - 800007

पत्रांक : 32/315

पटना /दिनांक : 19-01-2022

प्रेषक ,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना-7

सेवा में ,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल पाल्ना

विषय :- योजना / गैर योजना शीर्ष NR-3034 अंतर्गत निर्माणाधीन पथ/पुल/पुलिया कार्यों
में प्रयुक्त निर्माण सामग्रियों की गुणवत्ता के जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :- कार्यपालक अभियंता /सहायक अभियंता कार्य प्रमण्डल/कार्य अवर-प्रमण्डल पाल्ना
का पत्रांक 46(315) दिनांक 23/12/21

महाशय ,

उपर्युक्त बिषयक प्रासंगिक पत्र के संदर्भ में योजना / गैर योजना शीर्ष NR-3034 अंतर्गत
निर्माणाधीन पथ/पुल/पुलिया कार्यों में प्रयुक्त निर्माण सामग्रियों के गुणवत्ता जाँचफल प्रतिवेदन आवश्यक
कारवाई हेतु भेजी जाती है जो निम्नवत है:-

क्रम संख्या	पथ/पुल/पुलिया का नाम	जाँच का प्रकार
1.	Saidabad Masjid to Sarda Chapra	Stone chips (13.2mm to 9mm) sore chips Bitumen content for sore
2.		

अनु० :- यथोक्त

विश्वासभाजन

19/01/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग

क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना-7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Saidabadi Masjid to Sarda Chabra

Name of Scheme:- MR-3054

Name of Agency :- Sanjosh Kumar

Nature of sample : Mix seal (13.2mm to 0.075mm)

Date of Collection/Received :- 12/1/2022

Location :- 750M

Date of Test :- 19/1/22

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Patna

vide letter No. 46(243)dt. 23/12/21

Agreement No / Package No. : 05/0030/2020-21

Sl. No.	A.I.V.	
	Average Test Value	Required Value(Max)
1.		30%

Sl. No.	Sieve Size in (mm)	Weight of Sample Taken Kgs <u>19.365</u>				Required Value		Remarks
		Weight Retd.	% of Wt. Retained	% of Cum. Retained	% of Passing	Type A	Type B	
1	13.2	0.000	0.00	0.00	100	---	100	
2	11.2	0.881	4.55	4.55	95.45	100	88-100	
3	5.6	8.685	44.85	49.40	50.60	52-88	31-52	
4	2.8	5.380	27.80	77.20	22.80	14-38	5-25	
5	0.09	3.747	19.35	96.55	3.45	0-5	0-5	

Sanjosh Kumar
12/1/2022
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

Sanjosh Kumar
19/01/2022
A.E.
Regional Laboratory
R.W.D Guljarbagh
patna - 7

Sanjosh Kumar
19/01/22
E. E.
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

PHYSICAL AND GRADATION TEST OF COARSE AGGREGATE

Name of Project/Road :- Saidabad Masjid to Sarda Chapra

Name of Scheme :- MR-3554

Name of Agency :- Santosh Kumar

Nature of sample : Semi Dense Bituminous Concrete Date of Collection/Received :- 12/01/22

Location :- 750 m Date of Test :- 19/01/22

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division - Patiganj

vide letter No. 46(313) 27/12/21

Agreement No / Package No. : 05(MR80/2020-21)

Sl.No	A.I.V.	
	Average Test Value	Required Value(Max)
1.		30%

Sl. No	Sieve Size in (mm)	Weight of Sample Taken Kgs 18.760				Required Value	Remarks
		Weight Retd.	% of Wt. Retained	% of Cumm. Retained	% of Passing		
1	13.2	0.000	0.00	0.00	100	100	
2	9.5	0.854	4.55	4.55	95.45	90-100	
3	4.75	9.146	48.75	53.30	46.70	35-51	
4	2.36	2.645	14.10	67.40	32.60	24-39	
5	1.18	0.788	4.20	71.60	28.40	15-30	
6	0.300	2.073	11.05	82.65	17.35	9-19	
7	0.075	2.383	12.70	95.35	4.65	3-8	

Roy
L.A.
19/01/2022
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

19/01/2022
A.E.
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

19/01/22
E. E.
Regional Laboratory
R.W.D. Guljarbagh
patna - 7

Letter No. _____

Date ____/____/____

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULZARBAGH, PATNA - 7

Name of Project/Road :- Saidabad Masjid to Sarda chakraName of Scheme:- MR-3054Name of Agency :- Sardar SamraNature of sample :- Bitumen content for - S.D.B.CLocation :- 260 m/hrRef :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Patna Date of Collection/Received :- 12/11/22Agreement No / Package No. : 05/030/2022-24 Date of Test :- 14/12/22vide letter No. 19/12/22 Dt. 20/12/22

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	509.00	506.00	505.00	
2	Wt. of Dry chips after extraction (b)	483.48	480.30	479.65	
3	Percentage of bitumen (in the mix) [(a-b)*100/a] (%)	S.04	S.00	S.02	
4	Average % bitumen	S.01			

Regional Laboratory
R.W.D. Gulzarbagh patna - 7Ravi
19/11/22Regional Laboratory
R.W.D. Gulzarbagh patna - 7S.01
19/10/22
A.E.Regional Laboratory
R.W.D. Gulzarbagh patna - 719/10/22
19/10/22
E.E.

જિલ્લા એન્જિનીયરિંગ ઓફિસ

જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ
જિલ્લા એન્જિનીયરિંગ ઓફિસ

Ag. No. - 05MBD/MR-3054/2020-21

Measurement Book

Schedule XLY-Form No. 134

EXECUTIVE ENGINEER

પાલિગાંધી

DIVISION

બાંધકામ

SUB-DIVISION

સાંચી - ૨૫૧ સ્થાનિક કુમાર

M.B. NO. 624

જિલ્લા એન્જિનીયરિંગ ઓફિસ

Abstract of cost
Est on A/c Bill

1/1

clearing & grubbing

Road land do-do

0.198 Hec chn No-1 P-01

@ 51161.75/Hec $\rightarrow$ 10,130 = 00

2/2

scarifying existing

Bituminous surface

129.05 m² chn No-2 P-02

@ 15.43/m² $\rightarrow$ 1,991 = 00


12,121 = 00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
3/5 Pro/laying, spreading & compacting stone aggregate to W.B.M.G-2					
25.28 m ³ item No - 3 P-02					
@ 3730.10/m ² B					94,297=00
4/5 Pro/lay/spreading & compacting W.B.M.G-3					
59.31 m ³ item No - 4 P-3					
@ 3455.86/m ³ B					204,967=00
5/6 Pro/laying & applying Primer coat with Bitumen emulsion					
SS, do-do					
790.80 m ² item No - 5 P-4					
@ 44.57/m ² B					35,246=00
6/7 Pro/laying Tack coat with Bitumen emulsion					
RS, do-do					
889.90 m ² item No - 6 P-5					
@ 15.16/m ² B					13,491=00
7/9 M.S.B					
Pro/laying & rolling of 20mm M.S.B do do					
889.90 m ² item No - 7 P-6					
@ 204.51 B					181,993=00
					542,115=00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
8/9	Pro/applying Tack coat with B/emulsion PS				
	3676.39 M ² ch No-9 P-7				
	@ 12.56/m ² B				46,175=00
9/10	SDR				
	Pro/laying semi dense bituminous concrete				
	do do				
	91.91 M ³ ch No-10 P-8				
	@ 10132.11/m ³ A				936,757=00
10/9	Pro/applying finishing of raised structure				

Asy Sign Board					
With Logo do do					
2 No ch No-8 P-7					
@ 9202.99 each A					18,406=00
					15,43,453=00
Add 12.0% G.S.T					185,214=00
Add 1% Labour cess					15,439=00
Add 10% Signage					
Free of 10% of 62970.00					6,297=00
					17,50,398=00
Less 1% Below Prag					17,504=00
					17,32,894=00
 21/2/2022  24/02/2021 A.S.					

Continuation

Scanned with CamScanner
