

**कार्यपालक अभियंता का कार्यालय**  
**ग्रामीण कार्य विभाग, कार्य प्रमंडल, उदाकिशुनगंज**  
पत्रांक.....1200.....उदाकिशुनगंज, दिनांक.....10/08/.....2021

प्रेषक,

कार्यपालक अभियंता,  
ग्रामीण कार्य विभाग,  
कार्य प्रमंडल— उदाकिशुनगंज ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी —सह— सचिव,  
ग्रामीण कार्य विभाग,  
बिहार, पटना।

**विषय :-** MR New maintenance Policy 2018 योजना से संबंधित कार्यों के भुगतान हेतु आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त बिषयक संबंध में कहना है, कि ग्रामीण कार्य विभाग, कार्य प्रमंडल उदाकिशुनगंज में MR New maintenance Policy 2018 योजना के अंतर्गत चल रहे कार्यों के भुगतान हेतु विहित प्रपत्र में अधियाचना पत्र तैयार कर समर्पित किया जाता है।

अतः अनुरोध है, कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय, ताकि संवेदक को भुगतान किया जा सके।

अनु०:- यथोक्त विहित प्रपत्र में।

विश्वासभाजन

  
कार्यपालक अभियंता,  
ग्रामीण कार्य विभाग,  
कार्य प्रमंडल उदाकिशुनगंज।

**FORM GFR 19-A**

Letter No- 1200 Date- 10/08/21

(See Government of India's Decision (1) below Rule-150)

Form of Utilisation Certificate up to January .2022

MR New Maintenance Policy 2018

Executive Engineer Rural Works Department Works Division Udakishunganj


| Sl No | Name of Scheme                 | Sanction No.& Date with Amount (in Rs. Lacs)                        | Amount Received (in Rs. lac) | particulars                                                                                                                                                                                                                                                                                                                            |
|-------|--------------------------------|---------------------------------------------------------------------|------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 1     | MR New Maintenance Policy 2018 | Authorisation Letter No.-08 Dated 29.01.2022 Amount- 638.10253 Lacs | 638.10253                    | Certified that Rs:- 638.10253 Lac received Till the date in favour of Executive Engineer, RWD Work Division Udakishunganj. A sum of Rs.638.10253 Lac has been utilized for the purpose of MR New maintenance Policy 2018 Scheme as given in the margin for which it was sanctioned and that the balance of Rs.0.00000 Lacs remaining . |
| TOTAL |                                |                                                                     | 638.10253                    |                                                                                                                                                                                                                                                                                                                                        |

2. Certified that I have satisfied myself that conditions on which the grants in -aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned. kind of checks exercised:-

- (i) Works have been supervised by Executive Engineer
- (ii) periodical inspection has been conducted by Executive Engineer
- (iii) construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer,
- (v) All other codal formalities have been observed.

3. Physical progress achieved: as per progress report.

  
DAO  
Rural Works Department  
Works Division Udakishunganj

  
Executive Engineer  
Rural Works Department  
Works Division Udakishunganj

Name of Division : Udakishunganj

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

| Sl.No | Package no.       | Name of Road                                  | Project ID as per MIS | Administrative Approval (AA) Letter No. & Date | Administrative Approval (AA) |                 | Agreement Amount (in Lac)                           |                                      | Agreement No. & Date           | Date of Completion as per Agreement | Actual Date of Completion | Value of RRI (in mm/km) | Thickness of Bitumen Layer (in mm) | Value of Bitumen Content in percentage | Previous Total Allocated Amount (Lac) | up to date expenditure as per MIS (in Lac) | Requisition Against work done (in lac) | Remarks                                                            |
|-------|-------------------|-----------------------------------------------|-----------------------|------------------------------------------------|------------------------------|-----------------|-----------------------------------------------------|--------------------------------------|--------------------------------|-------------------------------------|---------------------------|-------------------------|------------------------------------|----------------------------------------|---------------------------------------|--------------------------------------------|----------------------------------------|--------------------------------------------------------------------|
|       |                   |                                               |                       |                                                | Length (In Km)               | Amount (in Lac) | Initial Rectification with Surface Renewal (in lac) | 5 years Routine Maintenance (in lac) |                                |                                     |                           |                         |                                    |                                        |                                       |                                            |                                        |                                                                    |
| 1     | RM/MA/UDA/20/0004 | kalasan bazar to polytechnic college- Dhuriya | 210481032932          | 1343/ 20.05.2021                               | 1.950                        | 72.67300        | 42.72300                                            | 24.24596                             | 44 MBD/2020-21 Dt:- 09.06.2020 | 08.03.2021                          | 06.08.2021                | 2557                    | 25mm                               | 5%                                     | 0                                     | 0                                          | 20.83567                               | Only 0.900 K.M Constructed Rest length constructed by other scheme |
|       |                   |                                               |                       |                                                |                              |                 |                                                     |                                      |                                |                                     |                           |                         |                                    |                                        |                                       |                                            | 20.83567                               |                                                                    |

D.A.O  
RWD Works Division  
Udakishunganj

08/09/21

Executive Engineer  
RWD Works Division  
Udakishunganj

08/09/21

Name of Customer : Kunchan Kumari  
Name of Work/ Road : azar polytechnic college dhuriya  
Lab Job number :  
Date : 01-Aug-21  
Section No. : 78

Test Date : 01-Aug-21  
Machine No : 434  
Start S No :  
Start E No :  
Weather :  
Start Location : kalasan bazar  
End Location : Dhuriya  
Road Name : azar polytechnic college dhuriya  
Road Type : (R) RURAL ROAD  
Side : 1  
Interval :  
UIV Range : 1148 To 4000 1000 mm/km  
Dist Range : 0 To 1 0.1 \* 1000 m  
Equation :  $Y = 0 * X^2 + 0.920 * X + 216.7$

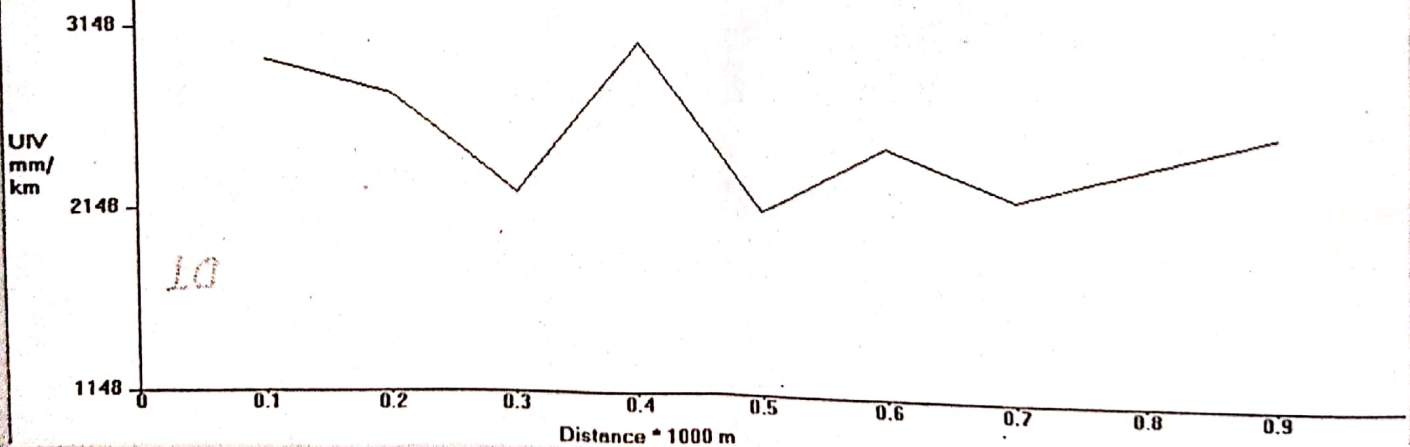
Print

Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BRRDA64\Desktop\01081340.Xls, Section No. : 78, Eqn :  $Y = 0 * X^2 + 0.920 * X + 216.7$   
Name of Customer : Kunchan Kumari, Name of Work/ Road : kalasan Bazar polytechnic college dhuriya, Lab Job



AK  
01/8/2021  
AE

2021/08/01

| Date   | Time     | Section No. | Length in km | Bumps in mm | Speed Rate | OR mm/km | IRI mm/km | TEGORY ROAD | Latitude | Longitude | Event         |
|--------|----------|-------------|--------------|-------------|------------|----------|-----------|-------------|----------|-----------|---------------|
| 1/8/21 | 13:35:39 | 78          | 0.1          | 300         | 10.1       | 3000     | 2976 G    |             | 25.57363 | 87.36902  | Normal        |
| 1/8/21 | 13:36:0  | 78          | 0.1          | 280         | 20.2       | 2700     | 2792 G    |             | 25.57403 | 87.35992  | Normal        |
| 1/8/21 | 13:36:0  | 78          | 0.1          | 220         | 10.1       | 2200     | 2240 G    |             | 25.57443 | 87.3508   | Normal        |
| 1/8/21 | 13:36:36 | 78          | 0.1          | 310         | 20.2       | 3100     | 3068 G    |             | 25.5748  | 87.34192  | Speed Breaker |
| 1/8/21 | 13:38:0  | 78          | 0.1          | 210         | 0          | 2100     | 2148 G    |             | 25.57512 | 87.33265  | Normal        |
| 1/8/21 | 13:38:35 | 78          | 0.1          | 250         | 10.1       | 2500     | 2516 G    |             | 25.57446 | 87.3281   | Normal        |
| 1/8/21 | 13:38:35 | 78          | 0.1          | 220         | 20.2       | 2200     | 2240 G    |             | 25.57367 | 87.3234   | Speed Breaker |
| 1/8/21 | 13:39:11 | 78          | 0.1          | 240         | 10.1       | 2400     | 2424 G    |             | 25.5729  | 87.318    | Normal        |
| 1/8/21 | 13:39:14 | 78          | 0.1          | 260         | 10.1       | 2600     | 2608 G    |             | 25.5729  | 87.318    | Normal        |

*Handwritten signature and initials*

$$Y = 0 * X^2 + 0.920 * X + 216.7$$

$$X = 6900$$

$$Y = 6564$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

1st and Final Bill

4-1

Name of Work-  
 Situation of Work-  
 Agency by which work is executed-  
 Date of Measurement-  
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

| Particulars                   | Details of actual measurement |                     |      |    | Contents of area      |
|-------------------------------|-------------------------------|---------------------|------|----|-----------------------|
|                               | No.                           | L.                  | B.   | D. |                       |
| Name of Road :                |                               | Kala San            |      |    |                       |
|                               |                               | Bazar to            |      |    |                       |
|                               |                               | Polytechnic         |      |    |                       |
|                               |                               | College, Dhurva     |      |    |                       |
| Scheme                        |                               | : MP 3054           |      |    |                       |
| Agency :                      |                               | Kandam Kumari       |      |    |                       |
|                               |                               | Ward No-0, High     |      |    |                       |
|                               |                               | School Road         |      |    |                       |
|                               |                               | Bhadrachari         |      |    |                       |
|                               |                               | Dist. Machilipatnam |      |    |                       |
| Agreement No.                 |                               | 44 MB/2020-21       |      |    |                       |
| Package No                    |                               | : MP-4/19-22        |      |    |                       |
|                               |                               | Wakishemgaraj/07    |      |    |                       |
| Date of Start                 |                               | 6-06-2020           |      |    |                       |
| Date of Comp                  |                               | 08-03-2021          |      |    |                       |
| ① clearing and grubbing       |                               |                     |      |    |                       |
| Road Land Including uprooting |                               |                     |      |    |                       |
| ing                           |                               |                     |      |    | 4/1                   |
| del<br>Bx                     | 2x                            | 10x30.00x           | 1.00 | =  | 600.00m <sup>2</sup>  |
|                               | 2x                            | 10x30.00x           | 1.00 | =  | 600.00m <sup>2</sup>  |
|                               | 2x                            | 10x30.00x           | 1.00 | =  | 600.00m <sup>2</sup>  |
|                               |                               |                     |      |    | 1800.00m <sup>2</sup> |
|                               |                               |                     |      |    | 0.180 Hec.            |

Continuation

4-1  
 20/12/21  
 50

2  
Sch. XLV-Form No. 134

| Particulars                                          | Details of actual measurement |       |       |    | Contents of area      |
|------------------------------------------------------|-------------------------------|-------|-------|----|-----------------------|
|                                                      | No.                           | L.    | B.    | D. |                       |
| ② uncrumpled<br>well coated material                 |                               |       |       |    |                       |
|                                                      | 2x5                           | 20x   | 1.30  | =  | 13.52 m <sup>2</sup>  |
|                                                      | 1x                            | 5.80x | 1.40  | =  | 7.67 m <sup>2</sup>   |
|                                                      | 2x                            | 5.50x | 1.40  | =  | 15.40 m <sup>2</sup>  |
|                                                      | 4x                            | 4.30x | 1.20  | =  | 20.64 m <sup>2</sup>  |
|                                                      | 3x                            | 4.70x | 1.20  | =  | 16.92 m <sup>2</sup>  |
|                                                      | 4x                            | 5.20x | 1.40  | =  | 29.12 m <sup>2</sup>  |
|                                                      | 5x                            | 4.20x | 1.00  | =  | 21.00 m <sup>2</sup>  |
|                                                      | 4x                            | 4.40x | 1.20  | =  | 22.56 m <sup>2</sup>  |
|                                                      |                               |       |       |    | 146.83 m <sup>2</sup> |
|                                                      | 146.83 m <sup>2</sup>         |       | 0.150 | =  | 22.02 m <sup>3</sup>  |
| ③ water Bound Macadam<br>with stone screening WBM-II |                               |       |       |    |                       |
|                                                      | 2x                            | 5.70x | 1.40  | =  | 15.96 m <sup>2</sup>  |
|                                                      | 1x                            | 6.40x | 1.50  | =  | 9.60 m <sup>2</sup>   |
|                                                      | 2x                            | 6.10x | 1.50  | =  | 18.30 m <sup>2</sup>  |
|                                                      | 4x                            | 4.70x | 1.30  | =  | 24.44 m <sup>2</sup>  |
|                                                      | 3x                            | 5.20x | 1.30  | =  | 20.28 m <sup>2</sup>  |
|                                                      | 4x                            | 5.70x | 1.50  | =  | 34.20 m <sup>2</sup>  |
|                                                      | 5x                            | 4.60x | 1.10  | =  | 25.30 m <sup>2</sup>  |
|                                                      | 4x                            | 5.20x | 1.30  | =  | 27.04 m <sup>2</sup>  |
|                                                      |                               |       |       |    | 175.12 m <sup>2</sup> |
| Net Quantity of WBM-II                               |                               |       |       |    |                       |
|                                                      | 175.12 m <sup>2</sup>         |       | 0.075 | =  | 13.134 m <sup>3</sup> |

Continuation

Jy  
24/07/21  
SD

AE  
24/07/2021  
AE

3  
Sch. XLV-Form No. 134

| Particulars                    | Details of actual measurement |      |        |    | Contents of area      |
|--------------------------------|-------------------------------|------|--------|----|-----------------------|
|                                | No.                           | L.   | B.     | D. |                       |
| ④ WBM Urching - 1: providing   |                               |      |        |    |                       |
| Leaving spreading and compa-   |                               |      |        |    |                       |
| ring stone aggregate - 4/1     |                               |      |        |    |                       |
|                                | 2x                            | 7.10 | x 1.80 | =  | 25.56 m <sup>2</sup>  |
|                                | 3x                            | 8.00 | x 1.90 | =  | 45.60 m <sup>2</sup>  |
|                                | 2x                            | 7.60 | x 1.90 | =  | 28.88 m <sup>2</sup>  |
|                                | 4x                            | 5.90 | x 1.60 | =  | 37.76 m <sup>2</sup>  |
|                                | 3x                            | 6.50 | x 1.60 | =  | 31.20 m <sup>2</sup>  |
|                                | 4x                            | 7.10 | x 1.90 | =  | 53.96 m <sup>2</sup>  |
|                                | 5x                            | 5.80 | x 1.40 | =  | 40.60 m <sup>2</sup>  |
|                                | 4x                            | 6.50 | x 1.60 | =  | 41.60 m <sup>2</sup>  |
|                                |                               |      |        |    | 305.16 m <sup>2</sup> |
| Net quantity WBM Urch :        |                               |      |        |    |                       |
|                                | 305.16                        | x    | 0.075  | =  | 22.88 m <sup>3</sup>  |
|                                |                               |      |        |    |                       |
| ⑤ Prime Coat : providing and   |                               |      |        |    |                       |
| applying prime coat with mini- |                               |      |        |    |                       |
| men emulsion (SS-1) - - - 1/1  |                               |      |        |    |                       |
| Same quantity as item ④        |                               |      |        |    |                       |
| ④                              |                               |      |        | =  | 305.16 m <sup>2</sup> |
|                                |                               |      |        |    |                       |
| ⑥ Patch work over WBM urch     |                               |      |        |    |                       |
| mix sand (Type B) (waste       |                               |      |        |    |                       |
| plastic) surface for diff-     |                               |      |        |    |                       |
| minous and continuation of pr- |                               |      |        |    |                       |
| vement - - - - - 1/1           |                               |      |        |    |                       |

## Sch. XLV-Form No. 134

| Particulars                | Details of actual measurement |                            |    |    | Contents of area |
|----------------------------|-------------------------------|----------------------------|----|----|------------------|
|                            | No.                           | L.                         | B. | D. |                  |
| Qty as per Pot measurement |                               |                            |    |    | $= 305.16 m^2$   |
| Impcc portion              |                               |                            |    |    | +                |
|                            | 2                             | $10 \times 2.50$           |    |    | $= 75.00 m^2$    |
|                            |                               | $12 \times 8 \times 1.75$  |    |    | $= 168.00 m^2$   |
|                            |                               | $11 \times 10 \times 0.75$ |    |    | $= 82.50 m^2$    |
|                            |                               | $2 \times 5 \times 1.20$   |    |    | $= 12.00 m^2$    |
|                            |                               |                            |    |    | $337.50 m^2$     |
| Net Area                   |                               |                            |    |    | $642.66 m^2$     |

⑦ Tack Coat: Providing  
and applying tack coat

|                       |    |                                   |  |  |                 |
|-----------------------|----|-----------------------------------|--|--|-----------------|
| with bitumen emulsion |    |                                   |  |  |                 |
| using emulsion        |    |                                   |  |  |                 |
|                       | 10 | $16.00 \times 8.50$               |  |  | $= 120.00 m^2$  |
|                       |    | $\frac{8.50 + 3.75}{2}$           |  |  | $= 60.00 m^2$   |
|                       | 2  | $30.00 \times 3.75$               |  |  | $= 225.00 m^2$  |
|                       | 1  | $15 \times \frac{3.75 + 5.00}{2}$ |  |  | $= 73.125 m^2$  |
|                       | 1  | $20 \times \frac{6.00 + 3.75}{2}$ |  |  | $= 97.50 m^2$   |
|                       | 5  | $30 \times 3.75$                  |  |  | $= 562.50 m^2$  |
|                       | 10 | $30 \times 3.75$                  |  |  | $= 1125.00 m^2$ |
|                       | 1  | $15 \times \frac{6.00 + 3.75}{2}$ |  |  | $= 73.125 m^2$  |
|                       | 1  | $15 \times \frac{3.75 + 6.00}{2}$ |  |  | $= 73.125 m^2$  |
|                       | 10 | $30 \times 3.75$                  |  |  | $= 1125.00 m^2$ |
|                       | 1  | $10 \times 3.75$                  |  |  | $= 37.50 m^2$   |

Continuation

 $3570.075 m^2$ 

By  
30/07/21  
JE

| Particulars                                                       | Details of actual measurement |    |    |    | Contents of area            |
|-------------------------------------------------------------------|-------------------------------|----|----|----|-----------------------------|
|                                                                   | No.                           | L. | B. | D. |                             |
| ⑧ Semi-dense bituminous concrete providing out layer SBC. --- e/I |                               |    |    |    |                             |
| 1 x 18.00 x $\frac{16.50+9.00}{2}$ x 0.025                        |                               |    |    |    | = 5.757 m <sup>3</sup>      |
| 1 x 12.00 x $\frac{9.00+6.00}{2}$ x 0.025                         |                               |    |    |    | = 2.250 m <sup>3</sup>      |
| 1 x 10 x $\frac{6.00+3.75}{2}$ x 0.025                            |                               |    |    |    | = 1.218 m <sup>3</sup>      |
| 2 x 30 x 3.75 x 0.025                                             |                               |    |    |    | = 5.625 m <sup>3</sup>      |
| 1 x 10 x $\frac{3.75+6.50}{2}$ x 0.025                            |                               |    |    |    | = 1.281 m <sup>3</sup>      |
| 1 x 10 x $\frac{6.50+3.75}{2}$ x 0.025                            |                               |    |    |    | = 1.281 m <sup>3</sup>      |
| 10 x 30.00 x 3.75 x 0.025                                         |                               |    |    |    | = 28.125 m <sup>3</sup>     |
| 10 x 30.00 x 3.75 x 0.025                                         |                               |    |    |    | = 28.125 m <sup>3</sup>     |
| 6 x 30.00 x 3.75 x 0.025                                          |                               |    |    |    | = 11.875 m <sup>3</sup>     |
|                                                                   |                               |    |    |    | <u>90.517 m<sup>3</sup></u> |
| <u>10/08/2021</u>                                                 |                               |    |    |    |                             |
| ⑨ Construction of Subgrade and Rebar shoulders. e/I               |                               |    |    |    |                             |
| BT Portion                                                        |                               |    |    |    |                             |
| 2 x 10 x 30.00 x 1 x 0.60                                         |                               |    |    |    | = 360.00 m <sup>3</sup>     |
| 2 x 20 x 30.00 x 0.50 x 0.300                                     |                               |    |    |    | = 180.00 m <sup>3</sup>     |
|                                                                   |                               |    |    |    | <u>540.00 m<sup>3</sup></u> |
| <u>10/08/2021</u>                                                 |                               |    |    |    |                             |
| ⑩ Kilometer Stone, RCC                                            |                               |    |    |    |                             |
| M15 Gate Kilometer Local                                          |                               |    |    |    |                             |
| Stone --- --- --- e/I                                             |                               |    |    |    |                             |
| ① Km stone                                                        |                               |    |    |    | 2 Nos                       |
| Continuation                                                      |                               |    |    |    |                             |
| ① 200 m stone                                                     |                               |    |    |    | 4 Nos                       |

Sch. XLV-Form No. 134

6

| Particulars                                                                                                     | Details of actual measurement |     |     |     | Contents of work  |
|-----------------------------------------------------------------------------------------------------------------|-------------------------------|-----|-----|-----|-------------------|
|                                                                                                                 | No.                           | L.  | B.  | D.  |                   |
| (1) Retro-reflectorised traffic signs                                                                           | -                             | -   | -   | -   | cf                |
| (i) 600mm equilateral triangle                                                                                  |                               |     |     | =   | 60 NOS            |
| (ii) 600mm circular                                                                                             |                               |     |     | =   | 10 NOS            |
| (iii) 600mm x 450mm rectangular                                                                                 |                               |     |     | =   | 05 NOS            |
| (iv) 900mm side octagon                                                                                         |                               |     |     | =   | 03 NOS            |
| (12) Boundary Pillor/ward post                                                                                  |                               |     |     |     |                   |
| (13) Printing new letters and figures of any size                                                               |                               |     |     |     | 56 NOS            |
| ---                                                                                                             | ---                           | --- | --- | --- | 8/2               |
| 44.00 x 1.50                                                                                                    |                               |     |     | =   | 44.00             |
| (14) Road Marking with hot applied thermoplastic Compound with reflectorising white beads on bituminous surface |                               |     |     |     |                   |
| 2x 300 cm x 1.00                                                                                                |                               |     |     | =   | 180m <sup>2</sup> |
| Pedestrian Crossing                                                                                             |                               |     |     |     |                   |
| 6x 2.00 x 0.50 x 2                                                                                              |                               |     |     | =   | 12.00             |
| (15) Providing and fixing 'Logo of Maintained Project'                                                          |                               |     |     |     |                   |
| ---                                                                                                             | ---                           | --- | --- | --- | cf                |

Continuation

2 NOS

By  
06/08/21  
JB

AE = 2 NOS  
6/8/2021  
AE

Continuation

8  
Sch. XLV-Form No. 134

| Particulars                                              | Details of actual measurement |    |    |    | Contents of area |
|----------------------------------------------------------|-------------------------------|----|----|----|------------------|
|                                                          | No.                           | L. | B. | D. |                  |
| (1/1) Clearing & grubbing<br>Road Land - - - - - 1/5     |                               |    |    |    |                  |
| Qty. vid. TMB P-1                                        |                               |    |    |    |                  |
| 0.18 Hec @ RS 51133.75 = RS                              |                               |    |    |    | 9204.07          |
| (2/3) VSB for working-II Matedy.                         |                               |    |    |    |                  |
| Qty. vid. TMB P-2                                        |                               |    |    |    |                  |
| 22.02 m <sup>3</sup> @ RS 1858.45 = RS                   |                               |    |    |    | 40923.06         |
| (3/4) Water Boundary caton<br>with stone screening wr-II |                               |    |    |    |                  |
| Qty. Vid. TMB P-2                                        |                               |    |    |    |                  |
| 13.134 m <sup>3</sup> @ RS 3352.34 = RS                  |                               |    |    |    | 44029.65         |
| (4/5) Labor wr-II - - - - - 1/5                          |                               |    |    |    |                  |
| Qty. vid. TMB P-2                                        |                               |    |    |    |                  |
| 22.88 m <sup>3</sup> @ RS 3007.64 = RS                   |                               |    |    |    | 68814.80         |
| (5/6) Prime Coat - - - - - 1/5                           |                               |    |    |    |                  |
| Qty. vid. TMB P-3                                        |                               |    |    |    |                  |
| 305.14 m <sup>2</sup> @ RS 44.97 = RS                    |                               |    |    |    | 13723.04         |
| (6/7) Patchwork over WBM using<br>mix Seal - - - - - 1/5 |                               |    |    |    |                  |
| Qty. vid. TMB P-4                                        |                               |    |    |    |                  |
| 642.56 m <sup>2</sup> @ 196.45 = RS                      |                               |    |    |    | 126250.55        |
| (7/8) Tree Coat                                          |                               |    |    |    |                  |
| Qty. vid. TMB P-4                                        |                               |    |    |    |                  |
| 3570.075 m <sup>2</sup> @ RS 15.29 =                     |                               |    |    |    | 54586.74         |
| (8/9) SDB - - - - - 1/5                                  |                               |    |    |    |                  |
| Qty. vid. TMB P-5                                        |                               |    |    |    |                  |

Continuation

90.517 m<sup>3</sup> @ RS 10015.46 = RS 906569.30

RS 1264100.98

| Particulars                                                     | Details of actual measurement |    |    |    | Contents of area |
|-----------------------------------------------------------------|-------------------------------|----|----|----|------------------|
|                                                                 | No.                           | L. | B. | D. |                  |
| (9/2) Construction of Subgate<br>and Right hand Shoulder -- 9/1 |                               |    |    |    |                  |
| Qty. via TMB P-5                                                |                               |    |    |    |                  |
| 540. comp @ RS 187.61 = RS                                      |                               |    |    |    | 101303.40        |
| (10/10) Reinforced concrete<br>Concrete 115 gmt. kilometre      |                               |    |    |    |                  |
| Qty. via TMB P-5                                                |                               |    |    |    |                  |
| (i) Km stone                                                    |                               |    |    |    |                  |
| 20 Nos @ RS 1997.58 = RS                                        |                               |    |    |    | 3995.16          |
| (ii) 200m stone                                                 |                               |    |    |    |                  |
| 04 Nos @ RS 5551.8 = RS                                         |                               |    |    |    | 2220.72          |
| (11/11) Retro-reflective<br>material 25m -- -- 9/1              |                               |    |    |    |                  |
| Qty. via TMB P-66                                               |                               |    |    |    |                  |
| (i) 600mm equilateral<br>triangle                               |                               |    |    |    |                  |
| 60 Nos @ RS 3532.64 = RS                                        |                               |    |    |    | 211961.4         |
| (ii) 600mm circular                                             |                               |    |    |    |                  |
| 10 Nos @ RS 3629.23 = RS                                        |                               |    |    |    | 36292.30         |
| (iii) 600mm x 450mm rectangular                                 |                               |    |    |    |                  |
| 05 Nos @ RS 3500.11 = RS                                        |                               |    |    |    | 17500.55         |
| (iv) 900mm side octagon                                         |                               |    |    |    |                  |
| 03 Nos @ RS 7492.90 = RS                                        |                               |    |    |    | 22478.70         |
| (12/12) Boundary Pillar/Gravel post                             |                               |    |    |    |                  |
| Qty. via TMB P-6                                                |                               |    |    |    |                  |
| 36 Nos @ RS 467.07 = RS                                         |                               |    |    |    | 26155.92         |
| (13/13) Painting New Gutter and                                 |                               |    |    |    |                  |
| Figures -- Continuation -- 9/1                                  |                               |    |    |    |                  |
| Qty. via TMB P-5                                                |                               |    |    |    |                  |
| 44 m @ RS 52 = RS                                               |                               |    |    |    | 22.88            |
|                                                                 |                               |    |    |    | 1686038.01       |

Continuation
