

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

पत्रांक :- 05

/कटिहार, दिनांक-05-01-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, 3री मंजिल, भूमि विकास बैंक भवन,
बिहार, पटना।

विषय :- शीर्ष New Maintenance Policy-2018 योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:-यथोक्त।

विश्वासभंजन,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

ज्ञापांक:- 05

/कटिहार, दिनांक:-05-01-2022

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

RWD, Works Division, Katihar

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Katihar

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allocated Amount (in Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
1	MR-N/19-20 Katihar/05	NH-31 to Mahinathpur Chowk Bisharai	21105602047	1847/24.06.19	4.900	186.70190	122.32993	47.91139	11MBD/20-21, 01.09.2020	31.05.2021	28.08.2021	1865.65	25mm	5.1%	0.00000	0.00000	122.00920	Complete
2	MR-N/19-20 Katihar/05	Parmanandpur road to Parmanandpur	21105602051	1847/24.06.19	2.700	113.74180	74.93087	29.79264	11MBD/20-21, 01.09.2020	31.05.2021	27.08.2021	1954.63	25mm	5.1%	0.00000	0.00000	74.40443	Complete
3	MR-N/19-20 Katihar/09	Dumar Chowk To Bhangsha Via Chhohar	21105508073	5129/24.09.19	2.300	90.731	64.44034	23.20366	02MBD/20-21, 02.07.2020	01.04.2021	26.06.2021	2848.04	25mm	5.1%	47.58126	47.58126	16.84447	Complete
4	MR-N/19-20 Katihar/09	Construction of Road from State Highway to Khota Chowk via Malharia under Chandpur Paschim Panchayat Road	21105601018	5129/24.09.19	3.850	134.646	82.71322	38.94678	02MBD/20-21, 02.07.2020	01.04.2021	13.06.2021	1668.08	25mm	5.1%	80.71322	80.71322	1.04730	Complete
Total																128.29448	214.30540	

24/05/2022
Divisional Accounts Officer
RWD, Works Division, Katihar

Executive Engineer
RWD, Works Division, Katihar
24/05/2022

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of Jan, 2022

New Maintenance Policy-2018								
Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars				
1	New Maintenance Policy-2018	Lt. No.- 017 Dt.- 26.02.21	80.03702	Certified that out of Rs. 2179.99409 lacs received upto the year-2021-22 in favour of Ex. Engineer, RWD, Katihar a sum of Rs. 2106.90180 lacs has been utilized for the purpose of NMP-2018 rural roads Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 73.09229 lacs remaining unutilized at the end of the period under.				
		Lt. No.- 027 Dt.- 04.05.21	70.40501					
		Lt. No.- 040 Dt.- 14.06.21	368.10325					
		Lt. No.- 052 Dt.- 24.08.21	273.38928					
		Lt. No.- 058 Dt.- 27.10.21	161.36000					
		Lt. No.- 060 Dt.- 09.11.21	357.44478					
		Lt. No.- 064 Dt.- 06.12.21	765.74778					
		Lt. No.- 068 Dt.- 23.12.21	98.70000					
		Lt. No.- 001 Dt.- 03.01.22	4.80697					
			Total :-			2179.99409		

- Kind of Checks exercised :-**

- i. Works have been supervised by Executive Engineer/Superintending Engineer.
 - ii. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
 - iii. Construction materials have been tested.
 - iv. Measurements have been recorded in the MBs and test check conducted by the Assistant.
 - v. All other codal formalities have been observed.
3. Physical Progress achieved :-
 - i. Construction of Road Works.
 - ii. Construction of CD Works.
4. Certified that:-
 - i. Work has been done as per specification and with quality.
 - ii. Work done measurement entered in MB has been verified 100 % by JE, 50% by AE and 10% by EE.

Executive Engineer,
RWD Division, Katihar.

Lab Job number :36

Date :13-12-2021

Name of Customer :Parmanandpur road to Parmanandpur

Name of Work/ Road :Dhananajay Kumar Singh

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road category
1	0.100	3272	G
2	0.200	2109	G
3	0.300	1624	G
4	0.400	2206	G
5	0.500	2593	G
6	0.600	1528	G
7	0.700	1915	G
8	0.800	1915	G
9	0.900	1915	G
10	1.000	2206	G
11	1.100	2400	G
12	1.200	3078	G
13	1.300	2109	G
14	1.400	2109	G
15	1.500	1528	G
16	1.600	1721	G
17	1.700	1624	G
18	1.800	1624	G
19	1.900	1431	G
20	2.000	1624	G
21	2.100	1721	G
22	2.200	1915	G
23	2.300	1431	G
24	2.400	1528	G
25	2.500	1818	G
26	2.600	1528	G
27	2.700	2303	G
Average IRI Value		1954.63	

Signature
13/12/2021
J.E

Signature
13.12.2021
A.E

Signature
13/12/2021
Executive Engineer
R.W.D. (W) Division
Katihar

Lab Job number :36

Date :13-12-2021

Name of Customer :Parmanandpur road to Parmanandpur

Name of Work/ Road :Dhananjay Kumar Singh

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
13/12/21	8:40:19	36	0.1	330	0	3300	3272	G	25.66456	87.42700	Normal
13/12/21	8:40:54	36	0.1	210	20.2	2100	2109	G	25.66547	87.42709	Normal
13/12/21	8:41:0	36	0.1	160	20.2	1600	1624	G	25.66632	87.42694	Normal
13/12/21	8:41:0	36	0.1	220	20.2	2200	2206	G	25.66711	87.42646	Curve
13/12/21	8:41:29	36	0.1	260	20.2	2600	2593	G	25.66795	87.42652	Culvert
13/12/21	8:41:29	36	0.1	150	30.3	1500	1528	G	25.66886	87.42677	Normal
13/12/21	8:42:5	36	0.1	190	30.3	1900	1915	G	25.66970	87.42704	Normal
13/12/21	8:42:5	36	0.1	190	30.3	1900	1915	G	25.67062	87.42712	Culvert
13/12/21	8:42:5	36	0.1	190	30.3	1900	1915	G	25.67152	87.42714	Normal
13/12/21	8:42:5	36	0.1	220	20.2	2200	2206	G	25.67241	87.42739	Curve
13/12/21	8:43:0	36	0.1	240	10.1	2400	2400	G	25.67317	87.42786	Speed Breaker
13/12/21	8:43:15	36	0.1	310	10.1	3100	3078	G	25.67398	87.42825	Normal
13/12/21	8:43:50	36	0.1	210	20.2	2100	2109	G	25.67480	87.42864	Normal
13/12/21	8:44:0	36	0.1	210	20.2	2100	2109	G	25.67565	87.42902	Normal
13/12/21	8:44:26	36	0.1	150	20.2	1500	1528	G	25.67630	87.42966	Normal
13/12/21	8:44:26	36	0.1	170	30.3	1700	1721	G	25.67705	87.43015	Normal
13/12/21	8:44:26	36	0.1	160	30.3	1600	1624	G	25.67797	87.43054	Normal
13/12/21	8:45:1	36	0.1	160	30.3	1600	1624	G	25.67882	87.43091	Normal
13/12/21	8:45:1	36	0.1	140	30.3	1400	1431	G	25.67971	87.43099	Normal
13/12/21	8:45:1	36	0.1	160	30.3	1600	1624	G	25.68056	87.43103	Normal
13/12/21	8:45:1	36	0.1	170	30.3	1700	1721	G	25.68150	87.43104	Normal
13/12/21	8:45:36	36	0.1	190	30.3	1900	1915	G	25.68244	87.43099	Normal
13/12/21	8:45:36	36	0.1	140	30.3	1400	1431	G	25.68328	87.43082	Normal
13/12/21	8:46:0	36	0.1	150	30.3	1500	1528	G	25.68411	87.43037	Curve
13/12/21	8:46:12	36	0.1	180	30.3	1800	1818	G	25.68483	87.42978	Curve
13/12/21	8:46:12	36	0.1	150	30.3	1500	1528	G	25.68545	87.42909	Normal
13/12/21	8:46:47	36	0.1	230	10.1	2300	2303	G	25.68612	87.42800	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2300$$

$$Y = 2303$$

(R) RURAL ROAD

Good Average Poor


<4000 4001-5000 >5001

13/12/2021
13.12.2021

13.12.2021
A.E.

Executive Engineer
R.W.D. (W) Division
Kathihar

File : C:\RAM KUMAR\MISC Files\Bump integrator\Korha\Parmanandpur To Parmanandpur To Parmanandpur\13120847.Xls. Section
 Name of Customer : Parmanandpur road to Parmanandpur. Name of Work/ Road : Dhananajay Kumar Singh. Lab

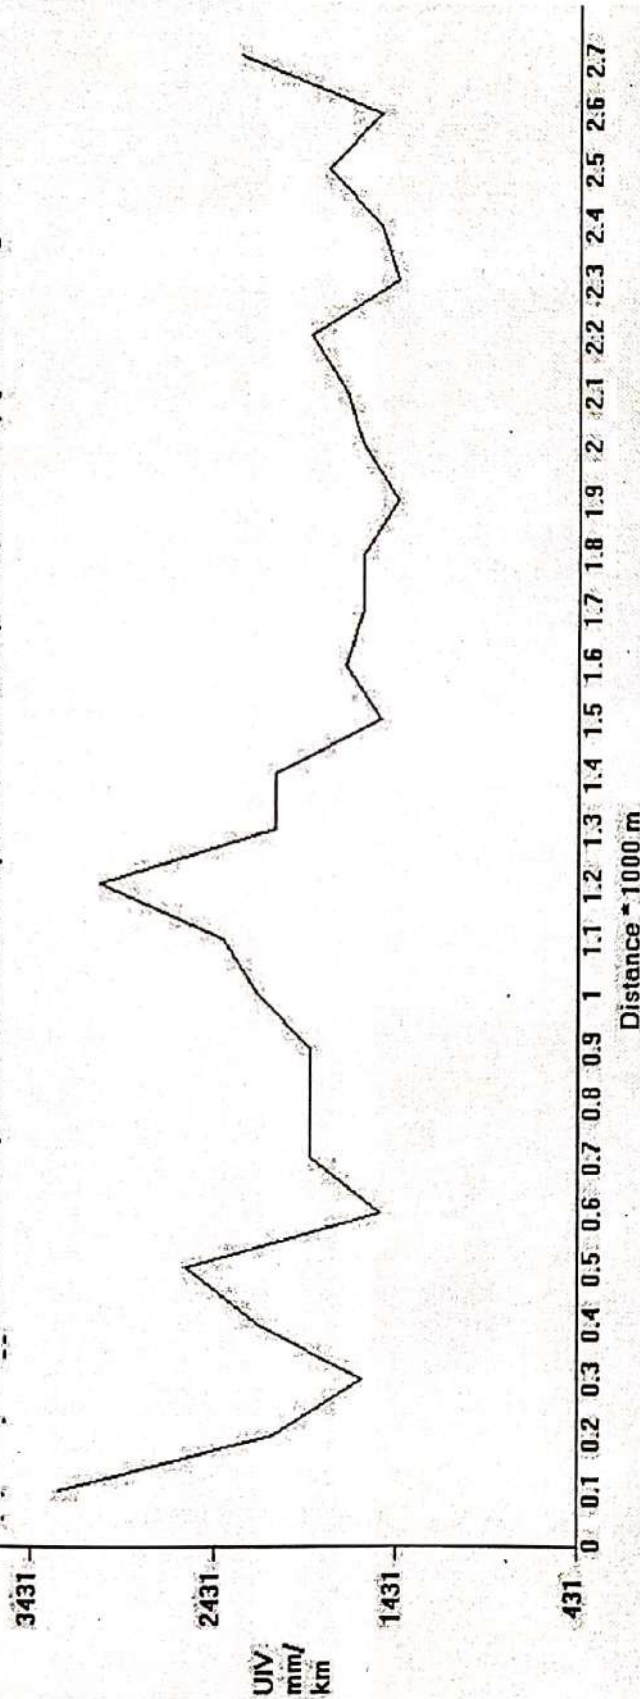

12/12/2021
 A. E.

13. 12. 2021
 A. E.

Signature
 Executive Engineer
 R.W.D. (W) Division
 Katihar

DHANANJAY KUMAR SINGH

MR-N/19-20 (3054)

Schedule XLV-Form No. 134

PARMANANDPUR ROAD TO PARMA-
NANDPUR.

R.W.D. KATHAR - DIVISION

KORHA - SUB-DIVISION

(NO - 2094)

MEASUREMENT BOOK

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					1st on A/c Bill
Name of work					Construction & Maintenance
					of Road from permanent pvt
					Road to permanent pvt
Name of Agency					Dhanangay for Singh
					AT Gharan Mirganj
					Dhamdha, Punjab
Agreement No.					11 MBP/2020-2021
Work order					11/09/2020
Work completion					31/05/2021
Abstract of cost					

					Information board
B/E/P 1-	Item NO 1 Qty	2.0 NOS			
	@ 9229.12 each				18458.24
2/1	cleaning and grading				
	road land d/c				
B/E/P 2-	Item NO 2 Qty	0.540 HRC			
	@ 49496.70/HRC				26728.00
3/22	Earth work in excavation				
	for foundation				
B/E/P 2-	Item NO 3 Qty	148.99 M ³			
	@ 260.59/M ³				38825.00
4/23	providing p/c M/S				
B/E/P 2-	Item NO 4 Qty	22.96 M ³			

Continuation
 @ 5009.91/H³ B 115029.00
 10199040.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			BFB	6526	891=00
2/12(i) providing and fixing 600mm circular					
B/F/P 21-17mm NOB & ty 14.0 NOS @ 3676.23 each BS					51467=00
3/12(ii) providing and fixing 600 X 450 mm					
B/F/P 21-17mm NOB & ty 8.0 NOS @ 3547.11 each BS					28377=00
4/12(iii) providing and fixing 900mm side octagon					
B/F/P 21-17mm NOB & ty 4.0 NOS @ 7539 each BS					30160=00
			Total BS	6636895	=00
Add 12% G.S.T (+)				796427	=00
Add 1% L.C.P.S.S (+)				66369	=00
			Total BS	7499691	=00
Less 0.79% below (-)				59248	=00
			Total BS	7440443	=00
(i) Work has been done as per specification.					
