

कार्यपालक अभियंता, ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दलसिंहसराय, समस्तीपुर

पत्रांक 2093 अ.उ.०

दलसिंहसराय/दिनांक 30/12/2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दलसिंहसराय

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
सचिव-सह-प्राधिकृत पदाधिकारी
ग्रामीण पथ विकास एजेंसी पटना ।

विषय-

New Maintenance Policy 2018(MR New) योजनान्तर्गत पथ में आवंटन
उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि **New Maintenance Policy 2018(MR New)** योजनान्तर्गत चल रहे पथ के निर्माणधीन कार्य के विरुद्ध चल रहे योजनाओं का भुगतान हेतु **Rs.-4.48398(Four Lakh Forty Eight Thousand Three Hundred Ninety Eight Rupees)** की आवश्यकता है। अधियाचना का निर्माण कार्य विशिष्टों के अनुरूप है तथा कार्य संतोषप्रद है।

अतः अनुरोध है कि अधियाचना पत्र के आधार पर आवंटन **Rs.-4.48398(Four Lakh Forty Eight Thousand Three Hundred Ninety Eight Rupees)** उपलब्ध कराने की कृपा की जाये।

- अनु०- 1) अधियाचना प्रपत्र।
2) 19 ए फ़ॉर्म।
3) IRI Report की छायाप्रति सलग्न।

विश्वनाथ झा

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दलसिंहसराय

Rural Works Department, Works Division Dalsinghsarai
Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018
(Initial Rectification and Surface Renewal)

Name of Division : PIU(Dalsinghsarai)

Sl No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allocated Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1		Bande Pokhar Se Patori AND Collage	10105105	2200 08.07.2019	4.90	106.93000	115.93343	38.16306	69 MBD/ 2019-20 17.12.2019	16.12.2020	26.06.20	3220	25mm	5.10%	110.98387	96.03189	4.48398	Work Completed
		2.55	53.96300		50.42741	19.74842	22.06.20	3669			25mm	5.10%	48.32788	46.65120	0	Work Completed		
2		NH-103 se Pursotampur	10105107															
3		Samastipur jila antargat morwa gram panchayt rajindawara ramlogan sahani ke ghar se kali ashan vai gango sahani ke gharhote kantu sahani ke chay dukan PMGSY sadak tak or kali ashan nandkishor mishar ke ghar hote hua shivchandar sah ke dukan PMGSY tak path nitman	32010403007		2.47	63.03400	56.68441	22.681220			30.06.20	3417	25mm	5.10%	56.47496	56.47496	0	Work Completed
TOTAL				9.92	223.92700	223.04525	80.59270					10306.00			215.78671	199.15805	4.48398	

Screened Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed

1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
2 Up-to date Physical Progress has been uploaded in MIS.

Divisional Account Officer
Rural Works Department,
Works Division Dalsinghsarai

Executive Engineer
Rural Works Department,
Works Division Dalsinghsarai

FORM GFR-19-A

(See Govt. of India's decision(i) below rule 150)
Form of Utilisation Certificate upto DECEMBER 2021

New Maintenance Policy 2018(MR New)

PIU:- RWD Works Division Dalsinghsarai

Sl No	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lakh)	Amount Received (in Lakh)	Particulars
1	2	3	4	5
1	New Maintenance Policy 2018 (MR New)	1694.53387	1694.53387	Certified that out of Rs-16.94.53387 Lakh received till date in favour of Executive Engineer, RWD Works Division Dalsinghsarai a Sum of Rs-1531.46712 Lakh has been utilized for the New Maintenance Policy 2018(MR New) Scheme as given in the margin for which it was Sanctioned and that the Balance of Rs-163.06675 Lakh remaining unutilized at the end of period under the time of completion
		1694.53387	1694.53387	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was

Kind of Checks Exercised:-

- (i) Workers have been supervised by Executive Engineer/ Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- (iii) Construction materials have been tested
- (iv) Measurements have been recorded in the MB's and test check conducted by the
- (v) All other codal formalities have observed

3. Physical Progress Achieved

- (i) Construction of Road Works
- (ii) Construction of CD Works




Sr.DAO

Rural Works Department,
Works Division Dalsinghsarai


Executive Engineer
Rural Works Department,
Works Division Dalsinghsarai

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल दलसिंहसराय
नयी अनुरक्षण नीति 2018 के अधियाचना हेतु प्रमाण पत्र

क्र० सं०	शर्त	अभियुक्ति
1	मापि पुस्त पर इस आशय का प्रमाण पत्र दर्ज है कि कार्य गुणवत्ता पूर्ण कराया गया है एवं विशिष्टियों के अनुरूप है ।	निर्माण कार्य गुणवत्ता पूर्ण कराया गया है एवं विशिष्टियों के अनुरूप है ।
2	कराये गए कार्यो के सभी अवयवो के अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन कनीय अभियंता, कम से कम 50 प्रतिशत मापी का सत्यापन सहायक अभियंता एवं कम से कम 10 प्रतिशत मापी का सत्यापन कार्यपालक अभियंता द्वारा किये जाने का प्रमाण पत्र को विभागीय MIS पर अपलोड जाय ।	कराये गए कार्यो के सभी अवयवो के अवयववार मापी का सत्यापन कनीय अभियंता, सहायक अभियंता एवं कार्यपालक अभियंता द्वारा किया गया है ।

 कनीय अभियंता ग्रामीण कार्य विभाग, कार्य प्रमंडल दलसिंहसराय	 सहायक अभियंता ग्रामीण कार्य विभाग, कार्य प्रमंडल दलसिंहसराय	 कार्यपालक अभियंता ग्रामीण कार्य विभाग, कार्य प्रमंडल दलसिंहसराय
---	---	--



बिहार BIHAR

AL 314601

6690
31/08/21 9:00 AM - 9:00 PM
मजदूर का न्यायिक प्रमाण पत्र, एन.जी.क्यू.ए.
समस्तीपुर

Sanjay Kumar Singh
Senior Treasury Officer
District Treasury, Samastipur

MR-3054

Supplementary Agreement

To The Original Agreement No- 69/ MBD/19-20

This Agreement is drawn as a Supplementary to the Original Agreement No. 69/ MBD/19-20, between Executive Engineer, R.W.D, Works Division, Dalsinghsarai, Samastipur and **ANJANI KUMAR**, Address:- Ward No-12, Kashipur, District- Samastipur. for carrying out supplementary items as sanctioned for the construction of the road from 1. Bande Pokhar to Patori And College :- 1971887.00

2. NH 103 se Pursotampur :- 223179.00

Total :- 2195066.00

approved by the S.E, RWD, Circle, Samastipur on Letter No-1577 dated 31.08.21 at a price of Rs. 21,95,066.00 (Twenty one lakh ninty five thousand sixty six rupees only) 10 % below of rate additional items, as sanctioned and approved.

And will be governed and guided by the terms and conditions and clauses of the Original agreement except that the revised bill of quantity including the supplementary items as sanctioned and post facto approval by the S.E, RWD, Circle Samastipur will form integral part for the execution of work under the Original as well as Supplementary Agreement.

Anjani Kumar.

16/09/21

16/9/21

कार्यवाहक अधिकारी
राज्यीय कार्य विभाग
समस्तीपुर
16/09/21

Revised BoQ
REPAIR OF ROAD FROM BANDE POKHAR TO PATORI AND COLLEGE UNDER MR-3054 Road

DIVISION : DALSINGH SARAI

BLOCK :

Morwa

LENGTH: 4.900 KM

SCHEDULE OF WORKS

Sl. No.	Description of work	No. or Qty.	Unit	Estimated Rate		AMOUNT Rs.
				Figure	Words	
1	Granular Sub-base with Well Graded Material (Table 400.1)(By mix in place method) For Grading II Material Construction of granular sub-base by providing well graded material, spreading in uniform layers with motor grader on prepared surface, mixing by mix in place method with rotavator at OMC, and compacting with smooth wheel roller to achieve the desired density, complete as per Technical Specification Clause 401.	283.490	Cum	1,934.23	#NAME?	548335.00
2	WBM Grading 2 (By Mechanical Means) Providing, laying, spreading and compacting stone aggregates of specific sizes to water bound macadam specification including spreading in uniform thickness, hand packing, rolling with three wheel 80-100 kN static roller in stages to proper grade and camber, applying and brooming, crushable screening to fill-up the interstices of coarse aggregate, watering and compacting to the required density Grading 2 as per Technical Specification Clause 405.	140.620	Cum	3,414.01	#NAME?	480078.00
3	WBM Grading 3 (By Mechanical Means) Providing, laying, spreading and compacting stone aggregates of specific sizes to water bound macadam specification including spreading in uniform thickness, hand packing, rolling with smooth wheel roller 80-100 kN in stages to proper grade and camber, applying and brooming, stone screening to fill-up the interstices of coarse aggregate, watering and compacting to the required density Grading 3 as per Technical Specification Clause 405.	140.615	Cum	3,155.75	#NAME?	443746.00
4	Prime Coat (Low porosity) Providing and applying primer coat with Bitumen emulsion (SS-1) on prepared surface of granular base including cleaning of road surface and spraying primer at the rate of 0.70- 1.0 kg/sqm using mechanical means as per Technical Specification Clause 502.	1874.870	Sqm	41.25	#NAME?	77338.00

Anjani Kumar


 सहायक अभियंता
 सड़क एवं विभाग
 जिला पंचायत
 बलिया

Revised BoQ
REPAIR OF ROAD FROM BANDE POKHAR TO PATORI AND COLLEGE UNDER MR-3054 Road

DIVISION : DALSINGH SARAI		BLOCK :		Morwa		LENGTH: 4.900 KM	
SCHEDULE OF WORKS							
Sl. No.	Description of work	No.or Qty.	Unit	Estimated Rate		AMOUNT Rs.	
				Figure	Words		
5	<u>Tack Coat</u> Providing and applying tack coat with bitumen emulsion using emulsion pressure distributor at the rate of 0.25 to 0.30 kg per sqm on the prepared granular surface tretaed with Primer and clenwed with hydrilloc broom as per technical specification aclause 503.	1874.870	Sqm	13.99	#NAME?	26229.00	
6	Patch work over WBM using Mix seal surface with Waste Plastic (for Bituminous and Existing CC Pavement Providing, laying and rolling of close-graded premix surfacing material of 20 mm thickness composed of 11.2 mm to 0.9 mm (Type-A) or 13.2 mm to 0.9 mm (Type-B) aggregates using penetration grade bitumen to required line, grade and level to serve as wearing course on a previously prepared base, including mixing in a suitable plant, laying and rolling with a three wheel 8-10 kN static roller and finishing to required level and grades as per Technical Specification Clause 509.	1874.870	Sqm	193.72	#NAME?	363200.00	
Total Cost						1938926.00	
ADD GST @ 12 %						232671.12	
ADD LABOUR CESS @ 1 %						19389.26	
Grand Total						2190986.38	
Rupees Twenty one lakh ninty thousand nine hundred eighty six only							

Anilani Kumar.

सर्वोच्च न्यायालय
नया दिल्ली

28.8.2021

आचार्य
26/09/21

मुख्य अभियंता -3 का कार्यालय
ग्रामीण कार्य विभाग, बिहार, पटना

पत्रांक:- II/मु0अ0-3,त0स्वी0-18-425/19

पटना दिनांक:-

प्रेषक,

मुख्य अभियंता-3,
ग्रामीण कार्य विभाग,
बिहार, पटना।

सेवा में,

अधीक्षण अभियंता,
ग्रामीण कार्य विभाग,
कार्य अंचल, समस्तीपुर।

विषय:- शीर्ष 3054 एम0आर0 योजना (नई अनुरक्षण नीति 2018) अन्तर्गत कार्य प्रमंडल, दलसिंहसराय के अधीन 02 अदद पथों के प्राक्कलन पर पुनरीक्षित तकनीकी स्वीकृति प्रदान करने के संबंध में।

प्रसंग:-आपका पत्रांक-1366 दिनांक-27.07.2021 एवं विभागीय पत्रांक-1293 अनु0 दिनांक-15.04.21

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र द्वारा प्राप्त कार्य प्रमंडल, दलसिंहसराय के अधीन स्वीकृत पथ के प्राक्कलन पर विभागीय पत्र में दिये गये निदेश के आलोक में पुनरीक्षित तकनीकी स्वीकृति प्रदान कर लौटाया जा रहा है जिसकी विवरणी निम्न है:-

Sl. No	Name of Division	Name of Scheme	Length (in KM)	Department Ref Lett. No./Date	A.A. Amount (in Lakh) Construction & Maintanance Cost	Revised T.S. Amount (in Lakh)
1.	Dalsinghsarai	Repair of Road From Bande Pokhar to Patori AND College Under MR 3054	4.900	2200/08.07.19	160.10	154.17
2	Dalsinghsarai	Repair of Road From NH-103 Se Pursotampur Under MR 3054	2.550	2200/08.07.19	81.42530	70.17

- निर्माण कार्य 3054 एम0आर0 योजना (नई अनुरक्षण नीति 2018) की मार्गदर्शिका के अनुरूप किया जाएगा।
- स्वीकृत प्राक्कलन की जाँच अधीक्षण अभियंता, अपने स्तर से कर लेंगे यदि किसी प्रकार की संशोधन की आवश्यकता हो, तो मुख्यालय को सूचित करेंगे।
- समर्पित किए गए प्राक्कलन की तकनीकी स्वीकृति इस आधार पर दी जाती है कि प्रस्तुत किए गए प्राक्कलन वास्तविक कार्य स्थल के निर्माण के लिए कार्य स्थल के अनुरूप तैयार की गई है, जिसमें पथ एवं पुल निरूपण सम्बंधित सारी आवश्यकता पूरी कर ली गई है।
- अधीक्षण अभियंता, पथों का निरीक्षण प्रतिवेदन एवं कार्यों के संबंध में समीक्षात्मक टिप्पणी मुख्यालय को 5वीं तिथि को उपलब्ध कराना सुनिश्चित करेंगे।
- पुनरीक्षित प्राक्कलन के नये मदों का दर प्राथमिक एकरारनामा के दर से निर्धारित होगी, जिसका तात्पर्य यह है कि प्राथमिक एकरारनामा के समय सक्षम पदाधिकारी द्वारा अनुमोदित दर अतिरिक्त मद की दर के लिए मार्गदर्शक होगी। यह उससे कम हो सकती है किन्तु किसी भी परिस्थिति में यह प्राथमिक एकरारनामा की दर से अधिक नहीं होगी। प्राक्कलन की स्वीकृति दरों की स्वीकृति नहीं समझी जाये।
- पुनरीक्षित प्राक्कलन का दर मूल एकरारनामा के दर के समान होगा तथा नया मद का दर भी मूल एकरारनामा के दर पर आधारित होगा।
- अधीक्षण अभियंता, कार्य अंचल, समस्तीपुर ऐसे मदों के दर जो अनुसूचित दर में नहीं हैं, कर दर अपने अंचल स्तर से राज्यस्तरीय, अनुसूचित दर निर्धारण समिति के द्वारा अनुमोदित सामाग्रियों के दर के

आधार पर MORD Data book analysis के आधार पर दर विश्लेषण करते हुए मुख्यालय को सूचित करेंगे। ताकि मुख्यालय अनुसूचित दर निर्धारण समिति की बैठक में उसका अनुमोदन का S.O.R तैयार करने की दिशा में कार्रवाई की जा सके।

9. स्थल पदाधिकारी द्वारा लम्ब काट एवं आडी काट के आधार पर मिट्टी की मात्रा की गणना कर भुगतान किया जायेगा।
 10. अधीक्षण अभियंता, कार्य अंचल, समस्तीपुर को निदेश दिया जाता है कि नये मद का दर विश्लेषण जाँच कर संतुष्ट हो लेंगे एवं पुनरीक्षित तकनीकी स्वीकृति के उपरान्त लोक निर्माण संहिता के सुसंगत कड़िका के अनुरूप अग्रेतर आवश्यक कार्रवाई करेंगे।
- अनु०- स्वीकृत प्राक्कलन की मूल प्रति।

विश्वासभाजन

ह०/-

मुख्य अभियंता-३, पटना

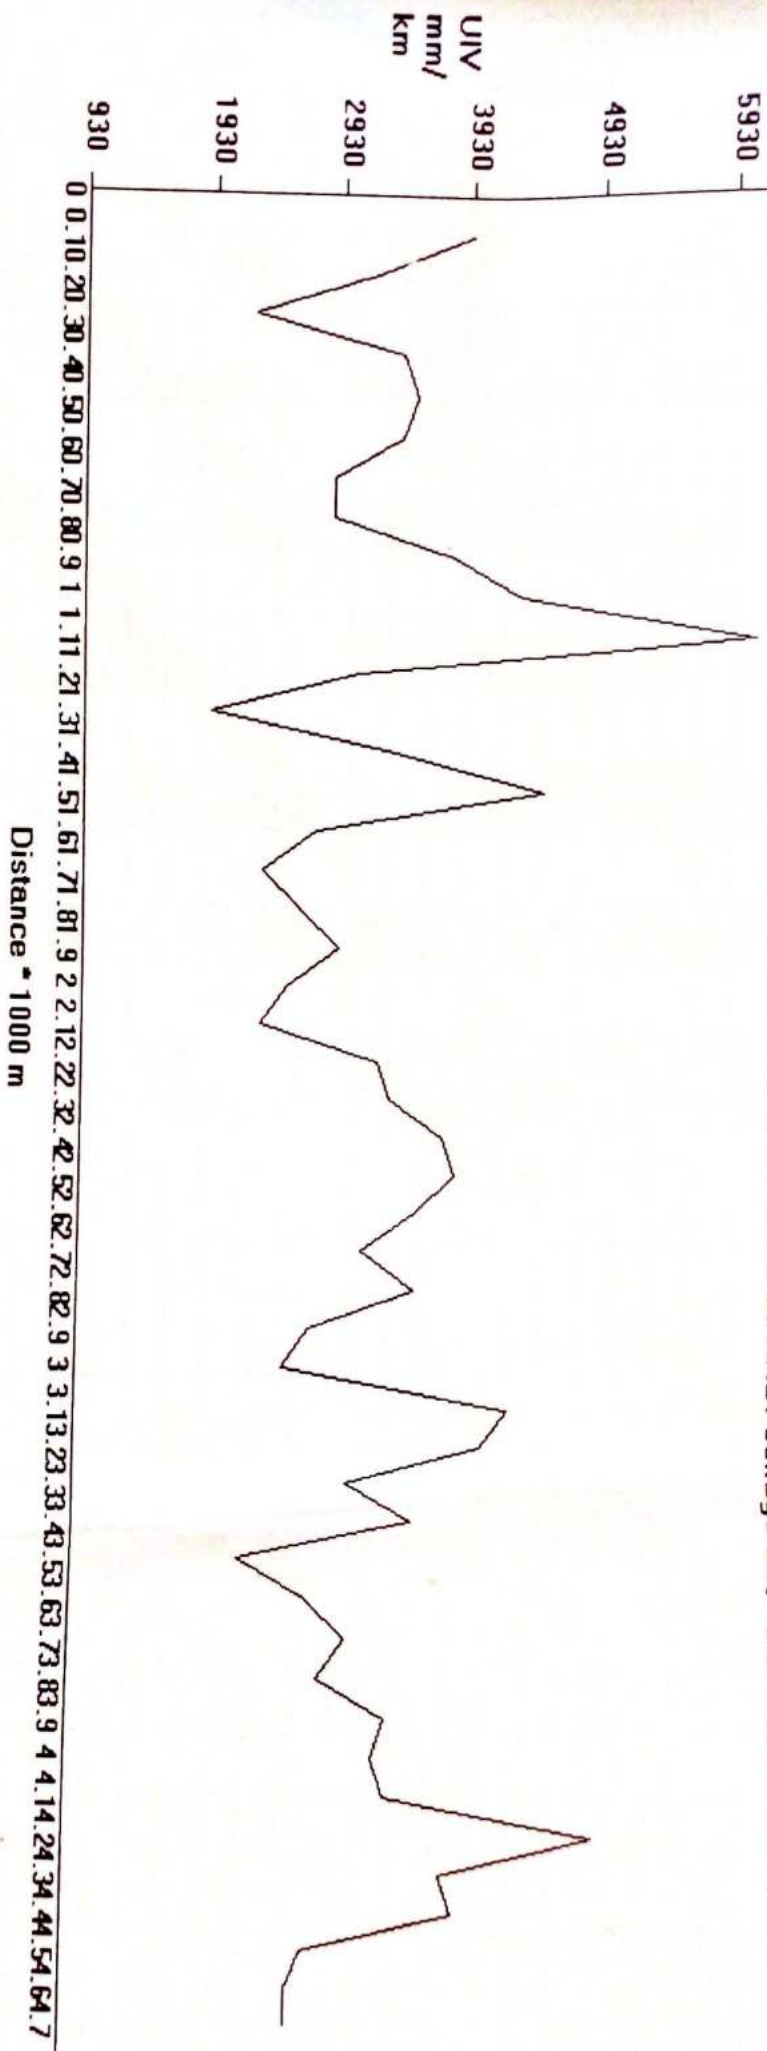
ज्ञापक- ५७९५

पटना, दिनांक- १-८-२१

प्रतिलिपि-कार्यपालक अभियंता, ग्रामीण कार्य विभाग, कार्य प्रमंडल, दलसिंहसराय को सूचना एवं आवश्यक कार्रवाई हेतु अग्रसारित।


मुख्य अभियंता-३, पटना

File : G:\BumpEntrigater\Bande pokhar se AND collage tak 490m sect 91.xlsx, Section No. :91, Eqn : $Y = 0 \cdot X^2 +$
 Name of Customer : Anjani kumar, Name of Work/ Road : Bande Pokhar se AND. Collage tak, Lab Job number :



(Signature)

(Signature)

कार्य प्रमंडल दलसिंहसराय
 ग्रामीण कार्य विभाग
 कार्यपालक अभियंता

Date	Time	ection	Length	Bumps	Speed	OR	IRI	TEGORY	Latitude	ongitude	Event			
27/5/20	18:0:8	No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
27/5/20	18:1:0	91	0.1	380	0	3800	3940	G	25.67294	85.56638	Normal	Y = 0 * X + 2 + 1.058 * X - 79.44		
27/5/20	18:1:18	91	0.1	310	25.2	3100	3200	G	25.67232	85.56714	Normal	X = 2600		
27/5/20	18:1:53	91	0.1	220	26.3	2200	2248	G	25.67174	85.5679	Normal	Y = 2671		
27/5/20	18:2:0	91	0.1	330	24.5	3300	3411	G	25.67129	85.56874	Normal			
27/5/20	18:2:28	91	0.1	340	25.2	3400	3517	G	25.67077	85.56958	Normal	(R) RURAL ROAD		
27/5/20	18:3:3	91	0.1	330	26.3	3300	3411	G	25.67028	85.57039	Normal	Good	Average	Poor
27/5/20	18:3:38	91	0.1	280	24.5	2800	2882	G	25.66978	85.57125	Normal	<4000	4001-5000	>5001
27/5/20	18:4:0	91	0.1	280	25.2	2800	2882	G	25.66933	85.57205	Normal			
27/5/20	18:4:13	91	0.1	370	26.3	3700	3835	G	25.66884	85.57293	Normal			
27/5/20	18:5:0	91	0.1	420	24.5	3000	3094	G	25.66852	85.57386	Normal			
27/5/20	18:5:24	91	0.1	590	25.2	4200	4364	A	25.66825	85.5748	Curve			
27/5/20	18:5:24	91	0.1	300	26.3	3000	3094	G	25.66741	85.57507	Normal			
27/5/20	18:5:24	91	0.1	190	24.5	1900	1930	G	25.66654	85.57529	Normal			
27/5/20	18:6:0	91	0.1	330	25.2	3300	3411	G	25.66574	85.57572	Normal			
27/5/20	18:6:35	91	0.1	440	26.3	4400	4575	A	25.66499	85.57625	Speed			
27/5/20	18:7:10	91	0.1	270	24.5	2700	2777	G	25.66418	85.577	Breaker			
27/5/20	18:7:10	91	0.1	230	25.2	2300	2353	G	25.6634	85.57712	Normal			
27/5/20	18:8:0	91	0.1	260	26.3	2600	2671	G	25.66254	85.57749	Normal			
27/5/20	18:8:20	91	0.1	290	24.5	2900	2988	G	25.66178	85.57795	Normal			
27/5/20	18:8:20	91	0.1	250	25.2	2500	2565	G	25.661	85.57843	Normal			
27/5/20	18:9:0	91	0.1	230	26.3	2300	2353	G	25.66028	85.57909	Normal			
27/5/20	18:9:31	91	0.1	320	24.5	3200	3306	G	25.65965	85.57976	Normal			
27/5/20	18:10:6	91	0.1	330	25.2	3300	3411	G	25.65881	85.5802	Normal			
27/5/20	18:10:6	91	0.1	370	26.3	3700	3835	G	25.65803	85.58066	Normal			
27/5/20	18:10:6	91	0.1	380	24.5	3800	3940	G	25.65725	85.58116	Normal			
27/5/20	18:10:42	91	0.1	350	25.2	3500	3623	G	25.65653	85.58173	Normal			
27/5/20	18:11:17	91	0.1	310	26.3	3100	3200	G	25.6557	85.58215	Curve			
27/5/20	18:11:17	91	0.1	350	24.5	3500	3623	G	25.6551	85.58288	Normal			
27/5/20	18:12:0	91	0.1	270	25.2	2700	2777	G	25.65437	85.58342	Normal			
27/5/20	18:12:27	91	0.1	250	26.3	2500	2565	G	25.65355	85.5838	Normal			
27/5/20	18:12:27	91	0.1	420	24.5	3100	3200	G	25.65265	85.58394	Normal			
27/5/20	18:13:3	91	0.1	400	25.2	3500	3623	G	25.65175	85.58404	Normal			
27/5/20	18:13:38	91	0.1	300	26.3	3000	3094	G	25.65084	85.58412	Normal			
27/5/20	18:14:0	91	0.1	350	24.5	3500	3623	G	25.64994	85.58421	Normal			

(Signature)

(Signature)
 18.05.2020
 गांधीनगर कार्य विभाग
 नगर प्रमुख कार्यालय

27/5/20	18:14:13	91	0.1	220	25.2	2200	2248	G	25.64904	85.58423	Normal					
27/5/20	18:14:49	91	0.1	270	26.3	2700	2777	G	25.64817	85.58409	Normal					
27/5/20	18:15:0	91	0.1	300	24.5	3000	3094	G	25.64729	85.58396	Normal					
27/5/20	18:15:24	91	0.1	280	25.2	2800	2882	G	25.64638	85.58396	Normal					
27/5/20	18:16:0	91	0.1	330	26.3	3300	3411	G	25.64548	85.58386	Normal					
27/5/20	18:16:0	91	0.1	320	24.5	3200	3306	G	25.64459	85.58365	Normal					
27/5/20	18:16:34	91	0.1	330	25.2	3300	3411	G	25.64374	85.5834	Normal					
27/5/20	18:17:10	91	0.1	480	26.3	4800	4998	A	25.64285	85.58323	Curve					
27/5/20	18:17:45	91	0.1	370	24.5	3700	3835	G	25.64207	85.58367	Normal					
27/5/20	18:18:0	91	0.1	380	25.2	3800	3940	G	25.64149	85.58444	Normal					
27/5/20	18:18:20	91	0.1	270	26.3	2700	2777	G	25.64088	85.58515	Curve					
27/5/20	18:19:0	91	0.1	260	24.5	2600	2671	G	25.64004	85.58549	Normal					
27/5/20	18:19:31	91	0.1	260	25.2	2600	2671	G	25.63917	85.58582	Normal					

(Signature)

(Signature)

कार्यपालक उपाध्याय
ग्रापीण कार्य विभाग
कार्य प्रमंडल दरसिंहसराय

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
3rd on A/c Bill					
Name of work - Bandey pokhar to Patori A. N. D college.					
Head - 3054 (MR)					
Authority - E. E.					
RWD. Dalsinghgarai					
Agency - Anjani Kumar.					
Agg. no - 69 MBD/2019-20					
Re Agg. no - 69 MBD/2019-20.					
Date of start - 17/12/19					
Date of comp - 16/12/20					
A/D/C - 26/6/2020.					
Record Measurement -					
Further Measurement is Nil.					
Sumed					
25/9/2021					
J. E.					

[illegible]
