

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल फुलपरास।

पत्रांक.....59.....

दिनांक...11/01/2022.

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी –सह–सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय:–

शीर्ष NEW MAINTENANCE POLICY- 2018 (MR-3054) में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष NEW MAINTENANCE POLICY – 2018 (MR-3054) योजना अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक का भुगतान किया जा सके।

अनु०:–

1. अधियाचना प्रमाण पत्र 1 पृष्ठ में ।
2. उपयोगिता प्रमाण पत्र एक प्रति ।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास।

Kausul/kr
11/01/2022

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilisation Certificate Upto the month of 11 January-2022

New Maintenance policy - 2018

PIU – Executive Engineer, R.W.D (W) Division, Phulparas

SL. No	Name of Scheme	Sanction No. & Date with Amount (In Rs. lacs)	Amount Received (In Rs. lacs)	Particulars
1	Construction of Rural roads under New maintenance policy-2018	Authorisation letter No-02 dt- 03/01/2022. Rs1138.69744.	1138.69744	Certified that out of 1138.69744 Lakh received during the years up to 2021-22 in favour of Ex. Engineer, RWD (W) Division Phulparas, Madhubani, Bihar, a sum of Rs. 1125.40787 Lakh has been utilized for the purpose of New maintenance policy-2018 as given in the margin for which the balance of Rs 13.28957 Lakh remaining unutilized at the end of the period under.

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D (W) Division
Phulparas
Kausal Kumar
11/01/2022

Format of Requisition under Head New Maintenance policy - 2018 (MR-3054) for the month of 11 January - 2022.
Name of Division :- RWD (W) Division phulparas.

SI No.	Package No.	Name of road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)			Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (In km)	Amount of (in lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	MR-N/20-21phulparas/01	Mahadev to Ghoghardiha Under MR-3054	31909804007	1860 24.06.2019	3.500	107.55	68.907	31.80196	59MBD/2019-20 21.03.2020	20.03.2021	—	2981.676	25	5	68.90700	66.43224	0.00000	Work Completed	
2		Piprauliya road to beharari	31909801006	1860 24.06.2019	2.500	77.198	49.613	22.51708	59MBD/2019-20 21.03.2020	20.03.2021	—		25	5	45.50199	45.40960	0.00000	Work Completed	
3		Suroti to Panchmaniya Road	31909801007	1860 24.06.2019	2.000	64.008	41.363	18.43566	59MBD/2019-20 21.03.2020	20.03.2021	—		25	5	39.91422	39.91422	0.00000	Work Completed	
4		Dahapatti to Guleria Tola	31909901009	1860 24.06.2019	2.240	68.024	43.3	20.26458	59MBD/2019-20 21.03.2020	20.03.2021	—		25	5	41.74164	41.74053	0.00000	Work Completed	
5		Brahmpur to Painta Under MR-3054	31909802032	1860 24.06.2019	4.550	154.53	103.972	39.31662	59MBD/2019-20 21.03.2020	20.03.2021	—		3052.72	25	5	103.97200	99.65743	0.00000	Work Completed
6	MR-N/23-21phulparas/03	T04 TO Mahthour Goth Road	31909902012	1860 24.06.2019	3.350	99.52	63.623	29.10752	60MBD/2019-20 21.03.2020	20.03.2021	—	2672.46	25	5	59.16598	59.16596	0.00000	Work Completed	
7		WKT TO Beldari Road	31909802086	1860 24.06.2019	5.200	154.59	99.808	44.26022	60MBD/2019-20 21.03.2020	20.03.2021	—	3166.78	25	5	92.00481	92.00481	0.00000	Work Completed	
8		Nemua Chowk to Dhanchiha	31909801012	1860 24.06.2019	4.000	116.61	80.159	36.01073	60MBD/2019-20 21.03.2020	20.03.2021	—	3290.01	25	5	74.31504	74.31504	0.00000	Work Completed	
9	MR-N/19-20phulparas/08	Kriaot Anachiri Road to Hariraha	31909801010	7387/ 04.10.2019	5.500	191.631	117.563	48.64630	21MBD/2020-21 23.11.2020	22.11.2021	—	2416.36	25	5	114.66052	114.66052	0.00000	Work Completed	
10		PWD ROAD - KURIBAN	31909802074	7387/ 04.10.2019	2.170	89.473	57.389	20.20020	21MBD/2020-21 23.11.2020	22.11.2021	—		25	5	55.51940	55.51940	0.00000	Work Completed	
11		Kariaut to amchiri	31909908021	7387/ 04.10.2019	2.030	87.119	56.027	18.67070	21MBD/2020-21 23.11.2020	22.11.2021	—		25	5	55.55942	54.53040	0.00000	Work Completed	
12	MR-N/19-20phulparas/12	T03 - AURAHA	31909902010	7387/ 04.10.2019	1.420	50.404	29.954	13.79370	21MBD/2020-21 23.11.2020	22.11.2021	—		25	5	29.31728	29.30150	0.00000	Work Completed	
13		W K T - JHITKI	31909802087	7387/ 04.10.2019	1.450	49.702	30.238	12.86825	21MBD/2020-21 23.11.2020	22.11.2021	—		25	5	30.23800	29.30182	0.00000	Work Completed	
14		SH 51 Khutauna Path To Khutauna Block Sastri Chowk	319991034782	656/ 10.02.2020	1.200	85.061	70.168	10.95310	40MBD/2020-21 03.03.2021	02.03.2022	18.06.2021		25	5	75.30419	71.38541	0.00000	Work Completed	
15	N/19-20phulparas/12	SH 51 Pahari Tol To Nahari Road Via bela	319991034780	656/ 10.02.2020	4.000	181.592	133.936	38.05595	40MBD/2020-21 03.03.2021	02.03.2022	18.06.2021	2966.33	25	5	133.93600	133.74433	0.00000	Work Completed	

Sl. No.	MR.	PIPRAJI	31909802073	656/ 10.02.2020	2.244	69.008	44.635	21.90035	40MBD/2020-21 03.03.2021	02.03.2022	18.06.2021	2692.73	25	5	44.63500	44.31971	0.000000	Work Completed
17	RM/MA/PHU/20/0003	NATABA TOL - NH14A	31909802069	7387/ 04.10.2019	3.380	120.474	104.340	30.33030	12MBD/2021-22 24.08.2021	23.08.2022	12.12.2021	2332.6	25	5	74.00495	74.00495	0.000000	Work Completed
18		MURLICHOWK - MATHOUR	31909802059	7387/ 04.10.2019	1.960	71.965	62.405	18.67560	12MBD/2021-22 24.08.2021	23.08.2022	—	—	25	5	0.000000	0.000000	0.000000	On Going
19	RM/MA/PHU/20/0005	KALAPATTI - EKRA	31909802043	5266/ 04.10.2019	2.62	79.928	53.219	23.17825	29MBD/2020-21 23.11.2020	22.11.2021	—	3157.12	25	5	0.000000	0.000000	53.49635	Work Completed
20		LAUKAHI MAHADEONATH - Chhatpuri	31909802051	5266/ 04.10.2019	2.03	51.289	35.516	14.17550	29MBD/2020-21 23.11.2020	22.11.2021	—	—	—	—	0.000000	0.000000	0.000000	On Going
21		KALAPATTI - BHATTABARI	31909802042	5266/ 04.10.2019	4.91	157.276	103.324	45.52225	29MBD/2020-21 23.11.2020	22.11.2021	—	3134.66	25	5	0.000000	0.000000	92.06129	Work Completed
22	MR-N/19-20phulpur/05	NH 104 - Anharban	NEA22000387	5266/ 04.10.2019	4.36	150.128	104.149	39.08020	29MBD/2020-21 23.11.2020	22.11.2021	—	—	—	—	0.000000	0.000000	0.000000	On Going
23	MR-N/19-20phulpur/07	Kariot Amchiri to Makhnaha road	31909801003	7387/ 04.10.2019	1.80	82.278	62.754	17.13300	31MBD/2020-21 19.12.2020	18.12.2021	—	—	—	—	0.000000	0.000000	0.000000	On Going
24		Bajubanh - Matahi	31909802012	7387/ 04.10.2019	4.00	140.911	93.764	42.70685	31MBD/2020-21 19.12.2020	18.12.2021	—	—	—	—	0.000000	0.000000	0.000000	On Going
25	MR-N/19-20phulpur/07	BHAWANIPUR - KHARAGPUR	31909802029	7387/ 04.10.2019	4.76	172.583	115.683	51.18280	31MBD/2020-21 19.12.2020	18.12.2021	—	—	—	—	0.000000	0.000000	0.000000	On Going
26		Piprahi se laukhe krishi farm chiraukha path.	31909804024	7387/ 04.10.2019	4.60	137.617	91.091	42.90180	31MBD/2020-21 19.12.2020	18.12.2021	—	—	—	—	0.000000	0.000000	0.000000	On Going
27	MR-N/19-20phulpur/11	Khopa Chauk N.H.-57 to Saini & Maini	31909803007	656/ 10.02.2020	7.04	241.725	173.0706	69.31575	01MBD/2021-22 07.06.2021	06.06.2022	—	—	—	—	0.000000	0.000000	0.000000	On Going
28		sananpatti nawtoliya path.	31909804025	656/ 10.02.2020	2.90	112.547	86.01518	29.13150	01MBD/2021-22 07.06.2021	06.06.2022	—	—	—	—	0.000000	0.000000	0.000000	On Going
29		Dakahi Thakurbari PMGSY Road To Vikramsher	3.19991E+11	656/ 10.02.2020	1.85	49.096	32.47979	17.56705	01MBD/2021-22 07.06.2021	06.06.2022	—	—	—	—	0.000000	0.000000	0.000000	On Going
Total															1138.69744	1125.40787	145.46764	


 Executive Engineer
 R.W.D(W)Div. Phulparas
 Kanchi/Koz
 11/01/2021

Name Of Contractor:- Saroj kumar yadav
Name Of Work:- Kalapatti to Ek dara

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI, TEGORY	Latitude	Longitude	Event
08/12/21	14:27:1	78	0.1	290	10.1	2900	ROAD	26.422605	86.458917	Normal
08/12/21	14:27:1	78	0.1	330	40.4	3300	G	26.422787	86.458407	Normal
08/12/21	14:27:1	78	0.1	220	30.2	2200	G	26.422803	86.457763	Normal
08/12/21	14:27:36	78	0.1	170	30.2	1700	G	26.423307	86.456817	Normal
08/12/21	14:27:36	78	0.1	300	40.4	3000	G	26.423442	86.455558	Normal
08/12/21	14:28:0	78	0.1	190	30.3	1900	G	26.423581	86.455033	Normal
08/12/21	14:28:12	78	0.1	150	20.2	1500	G	26.422839	86.454154	Curve
08/12/21	14:28:12	78	0.1	180	30.3	1800	G	26.421492	86.453446	Normal
08/12/21	14:28:47	78	0.1	220	20.2	2200	G	26.420639	86.453116	Normal
08/12/21	14:29:22	78	0.1	310	10.1	3100	G	26.42067	86.453023	Speed Breaker
08/12/21	14:29:22	78	0.1	280	10.1	2800	G	26.420299	86.450715	Speed Breaker
08/12/21	14:29:57	78	0.1	280	10.1	2800	G	26.420203	86.450577	Normal
08/12/21	14:29:57	78	0.1	330	20.2	3300	G	26.420433	86.449878	Normal
08/12/21	15:26:0	78	0.1	330	30.3	3300	G	26.419902	86.448595	Normal
08/12/21	15:26:0	78	0.1	260	10.1	2600	G	26.419592	86.447576	Normal
08/12/21	15:26:35	78	0.1	180	30.2	3300	G	26.419391	86.446805	Normal
08/12/21	15:26:35	78	0.1	220	20.1	2200	G	26.418878	86.446083	Normal
08/12/21	15:26:35	78	0.1	260	20.1	2600	G	26.418607	86.445264	Curve
08/12/21	15:27:0	78	0.1	230	10.1	2300	G	26.418257	86.444135	Normal
08/12/21	15:27:10	78	0.1	270	10.1	2700	G	26.417863	86.442785	Speed Breaker
08/12/21	15:27:10	78	0.1	200	20.2	2600	G	26.417578	86.440945	Normal
08/12/21	15:27:10	78	0.1	310	20.2	3100	G	26.417651	86.440553	Curve
08/12/21	15:28:0	78	0.1	340	20.2	3400	G	26.417718	86.439851	Normal
08/12/21	15:28:0	78	0.1	290	10.1	2900	G	26.417833	86.438792	Normal
08/12/21	15:28:21	78	0.1	250	10.1	2500	G	26.418124	86.438077	Normal
08/12/21	15:28:21	78	0.1	270	20.2	2700	G	26.418232	86.437511	Normal
Total IRI							3157.115			

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 900$$

$$Y = 1154$$


(R) RURAL ROAD

Good <4000
Average 4001-5000
Poor >5001

8.12.21

29/11/22

File :C:\Users\BRRDA107\Desktop\08012022 text.Xls, Section No. :78, Eqn :test
Name of Customer :Saroj kumar yadav, Name of Work/ Road :Kalapatti to Ekdara, Lab Job number :

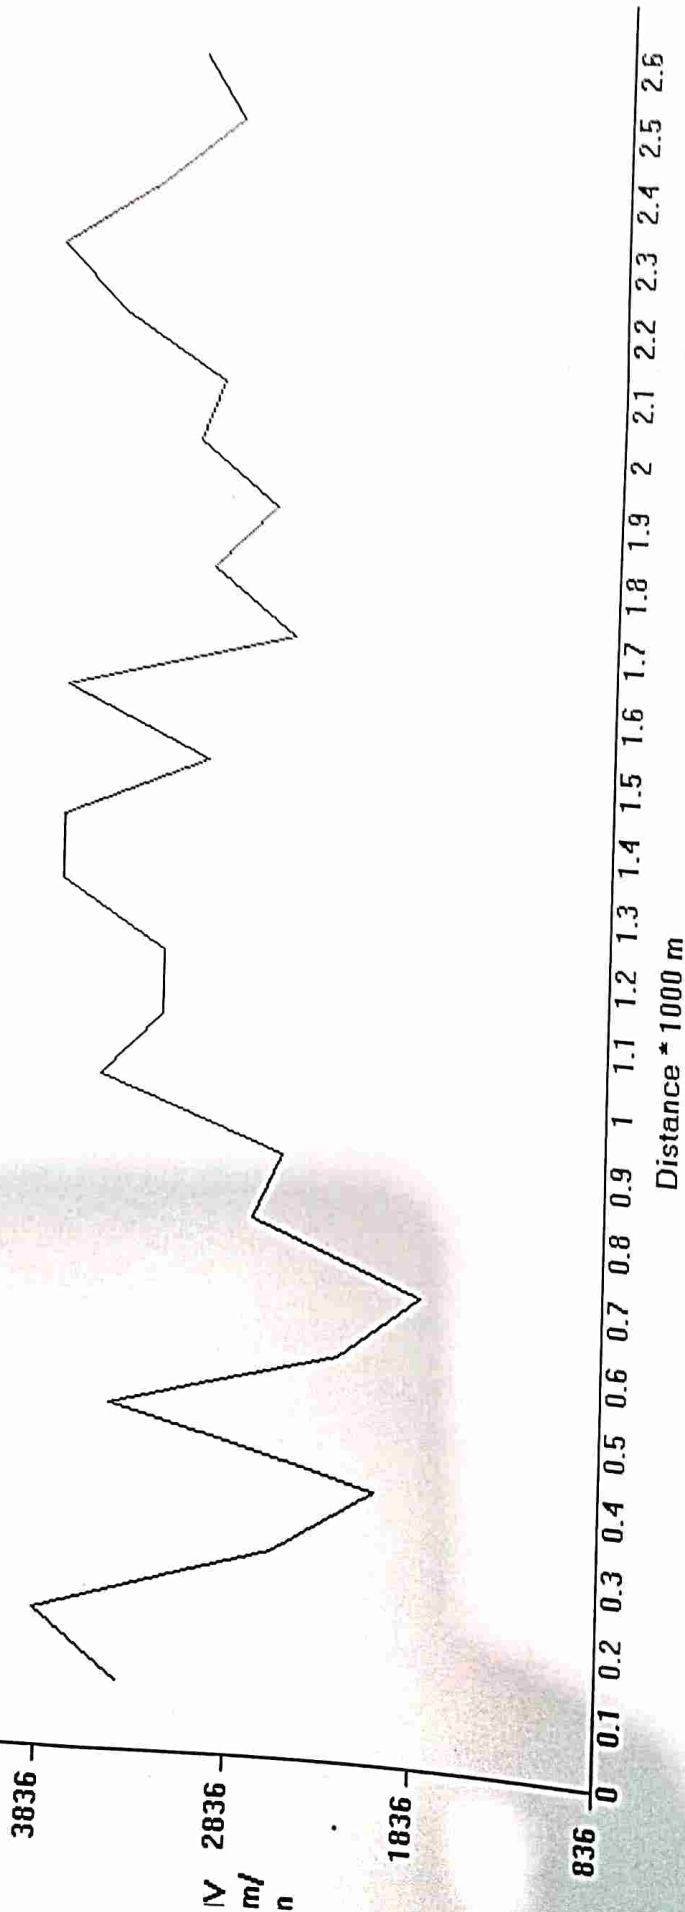

3005
11111111
1212

① M/R-3054 योजना अंर्ग-कालापदी से एकड़ 11

Schedule XLV-Form No. 134

R. M. D. PHULPARAS DIVISION

R. M. D. PHULPARAS SUB-DIVISION

MEASUREMENT BOOK

संबेदक-श्री सरोज कुमार यादव

Agency by

Date of Measurement-

No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Work:-					Maintenance of Road
& CD work from Kalapatti to Ekdra					
Under M.R. 3054					
Agency:-					Saroj Kumar Yadav.
Agreement No					2911 BD / 2020-21
Date of commencement:-					17.12.2020
Date of completion:-					18.12.2021 After agreement.
Date of Measurement:-					

Date 22/11/21

(1) Clearing & Grubbing					
of Road land including					
uprooting ----- ch.					
1st KM. 2 x 10 No x 30.0m x 1.0 =					600 m ²
2 x 10 No x 30.0m x 1.0 (m) =					600
2 x 13 No x 30.0m x 1.0 (m) =					780
2 x 1 No x 10 m x 1.0 (m) =					20
2nd KM. 2 x 10 No x 30.0m x 1.0 =					600
2 x 11 No x 30.0m x 1.0 (m) =					660
2 x 12 No x 30.0m x 1.0 (m) =					720
2 x 1. No x 10.0m x 1.0 (m) =					20
3rd KM. 2 x 10 No x 30.0m x 1.0 (m) =					600
2 x 10 No x 30.0m x 1.0 (m) =					600
2 x 20 No x 20.0m x 1.0 (m) =					400

5240 M²

Continuation OR. 0.524 Hect.

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	Abstract of cost:-				
(1) Clearing & grubbing					
of Road land including					
uprooting - - - - - etc.					
0.524 Hect		Vide TMB			
		P-1			
@ 51133.76/Hect					26794=00
(2) Cost of Gravel					
Sub base by providing					
Grading & materials - etc.					
50.636 M ³		Vide TMB			
		P-4			
@ 34.57 = 00/M ³					175049=00
(3) Providing & laying WBM					
with Compacting - etc.					
60.29 M ³		Vide TMB			
		P-6			
@ 4350.77/M ³					262553=00
(4) Providing & applying					
prime coat - - - - - etc.					
803.89 M ²		Vide TMB			
		P-9			
@ 4496/M ²					36143=00
(5) Providing & applying					
Top coat with bitumen					
emulsion - - - - - etc.					
803.89 M ²		Vide TMB			
		P-9			
7923.25 M ²		P-10			
10727.14 M ²		@ 15 = 29/M ²			164018=00
(6) Providing & laying 20					
mm thick Mix Seal Surface					
					R. 6,54,557=00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				B.F. - 2.6	64.557=00
803.87 M ²		Vide	TMB		
			P-9		
	@ 2	235=	09/M ² - 8		188987=00
(7) Providing & laying.					
25 mm thick Semi-dence					
bituminous Concrete - etc					
248.086 M ³		Vide	TMB		
			P-11		
	@ 2	12003=	38/M ³ &		2977871=00
(8) Const ⁿ of earthen shoulder					
with 1000 M Road - all					
complete.					
1573.50 M ³		Vide	TMB		
Limit 1572 M ³			P-11		
	@ 2	176=	86/M ³ - 8.		278024=00
(9) Brick Masonry in cm					
(1:3) in Parapet.					
10.80 M ³		Vide	TMB		
			P-11		
	@ 1	5213=	721 M ³ &		56398=00
(10) Plastering with cm(1:4)					
on B/w.					
74.88 M ²		Vide	TMB		
			P-12		
	@ 2	180=	52/M ² - 8.		13517=00
(11) Painting 2 coats on					
new surface.					
211.68 M ²		Vide	TMB		
			P-12		
	@ 1	97=	81/M ² - 8		20571=00
				B. 41.	99835=00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				BFR	4199.83500
(12) Road Marking of Hot					
applied thermoplastic					
compound.					
524 M ²		Vid.	TMB		
	@ 1	735	44 M ²	P-12	38537100
(13) Printing line down Arrow					
etc on Road.					
2620 M ²		Vid.	TMB		
	@ 2	77.72	1 M ²	P-12	203600
(14) Planting of trees by					
the road side.					
90 M ²		Vid.	TMB		
	@ 1	217.72	1 M ²	P-12	7379300
(15) Providing Rectangular					
boundary Pillar etc					
31 M ²		Vid.	TMB		
	@ 1	525	36 M ²	P-12	1528600
(16) Providing & fixing of					
recto. reflectorized sign					
(i) 600mm equilateral Triangle					
3 M ² @ 1	@ 2	37	20.70 M ²	P-12	3032700
(ii) 600mm Circular					
3 M ² @ 1	@ 2	37.50	31 M ²	P-12	1185100
(iii) 600mm x 450mm rectangular					
5 M ² @ 1	@ 2	32.5	20 M ²	P-12	1907900

Rs. 4738.57800

Continuation

Continuation
