

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल, बाँका-1

पत्रांक : 115 (अनु) बाँका-1

दिनांक :- 21/01/2022

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बाँका-1

सेवा में,

नोडल पदाधिकारी MR 3054,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय : MR 3054 New Maintenance Policy 2018 के अन्तर्गत आवंटन की अध्याचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR 3054 New Maintenance Policy 2018 के अन्तर्गत पथों में कराये जा रहे कार्यों के भुगतान हेतु अध्याचना विहित प्रपत्र में उपयोगिता प्रमाण-पत्र एवं मापी प्रमाण-पत्र सहित समर्पित किया जा रहा है।

अनुरोध है कि आवंटन उपलब्ध कराने हेतु अग्रेतर एवं आवश्यक कार्रवाई करने की कृपा की जाय।

अनु०-यथोक्त।

विश्वासभाजन

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बाँका-1

Amit
21/1/22

FORM GFR 19A

(See Government of India's Decision (1) below Rule-150)

Form of Utilization Certificate up to the month- January 2022

MIR 3054 (New Maintenance Policy-2018)

S. No.	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in Lacs Rs.)	Particulars
1	MR 3054 (New Maintenance Policy-2018)	CFMS Letter No.-02 WE, Dt-03.01.2022	6085.49024	Certified that out of Rs. 6085.49024 which was received in the Year 2021-22 in favor of E.E., R. W.D(W), Division Banka-1 Bihar & a sum of Rs. 6053.2640 lacs has been utilized for the purpose of MIR 3054 (New Maintenance Policy-2018) schemes as given in the margin for Rs. 32.26384 Lacs which it was remaining unutilized at the end of the period under.

2. certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled: are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the propose for which it was sanctioned.

Kind of checks exercised-

- Works have been supervised by Executive Engineer/Superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
 - Construction material have been tested.
 - Measurements have been recorded in the MBs and test check conducted by the Assistant.
 - All other codal formalities have been observed
3. Physical Progress achieved:
- construction of Road Works
 - Construction of CD Works


Sr. D.A.O.

RWD (W) Div. Banka-1


Executive Engineer
RWD (W) Div. Banka-1

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Banka-1

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allowed Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (in lac)	Remarks
					Length (in Km)	Amount (in Lac)	Initial Rectification on Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
1	RM/BA/BAN/19/0003	Khasia - Sardara	NEA22000335	1836/24.06.2019	3.35	108.4276	61.718	29.88338	7MBD/2019-20/16.12.2019	15.09.2020		3.43	25 mm	5%	0.000	0.000	44.70655	Physically Completed
2		Berhar sandipi REO Road to Jhikulia	20703502228	1836/24.06.2020	1.500	51.5596	28.909	13.84899	7MBD/2019-20/16.12.2019	15.09.2020		3.83	25 mm	5%	0.000	0.000	21.95650	Physically Completed
3	RM/BA/BAN/19/0011	BANKA KATORIA RD - CHUTIA	20703502028	5270/04.10.2019	2.500	75.677	49.176	21.2868	9MBD/2020-21/04.08.2020	03.05.2021		3.54	25 mm	5%	0.000	0.000	43.00000	Physically Completed


 Executive Engineer
 RWD Works Division
 Banka-1
 21/11/22


**OFFICE OF THE EXECUTIVE ENGINEER RWD
WORKS DIVISION BANKA-1**


Name of Road-	Khasia – Sardara
Name of Scheme-	MR 3054 (New Maintenance Policy-2018)
Name of Contractor/Agency-	LALSURYAPAL SINGH
Length of Road -	3.350 km
Project ID -	NEA22000335
Package No.-	RM/BA/BAN/19/0003
Name of Block -	Belhar


Certified that all item
wise 100% Measurement
has been taken by me

Certified that all item
wise 50% Measurement
has been taken by me

Certified that all item
wise 10% Measurement
has been taken by me


20/11/2022
Junior Engineer RWD
Work Section Belhar
Works Division, Banka-1


20/11/22
Assitant Engineer RWD
Work Sub Division Belhar
Works Division, Banka-1


21/01/22
Executive Engineer
RWD Works Division,
Banka-1

Lab Job number :48			
Date :28-12-2021			
Name of Customer :Lal Suryapal Singh			
Name of Work/ Road :Khasiya To Sardara			
Sr.no	Location of test(in km)	Corrected U.I value(mm/km)	Road catagory
1	0.1	3169	G
2	0.2	2983	G
3	0.3	3562	G
4	0.4	2787	G
5	0.5	2983	G
6	0.6	2757	G
7	0.7	2762	G
8	0.8	2781	G
9	0.9	2742	G
10	1	2786	G
11	1.1	2389	G
12	1.2	2371	G
13	1.3	2768	G
14	1.4	2854	G
15	1.5	2359	G
16	1.6	2497	G
17	1.7	2721	G
18	1.8	2819	G
19	1.9	2528	G
20	2	3352	G
21	2.1	3452	G
22	2.2	3424	G
23	2.3	3449	G
24	2.4	3137	G
25	2.5	3147	G
26	2.6	3641	G
27	2.7	3226	G
28	2.8	3147	G
29	2.9	3720	G
30	3	3136	G
31	3.1	3869	G
32	3.2	3147	G
33	3.3	3068	G
34	3.35	3018	G

Hydrology
28/12/21
J-B.

Aritam
28/12/21
A.E

28/12/21

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	:ATEGOR ROAD	IRI	Latitude	Longitude	Event	Y = 0 * X ^ 2 + 1.136 * X + 132.5		
													X = 2500	Y = 2466	(R) RURAL ROAD
28-12-2021	12:32:23	48	0.1	320	30.3	3200	3169	G	4.23	24.929202	86.512745	Normal	Normal		
28-12-2021	12:33:24	48	0.1	300	20.2	3000	2983	G	4	24.929294	86.512427	Normal	Normal		
28-12-2021	12:34:0	48	0.1	360	30.3	3600	3562	G	4.69	24.929385	86.512110	Normal	Normal		
28-12-2021	12:34:36	48	0.1	280	10.1	2800	2787	G	3.77	24.929477	86.511792	Curve	Curve		
28-12-2021	12:35:0	48	0.1	300	20.2	3000	2983	G	4.03	24.929568	86.511475	Normal	Normal		
28-12-2021	12:35:21	48	0.1	280	20.2	2800	2757	G	3.77	24.929660	86.511157	Normal	Normal		
28-12-2021	12:35:57	48	0.1	280	30.3	2800	2762	G	4.7	25.048860	86.883820	Normal	Normal		
28-12-2021	12:36:42	48	0.1	280	30.3	2800	2781	G	3.77	25.073776	86.879435	Normal	Normal		
28-12-2021	12:37:06	48	0.1	280	30.3	2800	2742	G	2.82	25.073849	86.879201	Normal	Normal		
28-12-2021	12:38:33	48	0.1	280	30.3	2800	2786	G	3.06	25.073922	86.878967	Normal	Normal		
28-12-2021	12:39:09	48	0.1	240	30.3	2400	2389	G	3.3	25.073995	86.878733	Normal	Normal		
28-12-2021	12:40:18	48	0.1	240	20.2	2400	2371	G	3.3	25.074068	86.878499	Normal	Normal		
28-12-2021	12:41:09	48	0.1	280	10.1	2800	2768	G	2.57	25.074141	86.878265	Normal	Normal		
28-12-2021	12:42:11	48	0.1	290	10.1	2900	2854	G	2.94	25.074214	86.878031	Normal	Normal		
28-12-2021	12:43:23	48	0.1	240	10.1	2400	2359	G	3.3	25.074287	86.877797	Normal	Normal		
28-12-2021	12:46:46	48	0.1	250	30.3	2500	2497	G	3.42	25.074360	86.877563	Normal	Normal		
28-12-2021	12:47:0	48	0.1	270	30.3	2700	2721	G	2.45	25.074433	86.877329	Normal	Normal		
28-12-2021	12:47:17	48	0.1	290	10.1	2900	2819	G	2.94	25.074506	86.877095	Normal	Normal		
28-12-2021	12:48:21	48	0.1	250	20.2	2500	2528	G	2.2	25.074579	86.876861	Normal	Normal		
28-12-2021	12:49:37	48	0.1	340	30.3	3400	3352	G	4.17	25.074652	86.876627	Normal	Normal		
28-12-2021	12:50:19	48	0.1	350	30.3	3500	3452	G	3.17	25.074725	86.876393	Normal	Normal		
28-12-2021	12:51:19	48	0.1	360	10.1	3500	3424	G	3.33	25.074798	86.876159	Curve	Curve		
28-12-2021	12:52:46	48	0.1	380	10.1	3500	3449	G	3.63	25.074871	86.875925	Normal	Normal		
28-12-2021	12:53:29	48	0.1	320	10.1	3200	3137	G	3.83	25.074944	86.875691	Normal	Normal		
28-12-2021	12:54:31	48	0.1	320	10.1	3200	3147	G	3.37	25.075017	86.875457	Normal	Normal		
28-12-2021	12:55:45	48	0.1	370	20.2	3700	3641	G	3.09	25.075090	86.875223	Normal	Normal		
28-12-2021	12:56:03	48	0.1	370	30.3	3300	3226	G	3.38	25.075163	86.874989	Normal	Normal		
28-12-2021	12:56:58	48	0.1	320	30.3	3200	3147	G	3.37	25.075236	86.874755	Normal	Normal		
28-12-2021	12:57:32	48	0.1	380	30.3	3800	3720	G	3.39	25.075309	86.874521	Normal	Normal		
28-12-2021	12:58:07	48	0.1	320	10.1	3200	3136	G	3.3	25.075382	86.874287	Normal	Normal		
28-12-2021	12:58:56	48	0.1	390	20.2	3900	3869	G	3.3	25.075455	86.874053	Normal	Normal		
28-12-2021	12:59:37	48	0.1	320	30.3	3200	3147	G	3.37	25.075528	86.873819	Normal	Normal		
28-12-2021	13:00:14	48	0.1	310	20.2	3100	3068	G	3.37	25.075601	86.873585	Normal	Normal		
28-12-2021	13:01:47	48	0.1	310	10.1	3100	3018	G	3.37	24.913710	86.495160	Normal	Normal		

28/12/21
A.E

Prithvi
28/12/21
A.E

Handwritten
28/12/21
D-2

Name of Customer : Lal Suryopal Singh
 Name of Work/ Road : Khasiya To Sardara
 Lab Job number : 48
 Date : 28-12-2021
 Section No. : 48

Test Date : 28-12-2021
 Machine No : 407
 Start S No : Khasiya
 Start E No : Sardara
 Weather :
 Start Location : 20286.512745
 End Location : 1371.864956
 Road Name : Khasiya To Sardara
 Road Type : (M) RURAL ROAD
 Side :
 UIV Range : 1359 To 5000
 Dist Range : 0 To 3.5
 Interval : 1000 mm/km
 Equation : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

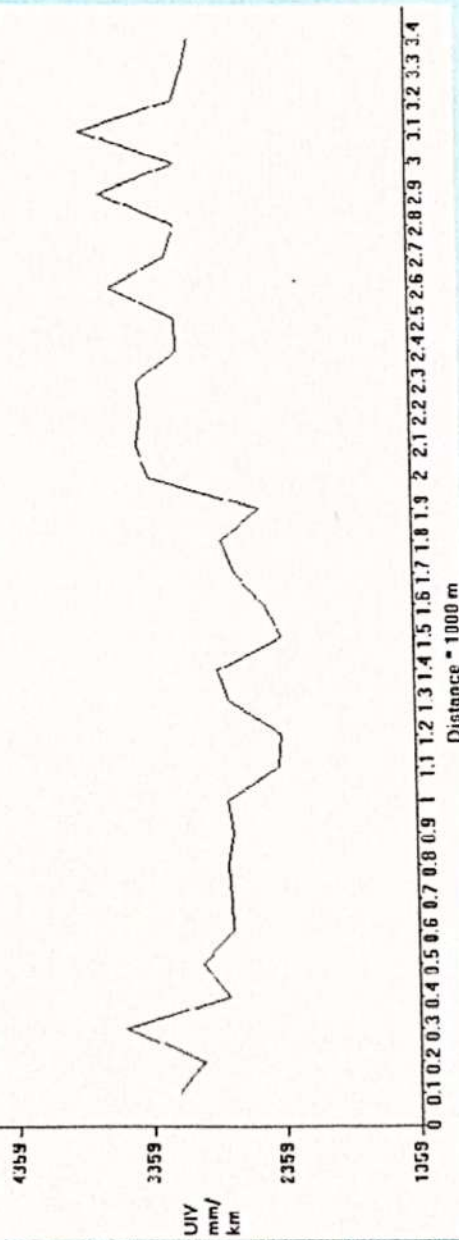
Print Generate Report and Graph

Redraw Graph

Map View

File : F:\42316511.Xbs, Section No. : 48, Equ. : $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$

Name of Customer : Lal Suryopal Singh, Name of Work/ Road : Khasiya To Sardara, Lab Job number : 48



Distance = 1000 m

Handwritten signature and date: 28/12/21

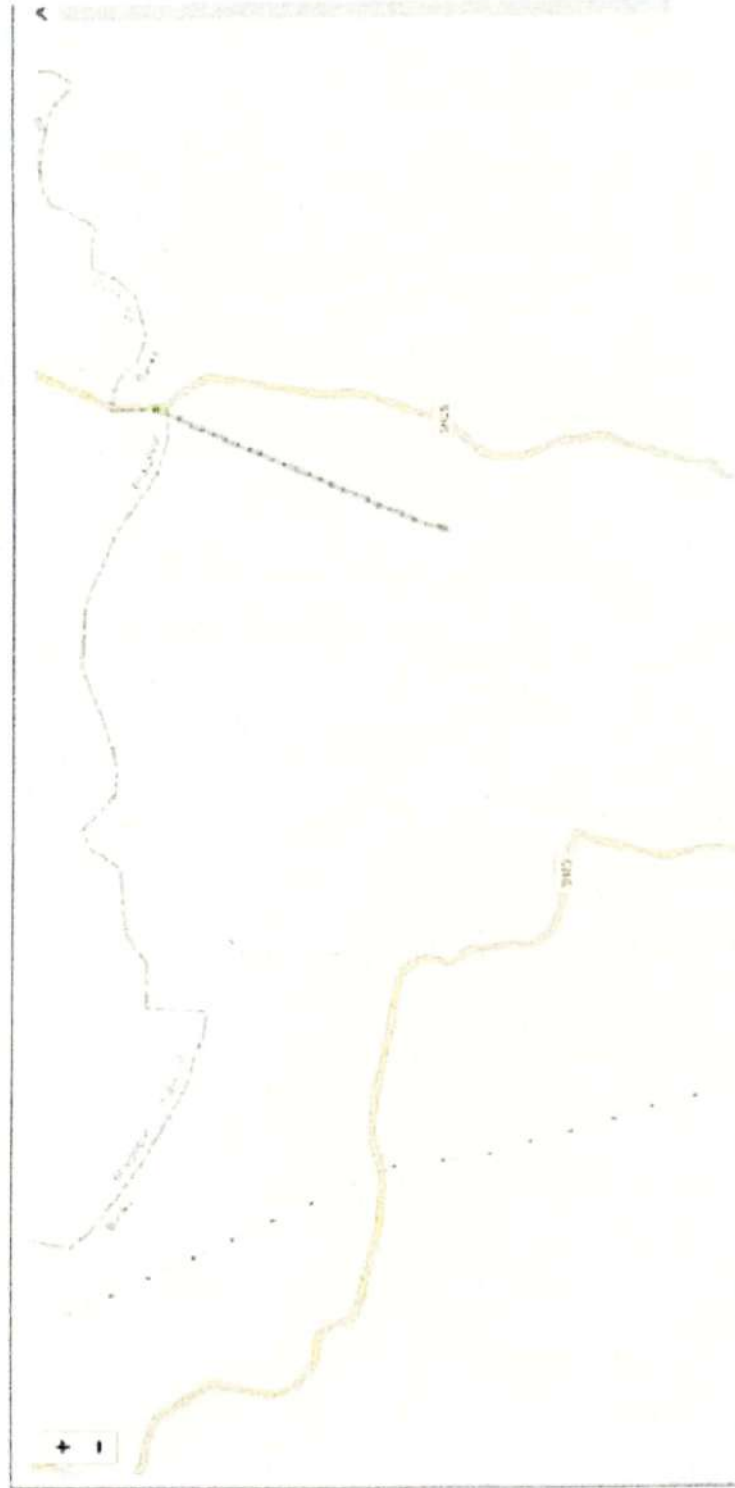
Handwritten signature and date: 28/12/21

Handwritten signature and date: 28/12/21

Map View

- 3 X

File : F:\42316511.XIs, Section No.: 48, Eqn: $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$



~~12/12/21~~

$\frac{147.400}{28.12.21}$
N.E

$\frac{17}{28} \frac{12}{12}$
J-2.

1ST ON A/C Bill

Name of work –1

Situation of work –

Agency by which work is executed –

Date of measurement.

No. and date of agreement

(These four lines should be repeated and the commencement of the measurement relating to each work.)

Particulars	Details of actual measurement				Contents or area
	No.	L.	B.	D.	
Name of Work → Const ⁿ of Road repair on Khasia to Sardara. Agency:- Lal surya Pal Singh Agreement No - 7 MBD / 2019-20 Date of work start → 16-12-2019 Date of Completion → 15-09-2020 Date of Measurement → 17/09/2021	New MR(3054).				
<u>Record Entry</u>					
① - Clearing and grubbing road land including uprooty vegetation, grass bushes all complete jobs - do-do-					
2 X 10 X 30.00 X 1.50 =					900.00m ²
2 X 10 X 30.00 X 1.50 =					900.00m ²
2 X 10 X 30.00 X 1.20 =					720.00m ²
2 X 7 X 30.00 X 1.20 =					504.00m ²
2 X 20 X 30.00 X 1.20 =					1440.00m ²
2 X 14 X 30.00 X 1.20 =					1008.00m ²
2 X 20 X 30.00 X 1.05 =					1260.00m ²
					6732.00m ²
6732.00m ² /10000 =					0.67 Ha

(Continuation)

Abstract of Cost

Sch. XLV- Form No. 134

Particulars	Details of actual measurement				Contents or area
	No.	L.	B.	D.	
① Clearing and grubbing Road Land including uprooting wild vegetation, grass - do - do -					
Qty TMB P-1 Item No-1					
Qty = 0.67 Ha @ Rs 49496.70/Ha = 33163 = 00					
② Const ⁿ of Subgrade and earthen Shoulder with approved material obtained from borrow pits					
Qty TMB P-9 Item No-1					
Qty = 1268.10 m ³ @ Rs 176.75/m ³ = 224137 = 00					
③ Const ⁿ of G.S.B grading II all complete jobs - do - do					
Qty TMB P-3 Item No-2					
Qty = 75.38 m ³ @ Rs 2166.37/m ³ = 163301 = 00					
④ Const ⁿ of WBM Gr. II all complete jobs - do - do					
Qty TMB P-4 Item No-2					
Qty = 79.70 m ³ @ Rs 3890.57/m ³ = 310078 = 00					
⑤ Const ⁿ of WBM Gr. III all complete jobs - do - do					
Qty TMB P-6 Item No-①					
Qty = 143.43 m ³ @ Rs 3589.94/m ³ = 514905 = 00					
⑥ P/A primer Coat with (SS) bitumen emulsion - do - do					
Qty TMB P-7 Item No-1					
Qty = 1931.52 m ² @ Rs 4125/m ² = 79675 = 00					

(Continuation)

1325259 = 00

Sch. XLV- Form No. 134

b.f = 1325259 = 0

Particulars	Details of actual measurement				Contents or area
	No.	L.	B.	D.	
⑦ ⑦ P/L and rolling of M.S. Close-graded premix Surface — do — do —					
Qty: TMB P-7 Item No-2 =					
Qty = 2026.40 m ² @ Rs 192.82/m ² = 390730 = 0					
⑧ ⑧ P/A tack Coat (RS ₁) with bitumen emulsion — do — do					
Qty TMB P-7 Item No-2 = 2026.40 m ²					
Qty TMB P-8 Item No-1 = 10259.10 m ²					
= 12285.50 m ²					
@ Rs 13.99/m ² = 171874 = 0					
⑨ ⑨ P/L SDBC 25 mm thick all complete jobs — do — do					
Qty TMB P-8 Item No-2					
Qty = 256.47 m ³ @ Rs 9688.59/m ³ = 2484320 = 0					
⑩ ⑩ P/Fixing of typical M.H.S.Y Informatory sign board — do — do					
Qty TMB P-6 Item No-2					
Qty = 1 Nos @ Rs 9224.79/No = 9225 = 0					
⑪ ⑪ Plastering with Cement Mortar (1:4) of existing Culvert — do — do					
Qty TMB P-2 Item No-1					
Qty = 60.48 m ² @ Rs 144.40/m ² = 8793 = 0					

(Continuation)

