

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल फुलपरास।

पत्रांक...111.....

दिनांक 27/01/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-

शीर्ष NEW MAINTENANCE POLICY- 2018 (MR-3054) में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष NEW MAINTENANCE POLICY - 2018 (MR-3054) योजना अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक का भुगतान किया जा सके।

अनु०:-

1. अधियाचना प्रमाण पत्र 1 पृष्ठ में।
2. उपयोगिता प्रमाण पत्र एक प्रति।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास।

Kausal K
25/01/2022

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate Upto the month of 25 January-2022

New Maintenance policy - 2018

PIU – Executive Engineer, R.W.D (W) Division, Phulparas

SL. No	Name of Scheme	Sanction No. & Date with Amount (In Rs. lacs)	Amount Received (In Rs. lacs)	Particulars
1	Construction of Rural roads under New maintenance policy-2018	Authorisation letter No-02 dt- 03/01/2022. Rs1138.69744.	1138.69744	Certified that out of 1138.69744 Lakh received during the years up to 2021-22 in favour of Ex. Engineer, RWD (W) Division Phulparas, Madhubani, Bihar, a sum of Rs. 1125.40787 Lakh has been utilized for the purpose of New maintenance policy-2018 as given in the margin for which the balance of Rs 13.28957 Lakh remaining unutilized at the end of the period under.

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.


Executive Engineer
R.W.D (W) Division
Phulparas


25/01/2022

SI No.	Package No.	Name of road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/20-21phulparas/01	Mahadev to Ghoghardha Under MR-3054	31909804007	1860 24.06.2019	3.500	107.55	68.907	31.80196	59MBD/2019-20 21.03.2020	20.03.2021	—	2981.676	25	5	68.90700	66.43224	0.00000	Work Completed
2		Piprauliya road to beharari	31909801006	1860 24.06.2019	2.500	77.198	49.613	22.51708	59MBD/2019-20 21.03.2020	20.03.2021	—	—	25	5	45.50199	45.40960	0.00000	Work Completed
3		Suroti to Pandhuniya Road	31909801007	1860 24.06.2019	2.000	64.008	41.363	18.43566	59MBD/2019-20 21.03.2020	21.03.2020	—	—	25	5	39.91422	39.91422	0.00000	Work Completed
4		Dahapati to Guleria Tola	31909901009	1860 24.06.2019	2.240	68.024	43.3	20.26458	59MBD/2019-20 21.03.2020	59MBD/2019-20 21.03.2020	—	—	25	5	41.74164	41.74053	0.00000	Work Completed
5		Brahmapur to Panna Under MR-3054	31909802032	1860 24.06.2019	4.550	154.53	103.972	39.31662	59MBD/2019-20 21.03.2020	20.03.2021	—	3052.72	25	5	103.97200	99.65743	0.00000	Work Completed
6	MR-N/20-21phulparas/03	TO4 TO Mahthour Goth Road	31909902012	1860 24.06.2019	3.350	99.52	63.623	29.10752	60MBD/2019-20 21.03.2020	20.03.2021	—	2672.46	25	5	59.16598	59.16596	0.00000	Work Completed
7		WKT TO Beldari Road	31909802086	1860 24.06.2019	5.200	154.59	99.808	44.26022	60MBD/2019-20 21.03.2020	20.03.2021	—	3166.78	25	5	92.00481	92.00481	0.00000	Work Completed
8		Nemua Chowk to Dhanchha	31909801012	1860 24.06.2019	4.000	116.61	80.159	36.01073	60MBD/2019-20 21.03.2020	20.03.2021	—	3290.01	25	5	74.31504	74.31504	0.00000	Work Completed
9		Krisot Amachiri Road to Haritraha	31909801010	7387/ 04.10.2019	5.500	191.631	117.563	48.64630	21MBD/2020-21 23.11.2020	22.11.2021	—	2416.36	25	5	114.66052	114.66052	0.00000	Work Completed
10		PWD ROAD - KURIBAN	31909802074	7387/ 04.10.2019	2.170	89.473	57.389	20.20020	21MBD/2020-21 23.11.2020	22.11.2021	—	—	25	5	55.51940	55.51940	0.00000	Work Completed
11	MR-N/19-20phulparas/08	Kuriant to amchiri	31909908021	7387/ 04.10.2019	2.030	87.119	56.027	18.67070	21MBD/2020-21 23.11.2020	22.11.2021	—	—	25	5	55.55942	54.53040	0.00000	Work Completed
12		TO3 - AURAIHA	31909902010	7387/ 04.10.2019	1.420	50.404	29.954	13.79370	21MBD/2020-21 23.11.2020	22.11.2021	—	—	25	5	29.31728	29.30150	0.00000	Work Completed
13		W.K.T - JHITKI	31909802087	7387/ 04.10.2019	1.450	49.702	30.238	12.86825	21MBD/2020-21 23.11.2020	22.11.2021	—	—	25	5	30.23800	29.30182	0.00000	Work Completed
14		SH 51 Khutauna Path To Khutauna Block Sastri Chowk	319991034782	656/ 10.02.2020	1.200	85.061	70.168	10.95310	40MBD/2020-21 03.03.2021	02.03.2022	18.06.2021	—	25	5	75.30419	71.38541	0.00000	Work Completed
15		SH 51 Pahari Tol To Nahari Road Via bela	319991034780	656/ 10.02.2020	4.000	181.592	133.936	38.05595	40MBD/2020-21 03.03.2021	02.03.2022	18.06.2021	2966.33	25	5	133.93600	133.74433	0.00000	Work Completed

16	MR	PIPRABI NATABA TOL - KHILAHII	31909802073	656/ 10.02.2020	2.244	69.008	44.635	21.90035	40MBD/2020-21 03.03.2021	02.03.2022	18.06.2021	2682.73	25	5	44.63500	44.31971	0.00000	Work Completed
17		PARSA NH-57 - LAKSENA	31909802069	7387/ 04.10.2019	3.380	120.474	104.340	30.33030	12MBD/2021-22 24.08.2021	23.08.2022	12.12.2021	2332.6	25	5	74.00495	74.00495	0.00000	Work Completed
18		MURLICHOWK - MATHOUR	31909802059	7387/ 04.10.2019	1.960	71.965	62.405	18.67560	12MBD/2021-22 24.08.2021	23.08.2022	—	—	25	5	0.00000	0.00000	0.00000	On Going
19		KALAPATTI - EKDRA	31909802043	5266/ 04.10.2019	2.62	79.928	53.219	23.17825	29MBD/2020-21 23.11.2020	22.11.2021	11.12.2021	3157.12	25	5	0.00000	0.00000	53.40635	On Going
20		LAUKAHI MAHADEONATH - Chhatpuri	31909802051	5266/ 04.10.2019	2.03	51.289	35.516	14.17550	29MBD/2020-21 23.11.2020	22.11.2021	—	—	—	—	0.00000	0.00000	0.00000	On Going
21		KALAPATTI - BHATTABARI	31909802042	5266/ 04.10.2019	4.91	157.276	103.324	45.52225	29MBD/2020-21 23.11.2020	22.11.2021	30.11.2021	3134.66	25	5	0.00000	0.00000	92.06129	On Going
22		NH 104 - Anharban	NEA22000387	5266/ 04.10.2019	4.36	150.128	104.149	39.08020	29MBD/2020-21 23.11.2020	22.11.2021	—	—	—	—	0.00000	0.00000	0.00000	On Going
23		Karot Amchiri to Makhnaha road	31909801003	7387/ 04.10.2019	1.80	82.278	62.754	17.13300	31MBD/2020-21 19.12.2020	18.12.2021	—	—	—	—	0.00000	0.00000	0.00000	On Going
24		Bajubanh - Matahi	31909802012	7387/ 04.10.2019	4.00	140.911	93.764	42.70685	31MBD/2020-21 19.12.2020	18.12.2021	—	—	—	—	0.00000	0.00000	0.00000	On Going
25		BHAWANIPUR - KHARAGPUR	31909802029	7387/ 04.10.2019	4.76	172.583	115.683	51.18280	31MBD/2020-21 19.12.2020	18.12.2021	10.12.2021	2899.38	25	5	0.00000	0.00000	111.94979	Work Completed
26		Piprahi se laukhe krishi farm chitrauikha path.	31909804024	7387/ 04.10.2019	4.60	137.617	91.091	42.90180	31MBD/2020-21 19.12.2020	18.12.2021	—	—	—	—	0.00000	0.00000	0.00000	On Going
27		Khopa Chauk N.H.-57 to Saini & Maini	31909803007	656/ 10.02.2020	7.04	241.725	173.0706	69.31575	01MBD/2021-22 07.06.2021	06.06.2022	—	—	—	—	0.00000	0.00000	0.00000	On Going
28		sanarpatti nawoliya path.	31909804025	656/ 10.02.2020	2.90	112.547	86.01518	29.13150	01MBD/2021-22 07.06.2021	06.06.2022	—	—	—	—	0.00000	0.00000	0.00000	On Going
29		Dakahi Thakurbari PMGSY Road To Vikramshar	3.19991E+11	656/ 10.02.2020	1.85	49.096	32.47979	17.56705	01MBD/2021-22 07.06.2021	06.06.2022	—	—	—	—	0.00000	0.00000	0.00000	On Going
Total			3213.833	2208.466	867.704	—	—	—	—	—	—	—	—	—	1138.69744	1125.40797	257.31743	

Name of Road:- Bhwanipur to Kharagpur

Name of Contractor:- M/S Laxmi Construction

Date	Time	Section No.	Name of Road	Length in km	Bumps in mm	Speed Rate	OR	IRI, TEGORY	Latitude	ongitude	Event
14/1/22	15:5:41	38		0.1	330	10.1	3300	3881 G	26.38446	86.58148	Normal
14/1/22	15:6:0	38		0.1	250	20.2	2500	2972 G	26.38535	86.58143	Normal
14/1/22	15:6:16	38		0.1	250	30.3	2500	2972 G	26.38625	86.5816	Normal
14/1/22	15:6:16	38		0.1	260	30.3	2600	3086 G	26.38708	86.58162	Normal
14/1/22	15:6:16	38		0.1	230	20.2	2300	2745 G	26.38785	86.58214	Normal
14/1/22	15:7:0	38		0.1	210	20.2	2100	2518 G	26.38745	86.58296	Curve
14/1/22	15:7:0	38		0.1	190	20.2	1900	2290 G	26.38755	86.58394	Normal
14/1/22	15:7:27	38		0.1	230	20.2	2300	2745 G	26.38744	86.58471	Normal
14/1/22	15:7:27	38		0.1	140	30.3	1400	1722 G	26.38815	86.58525	Normal
14/1/22	15:7:27	38		0.1	270	40.4	2700	3199 G	26.38893	86.58566	Normal
14/1/22	15:7:27	38		0.1	220	30.3	2200	2631 G	26.38986	86.58579	Normal
14/1/22	15:8:2	38		0.1	270	20.2	2700	3199 G	26.39034	86.5864	Normal
14/1/22	15:8:2	38		0.1	300	20.2	3000	3540 G	26.39067	86.5871	Normal
14/1/22	15:8:2	38		0.1	280	30.3	2800	3313 G	26.39124	86.58781	Normal
14/1/22	15:8:37	38		0.1	240	30.3	2400	2858 G	26.39159	86.5887	Normal
14/1/22	15:8:37	38		0.1	240	30.3	2400	2858 G	26.39183	86.5897	Curve
14/1/22	15:9:0	38		0.1	190	30.3	1900	2290 G	26.39265	86.58993	Normal
14/1/22	15:9:12	38		0.1	280	40.4	2800	3313 G	26.39359	86.59012	Normal
14/1/22	15:9:12	38		0.1	240	30.3	2400	2858 G	26.39448	86.59	Normal
14/1/22	15:10:0	38		0.1	320	30.3	3200	3767 G	26.39533	86.5903	Normal
14/1/22	15:10:0	38		0.1	300	10.1	3000	3540 G	26.39617	86.59069	Normal
14/1/22	15:10:23	38		0.1	280	10.1	2800	3313 G	26.39681	86.59049	Normal
14/1/22	15:10:23	38		0.1	320	10.1	3200	3767 G	26.39659	86.5897	Normal
14/1/22	15:10:23	38		0.1	230	30.3	2300	2745 G	26.39673	86.58869	Normal
14/1/22	15:10:58	38		0.1	290	20.2	2900	3426 G	26.39742	86.58806	Normal
14/1/22	15:11:0	38		0.1	230	30.3	2300	2745 G	26.39829	86.58803	Normal
14/1/22	15:11:0	38		0.1	240	30.3	2400	2858 G	26.39919	86.58801	Normal
14/1/22	15:11:34	38		0.1	290	30.3	2900	3426 G	26.39986	86.58854	Normal
14/1/22	15:11:34	38		0.1	220	40.4	2200	2631 G	26.40073	86.58906	Normal
14/1/22	15:11:34	38		0.1	270	40.4	2700	3199 G	26.40163	86.58916	Normal
14/1/22	15:12:0	38		0.1	190	10.1	1900	2290 G	26.40205	86.58835	Normal
14/1/22	15:12:9	38		0.1	300	20.2	3000	3540 G	26.40273	86.58788	Speed Breaker
14/1/22	15:12:9	38		0.1	230	30.3	2300	2745 G	26.40359	86.58786	Normal
14/1/22	15:12:44	38		0.1	290	40.4	2900	3426 G	26.40444	86.58758	Normal
14/1/22	15:13:0	38		0.1	240	40.4	2400	2858 G	26.40529	86.58744	Normal

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 3100$$

$$Y = 3654$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

18/01/2022
A.E. Gargi

18.01.2022
J.C.

25/1/22

14/1/22	15:13:0	38	0.1	190	40.4	1900	2290 G	26.40621	86.58753	Normal
14/1/22	15:13:19	38	0.1	150	40.4	1500	1836 G	26.40703	86.58741	Normal
14/1/22	15:13:19	38	0.1	190	40.4	1900	2290 G	26.40803	86.58751	Normal
14/1/22	15:13:19	38	0.1	290	40.4	2900	3426 G	26.40879	86.58726	Normal
14/1/22	15:13:19	38	0.1	200	40.4	2000	2404 G	26.40921	86.58641	Normal
14/1/22	15:13:55	38	0.1	200	40.4	2000	2404 G	26.40948	86.5854	Normal
14/1/22	15:14:0	38	0.1	240	40.4	2400	2858 G	26.40967	86.58443	Normal
14/1/22	15:14:0	38	0.1	190	40.4	1900	2290 G	26.4096	86.58345	Normal
14/1/22	15:14:0	38	0.1	250	30.3	2500	2972 G	26.40939	86.58246	Normal
14/1/22	15:14:29	38	0.1	200	40.4	2000	2404 G	26.40874	86.58178	Normal
14/1/22	15:14:29	38	0.1	180	40.4	1800	2177 G	26.40876	86.58089	Normal
14/1/22	15:14:29	38	0.1	310	30.3	3100	3654 G	26.40894	86.57978	Normal
		Total IRI				2899.382				

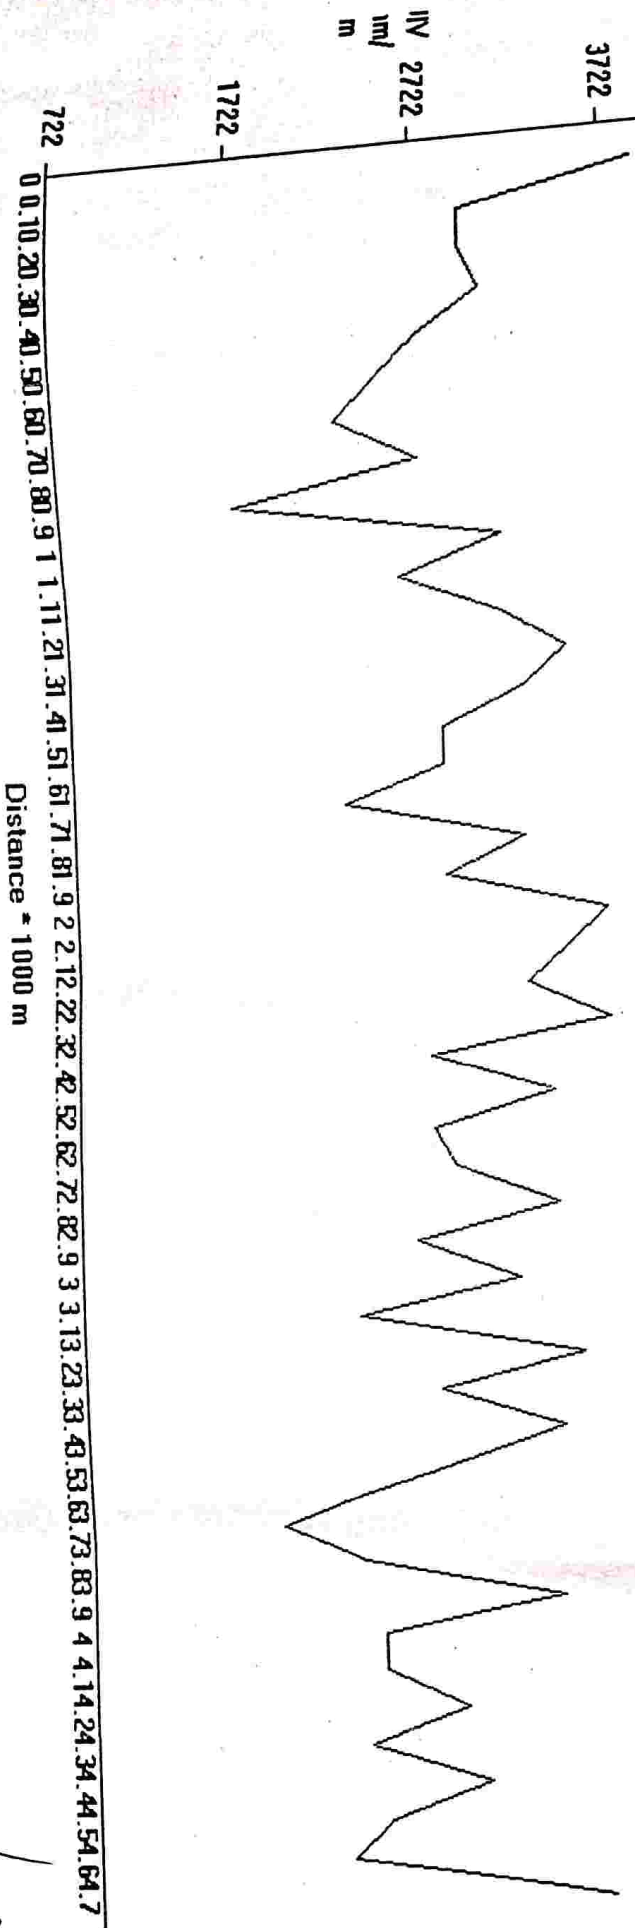
[Signature]
18/01/2022
P. E. Kaulakhi

[Signature]
18.01.2022
J. S. C.

[Signature]
18/1/22
B. E.

File : C:\Users\BRDA107\Desktop\14011525.Xls. Section No. : 38. Eqn : $Y = 0 * X^2 + 1.136 * X + 132.5$

Name of Customer : M/S Laxmi Construction. Name of Work/ Road : Bhawanipur to Kharagpur. Lab Job number :




[Signature]
18/01/2022
A.R. Lakshmi

[Signature]
18.01.2022
G
25338
25/1/22
R.R.

**OFFICE OF THE EXECUTIVE ENGINEER
RWD WORKS DIVISION PHULPARAS.**

Name of Scheme:- BHAWANIPUR – KHARAGPUR ,PACKAGE No-MR-N/19-20phulparas/07,
Project ID-31909802029.

**Certified that all item wise 100%
Measurement has been taken by me**


10.12.2021
J.C

Junior Engineer
RWD Work Section Laukahi
Works Division Phulparas

**Certified that all item wise 50%
Measurement has been cheked by me**



16/12/2021
A.R

Assistant Engineer
RWD Work Section Laukahi
Works Division Phulparas

**Certified that all item wise 10%
Measurement has been cheked by me**


25/1/22

Executive Engineer
Rural work Department
Works Division Phulparas


25/01/2022

(iii) MR-3054 ग्रीनर ग्रोव्स- भवानीपुर to कुनारगढ़

Schedule XLV-Form No. 134

पंचद पंचाद

DIVISION

दरुकरुनी

SUB-DIVISION

M.6.No-259
2020-21

MEASUREMENT BOOK

પ્રમાણિત બિનાર ધારક જે બિન રૂલ ના પાલન
 પૂર્વે નોંધાયેલ કુલ રૂ. ૫૦૦-૧૦૦ (ચાર હાજર)
 પૂરે અંતર જે બિન મહાનગર અમાનગર, ગામ
 બાંધકામ, બાંધકામ અથવા પ્રાથમિક, મધ્યમ
 શાળા નિર્માણ છે.


Executive Engineer
Rural Works Department
Works Division Phulpara
 3.3.21


Sch. XLV - Form No. 134

Phulpara DIVISION

Lauparhi SUB-DIVISION

Measurement Book

No. 259
 2020-21

Name of Officer 
Executive Engineer
Rural Works Department
Works Division Phulpara
 3.3.21

Date of first entry _____

Date of last entry _____

(iii) MR-3054 બિનાર કોલેજ- બનાવનિરુદ્ધ કુશાગર

Lst on A/C Bill

1

Name of Work-

Situation of Work-

Agency by which work is executed-

Date of Measurement-

No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Work:-					
Maintenance					
Work on					
Bhawaripur to					
Kharagpur under					
MOR (3054)					
Name of Agency					
Laxmi Construction					
Agreement No.					
31MBD/2020-21					
Date of Commencement:-					
19.12.2020					
Date of Measurement:-					
25.11.2021					
Item No. 01					
Cleaning and grubbing					
road land					
					9480.00
$2H \times 158H \times 30M \times 1.00 = MC$					
					40.00
$2H \times 106. \times 20M \times 1.00 = M^2$					
					9520.00 M ²
					Say 0.952 H
Item No. 02					
Const. of earthen					
shoulder					
					$2H \times 40H \times 30M \times (1.00 + 1.20 + 1.30) \times 0.30$
					3 = 840.00
					M ³
					$2H \times 106. \times 15M \times (1.00 + 1.20 + 1.30) \times 0.30$
					= 16.50 M ³

Continuation

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2 H ₂ x 25 H ₂ x 30 m x $\left(\frac{0.90 + 1.00 + 1.10}{3} \right)$					x 0.300
					= 450.00 m ³
2 H ₂ x 1 H ₂ x 3.00 m x $\left(\frac{0.90 + 1.00 + 1.10}{3} \right)$					x 0.300
					= 4.80 m ³
2 H ₂ x 84 H ₂ x 30 m x $\left(\frac{1.00 + 1.20 + 1.40}{3} \right)$					x 0.300
					= 1814.40 m ³
2 H ₂ x 1 H ₂ x 7 m x $\left(\frac{1.00 + 1.20 + 1.40}{3} \right)$ x 0.300					= 5.04 m ³
					<u>3,124.24 m³</u>
1 H ₂ x 1 H ₂ x 0.3					
Const. of granules					
sub base					
2 H ₂ x 5.20 x 2.20 x 0.100 = 2.29 m ³					
1 H ₂ x 3.10 x 1.50 x 0.100 = 0.465 m ³					
1 H ₂ x 10.00 x 1.30 x 0.100 = 1.300 m ³					
2 H ₂ x 6.00 x 2.00 x 0.100 = 2.400 m ³					
1 H ₂ x 3.00 x 1.80 x 0.100 = 0.540 m ³					
4 H ₂ x 4.00 x 1.50 x 0.100 = 2.400 m ³					
1 H ₂ x 3.00 x 1.70 x 0.100 = 0.510 m ³					
1 H ₂ x 4.00 x 1.50 x 0.100 = 0.600 m ³					
1 H ₂ x 4.00 x 1.40 x 0.100 = 0.560 m ³					
2 H ₂ x 8.20 x 2.40 x 0.100 = 3.936 m ³					
1 H ₂ x 6.00 x 3.20 x 0.100 = 1.920 m ³					

Continuation

Abstract of Est on A/c

14

Bill

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Date	10.12.2024				
Item No. 01					
Cleaning & grubbing road land (By manual men)					
Vide the M.B. Page 1					0.9524
0.9524 @ Rs 51,133 = 76/H					
→ Rs 48,670 = 00					
Item No. 02					
Const. of earthen shoulder with approved material					
3,124.74 m ³ @ Rs 176 = 86/m ³					
→ Rs 5,52,642 = 00					
Item No. 03					
Const. of granular sub base by providing well graded material					
Vide the M.B. Page 6					117.523 m ³
As per B.O.D - 115.36 m ³					
115.36 m ³ @ Rs 3,504 = 39/m ³					
→ Rs 4,04,260 = 00					
Item No. 04					
Providing, laying, spreading and compacting WBM Gr 2					

Rs 10,05,581 = 00

Continuation

R 10,05,581.00

Particulars	Details of actual measurement			Contents of area
	No.	L.	B.	
Vid the M.B. Page 9				242.449 m ²
As per B.O. 9				→ 240.165 m ²
240.165 m ² @ R 441296/m ²				
				→ R 10,59,598.00
Item No. 05				
Providing & applying primer coat				
Vid the M.B. Page 10				3232.65 m ²
As per B.O. 10				→ 3202.20 m ²
3202.20 m ² @ R 44275/m ²				
				→ R 1,42,298.00
Item No. 06				
Back Coat				
Vid the M.B. Page 10				3232.65 m ²
Vid the M.B. Page 11				18032.90 m ²
				21265.55 m ²
As per B.O. 11				→ 21230.70 m ²
21230.70 m ² @ R 15222/m ²				
				→ R 3,23,131.00
Item No. 07				
Providing, laying and rolling of clay graded premix surfacing 20mm thick				
Vid the M.B. Page 10				3232.65 m ²
As per B.O. 11				→ 3202.20 m ²
3202.20 m ² @ R 235069/m ²				

R 25,31,608.00

Continuation

Rs 25,31,608.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					→ Rs 7,54,727.00
Item no. 08					
Providing & laying					
semi dense bituminous					
Concrete as per MORTH					
specification					
Vide the M.B. Page 11					450.823 m ²
As per B.O.D					450.713 m ²
450.713 m ² @ Rs 12,031 = 53.67					
					→ Rs 54,22,722.00
Item no. 09					
Plastering with					
on brick work					
Vide this M.B. Page 11					174.95 m ²
174.95 m ² @ Rs 181 = 51.67					
					→ Rs 31,755.00
Item no. 10					
Painting two coats					
including prime					
coat as per specification					
Vide the M.B. Page 12					174.95 m ²
174.95 m ² @ Rs 97 = 18.67					
					→ Rs 17,002.00
Item no. 11					
R.C.C. Mason Kilometre					
local stone of					

Rs 87,57,814.00

Continuation

Rs 87,57,814.20

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
standard design					
i) Km stone					
Vide this M.B. Page 12 - 6 Nos					
6 Nos @ Rs 2455 = 26/Nos					
→ Rs 14,732.00					
ii) 200m stone					
Vide this M.B. Page 12 - 19 Nos					
19 Nos @ Rs 637.242/Nos					
→ Rs 12,111.20					
Item No 12					
Providing & fixing of					
subsoil surface					
containing					
sign					
i) 600mm equilateral triangle					
Vide this M.B. Page 12 - 14 Nos					
14 Nos @ Rs 3792 = 26/Nos					
→ Rs 53,162.00					
ii) 600mm circular					
Vide this M.B. Page 12 - 5 Nos					
5 Nos @ Rs 3956 = 67/Nos					
→ Rs 19,783.00					
iii) 600mm x 450mm rectangular					
Vide this M.B. Page 12 - 10 Nos					
10 Nos @ Rs 3822 = 16/Nos					
→ Rs 38,222.00					

Rs 88,95,824.00

Continuation

Rs 88,95,824

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Item No. 13					
R.C.C. M.S. grade boundary pillars of standard design					
Vide the M.B. Page 12	50 Nos.				
50 Nos. @ Rs 526 = 49/16					
→ Rs 26,324 = 00					
Item No. 14					
Planting of trees by the road side					
Vide the M.B. Page 12	460.00				
460 Nos. @ Rs 219 = 92/16					
→ Rs 23,274 = 00					

Item No. 15					
Providing & laying of hot applied thermoplastic compound 2.5mm thick					
Vide this M.B. Page 12	952.00				
952.00 m ² @ Rs 735 = 44/16					
→ Rs 7,00,139 = 00					

Item No. 16					
Providing & fixing of typised M.M.G.S.V. informatory sign board with logo as per M.O.R.D. specification					
Vide the M.B. Page 13	2 Nos.				

Rs 99,99,450 =

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2 Hrs @ Rs 9406265/A6					
					Rs 18813 = 00
Add 12% GST - Rs 12,02,182 = 00					
					Rs 1,12,20,455 = 00
Add 1% L.C. - Rs 1,00,183 = 00					
					Rs 1,13,20,638 = 00
Deduct 1.11% as per contract - Rs 1,25,659 = 00					
					Rs 1,11,94,979 = 00
 J.C. 16/12/2021 AE 16/12/2021					
