

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडलपुपरी (सीतामढ़ी)

पत्रांक :- 1325 पुपरी, दिनांक :- 05-07-2022
प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पुपरी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
सह-सचिव—
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय :- शीर्ष बिहार नई अनुरक्षण नीति 2018 (MR 3054) में आवंटन उपलब्ध कराने के संबंध में।

महाशय,


उपर्युक्त विषय के संबंध में कहना है कि इस प्रमंडल अन्तर्गत चल रहे नई अनुरक्षण नीति 2018 (MR 3054) में स्वीकृत योजनाओं के विभिन्न कार्यों के लिए मो0-171.64203 (एक करोड़ ईकहत्तर लाख चौसठ हजार दो सौ तीन) रुपया का आवंटन हेतु प्रतिवेदन विहित प्रपत्र में संधारित कर संलग्न करते हुए आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु0—यथोक्त।

विश्वास भाजन


02-07-22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल
पुपरी (सीतामढ़ी)



Requisition Format for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy-2018 (initial Rectification and Surface Renewal)
Name of Works Division RWD, Works Division-Sitamarhi.

Sli. No.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Length (in km)	Administrative Approval		Agreement Amount (in Lakh)		Agreement No. Date	Date of Completion as per agreement	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in lakh)	Up to Date expenditure as per MIS (in Lakh)	Requision against work done (in lakh)	Remarks
						5 Years Routine Maintenance (in lakh)	Amount (in lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (in lakh)									
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/2019-20 Pupri/ 15	NH 104 Jamuna Bridge to Sondahi	31607902157		1.730	41.4975	15.426	37.28449	15.47316	01 MBD/ 2021-22	11.01.2022	2709	0.025	5%	0.00	0.00	37.18582	Completed
2		Koriyahi to Bheenua	31607902096		3.200	70.873	29.860	64.37957	29.82949			2551	0.025	5%	0.00	0.00	60.53115	
3	MR-N/2019-20 Pupri/ 16	NH 104 Yadupatti Thana to Matauna	31607902156	6480/ 13.12.2019	3.752	83.193	32.710	73.32861	31.96482	42 MBD/ 2020-21	15.06.2022	2752	0.025	5%	0.00	0.00	65.46171	
4		Madhurapur REO Road to Bhatol REO Road	31607902136		0.320	9.56780	3.06500	8.50387	2.92155			2854	0.025	5%	0.00	0.00	8.46335	
Total					9.002	205.131	81.061	183.497	80.189						0	0	171.64203	

1. Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.

2. Up - to date Physical Progress has been uploaded in MIS.

(Signature)
Executive Engineer,
RWD, Works Div, Pupri

(Signature)
02/07/2020

Office of The Executive Engineer,
Rural Works Department, Works Division, Pupri

Name of Road:-NH 104 Jamura Bridge to Sondahi
Name of Scheme:- MR(NEW MAINT POLICY)
Name of Contractor:-Shree Awadh Mithila Construction Private Limited
Length of Road:-1.730 KM
Project ID:-31607902157
Package No.- MR-N/19-20/Pupri/15
Name of Block:-Sursand

Certified that all item wise
100% measurement has been
taken by me

[Signature]
20/05/22

Junior Engineer,
Rural Works Department,
Works Section, Sursand
Works Division, Pupri

Certified that all item wise 50%
measurement has been checked
by me

[Signature]
20/05/22

Assitant Engineer,
Rural Works Department,
Works Sub Division, Sursand
Works Division, Pupri

Certified that all item wise
10% measurement has been
checked by me

[Signature]
20/05/22

Executive Engineer,
Rural Works Department,
Works Division, Pupri

Name of Road - NH 104 Jamura bhidge to Sondahi

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY ROAD	Latitude	ongitude	Event
30/5/22	11:11:37	23	0.1	260	0	2600	2557 G	3.49	26.64754	85.6053 Normal
30/5/22	11:12:12	23	0.1	290	20.2	2900	2854 G	3.85	26.64682	85.60478 Normal
30/5/22	11:12:22	23	0.1	320	20.2	3200	3151 G	4.2	26.64604	85.60426 Normal
30/5/22	11:12:32	23	0.1	210	20.2	2100	2063 G	2.88	26.64519	85.60443 Normal
30/5/22	11:12:47	23	0.1	280	30.3	2800	2755 G	3.73	26.64443	85.60497 Normal
30/5/22	11:13:0	23	0.1	250	20.2	2500	2458 G	3.37	26.64349	85.60551 Normal
30/5/22	11:13:22	23	0.1	270	20.2	2700	2656 G	3.61	26.64266	85.60535 Normal
30/5/22	11:13:31	23	0.1	230	20.2	2300	2261 G	3.13	26.64178	85.60503 Normal
30/5/22	11:13:42	23	0.1	270	20.2	2700	2656 G	3.61	26.64091	85.60443 Normal
30/5/22	11:14:0	23	0.1	220	20.2	2200	2162 G	3	26.64013	85.60379 Normal
30/5/22	11:14:33	23	0.1	360	10.1	3600	3546 G	4.67	26.63944	85.60315 Normal
30/5/22	11:14:43	23	0.1	210	20.2	2100	2063 G	2.88	26.63869	85.60249 Normal
30/5/22	11:15:0	23	0.1	330	20.2	3300	3250 G	4.32	26.63796	85.60305 Normal
30/5/22	11:15:8	23	0.1	310	20.2	3100	3052 G	4.09	26.63725	85.60375 Normal
30/5/22	11:15:43	23	0.1	360	10.1	3600	3546 G	4.67	26.63636	85.60407 Normal
30/5/22	11:16:19	23	0.1	280	0	2800	2755 G	3.73	26.63568	85.60446 Normal
30/5/22	11:18:0	23	0.1	230	0	2300	2261 G	3.13	26.635	85.60483 Normal
							AVG:-	2709		

Y = 0 * X ^ 2 + 0.989 * X - 13.58
X = 1300
Y = 1272

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001


Handwritten signature
30/05/22
JE

Handwritten signature
30/5/22
AE

Handwritten signature
30/5/22
AE

File : C:\Users\BRRDA42\Desktop\Bump Report\Babu Sahab\BUMPI\21061121.Xls, Section No. :23, Eqn : $Y = 0 * X$

Name of Customer : Name of Work/ Road : Lab Job number :

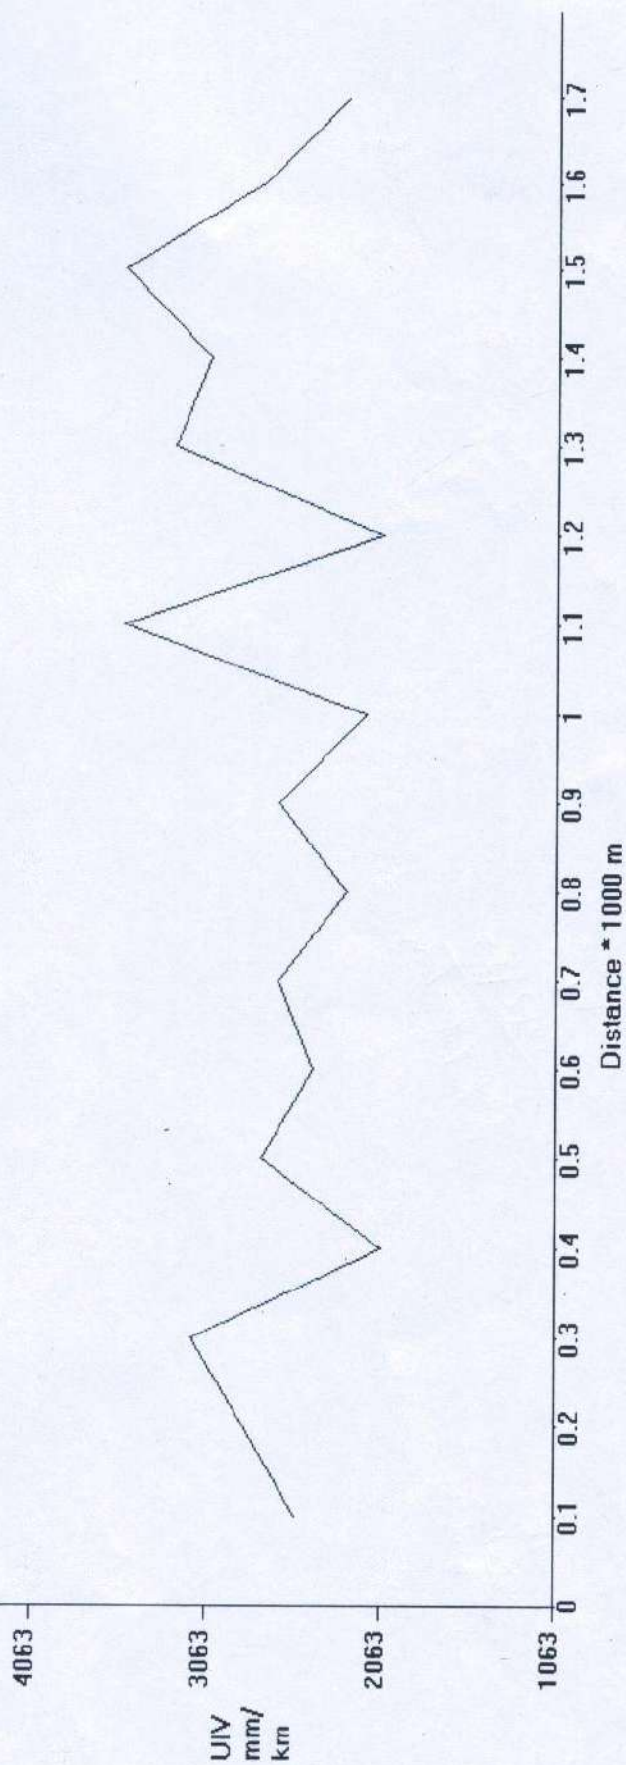

Handwritten signature
30/05/22
DE

Handwritten signature
30/05/22
DE

MR-3054(New) (Sarband)

Schedule XLV-Form No. 134

N/WORKI - M/R of road form. NH 10. 4 Jamuna Bridge to Sandahi
Agreement NO - 42/MBD/2021-22 Date 12.04.2021.

ग्रामीण कार्य विभाग कार्य प्रमोडल पुपरी

DIVISION

ग्रामीण कार्य विभाग कार्य अवर प्रमोडल
मुसंड

SUB-DIVISION

MEASUREMENT BOOK

NO-2522

Agency: - Shree Anandh Mithila Constn Pvt Ltd M42.

1st and final Bill

(These four lines should be repeated at the commencement of the measurement relating to each work)

of the measurement relating to each work)					
Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
N/WORKI-	MR	g road NH	104	Jamura	
	Bridge-to	Sondahi-		in	
	Surand	block under MR-			
	305A(New)				
Agency:-	Shree Anandh	Milkla Const.			
	Pvt Ltd-	Muzaffarpur-			
Agreement No/Date:-	01/	MBD/	2021-22		
		Date	12.	04-2021.	
Date of start:-	12.	04-2021.			
Date of completion:	11.	01 -	2022.		
Actual Date of completion:-	30.	05-2022			
Date of measurement:-	30.	05-2022			

Continuation

- Abstract of Cost :-

11

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(1) Clearing and Grubbing by (manual means) including uprooting wild vegetation - grass, bushes - etc alg vide TMB-P-01. alg 0.346 Ha @ 51133.76/m ³					17,692.00
(2) Construction of Subgrade and Earthen Shoulders - alg 674.70 m ³ @ 175.22/m ³					118,221.00
(3) Construction of G.S.B. Gr II by providing well graded material spreading in uniform layer alg vide TMB-P-03/- alg 85.05 m ³ @ 1973.69/m ³					1,67,862.00
(4) Providing laying, spreading and compacting WBM - Gr II alg vide TMB-P-05 alg 50.01 @ 3503.55/m ³					1,75,213.00
(5) Providing laying, spreading and compacting WBM - Gr III alg vide TMB-P alg 89.17 m ³ @ 3251.02/m ³					2,89,893.00

Continuation

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(6) Providing and applying with Bitumen emulsion (SS1).					
alg vide TMB-P-07.					
alg 1188.99 m ² @ 42.19/m ² =					50163.00
(7) Providing and applying with bitumen emulsion (RS1)					
alg vide TMB-P-07.					
alg 1222.74 m ² @ 14.34/m ² =					17534.00
(8) Providing laying and rolling Primix bitumen surfacing.					
20 mm thick.					
alg 1222.74 m ² @ 206.39/m ² =					2,52,361.00
(9) Providing and applying with bitumen emulsion (RS1)					
alg vide TMB-P-08.					
alg 6487.50 m ² @ 12.02 m ² =					77,980.00
(10) Providing laying and rolling SDBC.					
alg vide TMB-P-08.					
alg 162.19 m ³ @ 10503.56/m ³ =					1703572.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(11) R.C.C. M 15 grade concrete					
Kilometre stone-					
(i) Km stone-					
alg 03 Nos @ 2198.25/-					
					each = 6595.00/-
(ii) 200 mt Stone.					
alg 07 Nos @ 609.42					each = 4266.00/-
(12) Providing and fixing.					
Direction and plane.					
identification sign board					
alg 1.92 m ² @ 12307.01/m ²					23629.0
(13) Providing and fixing Retra-					
reflectorised, sign board -					
(i) 600 mm equilateral triangle -					
alg 2.00 Nos @ 3584.31					each = 7169.00/-
(ii) 600 mm circular -					
alg 2.00 Nos @ 3783.99					each = 7568.00/-
(iii) 600 mm x 450 mm.					
rectangular					
alg 2.00 Nos @ 3654.87					each = 7310.00

Continuation

Continuation

20.06.98
